

National Highways Authority of India
(Ministry of Road Transport & Highways)



PATEL DARAH-JHALAWAR HIGHWAY PRIVATE LIMITED

CONSTRUCTION OF 4-LANE ROAD ON NH-12 (NEW NH-52) FROM Km. 299.000 TO Km. 346.540 (DESIGN CHAINAGE 9.860 TO 58.740) (DARAH – JHALAWAR – TEENDHAR) IN THE STATE OF RAJASTHAN UNDER NHDP PHASE-III ON HYBRID ANNUITY PROJECT.

INDEPENDENT ENGINEER

LEA ASSOCIATES SOUTH ASIA PVT. LTD

MONTHLY PROGRESS REPORT

For The Month of July-2019

Executive Summary

The old National Highway 12 runs through two big states Rajasthan and Madhya Pradesh. The total length of the old NH- 12 was 897/00 Km. The length of Old NH 12 was 408/700 Km in the state of Rajasthan. Recently MORTH has amended the number and length of the National highways. The old NH 12 in the state of Rajasthan has become the part of the New National highway 52. The New NH 52 starting from its junction with NH-7 near Sangrur in the state of Punjab connecting Narwana, Hisar in the state of Haryana, Fatehpur, Jaipur, Tonk, Kota, Aklera in the state of Rajasthan, Rajgarh, Biora, Dewas, Indore, Sendhwa in the state of Madhya Pradesh, Dhule, Aurangabad, bed, Osmanabad, Solapur in the state of Maharastra, Bijapur, Hubli and terminating at its junction with NH-66 near Ankola in the state of Karnatka.

The Project stretch Darah-Teendhar is connected to Jaipur at one end and it is connected to Bhopal at the other end. The project highway is very important highway as it connects the Capital of Rajasthan states and National capital of country through Jaipur- Delhi Highway.

The project highway is very important highway as it connects to two state Rajasthan and Madhya Pradesh. The Darah-Jhalawar-Teendhar section of National Highway has moderate traffic density. In addition to this there are few sections where alignment needs geometric improvements to maintain riding quality of highway and safe movement of vehicles. Apart from this the present alignment of NH is passing through various congested towns and villages. All of the above factors are demanding the existing 2-lane highway to be developed as 4-lane divided carriageway with bypass provisions in congested towns/ villages.

The Project Highway traverses through two districts viz. Kota and Jhalawar in Rajasthan State. The project study corridor starts at the end of ROB approach near to Darah at km 289+500 and passes through five major towns Darah, Sarvada, Dabadeh, Suket and Jhalawar, and it ends at Teendhar, Existing km 346.540 Km. Existing road width is 2 lane standard. The Existing ROW varies from 15 m to 30 m. The entire project length is under the administrative control of PIU Kota.

Project Synopsis

National Highways Authority of India plans to undertake the Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage From 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Mode (Length 48.880 Km.) – Package II.

The National Highways Authority of India (NHAI) is undertaking the up-gradation of NH-12 from Existing two lane road to four lane divided carriageway in state of Rajasthan.


The project involves up gradation of 48.88 Km from two-lane to the four-lane divided carriageway. It includes the construction of bridges, intersections, service roads, culverts and related infrastructure, and the installation of signaling systems and signboards. The project will be developed under National Highways Development Project (NHDP) Phase-III on Hybrid Annuity Mode.

Existing and Proposed alignment

SR. NO.	Existing Chainage (Km)		Length	Design Chainage (Km)		Design Length (Km)	Name of Revenue Village
	To	From		To	From		
1	299	299.34	0.34	9.86	10.2	0.34	KAMALPURA
2	299.34	299.74	0.4	10.2	10.6	0.4	KAMALPURA
3	299.74	300.14	0.4	10.6	11	0.4	KAMALPURA
4	300.14	300.44	0.3	11	11.3	0.3	KAMALPURA
5	300.44	300.778	0.338	11.3	11.638	0.338	KOOKARA KHURD
6	300.778	301.255	0.477	11.638	12.115	0.477	MANPURA
7	Dabadeh & Sahrawad a Bypass			12.115	12.3	0.185	MANPURA
8				12.3	13.028	0.728	ZALIMPURA
9				13.028	14.2	1.172	SAHRAWADA
10				14.2	15.661	1.461	TELYA KHERI
11				15.661	17.242	1.581	ASKALI
12				17.242	19.273	2.031	HIRIYA KHERI
13				19.273	19.788	0.515	KHEEMACH
14	308.203	308.515	0.312	19.788	20.1	0.312	KHEEMACH
15	308.515	308.715	0.2	20.1	20.3	0.2	KHEEMACH
16	308.715	308.915	0.2	20.3	20.5	0.2	ATRALIYA
17	308.915	309.079	0.164	20.5	20.664	0.164	ATRALIYA
18	Atraliya Realignment			20.664	21.682	1.018	ATRALIYA
19	310.007	310.125		21.682	21.8	0.118	ATRALIYA
20	310.125	310.325		21.8	22	0.2	ATRALIYA
21	310.325	310.444		22	22.119	0.119	GORDHANPURA

SR. NO.	Existing Chainage (Km)		Length	Design Chainage (Km)		Design Length (Km)	Name of Revenue Village
22	Atraliya Realignment			22.119	22.464	0.345	GORDHANPURA & PAMA KHERI
23	310.789	311.125		22.464	22.8	0.336	PAMA KHERI
24	311.125	311.494		22.8	23.169	0.369	PAMA KHERI
25	311.494	311.625		23.169	23.3	0.131	PAMA KHERI
26	311.625	311.776		23.3	23.451	0.151	PAMA KHERI
27	311.776	312.025		23.451	23.7	0.249	PAMA KHERI
28	312.025	312.725		23.7	24.4	0.7	DEENGASI
29	312.725	312.925		24.4	24.6	0.2	DEENGASI
30	312.925	313.025		24.6	24.7	0.1	DEENGASI
31	313.025	313.125		24.7	24.8	0.1	DEENGASI
32	313.125	313.37		24.8	25.045	0.245	DEENGASI
33	313.37	313.535		25.045	25.21	0.165	DEENGASI
34				25.21	25.254	0.044	DEENGASI
35				25.254	26.124	0.87	UMMEDPURA
36				26.124	27	0.876	RAMPURIYA
37				27	27.358	0.358	SUKET
38				27.358	27.854	0.496	BEER MANDI
39				27.854	28	0.146	SUKET
40				28	29.571	1.571	ARANYA KHURD
41				29.571	31.212	1.641	SURERA
42				31.212	33.617	2.405	BANSYA HERI
43				33.617	35.565	1.948	ARANYA KALAN
44	Suket,			35.565	36.1	0.535	KALMANDI
45	Jhalawar & Jhalrapatan Bypass			36.1	38	1.9	HARISH PURA
46				38	38.537	0.537	RALAYTI
47				38.537	40.343	1.806	RALAYTA
48				40.343	41.784	1.441	JHALRAPATAN
49				41.784	44.224	2.44	MADHOPUR
50				44.224	49.8	5.576	HARIPURA
51				49.8	51.434	1.634	HARIPURA,
52				51.434	52.516	1.082	BANJARI &
53				52.516	54.2	1.684	BHANWARSA
54				54.2	54.565	0.365	BHANWARSA
55	342.895	343.673		54.565	55.343	0.778	BHANWARSA
56	343.673	347.127		55.343	58.74	3.397	BHANWARSA & ROOPAREL

KEY PLAN OF THE PROJECT

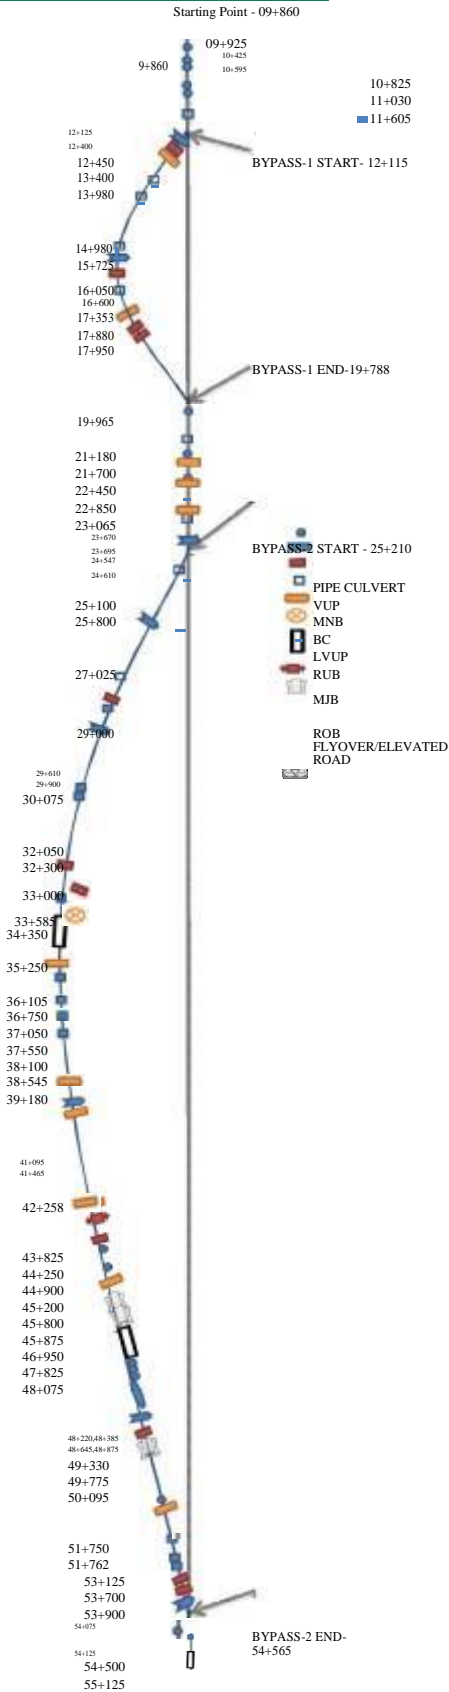

PROJECT SUMMARY

Project	Construction of 4-lane Road on NH-12 New NH-52 from Km 299.000 to 346.540 Design Chainage From 9.860 to 58.740 Darah-Jhalawar-Teendhar Section in the State of Rajasthan under NHDP Phase-III Length 48.880 km Package II on Hybrid Annuity Mode.
Owner/Client	National Highways Authority of India
Concessionaire	Patel Darah Jhalawar Highway Pvt. Ltd.
Independent Engineer	LEA ASSOCIATE SOUTH ASIA PVT. LTD
Project Length (In Km)	48.88 Km
Total Project Cost as per CA	1123.63 Cr.
Concession Period	15 Years
Construction Period	910 Days from the Appointed Date.
Date of Signing of Concession Agreement	16 th November 2017
Appointed Date	24 th May 2018 (Letter ref. No. NHAI /19030/Dara-Teen/Raj/2016/1/120723 dated 09 th July 2018.

1.2 Project Overview

1.2.1 Structures

S. No.	Feature	Description
1	Major Bridge	02 Nos. – (13 x 25mtr) & (13 x 31.6mtr_3-Lane)
2	Elevated Flyover cum MJB	01 Nos. – (20 x 25mtr)
3	Flyovers/ Interchange	03 Nos. (1 Nos. – 4x25mtr.) (2 Nos. – 3 x 24mtr.)
4	ROB/ RUB	1/1 = 2 Nos.
5	Minor bridges	11 Nos.
6	Vehicular underpass	09 Nos. – (1x24mtr)
7	Light Vehicular Underpasses	13 Nos.
8	Culverts (HP/BC)	37 Nos. (16 Nos. Pipe / 21 Nos. Box)
9	RE Wall	14.454 Km
10	Toll Plaza	1 No (16 Lanes)
11	Truck Lay Bys	1 (Both side)
12	Bus Shelter	5 Nos (Both side)
13	Rest Area	1no

Project Milestones

Project Milestone	Condition	Time Line	Date	Financial Progress
I	Commenced construction of Project and achieved 20% of Physical Progress	290 th Day from Appointed date	10 th March 2019	224.73 Cr.
II	Commenced construction of Project and achieved 35% of Physical Progress	430 th Day from Appointed date	28 th July 2019	393.29 Cr.
III	Commenced construction of all Project Facilities and achieved 75% of Physical Progress	690 th Day from Appointed date	13 th April 2020	842.76 Cr.
IV	Completion Of the Project	910 th Day from Appointed date	19 th Nov 2020	1123.68 Cr.

Progress Status as per submitted programme

Sr.No	Item	Unit	Scope of work as per schedule -B	Planned upto July.2019	Progress Achieved upto June-2019	This Month Progress	Cumulative Progress	Program for the month of Aug-2019
Highway Progress (Km.)								
1	C & G	Km	46.25	38.81	37.09	1.2	38.29	0
2	Embankment	Km	46.25	26.16	26.54	0	26.54	0
3	Subgrade	Km	46.25	23.75	12.5	0	12.5	0
4	G.S.B	Km	46.25	20.07	11	0	11	0
5	D.L.C	Km	46.25	14.283	9.723	0.79	10.513	0
6	P.Q.C	Km	46.25	12.6	8.280	0.93	9.210	0
Structure Progress: (No.s)								
1	HPC		16+25=41	15	30.5	0	30.5	0
2	BC		21+4=25	17	15	1.5	16.5	1
3	MNB		11	5	1.5	1.5	3	1
4	MJB		2	0	0	0	0	0
5	VUP		9	7	0	0	0	0
6	LVUP		13	9.5	7	1	8	1
7	Elevated		1	0	0	0	0	0
8	ROB		1	0	0	0	0	0
9	RUB		1	0	0	0	0	0
10	Flyover		3	1	0	0	0	0

1. Cumulative Physical Progress Planned upto March 2020:- 59.99%
2. Physical Progress Planned upto July-2019:- 35.77%
3. Physical Progress achieved upto June-2019:- 29.11%
4. Physical progress achieved in Month of July-2019:- 00.18%
5. Cumulative physical progress upto July-2019:- 29.29%

1.1 Summary of Progress
Summary of Progress (July 2019)

Highway Progress:

Sr. No.	Item	Unit	Scope of work	Completed / Work in progress	Balance work
1	C & G	Km	46.25	38.29	10.16
2	Earthwork	Km	46.36	26.54	20.32
3	Sub- Grade	Km	46.36	12.50	35.36
4	GSB	Km	46.36	11.00	36.86
5	DLC (MC)	Km	46.36	10.513	35.84
6	PQC (MC)	Km	46.36	9.210	37.15
7	Earthwork(SR)	Km	28.38	1.550	26.83
8	Sub- Grade(SR)	Km	28.38	0.490	27.89
9	GSB(SR)	Km	28.38	0	28.38
10	WMM (SR)	Km	28.38	0	28.38
11	DBM (SR)	Km	28.38	0	28.38
12	BC (SR)	Km	28.38	0	28.38

Structure Progress Status:-

Sl. No.	Structure Details:-	Unit	Scope	Completed	Work in progress	Balance	Remarks
1	Major Bridge	Nos	2	0	2	0	
2	Elevated Road	Nos	1	0	1	0	
3	Minor Bridge	Nos	11	3	4	4	
4	Box Culvert	Nos	25	16.5	2.5	6	4 (Additional)
5	Pipe Culvert	Nos	41	30.5	2.5	8	25(Additional)
6	Vehicular Underpass	Nos	9	0	7	2	
7	Light Vehicular Underpass	Nos	13	8	2	3	
8	Flyover	Nos	3	0	2	1	
9	ROB	Nos	1	0	0	1	
10	RUB	Nos	1	0	0	1	
11	Drain	Km	28.38	10.472	3	14.908	

1. Physical progress Achieved upto 31st July 2019- 29.29%

2. Financial Progress Achieved upto 30th June - Rs. 410.86 Crs i.e 36.57 %

(Financial S- Curve attached at the end)

Utility Shifting Progress

24-05-2018 is the Appointed Date for the project. 85% of the land measuring to Km 41.548 has been handed over by the Authority. 15% of land is balance due to presence of structures, religious structure and other land related issues.

1. Permission for cutting of trees on Government land and forest land received. Cutting of trees in progress. Ref. no 1594 dated 03 / 05 / 2018 (Jhalawar) & 1837-44 dated 22/05/2018(Kota)
2. Electrical Utilities estimate approved in both district Kota & Jhalawar vide letter 41010 & 41011 1/2016- Kota / US – Electric- Kota and Jhalawar / Package-2/7077 dated 24th August 2018. Work for shifting of electrical utilities under progress. Work is balance in existing alignment due to presence of structure.
3. Water Pipelines Estimate is approved vide letter no. _41024 / 1 / 2016- Kota/ US - PHED- Kota / Pkg-II/ 6998 dated 16-08 2018 and 41025 /_1 / 2016- Kota / US /6997 dated 16-08-2018 Shifting work in progress. Work balance only in stretches having LA related issues.
4. HT line have been identified and submitted to concern Department for preparation of estimate. Approval pending.

Details of numbers and length are as below: -

SI No	Utility	Length/ No.	Completed	Balance	Present Status/ Remarks
1	Electric Poles	741 Nos	704	37	Poor progress due to non availability of fronts. Work balance only in existing road alignment only. Payment to owners to be expedited.
2	Water Pipe Line (km)	21 Km	18.05	2.95	Poor progress due to non availability of fronts. Work balance only in stretches having LA related issues. Payment to owners to be expedited.
	Crossings	45 Nos.	38	7	
3	HT Line Crossing	6 nos			Estimate submitted to NHAI for Approval.

4	Trees	8156 Nos.	7507 Nos.	649	Cutting in progress
---	-------	-----------	-----------	-----	---------------------

Tre
e

Cutting Permission Status:-

S. No.	District	Category		Nos.	Status			Trees Cut	Balance to be cut	Remarks
					Cutting Permission	Approval Letter No.	Date			
1	Kota	Govt Trees	All	465	Yes	Revenue-III/2018/1837-44	22.05.2018	402	63	Disbursement in progress
		Private Trees	Fruit	2797	Yes	No.41002/2016-kota/L.A/Ramganjmandi/pkg-2/6243	17.04.2018	2797	0	
			Fruitless	1280	Yes			1215	65	
2	Jhalawar	Govt Trees	All	972	Yes	Revenue/18/1594,1861 & 2868	03.05.2018, 25.05.2018 & 06.11.2018	972	0	429 tree cutting approval vide letter no. 2868 dated 06.11.2018
		Private Trees	Fruit	1836	Yes	No.41003/2016-kota/L.A/Jhalawar/pkg-2/6242	17.04.2018	1417	419	Award finalized
			Fruitless	702	Yes			600	102	Disbursement in progress
		Forest		104	yes	F-14()2017/Jhalawar Road/FCA/1998	19.04.2018	104	0	
3	TOTAL			8156				7507	649	92%

- 1) Total No. of trees increased from 7727 to 8156 Nos. because of 429 trees along existing alignment added between Km.54.000 to 58.740.
- 2) Payment for private trees in jhalawar district pending.

Status of Conditions precedent

a	Provided Performance Security to the Authority	Submitted
b	Executed and procured execution of Escrow Agreement	Submitted. Vide this office letter no. PDJHPL / NHAI / FC / 039 .2018 Dt. 21-05-2018.
c	Executed and procured execution of Substitution Agreement	Submitted. Vide this office letter no. PDJHPL / NHAI / FC / 039 .2018 Dt. 21-05-2018.
d	Procure all Applicable Permits as per Schedule -E	Obtained/ under progress
e	Executed Financing Agreements and delivered 3 copies duly attested by Director of the Concessionaire	Submitted. Vide this office letter no. PDJHPL / NHAI / FC / 039 .2018 Dt. 21-05-2018
f	Delivered to Authority 3 true copies of Financial Package and Financial Model duly attested by Director of the Concessionaire	Submitted. Vide this office letter no. PDJHPL / NHAI / FC / 039 .2018 Dt. 21-05-2018.
g	Delivered to Authority from Selected Bidder its respective confirmation in original of the correctness of their representations and warranties set forth in Sub Clause (k), (l) and (m) of Clause 7.1 of CA	Submitted
h	Environment	Done
i	Forest Land	Stage –II Clearance obtained
j	Wild Life	NA

Status of Railway Approvals

Proposal Description	Status	Length Impacted	Current Stage	Issues/ Comments
1. Rail ROB	GAD of ROB Approved	-	Detailed design and drawing Approved by Railways.	Foundation Work in Progress.
2. RUB	GAD of RUB Approved	-	Detailed design and drawing Approved by Railways.	Falling in DLC issue stretch

ISSUES OF CONCERN: -

1. (a) DLC issue from Km- 33+500 to 36+000 and 51+400 to 52+100 (Haripura). The land is yet to be taken under possession.
(b) Court Case Chainages :- Possession of following chainages is balance because of pending cases in SDM court Ramganjmandi.

Sr no.	Chainage		Length (M)
	From	To	
1	10+890	11+000	110
2	20+580	20+730	150
3	20+750	20+830	80
4	21+380	21+500	120
5	23+000	23+400	400
6	24+000	24+100	100
7	30+150	30+270	120
8	30+500	30+585	85
9	41+200	41+300	100
10	42+330	42+400	70
11	Total		1335

2. Disbursement of payment for structures in both the districts Kota and Jhalawar started, but progress is very slow. No payment towards LA / structures has been released by CALA in Ramganjmandi (Kota district) in last one months. Disbursement of payment started in last week of June-2019. Because of non-removal of these hindrances the progress of electrical and water line shifting is affected, continuity of work fronts cannot be maintained. After disbursement of payment, it will take at-least 4-5 months for physical removal of these hindrance because of monsoon season. After removal of these structures, shifting of electrical and water utilities can be taken up. Private trees award amount deposited to CALA. Disbursement of funds yet to be started.
3. Villagers have reported the matter to D.M (Jhalawar) for early processing. Ramganjmandi payment has been released to CALA and payment under progress.
4. Approval of estimate for shifting of HT line Crossing yet to be done.
5. 3A of missing plots in Jhalawar district is pending.
6. Disbursement of payment of religious structure within PROW is yet to be done (Jhalawar District).
7. The progress of L.A disbursement in Ramganjmandi (Kota district) is very slow and needs to be expedited in order to maintain the continuity of work fronts. Discontinuity of work stretches is having a direct impact on progress of work.
8. The details of hindrances is attached as **Annexure-I**.

**MONTHLY PROGRESS REPORT
MONTH OF July- 2019**


Sr. No.	Name of Test	Number of Tests Conducted									Remarks
		Up To Previous Month			This Month			Total upto Date			
		Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test	
OGI & Cutting soil											
1	Free Swell Index	311	0	311	0	0	0	311	0	311	
2	Grain Size Analysis	311	0	311	0	0	0	311	0	311	
3	Plasticity Index	311	0	311	0	0	0	311	0	311	
4	Max. Dry Density	311	0	311	0	0	0	311	0	311	
5	CBR	6	0	6	0	0	0	6	0	6	
6	Density of Comp.Layer	5325	143	5468	10	0	10	5335	143	5478	
Borrow Area (Embankment & Subgrade)											
1	Free Swell Index	1285	42	1327	55	0	55	1340	42	1382	
2	Grain Size Analysis	1285	42	1327	55	0	55	1340	42	1382	
3	Plasticity Index	1285	42	1327	55	0	55	1340	42	1382	
4	Max. Dry Density	1293	42	1335	59	0	59	1352	42	1394	
5	CBR	202	25	227	27	3	30	229	28	257	
5	Direct shear test	1285	42	1327	55	0	55	1340	42	1382	
Earthwork Field test											
1	Density of Comp.Layer (Emb.)	33514	355	33869	870	19	889	34384	374	34758	
2	Density of Comp.Layer (Sub grade & Earthen shoulder)	4617	53	4670	219	9	228	4836	62	4898	
GSB											
1	Sieve Analysis	203	0	203	15	0	15	218	0	218	
2	Plasticity Index	200	0	200	15	0	15	215	0	215	
3	Max. Dry Density	4	0	4	0	0	0	4	0	4	
4	CBR	2	0	2	0	0	0	2	0	2	
5	Water Absorption	2	0	2	0	0	0	2	0	2	
6	AIV	3	0	3	0	0	0	3	0	3	

Sr. No.	Name of Test	Number of Tests Conducted									Remarks
		Up To Previous Month			This Month			Total upto Date			
		Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test	
OGL & Cutting soil											
7	Density of Comp.Layer	503	14	517	45	3	48	548	17	565	
PHYSICAL PROPERTIES OF AGGREGATE FOR CONCRETE											
1	Sieve Analysis of CA	655	0	655	60	0	60	715	0	715	
2	Sieve Analysis of FA	602	0	602	60	0	60	662	0	662	
3	Sieve Analysis of DLC	79	0	79	15	0	15	94	0	94	
4	Sieve Analysis of PQC	80	0	80	11	0	11	91	0	91	
5	Aggregate Impact Value	658	0	658	45	0	45	703	0	703	
6	Flakiness Index	658	0	658	45	0	45	703	0	703	
7	Silt Content	239	0	239	30	0	30	269	0	269	
8	Specific Gravity & W A	10	0	10	4	0	4	14	0	14	
Concrete Mix Design (cube sets)											
1	M15 7 Days	34	0	34	0	0	0	34	0	34	
	28 Days	64	0	64	0	0	0	64	0	64	
2	M20 Kerb 7 Days	6	0	6	0	0	0	6	0	6	
	28 Days	4	0	4	6	0	6	10	0	10	
	M20 7 Days	12	0	12	0	0	0	12	0	12	
	28 Days	18	0	18	0	0	0	18	0	18	
3	M25 7 Days	64	0	64	1	0	1	65	0	65	
	28 Days	103	0	103	1	0	1	104	0	104	
4	M30 7 Days	66	0	66	0	0	0	66	0	66	
	28 Days	121	0	121	0	0	0	121	0	121	
5	M35 7 Days	114	0	114	4	0	4	118	0	118	
	28 Days	193	0	193	6	0	6	199	0	199	
6	M35 Pile 7 Days	68	0	68	0	0	0	68	0	68	
	28 Days	140	0	140	0	0	0	140	0	140	
7	M35 RE block 7 Days	45	0	45	0	0	0	45	0	45	

Sr. No.	Name of Test	Number of Tests Conducted									Remarks
		Up To Previous Month			This Month			Total upto Date			
		Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test	
OGI & Cutting soil											
	28 Days	144	0	144	0	0	0	144	0	144	
8	M40 7 Days	70	0	70	0	0	0	70	0	70	
	28 Days	111	0	111	0	0	0	111	0	111	
9	M45 7 Days	53	0	53	0	0	0	53	0	53	
	28 Days	101	0	101	0	0	0	101	0	101	
10	M50 7 Days	0	0	0	0	0	0	0	0	0	
	28 Days	0	0	0	0	0	0	0	0	0	
11	M40 PQC 7 Days	110	0	110	8	0	8	118	0	118	
	28 Days	178	0	178	13	0	13	191	0	191	
12	M40 PQC Fl. Strength 7 Days	86	0	86	1	0	1	87	0	87	
	28 Days	104	0	104	0	0	0	104	0	104	
13	DLC 7 Days	27	0	27	0	0	0	27	0	27	
Field Concrete (cube sets)											
1	M15 7 Days	1037	0	1037	55	0	55	1092	0	1092	
	28 Days	1443	0	1443	174	0	174	1617	0	1617	
2	M20 Kerb 7 Days	10	0	10	19	0	19	29	0	29	
	28 Days	4	0	4	27	0	27	31	0	31	
3	M25 7 Days	1132	0	1132	114	0	114	1246	0	1246	
	28 Days	1367	0	1367	213	0	213	1580	0	1580	
4	M30 7 Days	171	0	171	45	0	45	216	0	216	
	28 Days	372	0	372	12	0	12	384	0	384	
5	M35 7 Days	1231	0	1231	154	0	154	1385	0	1385	
	28 Days	2635	0	2635	356	0	356	2991	0	2991	
6	M35 Pile 7 Days	67	0	67	0	0	0	67	0	67	
	28 Days	95	0	95	0	0	0	95	0	95	
7	M35 RE block 7 Days	659	0	659	25	0	25	684	0	684	

Sr. No.	Name of Test	Number of Tests Conducted									Remarks
		Up To Previous Month			This Month			Total upto Date			
		Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test	
OGL & Cutting soil											
	28 Days	2055	0	2055	98	0	98	2153	0	2153	
8	M40 7 Days	55	0	55	3	0	3	58	0	58	
	28 Days	47	0	47	3	0	3	50	0	50	
9	M45 7 Days	9	0	9	9	0	9	18	0	18	
	28 Days	20	0	20	6	0	6	26	0	26	
10	M50 7 Days	0	0	0	0	0	0	0	0	0	
	28 Days	0	0	0	0	0	0	0	0	0	
11	M40 PQC 7 Days	130	0	130	26	0	26	156	0	156	
	28 Days	137	0	137	6	0	6	143	0	143	
12	M40 PQC Flexural Strength 7 Days	130	0	130	26	0	26	156	0	156	
	28 Days	140	0	140	6	0	6	146	0	146	
13	DLC 7 Days	99	0	99	20	0	20	119	0	119	
14	DLC FDD	403	0	403	66	0	66	469	0	469	
Cement											
1	Fineness	69	0	69	7	0	7	76	0	76	
2	Consistency	69	0	69	7	0	7	76	0	76	
3	Setting Time	69	0	69	7	0	7	76	0	76	
4	Soundness	49	0	49	7	0	7	56	0	56	
5	Compressive Strength										
	a) 3 Days	63	0	63	7	0	7	70	0	70	
	b) 7 Days	60	0	60	8	0	8	68	0	68	
	c) 28 Days	69	0	69	8	0	8	77	0	77	

Sl. No.	Date	Temperature C		Humidity %		Rainfall (mm)
		Min. Temp. (°C)	Max. Temp. (°C)	Min.	Max.	
1	01-07-19	25.9	34.0	10.0	11.0	0.0
2	02-07-19	26.8	36.0	10.0	11.0	0.0
3	03-07-19	26.0	30.2	10.0	14.0	19.4
4	04-07-19	25.8	29.9	10.0	15.0	64.6
5	05-07-19	26.5	29.2	10.0	15.0	2.4
6	06-07-19	25.5	29.5	10.0	14.0	18.8
7	07-07-19	25.8	32.3	10.0	14.0	43.0
8	08-07-19	27.1	31.6	10.0	14.0	0.0
9	09-07-19	27.9	32.2	10.0	11.0	0.0
10	10-07-19	27.6	35.8	10.0	10.0	0.0
11	11-07-19	29.0	39.1	10.0	10.0	0.0
12	12-07-19	28.9	34.1	10.0	10.0	0.0
13	13-07-19	28.8	32.6	10.0	10.0	0.0
14	14-07-19	27.6	33.9	10.0	10.0	2.0
15	15-07-19	28.8	32.7	10.0	10.0	0.0
16	16-07-19	29.1	35.4	10.0	10.0	0.0
17	17-07-19	29.1	34.8	10.0	10.0	0.0
18	18-07-19	28.8	35.2	10.0	10.0	0.0
19	19-07-19	28.9	34.6	10.0	10.0	0.0
20	20-07-19	29.4	37.9	10.0	10.0	0.0
21	21-07-19	29.6	38.4	10.0	10.0	0.0
22	22-07-19	30.1	39.2	10.0	10.0	0.0
23	23-07-19	28.2	37.1	10.0	11.0	0.0
24	24-07-19	27.1	35.2	10.0	10.0	0.0
25	25-07-19	25.9	35.1	10.0	10.0	20.4
26	26-07-19	23.1	30.4	10.0	12.0	1.0
27	27-07-19	24.2	28.3	10.0	14.0	21.0
28	28-07-19	24.1	28.5	10.0	14.0	23.5
29	29-07-19	26.8	30.7	10.0	14.0	2.5
30	30-07-19	25.4	31.9	10.0	13.0	36.0

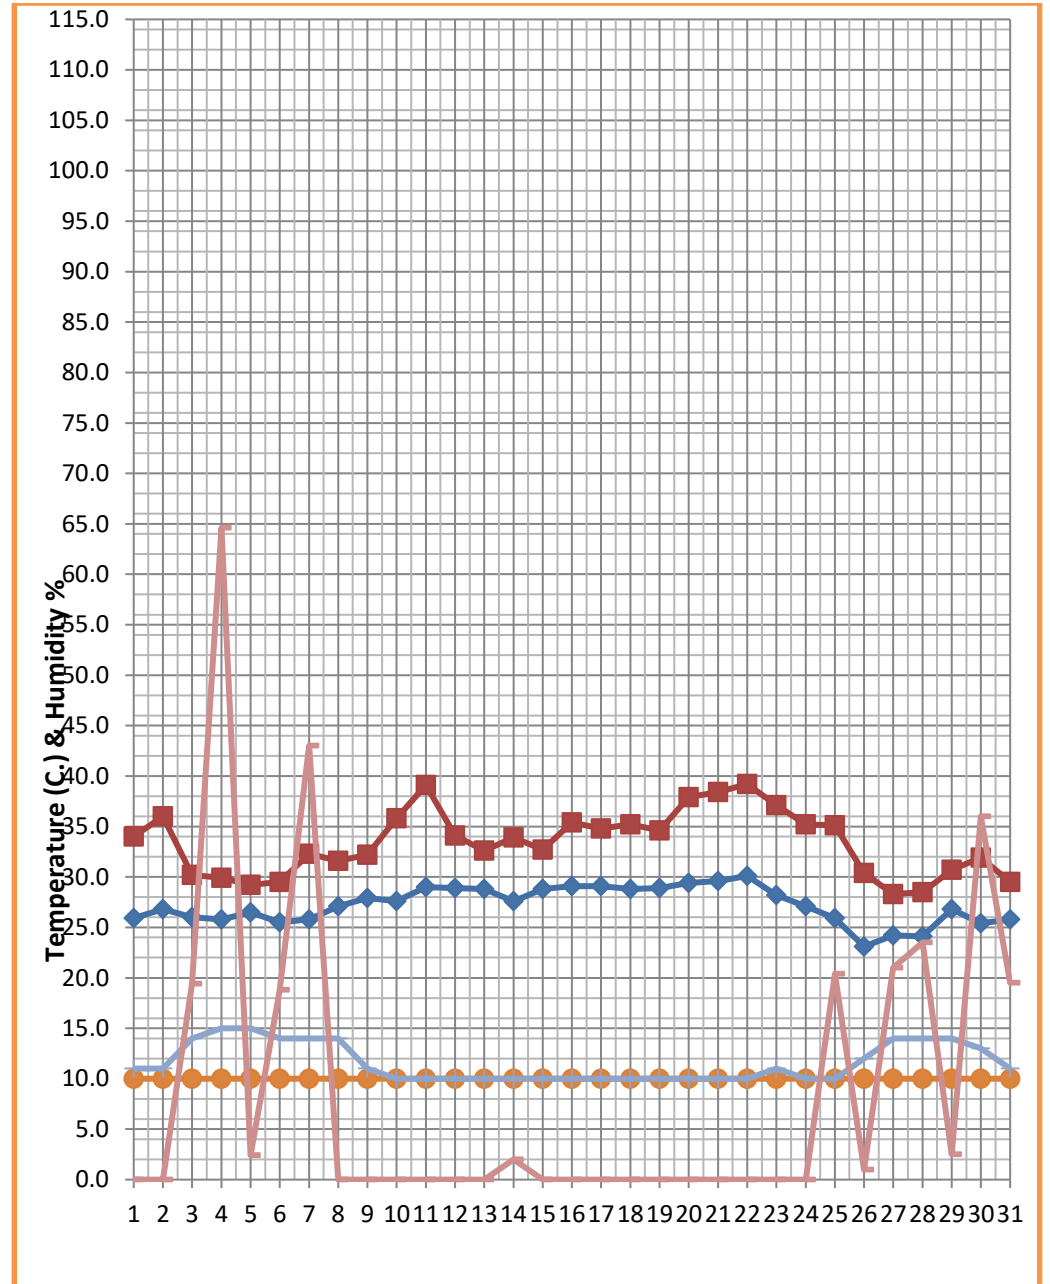

Status of Design Mixed and source approval

Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
1	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	Submission of Mix Design	LASA/Concessionaire/ DJ/IE/2018/0003	21.08.2018
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-15(PCC Work) with flyash		
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-25(RCC Work) with flyash		
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-30(RCC Work) with flyash		
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-35(RCC Work) with flyash		
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-35(Pile Work with flyash		
2	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	Submission of Mix Design of Concrete from Ultratech & Mangalam Cement	LASA/Concessionaire/ DJ/IE/2018/0003	21.08.2018
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-35 RE Block (Ultratech & Mangalam cement)		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-35 with flyash RE Block (Ultratech & Mangalam cement)		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-15 PCC		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-25 RCC		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-30 RCC		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-35 RCC		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-35 Pile work		
3	PIL/CAMP/DJT/NHAI/2018-04/08	26.04.2018	Submission of Company profile & credential for the D.P. Wires	LASA/Concessionaire /Darah- Jhalawar/IE/2018/191	08.12.2018
4	PIL/CAMP/DJT/NHAI/2018-04/09	26.04.2018	Submission of Company profile & credential for the Shyam, Electrosteel and Premier Steel		
5	PDJHPL/NHAI/DJT/2018/019	12.03.2018	Submission of Company profile & credential for the Rashtriya Ispat Nigam Ltd (Vizag Steel),Nilkanth Steel Pvt.ltd. ,Steel authority of India limited (SAIL) ,Jindal steel & power limited ,Rashmi group ,Madhav Alloys Pvt.limited	LASA/Concessionaire/ DJ/IE/2018/17 and 58, 59 (10.09.2018)	30.08.2018
7	PIL/CAMP/DJP/N HAI/2018 -04 / 063	21.06.2018	Submission of construction material for testing.		
8	PIL/CAMP/DJP/N HAI/2018 -04 / 063	21.06.2018	Steel Dia 20mm JSW Steel (Fe-5.50D)		
10	PIL/CAMP/DJP/N HAI/2018 -04 / 063	21.06.2018	Steel - Dia 12,25 & 32mm SAIL (Fe-500D)		
10	PDJHPL/NHAI/DJT/2018/013	26.02.2018	Submission of Company profile & credential for the Birla Corporation Limited , Mangalam Cement Limited , Wonder cement Limited . Ultrtech cement Limited , Vadraj cement . Shree cement Limited	LASA/Concessionaire/ DJ/IE/2018/14	28.08.2018

Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
11	PIL/CAMP/DJT/NHAI/2018-04/01	26.04.2018	Submission of Company profile & credential for the BASF India Ltd.for Admixture,Grout and joint Sealant , Unirock Chemicals (Admixture) , Tikitar Ltd. For Joint Sealant	LASA/Concessionaire/ DJ/IE/2018/016	30.08.2018
12	PDJHPL/NHAI/DJT/2018/020	22.03.2018	Submission of Company profile & credential for Admixture and curing compund ,Kunal conchem pvt.ltd.,National Chemicals Industries, Rheoplast technology pvt.ltd.,Molecules Conchem Pvt ltd.,Grout and joint Sealant ,STPLlimited & Chembond Chemicals Ltd.		
13	PIL/CAMP/DJP/N HAI/2018 -04 / 063	21.06.2018	Adrnixture - PC 100R (Kunal Industries)		
14	PDJHPL/PIU/CLO-179/201 8/095	04.07.2018	DLC Flyash		
15	PDJHPL/PIU/CLO-179/201 8/095	04.07.2018	DLC without Flyash		
16	PIL/CAMP/DJP/N HAI/2018 -04 / 063	21.06.2018	GSB (Julmi PIL Crusher)		
18	PIL/CAMP/DJT/NHAI/2018-04/06	26.04.2018	Submission of Company profile & credential for the IOCL (Bitumen) ,HPCL (Bitumen) ,ESSAR (Bituman) , GP global (Emulsions) , HINCOL (Emulsions) Total oil India pvt ltd. (Emulsions)	LASA/Concessionaire/ DJ/IE/2018/020 Bitumen& 19 for Emulsion	31.08.208
19	PIL/CAMP/DJT/NHAI/2018-04/02	26.04.2018	Submission of Company profile & credential for the SGG spun pipes	LASA/Cocessionaire/ Darah- Jhalawar/IE/2018/050	07.09.2018
20	PIL/CAMP/DJT/NHAI/2018-04/03	26.04.2018	Submission of Company profile & credential for the TIKIDAN Danosa India	LASA/Concessionaire /Darah- Jhalawar/IE/2018/212	14.12.2018
21	PIL/CAMP/DJT/NHAI/2018-04/04	26.04.2018	Submission of Company profile & credential for the KANTAFLEX India Pvt.ltd. (Elastomeric & Pot bearing)	LASA/Concessionaire /Darah- Jhalawar/IE/2018/206	13.12.2018
22	PIL/CAMP/DJT/NHAI/2018-04/05	26.04.2018	Submission of Company profile & credential for the Dynamic Prestress (I) Pvt Ltd.	LASA/Concessionaire /Darah- Jhalawar/IE/2018/195	08.12.2018
23	PIL/CAMP/DJT/NHAI/2018-04/07	26.04.2018	Submission of Company profile & credential for the Amitek Infra (Thermoplastic Road Marking Paint)	LASA/Concessionaire/ DJ/IE/2018/018	30.08.2018
24	PDJHPL/NHAI/DJT/2018/021	22.03.2018	Submission of Company profile & credential for the Nakoda spun pipes		
25	PDJHPL/NHAI/DJT/2018/022	22.03.2018	Submission of Laboratory profile & credentials for the Star wire INDIA Pvt., Third party, Hind Heat		
26	PDJHPL/PIU/CLO-179/201 8/047	21.06.2018	Submission of Gompany Profile & Gredential for source approval of Hercules Bridge Bearings & Bridge Expansion Joints	LASA/Concessionaire /Darah- Jhalawar/IE/2018/003	21.08.2018
27	PDJHPL/PIU/CLO-179/201 8/096	04.07.2018	Submission of Company Profile & Gredential for Arihant Prefab	LASA/Concessionaire/ Darah- Jhalawar/IE/2018/052	07.09.2018
28	PDJHPL/PIU/CLO-179/201 8/100	05.07.2018	Submission of Gompany profile & Gredeniir for M.E. Testing Laboratory	LASA/Concessionaire /Darah- Jhalawar/IE/2018/178	04.12.2018

Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
29	PDJHPL/PIU/CLO-179/2018/101	05.07.2018	Submission of Company Profile & Credential for Maruti Bitumin Pvt. Ltd	LASA/Concessionaire /Darah-Jhalawar/IE/2018/054	07.09.2018
30	PDJHPL/PRJ/TEC/CLO-179/2018/022	02.06.2018	Submission of profite,Credentials & Basic design report on RE walls	LASA/Concessionaire /Darah-Jhalawar/IE/2018/055	07.09.2018
31	PDJHPL/PIU/D/2018/032	16.04.2018	Submission of Quality assurance Plan		
32	PDJHPL/PIU/CLO-179/2018/043	13.06.2018	Submission of Mix Design of Granular Sub-Base	LASA/Concessionaire /Darah-Jhalawar/IE/2018/155	28.11.2018
33	PDJHPL/PIU/CLO-179/2018/044	13.06.2018	Submission of Summary of OGL test results		
34	PDJHPL/PIU/CLO-179/2018/045	13.06.2018	Submission of Galibration Certificate of Batching Plant & Lab Equipments		
35	PDJHPL/PIU/CLO-179/2018/046	13.06.2018	Submission of Third party test reports of the material related to the project		
36	PDJHPL/PIU/CLO-179/2018/056	18.06.2018	Submission of Petrographic Test Report of Coarse Aggregate		
37	PDJHPL/PIU/CLO-179/2018/108	06.07.2018	Submission of Borrow Area - 1,3,6,7,9,10,11,12,14,15,17,18,20,21,22,23, 24,26,27,29,30,31,32,33,34 & 35		
38	PDJHPL/PIU/CLO-179/2018/110	07.07.2018	Submission of Company Profile & Credential for Earthcon Systems Pvt. Ltd	LASA/Concessionaire /Darah-Jhalawar/IE/2018/049	06.09.2018
39	PDJHPL/PIU/CLO-179/2018/111	07.07.2018	Submission of Construction Design (Geogrid Reinforced Soil Wall)	LASA/Concessionaire /Darah-Jhalawar/IE/2018/063	15.09.2018
40	PDJHPL/PIU/CLO-179/2018/122	10.07.2018	Testing for C & O Value of soil samples of Borrow area No. 1 & 2		
41	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	Submission of Mix-Design	LASA/Concessionaire/ Darah-Jhalawar/IE/2018/003	21.08.2018
42	PDJHPL/PIU/CLO-179/2018/133	16.07.2018	Submission of Trial Patch Report of GSB & DLC		
43	PDJHPL/IE/ICO-181/2018/241	28.08.2018	Submission of Company Profile & Credential OF Maruti Rub Plast Pvt. Ltd.	LASA/Concessionaire/ Darah-Jhalawar/IE/2018/088	15/10/2018
44	PDJHPL/IE/ICO-181/2018/242	28.08.2018	Submission of Company Profile & Credential Of Tar Products Pvt. Ltd.	LASA/Concessionaire/ Darah-Jhalawar/IE/2018/053	07/09/2018
45	PDJHPL/NHAI/DJT/013/2018	28.08.2018	Submission of Company Profile & Credentials for Birla Corporation, Mangalam Cement, Wonder Cement, Ultratech Cement, Vadrj Cement & Shree Cement.	LASA/Concessionaire/ Darah-Jhalawar/IE/2018/014	28/08/2018
46	PDJHPL/IE/ICO-181/2018/260	07.09.2018	Submission of Company Profile & Credential Of Sanfield (India) Ltd.	LASA/Concessionaire/ Darah-Jhalawar/IE/2018/072	28/09/2018
47	PDJHPL/IE/ICO-181/2018/286	18.09.2018	Submission of Company Profile & Credential for RAMA TMT Bars	LASA/Concessionaire/ Darah-Jhalawar/IE/2018/074	28/09/2018

Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
48	PDJHPL/IE/ICO-181/2018/287	18.09.2018	Submission of Company Profile & Credential for SHYAM Steel	LASA/Concessionaire/ Darah- Jhalawar/IE/2018/073	28/09/2018
49	PDJHPL/IE/ICO-181/2018/318	29.09.2018	Submission of Company Profile & Credential of Sanfield (India) Ltd.-reg	LASA/Concessionaire /Darah- Jhalawar/IE/2018/078	03.10.2018
50	PDJHPL/IE/ICO-181/2018/348	09.10.2018	Submission of Company Profile & Credentials of Kataline paints.-reg	LASA/Concessionaire/ Darah- Jhalawar/IE/2018/091	15/10/2018
51	PDJHPL/IE/ICO-181/2018/353	10.10.2018	Submission of Third party testing of RE wall concrete block in km. 23+600-reg	LASA/Concessionaire /Darah- Jhalawar/IE/2018/130	13.11.2018
52	PDJHPL/IE/ICO-181/2018/362	12.10.2018	Submission of Company Profile & Credentials of PNT designs Pvt. Ltd.	LASA/Concessionaire /Darah- Jhalawar/IE/2018/126	13.11.2018
53	PDJHPL/IE/ICO-181/2018/367	13.10.2018	Submission of GSB Mix design for approvals	LASA/Concessionaire/ Darah -Jhalawar/IE/2018/111	29/10/2018
54	PDJHPL/IE/ICO-181/2018/381	18.10.2018	Submission of Filter media Mix-design – reg	LASA/Concessionaire /Darah- Jhalawar/IE/2018/217	13.11.2018
55	PDJHPL/IE/ICO-181/2018/408	26.10.2018	Submission of Company Profile and Credential of M/s Deevin Seismic Systems Pvt. Ltd. for Expansion Joints- reg	LASA/Concessionaire /Darah- Jhalawar/IE/2018/127	13.11.2018
56	PDJHPL/IE/ICO-181/2018/429	02/11/2018	Submission of DLC Mix Design Confirmatory Reports-reg	LASA/Concessionaire /Darah- Jhalawar/IE/2018/163	03.12.2018
57	PDJHPL/IE/ICO-181/2018/450	17/11/2018	Submission of Company profile & Credetials of M/s Deevin Seismic Systems Pvt. Ltd. for Expansion joints - reg	LASA/Concessionaire /Darah- Jhalawar/IE/2018/199	12.12.2018
58	PDJHPL/IE/ICO-181/2018/451	17/11/2018	Submission of third party test report of construction materials-reg		
59	PDJHPL/IE/ICO-181/2018/452	17/11/2018	Submission of Company profile & Credential of JK Lakshmi Cement Ltd-reg	LASA/Concessionaire/ Darah -Jhalawar/IE/2018/148	26/11/2018
60	PDJHPL/IE/ICO-181/2018/453	17/11/2018	Submission of company Profile & Credentials of Supreme Bitumen India Pvt. Ltd.	LASA/Concessionaire /Darah- Jhalawar/IE/2018/162	03.12.2018
61	PDJHPL/IE/ICO-181/2018/454	17/11/2018	Resubmission of Company Profile & Credentials of M/s Hind Heat Treatment & Testing House-reg	LASA/Concessionaire /Darah- Jhalawar/IE/2018/158	30.11.2018
62	PDJHPL/IE/ICO-181/2018/455	17/11/2018	Submission of Company Profile & Credentials of M/s Yash Enterprises-reg	LASA/Concessionaire /Darah- Jhalawar/IE/2018/177	04.12.2018
63	PDJHPL/IE/ICO-181/2018/460	20/11/2018	Submission of Company Profile & Credentials of M/s Electrotherm India Ltd. -	LASA/Concessionaire /Darah- Jhalawar/IE/2018/190	08.12.2018
64	PDJHPL/IE/ICO-181/2018/461	20/11/2018	Submission of Mix Design of WMM-reg	LASA/Concessionaire/ Darah -Jhalawar/IE/2018/152	27/11/2018
66	PDJHPL/IE/ICO-181/2018/473	22/11/2018	Submission of Concrete Mix Design Done only with Wonder & Ultratech Cement-reg	LASA/Concessionaire /Darah- Jhalawar/IE/2018/211	15.12.2018
67	PDJHPL/IE/ICO-181/2018/475	22/11/2018	Submission of Concrete Mix Design Using Fly ash with Wonder & Ultratech Cements-reg		

Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
68	PDJHPL/IE/ICO-181/2018/479	23/11/2018	Submission of PQC M-40 Design Using Fly ash with Ultratech Cement-reg	LASA/Concessionaire /Darah- Jhalawar/IE/2018/176	04.12.2018
69	PDJHPL/IE/ICO-181/2018/480	23/11/2018	Submission of Company Profile & Credentials of M/s Kunal Conchem Pvt. Ltd.-reg	LASA/Concessionaire/ Darah -Jhalawar/IE/2018/147	26/11/2018
70	PDJHPL/IE/ICO-181/2018/510	30/11/2018	Submission of PQC M-40 Design with Ultratech Cement.		
71	PDJHPL/IE/ICO-181/2018/511	30/11/2018	Submission of Company Profile & Credentials of M/s. Normat India Pvt.Ltd	LASA/Concessionaire/ Darah -Jhalawar/IE/2018/207	13/12/2018
72	PDJHPL/IE/ICO-181/2018/521	03/12/2018	Submission of Julmi Crusher Aggregate Test Reports-reg	LASA/Concessionaire/ Darah- Jhalawar/IE/2018/196	10/12/2018
73	PDJHPL/IE/ICO-181/2018/522	03/12/2018	Submission of Fine Aggregate Test Report of Kalisindh River-reg	LASA/Concessionaire/ Darah- Jhalawar/IE/2018/197	10/12/2018
74	PDJHPL/IC/ICO-181/2018/542	08/12/2018	Submission of company profile & credential of M/s HI-TECH Engineering Solutions - reg		
75	PDJHPL/IC/ICO-181/2018/599	21/12/2018	Submission of Test Report of Spun pipes for NP-4 pipe - reg	LASA/Concessionaire/ Darah- Jhalawar/IE/2018/226	24/12/2018
76	PDJHPL/IC/ICO-181/2018/620	31/12/2018	Submission of Inspection Report of Elastomeric Bearing Testing (KANTAFLEX) - reg	LASA/Concessionaire /Darah- Jhalawar/IE/2018/247	04.01.2019
77	PDJHPL/IC/ICO-181/2018/626	02/01/2019	Submission of Chemical Composition Test Report of Steel.	LASA/Concessionaire/ Darah- Jhalawar/IE/2018/288	24/01/2019
78	PDJHPL/IC/ICO-181/2019/638	05/01/2019	Submission of PQC (M-40) Mix Design with Ultratech Cement.	LASA/Concessionaire/ Darah- Jhalawar/IE/2018/252	11/01/2019
79	PDJHPL/IC/ICO-181/2019/639	05/01/2019	Submission of PQC (M-40) Mix Design using Flyash with Ultratech Cement.	LASA/Concessionaire/ Darah- Jhalawar/IE/2018/250	10/01/2019
80	PDJHPL/IC/ICO-181/2019/643	07/01/2019	Submission of Company Profile and Credentials of Molecule Conchem Pvt.Ltd	LASA/Concessionaire/ Darah- Jhalawar/IE/2018/273	21.01.2019
81	PDJHPL/IC/ICO-181/2019/653	10/01/2019	Submission of Test Report of T.M.T Bars from Electrotherm (India) Ltd.	LASA/Concessionaire/ Darah- Jhalawar/IE/2019/297	04/02/2019
82	PDJHPL/IC/ICO-181/2019/665	15/01/2019	Submission of Third Party Test Report of Reinforcement Steel (Hind Heat Treatment)	LASA/Concessionaire/ Darah- Jhalawar/IE/2019/292	28/01/2019
83	PDJHPL/IC/ICO-181/2019/666	15/01/2019	Review of Mix Design of PQC (M-40) with Ultratech Cement & Unirock Plasticizers.		
84	PDJHPL/IC/ICO-181/2019/672	16/01/2019	Review of Mix Design of PQC (M-40) with Ultratech Cement , Flyash & Unirock Plasticizers.		
85	PDJHPL/IC/ICO-181/2019/685	21/01/2019	Submission of Company Profile and Credentials of Choksey Chemicals Pvt.Ltd.	LASA/Concessionaire/ Darah- Jhalawar/IE/2019/289	28/01/2019
86	PDJHPL/IC/ICO-181/2019/686	21/01/2019	Submission of Company Profile and Credentials of J.K Cement Ltd.	LASA/Concessionaire/ Darah- Jhalawar/IE/2019/290	28/01/2019
87	PDJHPL/IC/ICO-181/2019/713	31/01/2019	Submission of Test Report of POT/ PTFE Bearings for Flyover+Major Bridge 47+650 to 48+150 (Dynamic Prestress Pvt. Ltd).	LASA/Concessionaire/ Darah- Jhalawar/IE/2019/304	06/02/2019

Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
88	PDJHPL/IC/ICO-181/2019/732	06/02/2019	Submission of PQC Trial patch Report from Ch.28+400 to 28+147(LHS) - reg		
89	PDJHPL/IC/ICO-181/2019/753	12/02/2019	Submission of Company Profile & Credentials of Ooms Avenhorn Holding India Pvt. Ltd. & Ooms Polymer Modified Bitumen Pvt. Ltd.-reg	LASA/Concessionaire/Darah-Jhalawar/IE/2019/307	18/02/2019
90	PDJHPL/IC/ICO-181/2019/761	14/02/2019	Submission of Company Profile & Credential of Unirock Chemicals Pvt. Ltd.-reg	LASA/Concessionaire/Darah-Jhalawar/IE/2019/308	18/02/2019
91	PDJHPL/IC/ICO-181/2019/788	20/02/2019	Submission of Company Profile & Credential of MSP Group for procurement of Dowel Bars - reg		
92	PDJHPL/IC/ICO-181/2019/798	25/02/2019	Submission of Company Profile & Credetial of M/s Sika India - reg	LASA/NHAI/Darah-Jhalawar/IE/2019/350	16.03.2019
93	PDJHPL/IC/ICO-181/2019/804	26/02/2019	Submission of Company Profile & Credential of M/s STP Ltd - reg	LASA/NHAI/Darah-Jhalawar/IE/2019/351	16.03.2019
94	PDJHPL/IC/ICO-181/2019/812	28/02/2019	Submission of Company Profile & Credetial of MSP steel & Power Ltd - reg.		
95	PDJHPL/IC/ICO-181/2019/833	07/03/2019	Submission of Company Profile & Credetial of Chembond Chemicals - reg	LASA/Concessionaire/Darah-Jhalawar/IE/2019/352	16.03.2019
96	PDJHPL/IC/ICO-181/2019/962	23/04/2019	Submission of Company Profile & Credetial of Fortune Ltd - reg		
97	PDJHPL/IC/ICO-181/2019/967	25/04/2019	Submission of Company Profile & Credetial of Balajee Loha Ltd - reg		
98	PDJHPL/IC/ICO-181/2019/1018	09/05/2019	Submission of Company Profile & Credetial of Essar Steel - reg		
99	PDJHPL/IC/ICO-181/2019/1019	09/05/2019	Submission of Company Profile & Credetial of Bostik Pvt Ltd - reg	LASA/Concessionaire/Darah-Jhalawar/IE/2019/415	16/05/2019
100	PDJHPL/IC/ICO-181/2019/1031	11/05/2019	Submission of Methodology of Pile Load Test of Routine Pile @ 57+127 (MJB)		
101	PDJHPL/IC/ICO-181/2019/1048	16/05/2019	Submission of Methodology of Pile Load Test of Routine Pile @ 36+070 (MJB)	LASA/Concessionaire/Darah-Jhalawar/IE/2019/429	24/05/2019
102	PDJHPL/IC/ICO-181/2019/1074	25/05/2019	Submission of Plate Load Test Report Conducted at 36+070 (MJB) & 58+128 (Flyover).		
103	PDJHPL/IC/ICO-181/2019/1083	28/05/2019	Submission of Initial Load Test Report Conducted on Test Pile .		
104	PDJHPL/IC/ICO-181/2019/1088	30/05/2019	Submission of Company Profile & Credetial of Nuvoco Vistas Corp. Ltd - reg		
105	PDJHPL/IC/ICO-181/2019/1098	03/06/2019	Submission of Kerb (M-20) with Ultratech Cement without Flyash.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/446	10/06/2019
106	PDJHPL/IC/ICO-181/2019/1099	03/06/2019	Submission of SPT Test Report for Ch.36+070 (MJB)		
107	PDJHPL/IC/ICO-181/2019/1100	03/06/2019	Submission of Bore Log Test Report @ 36+070 (MJB) & 58+128 (Flyover).		
108	PDJHPL/IC/ICO-181/2019/1189	30/06/2019	Submission of Company Profile & Credential of STECOL (Essar TMT Brand)		

Status of submitted Drawings

S.No	Type of Structure	Scope in Nos	No. of Drawing Submitted	Vide Letter No.	Date	Proof Check	Remarks
1	Pipe Culvert	16	R0-16 Nos.	PDJHPL/PIU/D/016/2018	27.02.2018	NIL	
				PDJHPL/PIU/CLO-179/2018/146	23.07.2018	NIL	
			R1-8 Nos.	PDJHPL/PIU/CLO-179/2018/146	23.07.2018	NIL	Approved
2	Box Culvert	21	R0-20 Nos.	PDJHPL/PIU/D/016/2018	27.02.2018	NIL	
				PDJHPL/PIU/CLO-179/2018/093	04.07.2018	NIL	
				PDJHPL/PIU/CLO-179/2018/041	12.06.2018	NIL	
				PDJHPL/PIU/CLO-179/2018/037	07.06.2018	NIL	
			R1-20 Nos.	PDJHPL/PIU/CLO-179/2018/093	04.07.2018	NIL	
				PDJHPL/PIU/CLO-179/2018/137	18.07.2018	NIL	
				PDJHPL/PIU/CLO-179/2018/138	18.07.2018	NIL	
				PDJHPL/PIU/CLO-179/2018/228	22.08.2018	NIL	
				PDJHPL/PIU/CLO-179/2018/388	18.10.2018	NIL	
				PDJHPL/PIU/CLO-179/2018/463	20.11.2018	NIL	Approved
3	Minor Bridge	11	R0-10 Nos.	PDJHPL/PIU/D/016/2018	27.02.2018	NIL	
				PDJHPL/PIU/CLO-179/2018/146	23.07.2018	NIL	
				PDJHPL/PIU/CLO-189/2018/191	09.08.2018	NIL	
			R1-05 Nos	PDJHPL/PIU/CLO-179/2018/037	07.06.2018	NIL	
				PDJHPL/IE/ICO-181/2018/317	29.09.2018	NIL	
			Compliance	PDJHPL/IE/ICO-181/2018/487	23.11.2018	NIL	
				PDJHPL/IE/ICO-181/2018/488	26.11.2018	NIL	
				PDJHPL/IC/ICO-181/2018/562	11.12.2018	NIL	
				PDJHPL/IC/ICO-181/2018/582	17.12.2018	NIL	
			R1 – 01 Nos	PDJHPL/IC/ICO-181/2018/816	01.03.2019		
4	Major Bridge	2	R0-02 Nos	PDJHPL/PIU/D/034/2018	19.04.2018	NIL	
			R1-03 Nos	PDJHPL/PIU/CLO-179/2018/037 01 Nos. (Letter -119 date- 09.07.2018) (Proof Checked)	07.06.2018	1 set	
				PDJHPL/PIU/CLO-179/2018/072	25.06.2018		Approved
				PDJHPL/IE/ICO-181/2018/272	12.09.2018		Approved
				PDJHPL/HO/DJT/IE/578/2018	15.12.2018	1 set	Approved
5	Elevated Road	1	R1-01 Nos	PDJHPL/PIU/CLO-179/2018/037 01 Nos. (Letter -119 date- 09.07.2018) (Proof Checked)	07.06.2018	1 set	Approved
6	VUP	9	R0-09 Nos	PDJHPL/PIU/D/018/2018	12.03.2018		
				PDJHPL/PIU/D/014/2018	27.02.2018		
				Letter No- 041 (IIT Certified)	12.06.2018	1 set	

S.No	Type of Structure	Scope in Nos	No. of Drawing Submitted	Vide Letter No.	Date	Proof Check	Remarks
				Copy)			
			R1-06 Nos	Letter No- 041 (IIT Certified Copy) (Letter -158 date- 28.07.2018)	12.06.2018	1 set	
				(Letter -188 date- 08.08.2018)	08.08.2018		Approved (05 Nos)
			R2-04 Nos.	PDJHPL/IC/ICO-181/583	17.12.2018		
				PDJHPL/IC/ICO-181/632	03.01.2019		
7	LVUP	13	R0-13 Nos	PDJHPL/PIU/D/016/2018	27.02.2018	NIL	
				PDJHPL/PIU/CLO-179/2018/067	22.06.2018	NIL	Approved (06 Nos)
			R1-06 Nos	PDJHPL/PIU/CLO-179/2018/067	22.06.2018	NIL	
				PDJHPL/IC/ICO-181/2019/811	28/02/2019		
8	FlyOver	3	R0-03 Nos	PDJHPL/PIU/D/034/2018	19.04.2018	1 set	
			R1-03 Nos	PDJHPL/PIU/CLO-179/2018/115	09.07.2018	NIL	
			R2-03 Nos	PDJHPL/IC/ICO-181/2018/431	03.11.2018	2 set	
9	ROB	1	R1-01 Nos	PDJHPL/PIU/CLO-179/2018/118 01 Nos. (Letter-118 date- 09.07.2018) Proof Checked)	09.07.2018	1 set	Approved
				PDJHPL/IC/ICO-181/2018/550	10.12.2018	2 set	
10	RUB	1	R1-01 Nos	PDJHPL/PIU/TEC/CLO- 179/2018/019 Hard Copy of Trecing Paper Drawing	31.05.2018	1 set	Approved
	Total	78					
1	Plan & Profile	48.88 Km	R0-01 Nos	PDJHPL/PIU/CLO-179/2018/106	06.07.2018	NIL	
				PDJHPL/IC/ICO-181/2018/364	12.10.2018	NIL	
			R1-01 Nos	PDJHPL/IC/ICO-181/2018/474	22.11.2018	NIL	
				PDJHPL/HO/DJT/IE/001/2019	07.01.2019	NIL	
				PDJHPL/HO/DJT/IE/007/2019	19.01.2019		Approved upto 48.88 Km
2	TOLL PLAZA		R0-01 Nos	PDJHPL/IC/ICO-181/2018/316	29.09.2018		Approved
3	POT/PTFE Bearing		46+950, 50+095, 58+128	PDJHPL/IC/ICO-181/2018/430	03.11.2018		Approved
4	Pavement Design			PDJHPL/HO/DJT/IE/008/2019	19.01.2019		Approved
5	RE wall		VUP (12+125) & 12+450 (LVUP)	PDJHPL/IC/ICO-181/2018/658	12/01/2019		
			LVUP (15+725)	PDJHPL/PIU/CLO-189/2018/200	11/08/18		

S.No	Type of Structure	Scope in Nos	No. of Drawing Submitted	Vide Letter No.	Date	Proof Check	Remarks
			LVUP (17+353)	PDJHPL/PIU/CLO-189/2018/201	11/08/18		
			VUP (19+970)	PDJHPL/IC/ICO-181/2018/659	12/01/2019		
			LVUP (21+183)	PDJHPL/IC/ICO-181/2018/660	12/01/2019		
			LVUP (23+065)	PDJHPL/IC/ICO-181/2018/661	12/01/2019		
			LVUP (23+687)	PDJHPL/IC/ICO-181/2018/662	12/01/2019		
			LVUP (24+547) & VUP (25+100)	PDJHPL/PIU/CLO-189/2018/202	11/08/18		
			LVUP (27+029)	PDJHPL/PIU/CLO-189/2018/203	11/08/18		
			LVUP (37+050)	PDJHPL/PIU/CLO-189/2018/204	11/08/18		
			LVUP (38+545)	PDJHPL/PIU/CLO-189/2018/205	11/08/18		
			VUP (49+330) (R0)	PDJHPL/IE/ICO-181/2018/534	07/12/2018		Approved
			VUP (49+330) (R1)	PDJHPL/IE/ICO-181/2018/603	24/12/2018		
			VUP (49+330) (R2)	PDJHPL/IC/ICO-181/2019/760	14/02/2019		
			Flyover (50+099) (R0)	PDJHPL/IE/ICO-181/2018/535	07/12/2018		Approved
			Flyover (50+099) (R1)	PDJHPL/IE/ICO-181/2018/602	24/12/2018		
			Flyover (50+099) (R2)	PDJHPL/IC/ICO-181/2019/759	14/02/2019		
			VUP (41+102) & LVUP (41+465) (R0)	PDJHPL/IE/ICO-181/2018/536	07/12/2018		Approved
			VUP (41+102) & LVUP (41+465) (R1)	PDJHPL/IC/ICO-181/2019/719	01/02/2019		
			LVUP (42+263) (R0)	PDJHPL/IE/ICO-181/2018/537	07/12/2018		Approved
			LVUP (42+263) (R1)	PDJHPL/IC/ICO-181/2019/720			
			Design & Drawing for Sandy Soil	PDJHPL/IE/ICO-181/2018/548	10/12/2018		

Mobilization of Manpower

Name of the Employee	Designation	Department
Amit	Garg	General Manager
Milind	Pande	Project Incharge
Atul Kumar	Mishra	Project Manager
Rajesh	Chaturvedi	Dy. Project Manager
Balram Singh	Shekhawat	Manager

Name of the Employee		Designation		Department
Rajesh	Raval	Material Engineer		QA/QC
Ranjay Kumar	Anju	Dy. Project Manager		Planning & Billing
Devesh	Pandey	Dy. Project Manager		QA/QC
Brijkishor	Ramsewak	Engineer		QA/QC
Mahesh	Pandey	Dy. Project Manager		Highway
Sajjan Lal	Sharma	Dy. Project Manager		Structure
Bal Krishna	Rath	Dy. Project Manager		Structure
Kuldeep singh	Shivnathsingh	Sr.Surveyor		Survey
Shubhash	Kumar	Sr.Manager		Mechanical
Dayanand	Prakash	Engineer		Health & Safety
Ravi Kishore Pandey	Dinanath Pandey	Sr.Accountant		Finance & Accounts
Ramesh Chandra	Barad	Dy. Manager (HR & Admin)		HR & Admin
Bhagwan	Jha	Manager		Purchase
HR & ADMIN DEPARTMENT				
Sr. Executive		2	Nos	HR & Admin
Sr.Officer(S & V)		1	Nos	HR & Admin
Executive		2	Nos	HR & Admin
Jr.Executive		2	Nos	HR & Admin
Security violation		2	Nos	HR & Admin
Office Boy		6	Nos	HR & Admin
PLANNING & BILLING DEPARTMENT				
Sr.Engineer		2	Nos	Planning & Billing
Engineer		1	Nos	Planning & Billing
Asst. Engineer		2	Nos	Planning & Billing
QA/QC DEPARTMENT				
Asst.Manager		1	Nos	QA/QC
Lab Asst.		1	Nos	QA/QC
Sr.Lab Technician		2	Nos	QA/QC
Lab Technician		7	Nos	QA/QC
Jr.Lab Technician		1	Nos	QA/QC
Engineer		3	Nos	QA/QC
Jr.Engineer		3	Nos	QA/QC
HIGHWAY DEPARTMENT				
Sr. Engineer		3	Nos	Highway
Engineer		3	Nos	Highway
Asst. Engineer		8	Nos	Highway
Jr.Engineer		6	Nos	Highway
Engineer Trainee		2	Nos	Highway
Jr. Supervisor		1	Nos	Highway
Supervisor		11	Nos	Highway
STRUCTURE DEPARTMENT				
Sr. Engineer		5	Nos	Structure
Engineer		6	Nos	Structure
Asst. Engineer		4	Nos	Structure
Jr.Engineer		4	Nos	Structure
Engineer Trainee		1	Nos	Structure
Sr.Supervisor		6	Nos	Structure
Supervisor		3	Nos	Structure
Jr.Supervisor		3	Nos	Structure

Name of the Employee	Designation		Department
SURVEY DEPARTMENT			
Sr. Surveyor	1	Nos	Survey
Surveyor	10	Nos	Survey
Jr.Surveyor	4	Nos	Survey
STORE DEPARTMENT			
Jr. Executive	5	Nos	Store
Executive	8	Nos	Store
WEIGH BRIDGE			
Jr.Executive	13	Nos	Weigh Bridge
PURCHASE DEPARTMENT			
Dy.Manager	1	Nos	Purchase
Sr.Executive	1	Nos	Purchase
Executive	1	Nos	Purchase
HEALTH & SAFETY DEPARTMENT			
Sr.Executive	1	Nos	Health & Safety
Engineer	1	Nos	Health & Safety
Executive	1	Nos	Health & Safety
IT DEPARTMENT			
Sr.Executive	1		IT
Executive	1		IT
MECHANICAL DEPARTMENT			
Sr.Supervisor	1	Nos	Mechanical
Sr. Engineer	3	Nos	Mechanical
Engineer	1	Nos	Mechanical
Asst. Engineer	3	Nos	Mechanical
Executive	1	Nos	Mechanical
Asst. Mechanic	3	Nos	Mechanical
Fitter	1	Nos	Mechanical
Tyre Fitter	4	Nos	Mechanical
Jr.Engineer	2	Nos	Mechanical
Jr.Executive	3	Nos	Mechanical
Engineer Trainee	1	Nos	Mechanical
Supervisor	6	Nos	Mechanical
Driver	69	Nos	Mechanical
Computer Operator	1	Nos	Mechanical
Operator / Helper / Mechanic	105	Nos	Mechanical
SPV DEPARTMENT			
Dy.Manager	1	Nos	SPV
Sr.Executive	1	Nos	SPV
Executive	1	Nos	SPV

Mobilization of Resources (Plant and Machineries)

S. No	Name of Machinery	Nos of Equipments	Remarks
1	Excavator	16	
2	Hywa / Tipper	69	
3	Soil Compactor	8	
4	Dozer	0	
5	Water Tanker	17	
6	Diesel Dispenser	4	
7	Grader	5	
8	Loader	7	
9	Back Hoe	4	
10	Transit Mixer	16	
11	Crusher	2	
12	Concrete Batching Plant	4	
13	Weigh Bridge	6	
14	WMM Plant	1	
15	Hydra Crane	4	
16	Hot Mix Plant	1	
17	Concrete Pump	1	
18	Sand Classifier	2	
19	Tractor	5	
20	Tower Light	8	
21	DG Set	15	
22	Light Vehicle	35	
23	Trailer	5	
24	JCB	2	
25	Concrete Boom Placer	1	
26	Tandem Roller	4	
27	Baby Tandem Roller	2	
28	Mobile Service Van	1	
29	DLC Paver	1	
30	Automatic PQC Paver	1	
31	Kerb Paver	2	
32	Chilling plant	1	
	TOTAL	249	

Site Progress Photo



VUP Girder Reinforcement Checking at Ch.30+075



Pier Completion @ Ch.50+095



Slab Casting @ Ch. 49+785



REDMI NOTE 6 PRO
MI DUAL CAMERA

2019/7/3 10:01

VUP Abutment @ Ch.30+078




2019-6-22 16:34



RE Wall Work @ Ch.38+533



Girder casting @ Ch.36+070(Major Bridge)

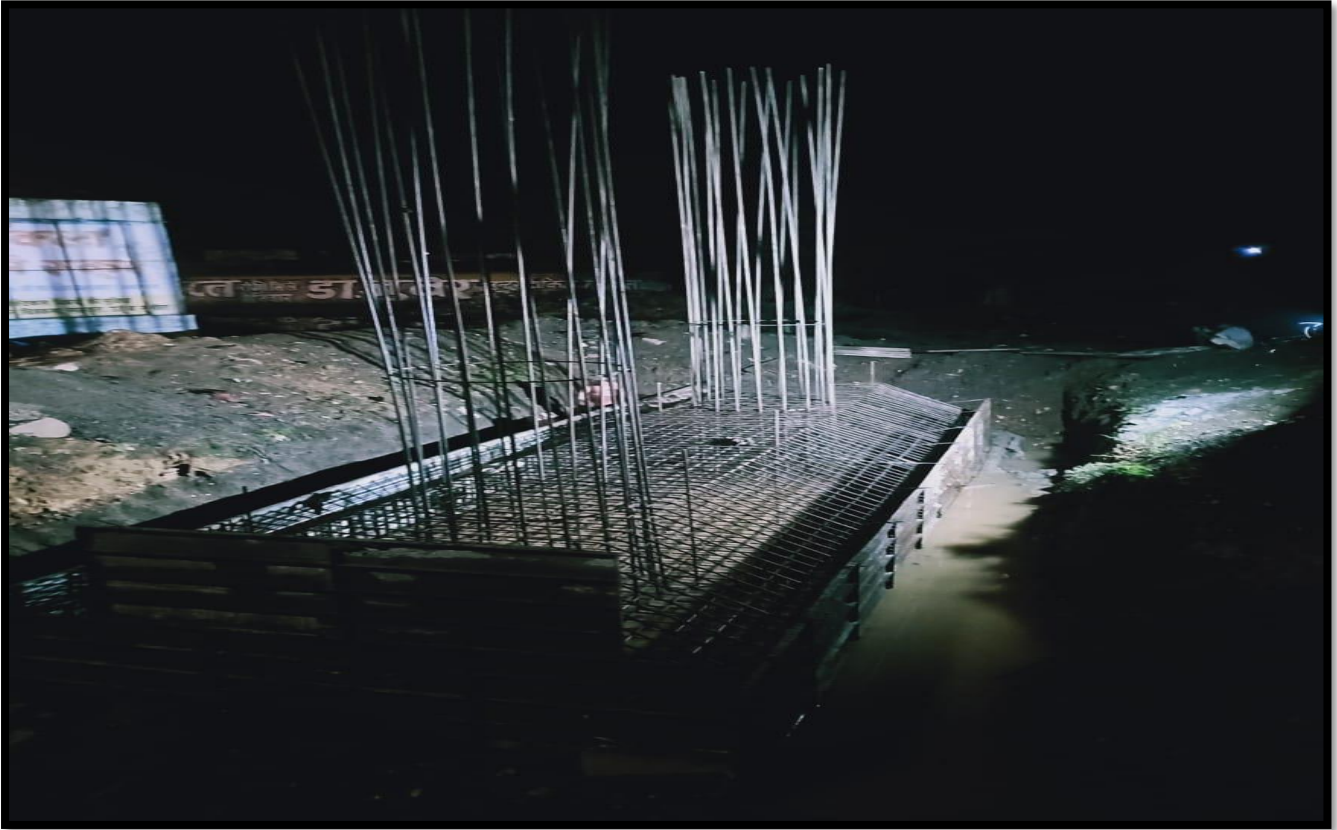

Steel & Reinforcement Work @ Ch.58+128 (Flyover)





Slab Casting at Elevated Highway @ Ch. 47+830

Highway Progress





Embankment Top at Ch. 10+400 to 10+650





Subgrade Top at Ch.9+960 to 10+150





2019-7-23 09:56

GSB @ Ch. 42+600 to 43+000





PQC Laying at Ch.25+540 (LHS)




PQC Median Filling at Ch.23+100



Kerb Laying at Ch. 13+300

KEY PLAN OF THE PROJECT

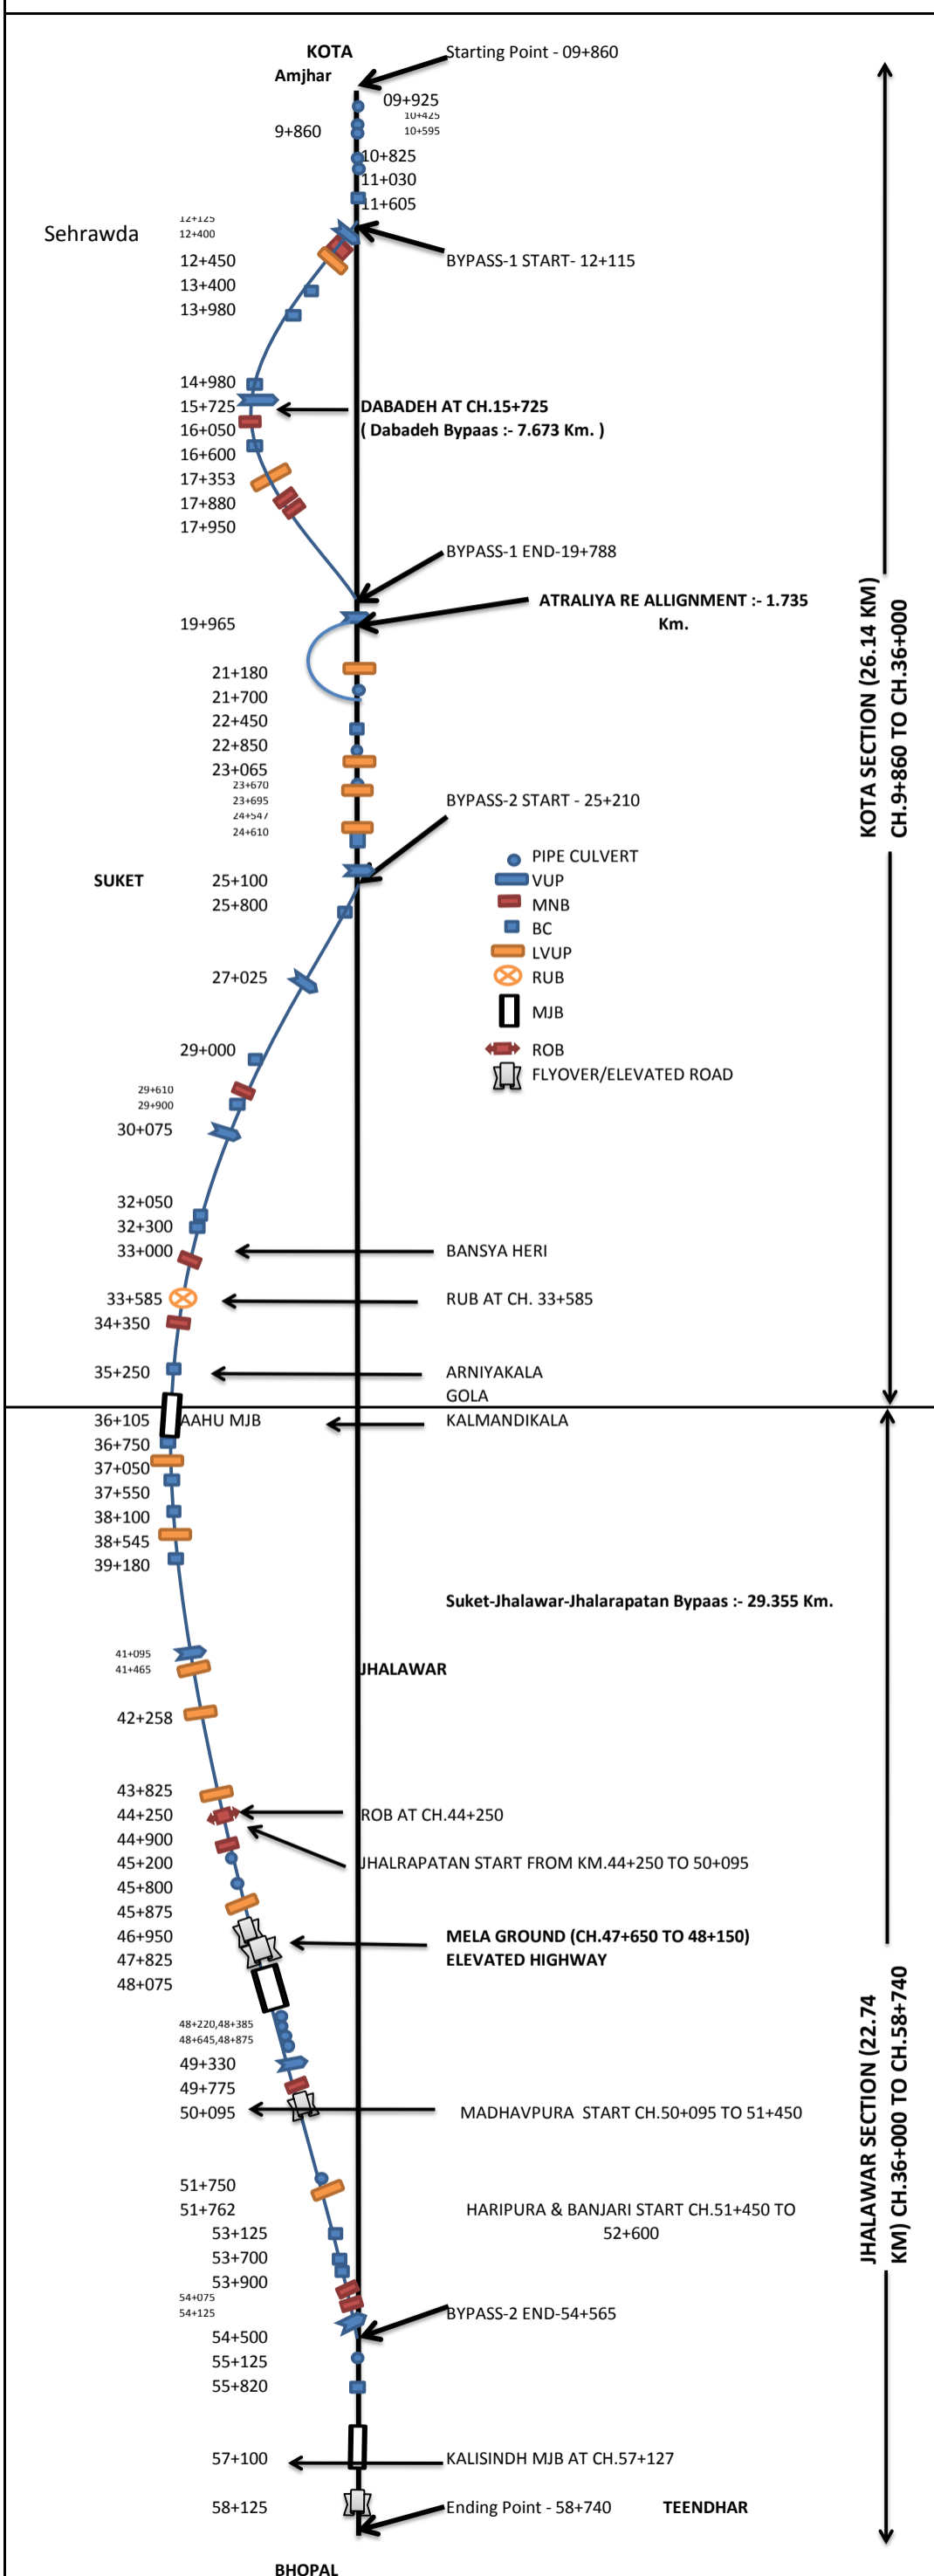

Index	C & G	
	Length	38.29Km

EMB	
Length	26.79Km

SG	
Length	12.697Km

GSB	
Length	11.293Km

DLC	
Length	10.513Km


PQC	
Length	9.210Km




		LHS	
PQC			
DLC			
GSB			
SG			
EMB			
C&G			
Chainage	38000		
	38100		
	38200		
	38300		
	38400		
	38500		
	38600		
	38700		
	38800		
	38900		
	39000		
	39100		
	39200		
	39300		
	39400		
	39500		
	39600		
	39700		
	39800		
	39900		
	40000		
	40100		
	40200		
	40300		
	40400		
	40500		
	40600		
40700			
40800			
40900			
41000			
41100			
41200			
41300			
41400			
41500			
41600			
41700			
41800			
41900			
42000			
42100			
42200			
42300			
42400			
42500			
42600			
42700			


		LHS	
PQC			
DLC			
GSB			
SG			
EMB			
C&G			
Chainage	42700		
	42800		
	42900		
	43000		
	43100		
	43200		
	43300		
	43400		
	43500		
	43600		
	43700		
	43800		
	43900		
	44000		
	44100		
	44200		
	44300		
	44400		
	44500		
	44600		
	44700		
	44800		
	44900		
	45000		
	45100		
	45200		
	45300		
45400			
45500			
45600			
45700			
45800			
45900			
46000			
46100			
46200			
46300			
46400			
46500			
46600			
46700			
46800			
46900			
47000			
47100			
47200			
47300			
47400			

		LHS	
PQC			
DLC			
GSB			
SG			
EMB			
C&G			
Chainage	47400		
	47500		
	47600		
	47700		
	47800		
	47900		
	48000		
	48100		
	48200		
	48300		
	48400		
	48500		
	48600		
	48700		
	48800		
	48900		
	49000		
	49100		
	49200		
	49300		
	49400		
	49500		
	49600		
	49700		
	49800		
	49900		
	50000		
50100			
50200			
50300			
50400			
50500			
50600			
50700			
50800			
50900			
51000			
51100			
51200			
51300			
51400			
51500			
51600			
51700			
51800			
51900			
52000			
52100			

MAJOR BRIDGE AT 57+127

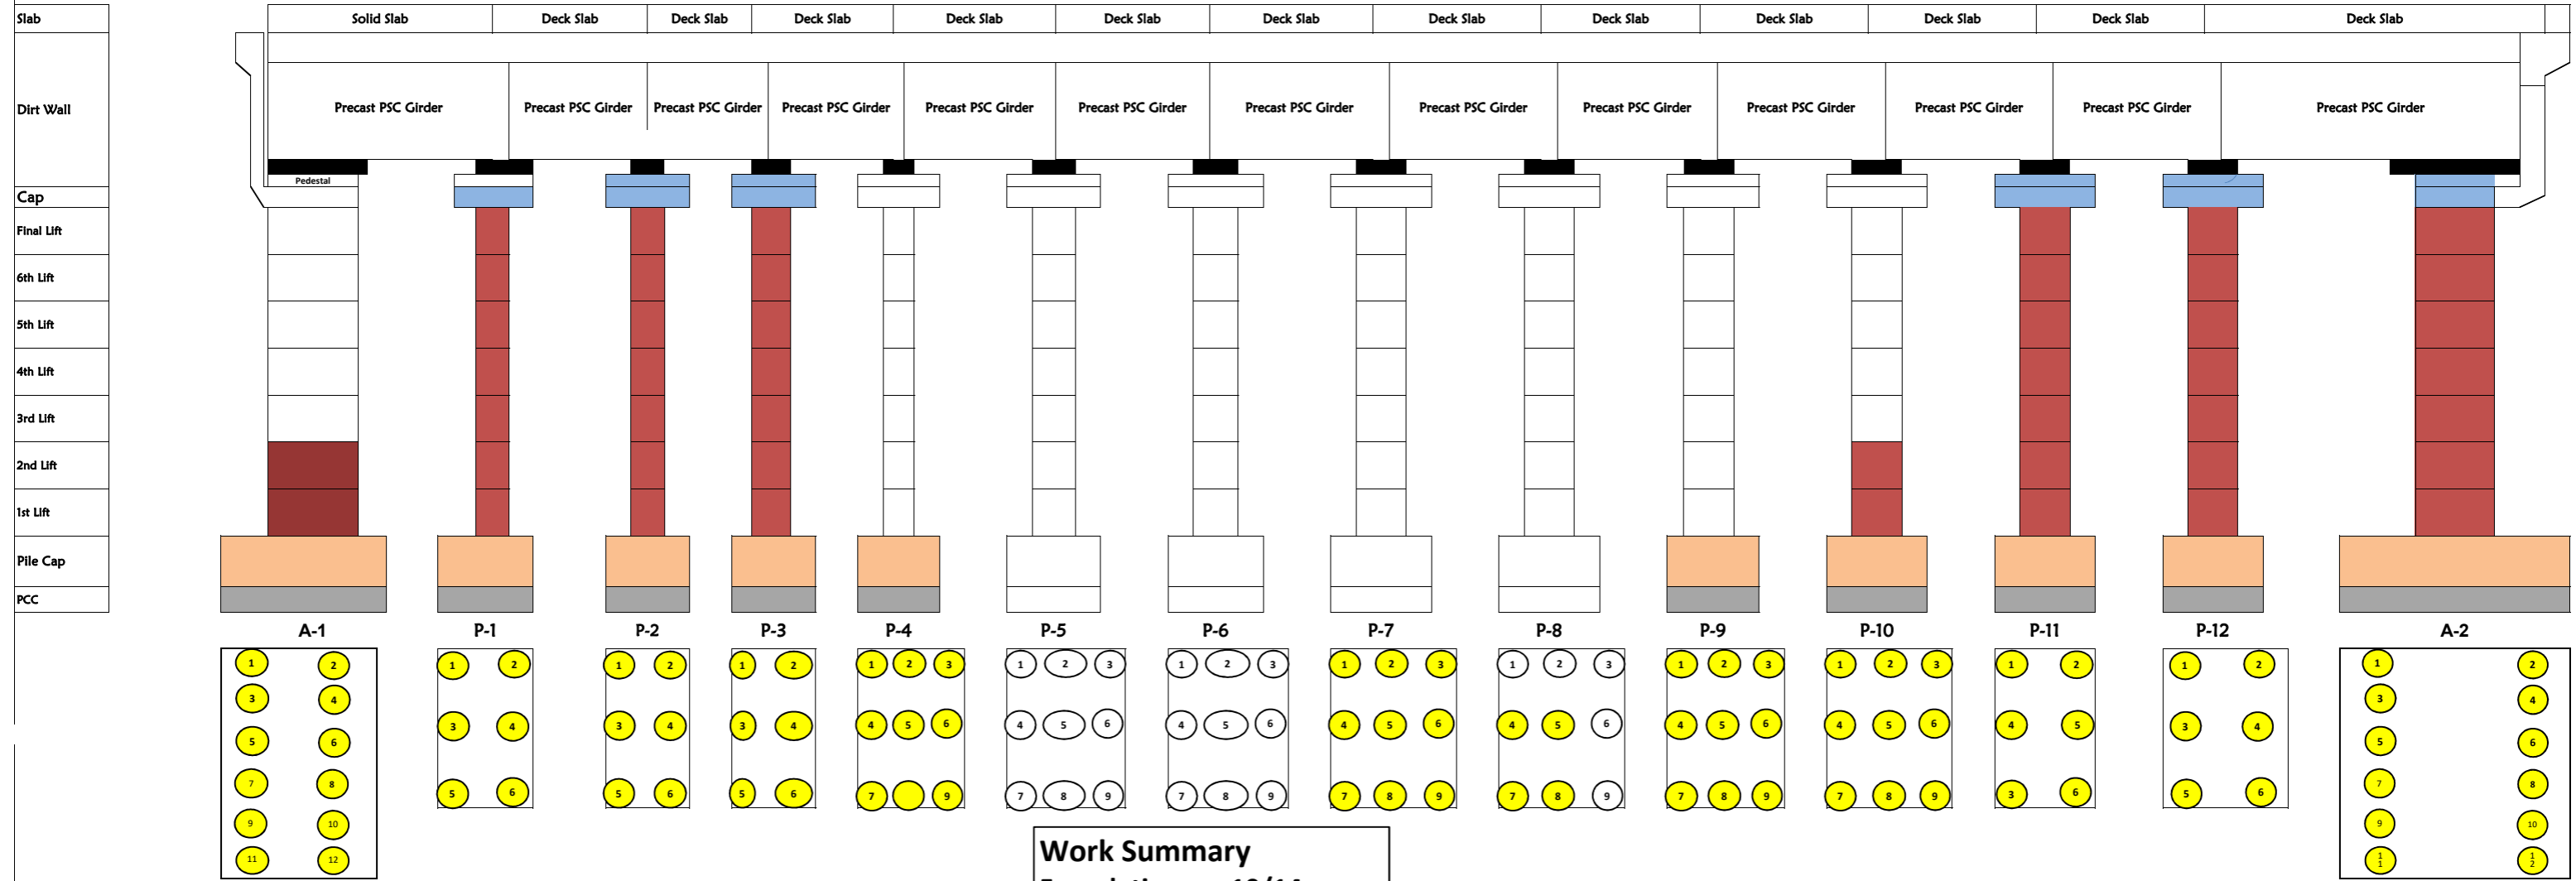


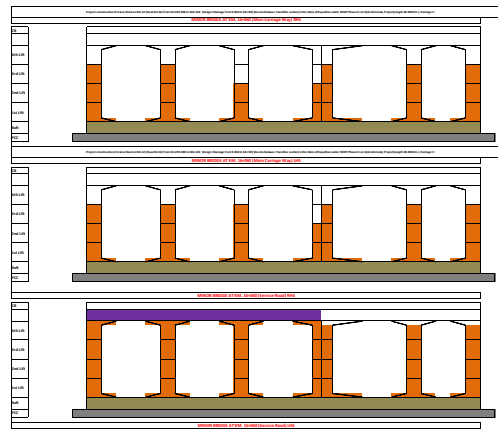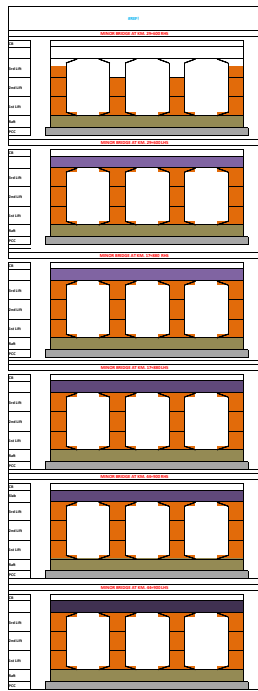

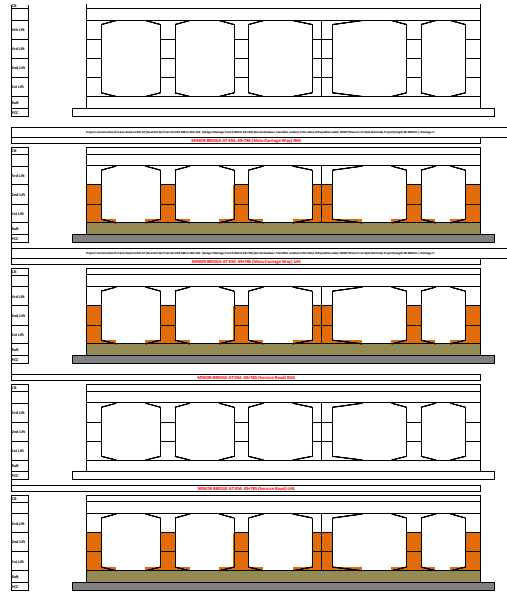


VEHICULAR UNDERPASS AT 12+125 A1 /A2RHS

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

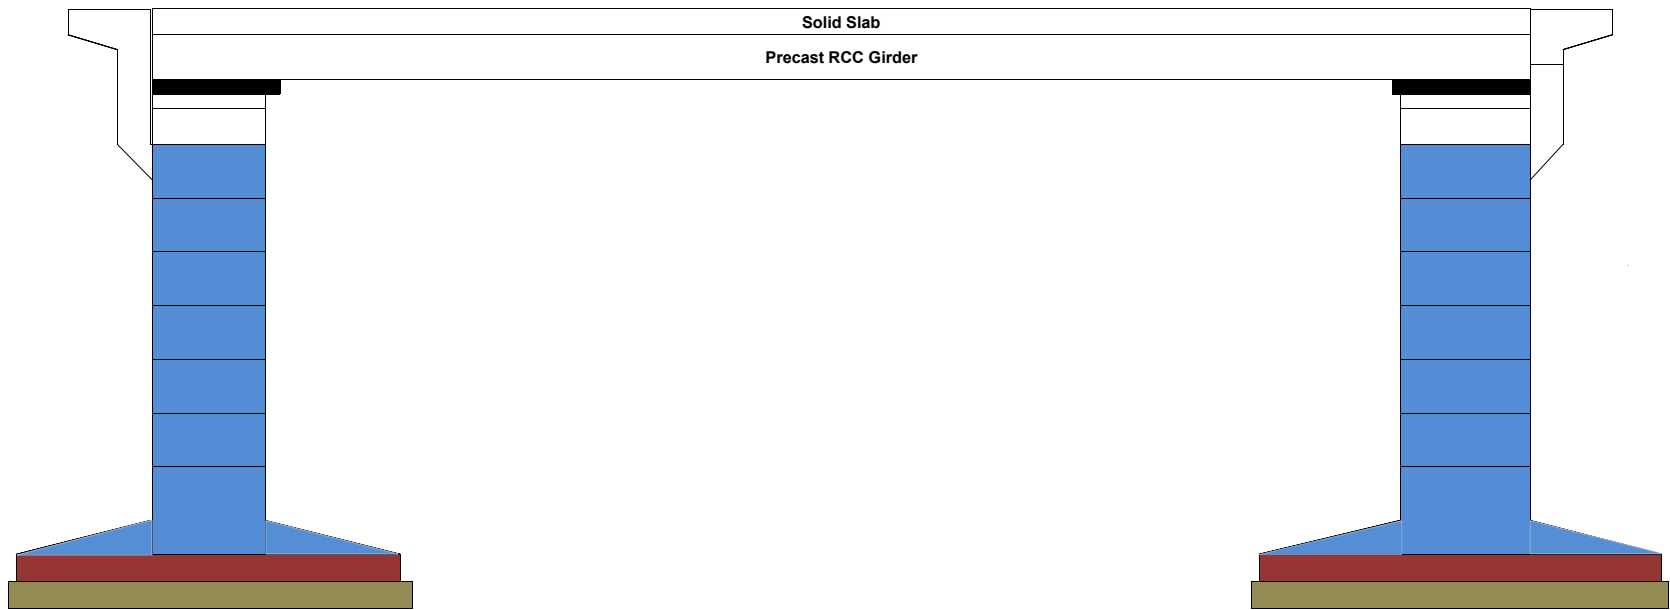


VEHICULAR UNDERPASS AT 12+125A1/ A2 LHS

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

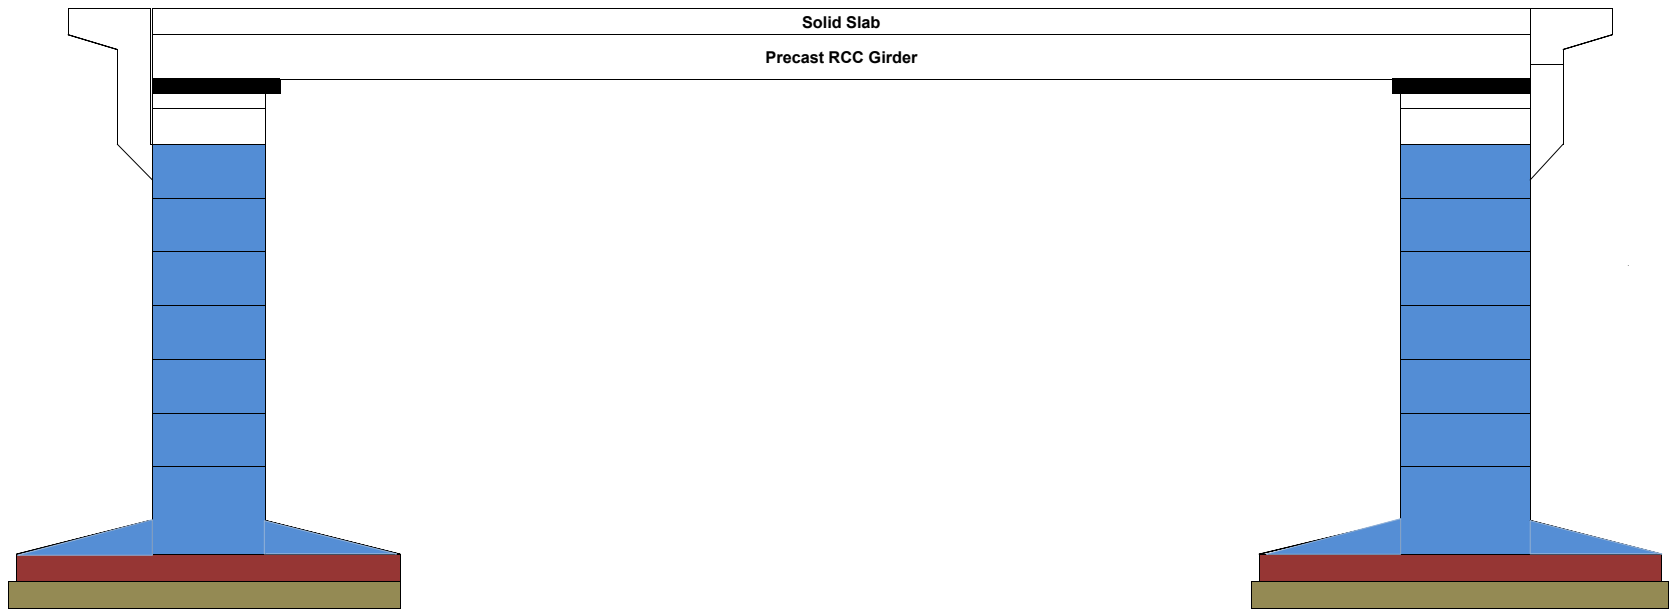


VEHICULAR UNDERPASS AT 15+725 A1/A2 RHS

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

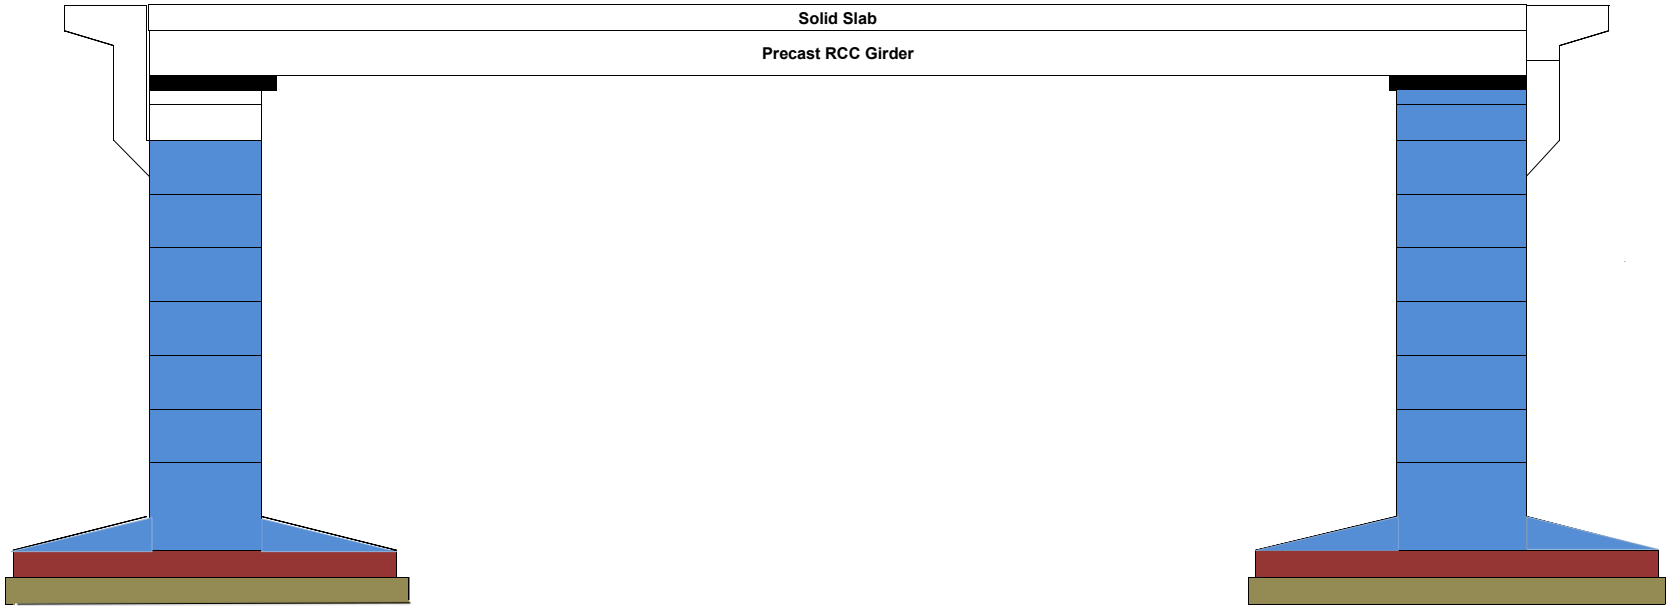


VEHICULAR UNDERPASS AT 15+725 A1/A2 LHS

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

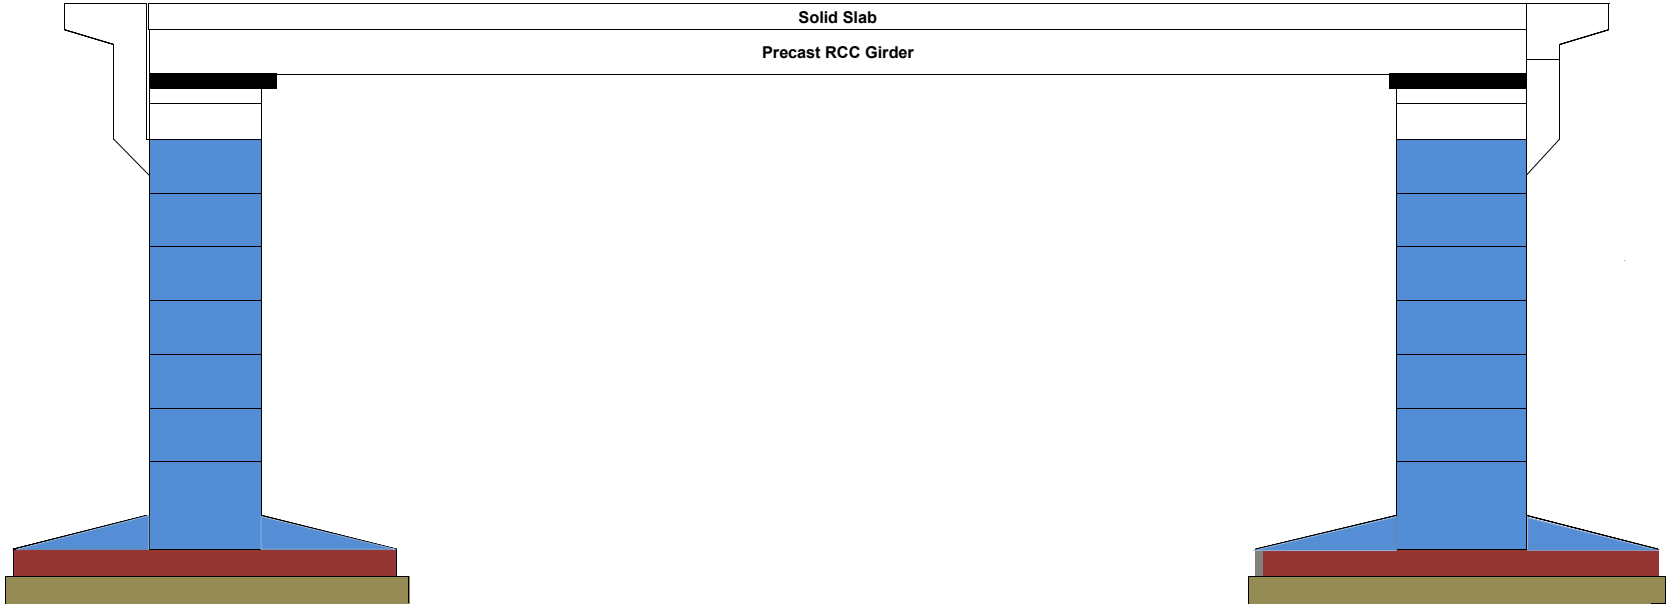


Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

VEHICULAR UNDERPASS AT 25+100 A1/A2 RHS

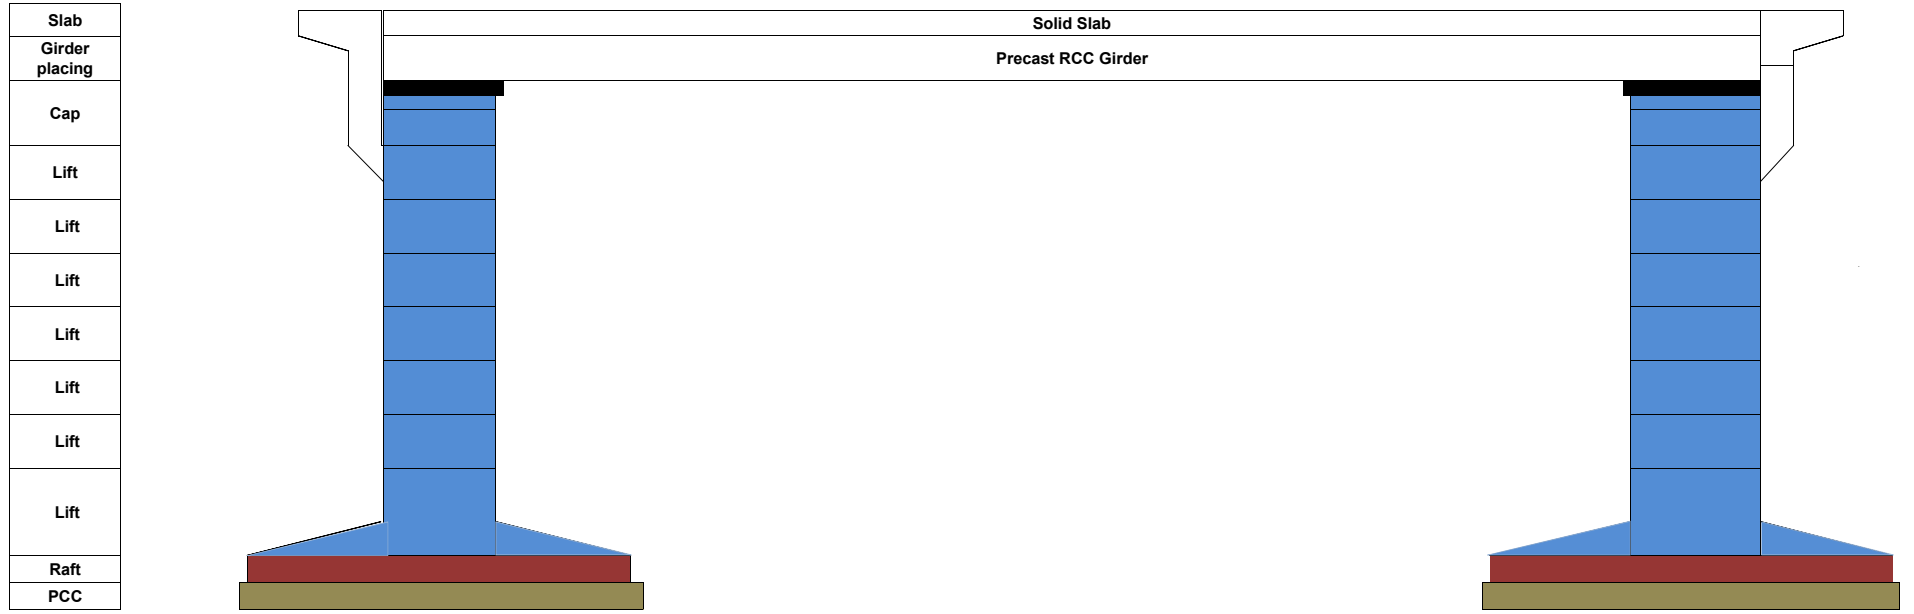


VEHICULAR UNDERPASS AT 25+100 A1/A2 LHS

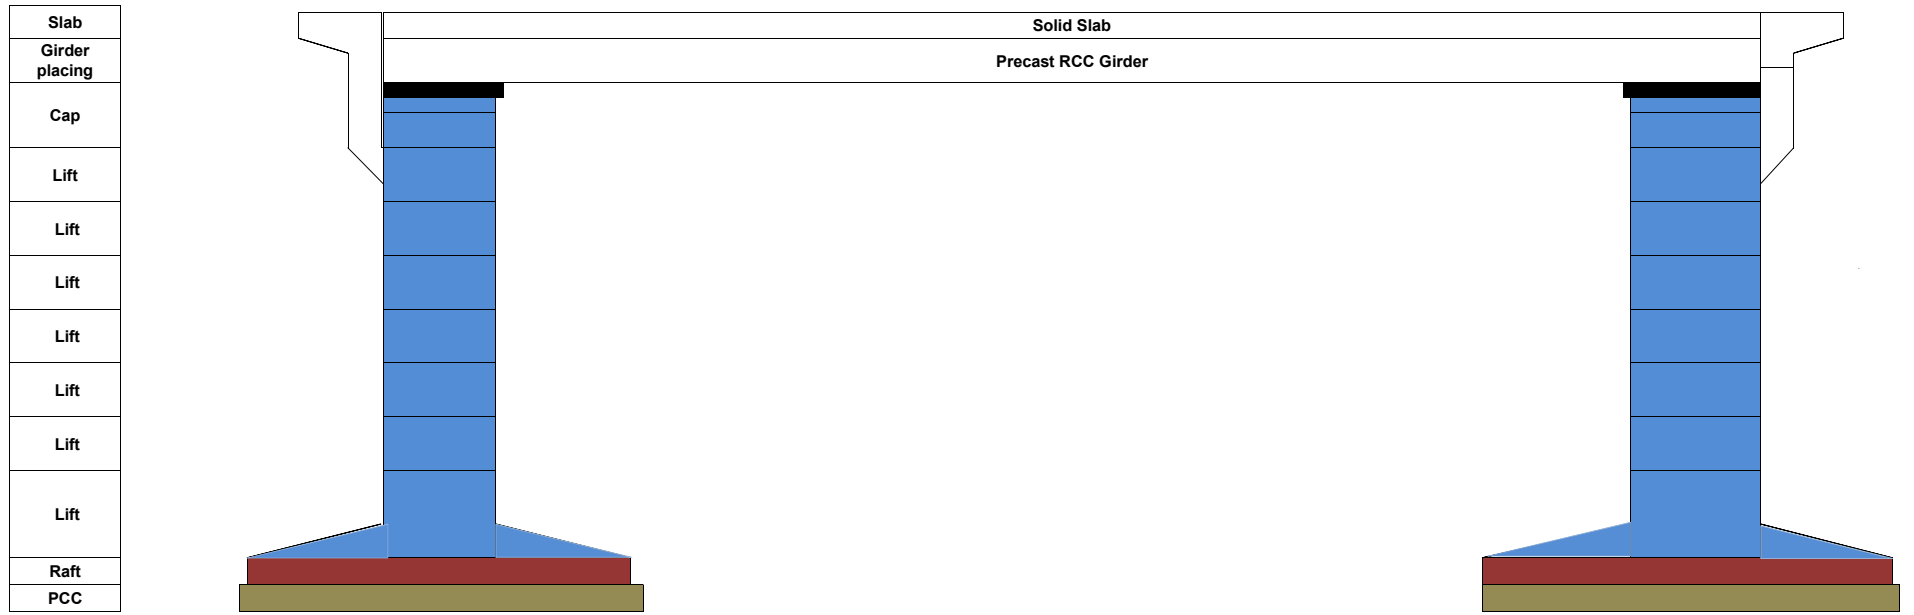


VEHICULAR UNDERPASS AT 49+330A1/ A2 LHS




VEHICULAR UNDERPASS AT 49+330 A1 /A2RHS

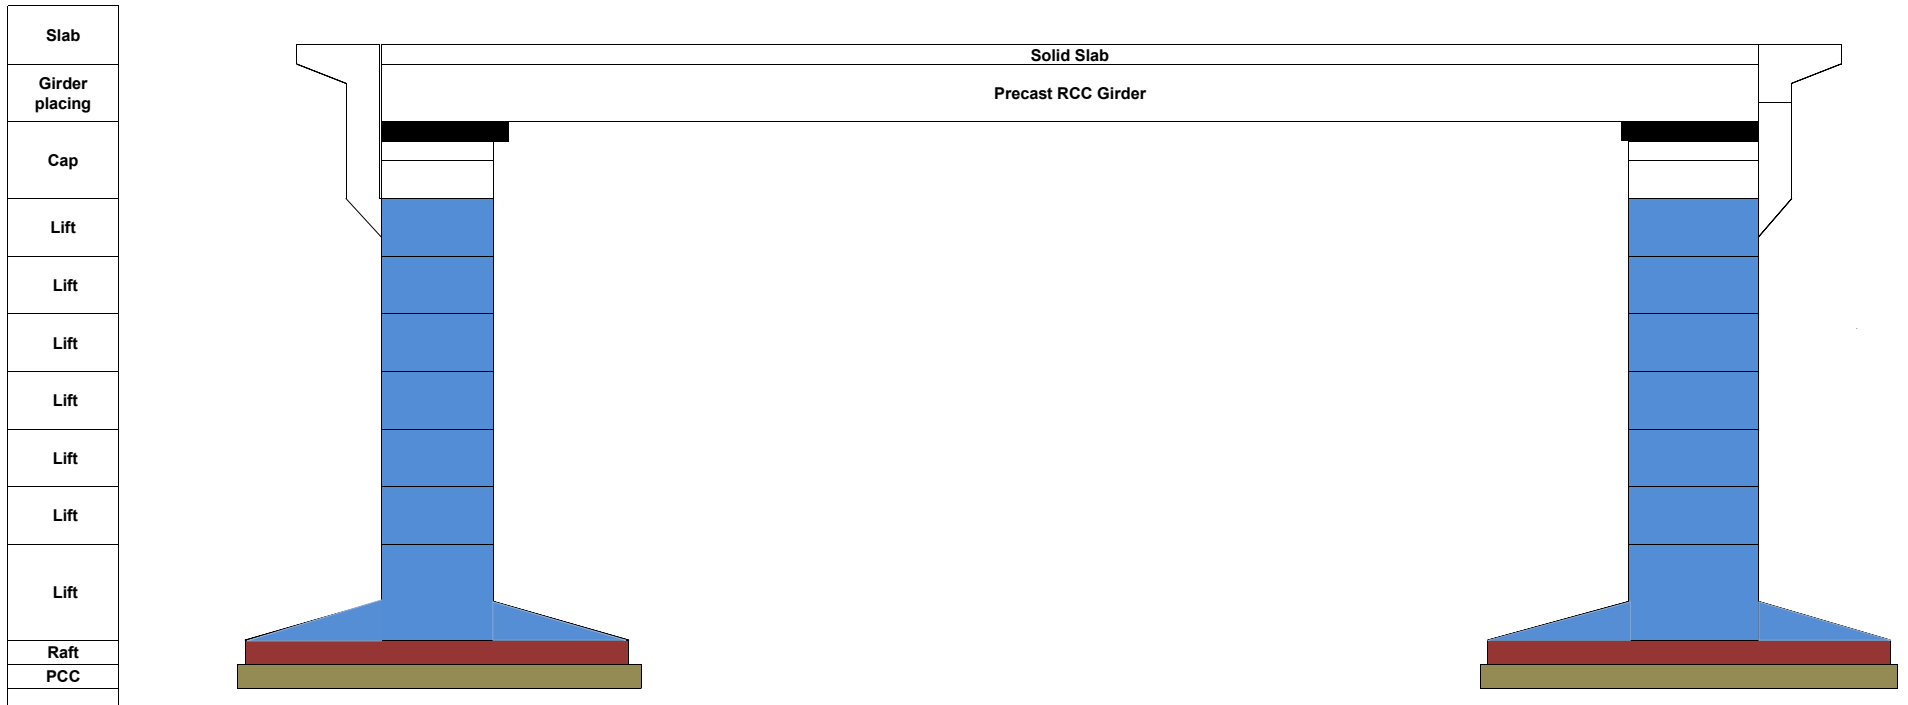




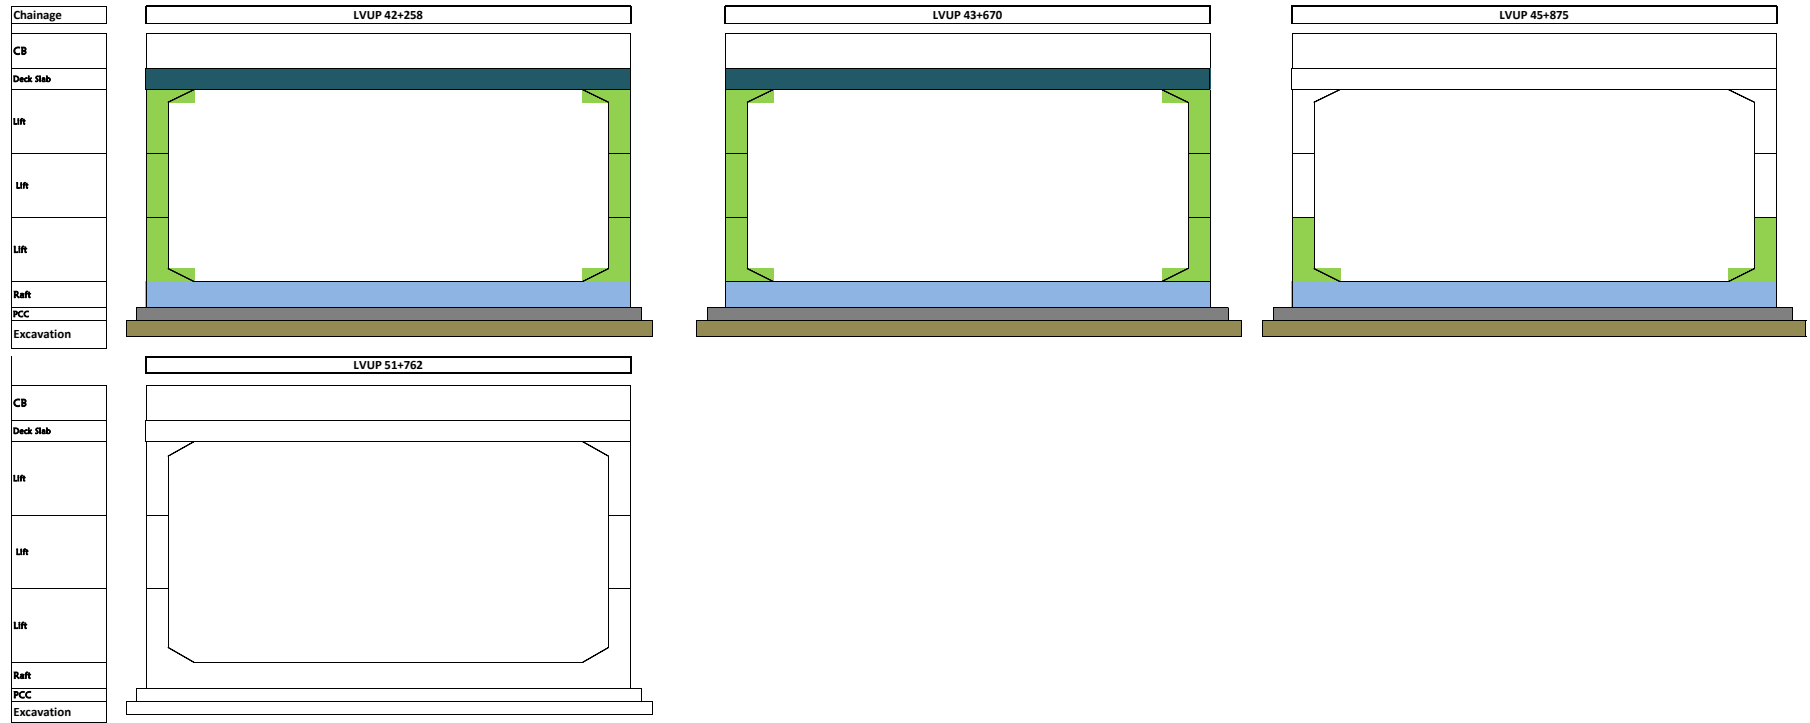


MAJOR BRIDGE AT 36+070 (AHU RIVER) LHS

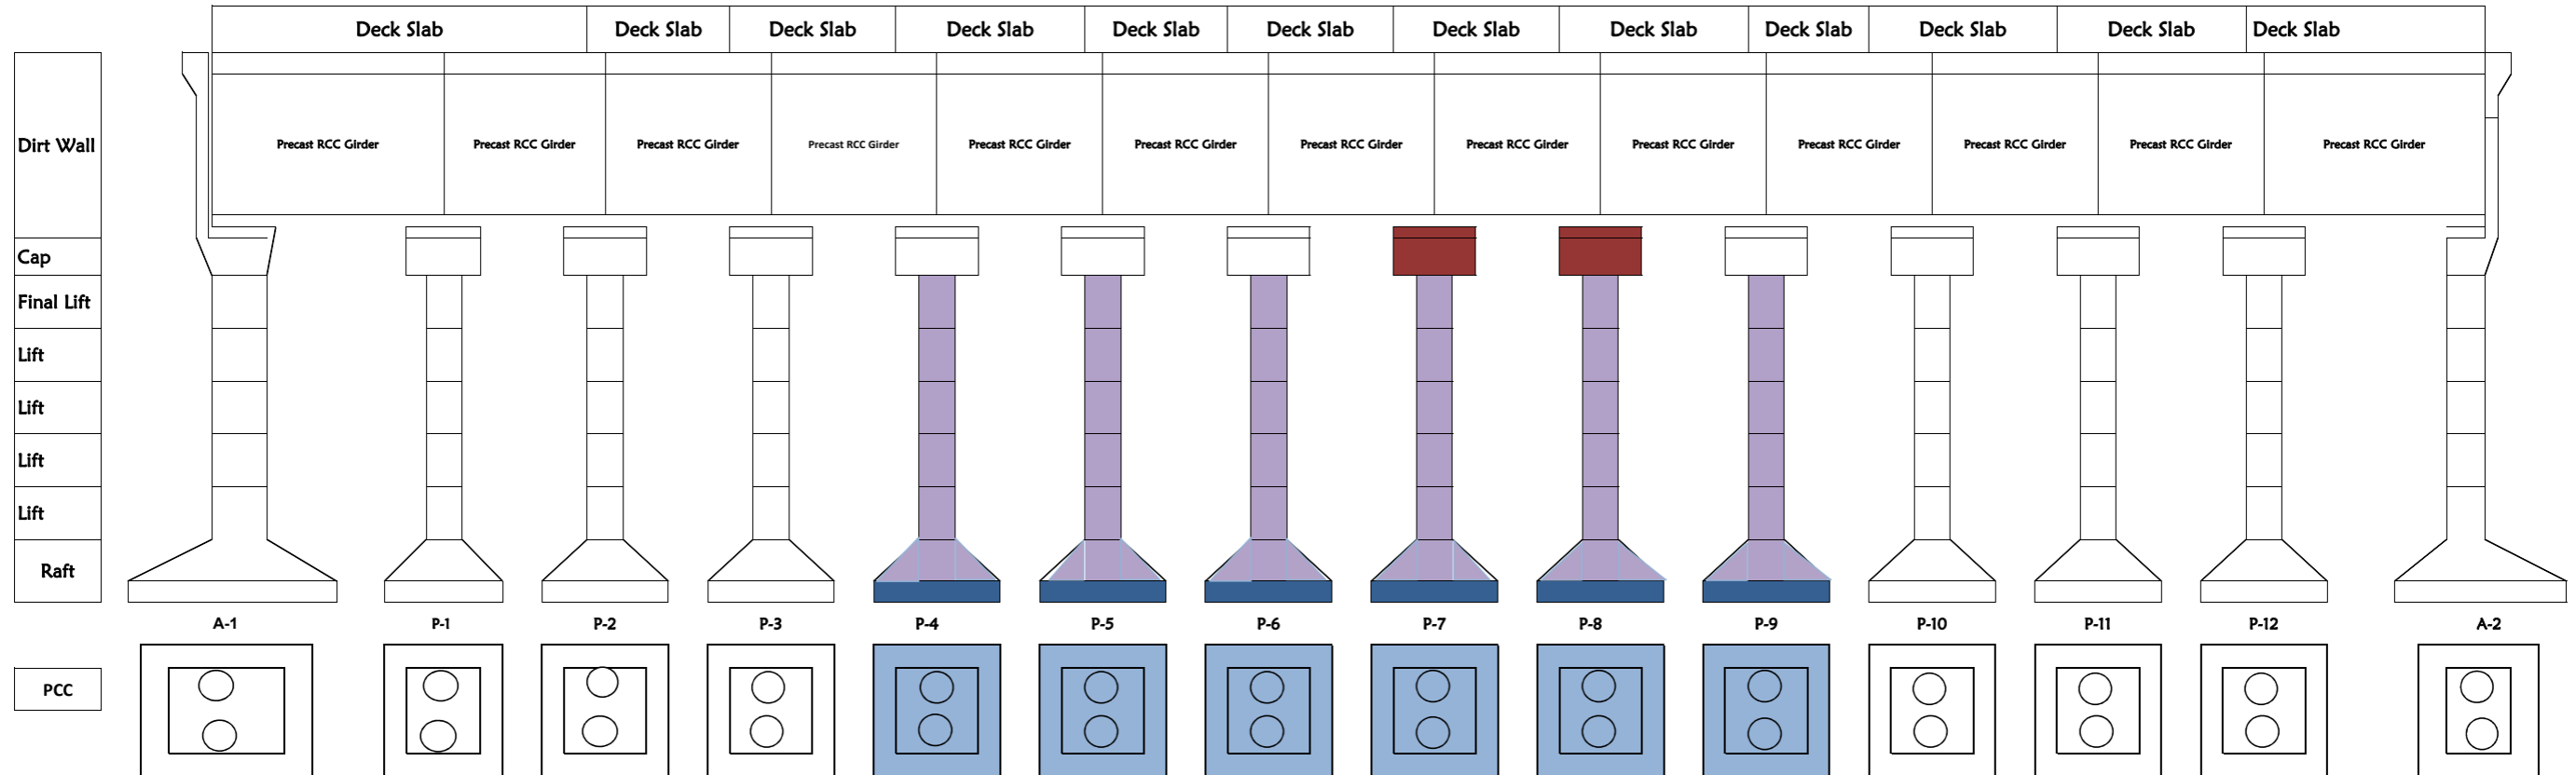


MAJOR BRIDGE AT 36+070 (AHU RIVER) RHS

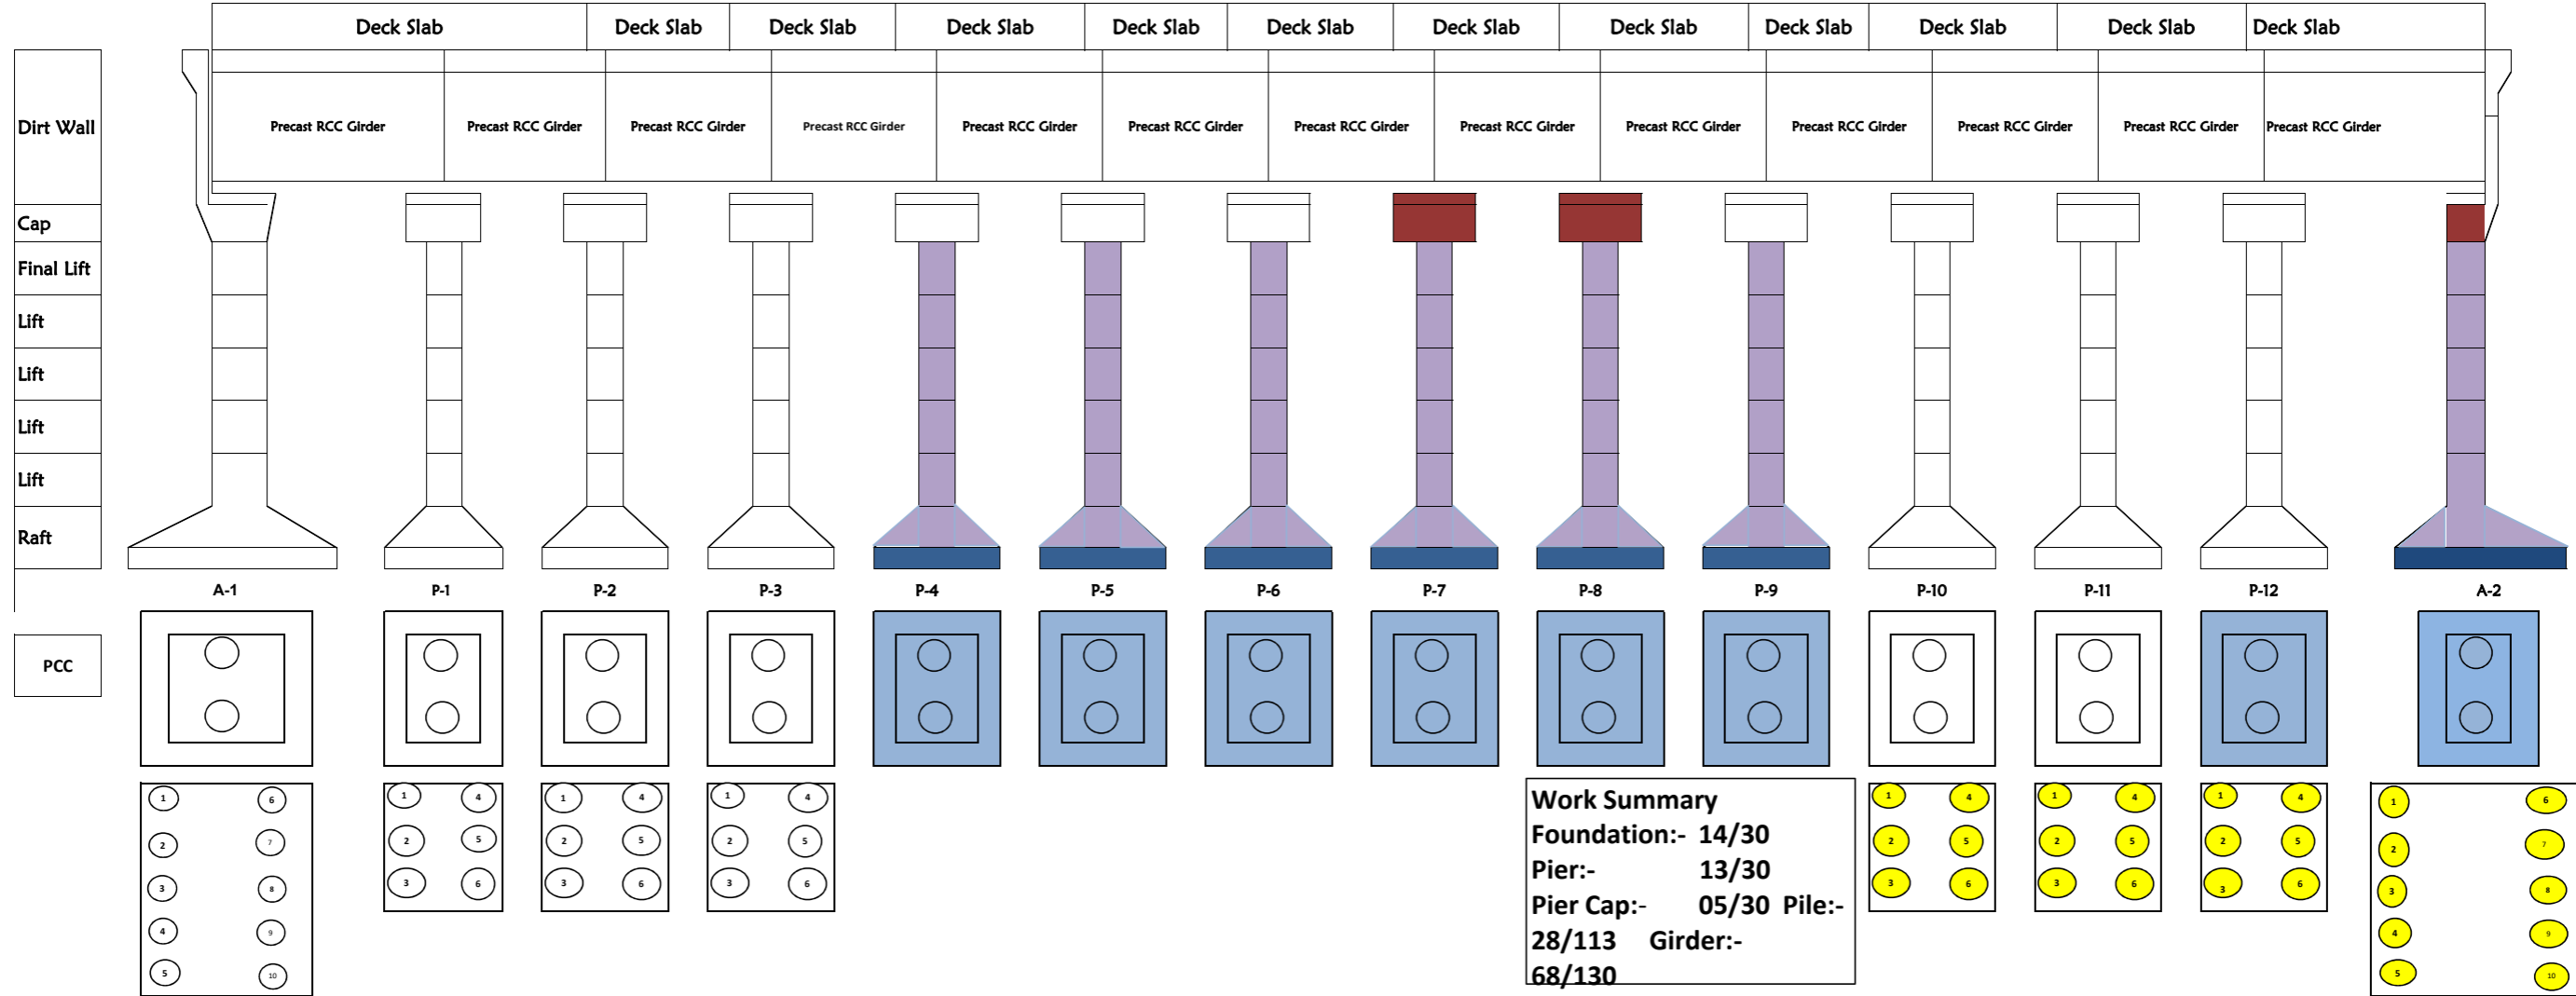


FLYOVER (46+950)LHS

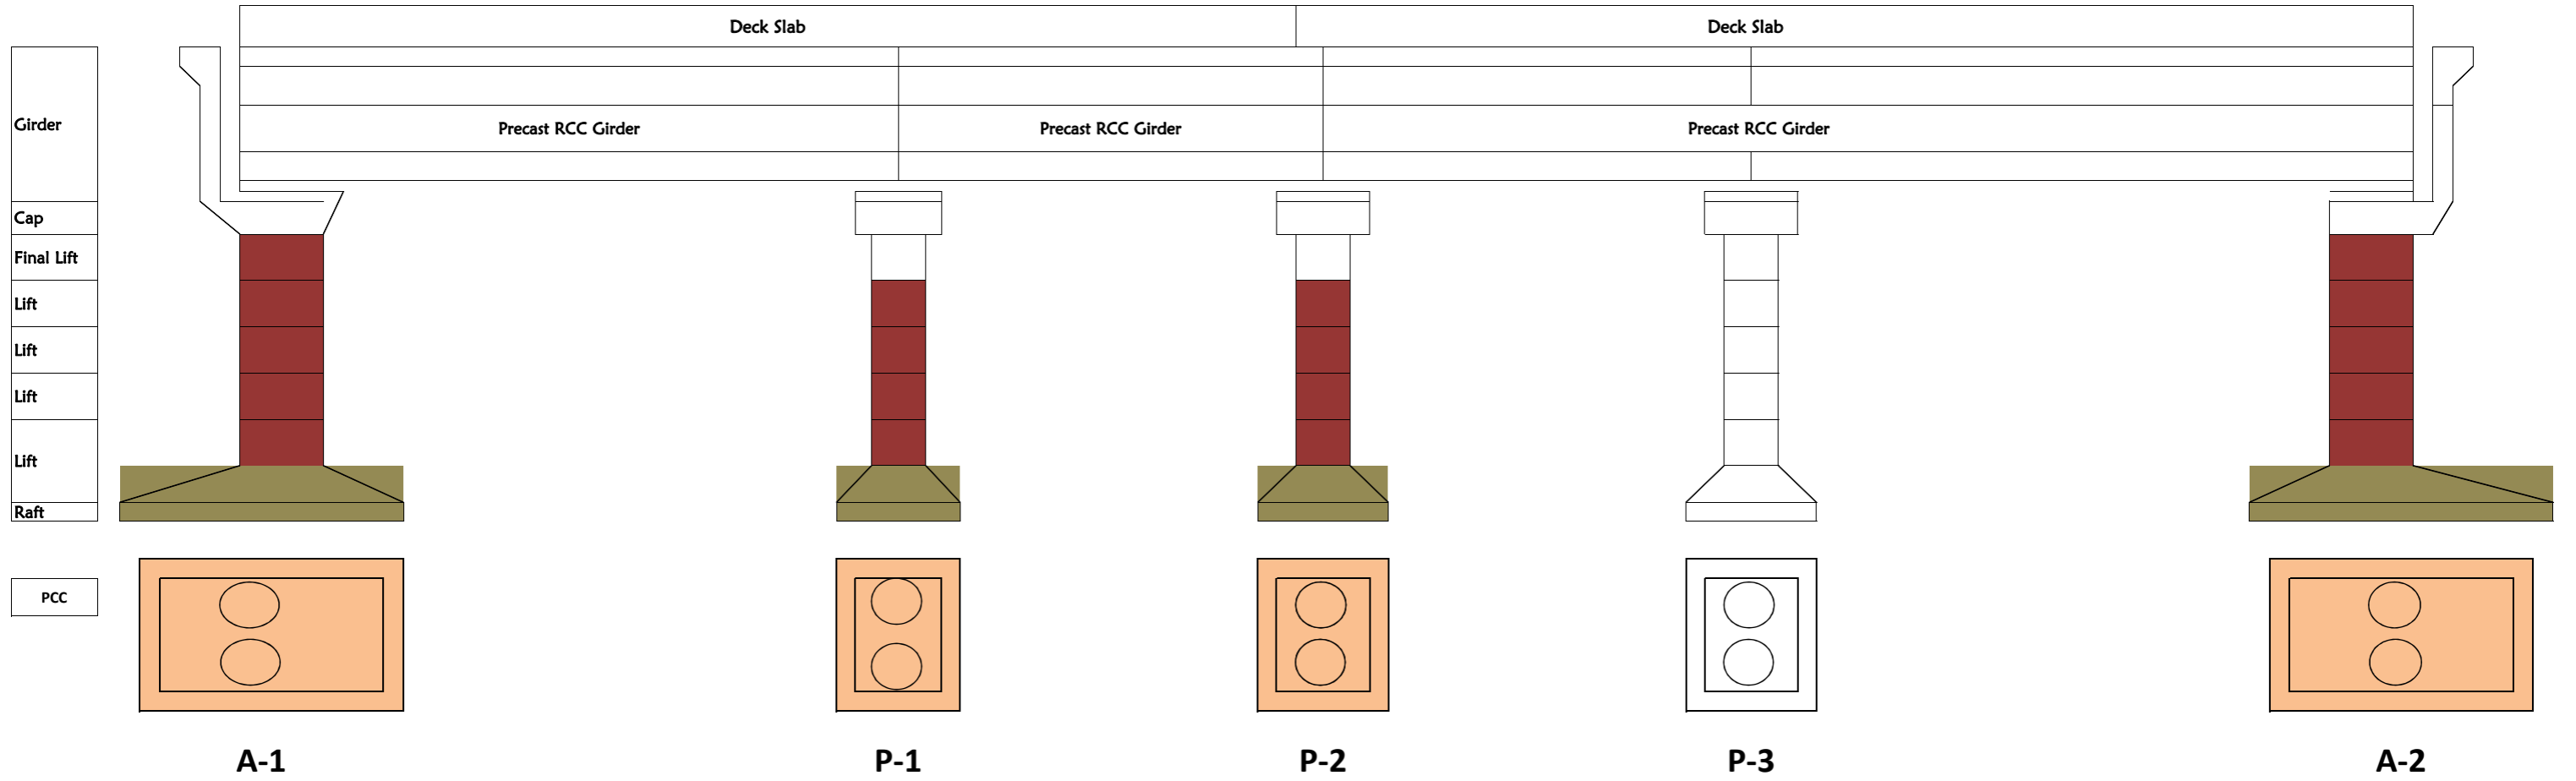


FLYOVER (46+950)RHS

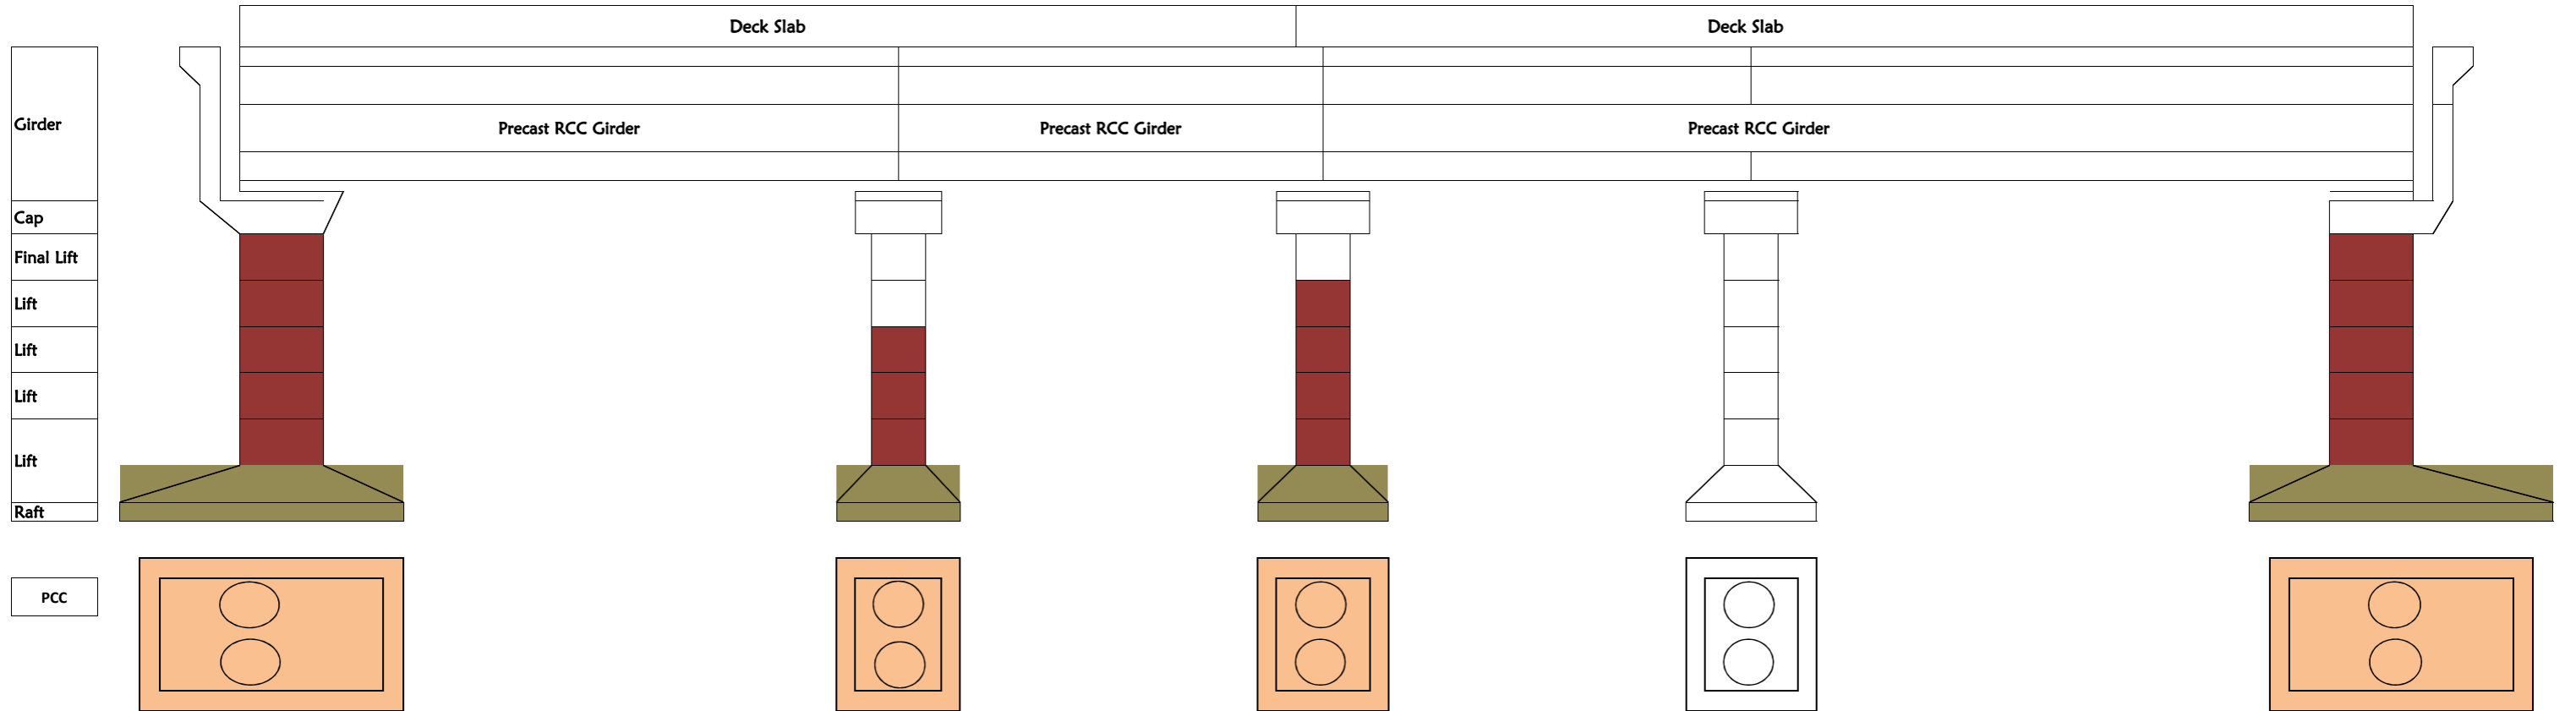


FLYOVER (50+095)RHS

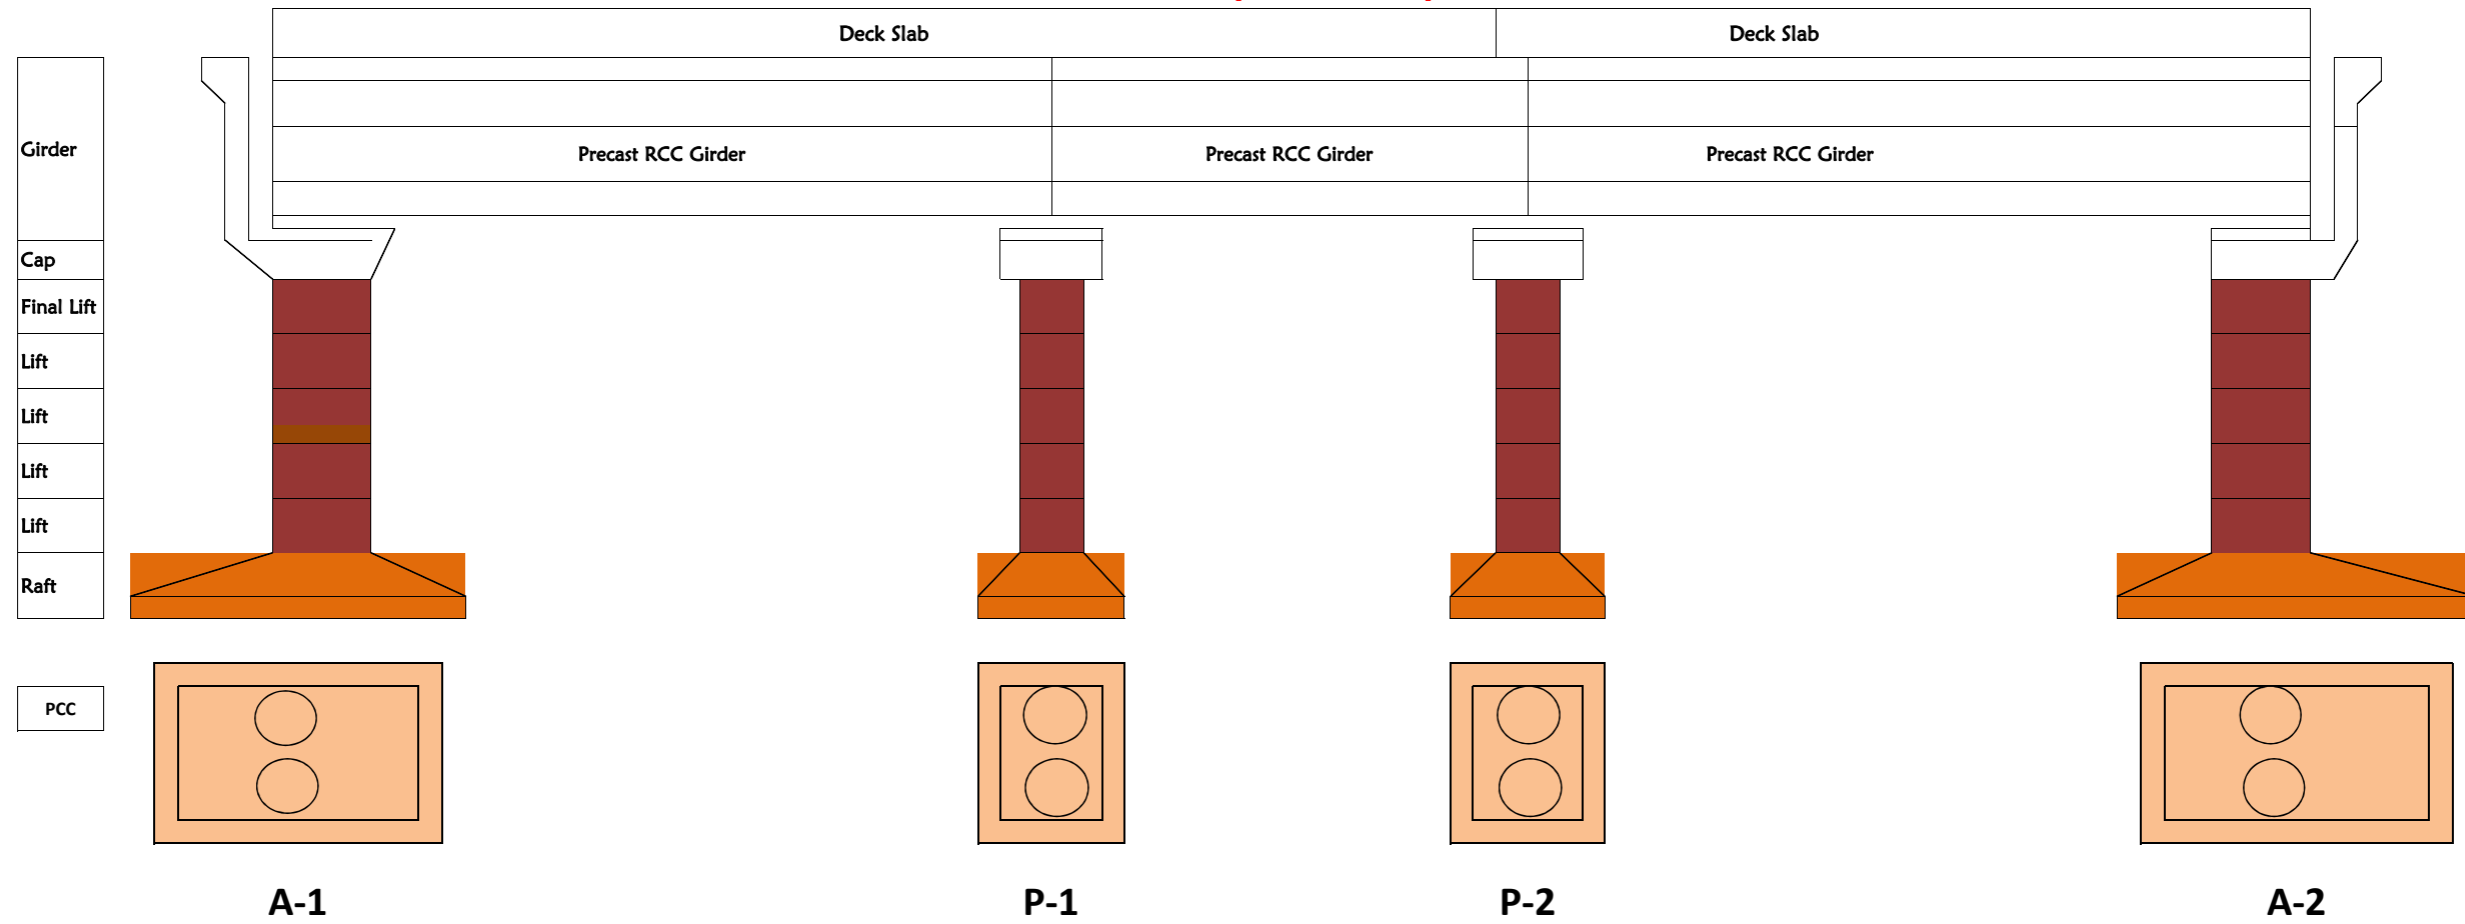


FLYOVER (50+095)LHS

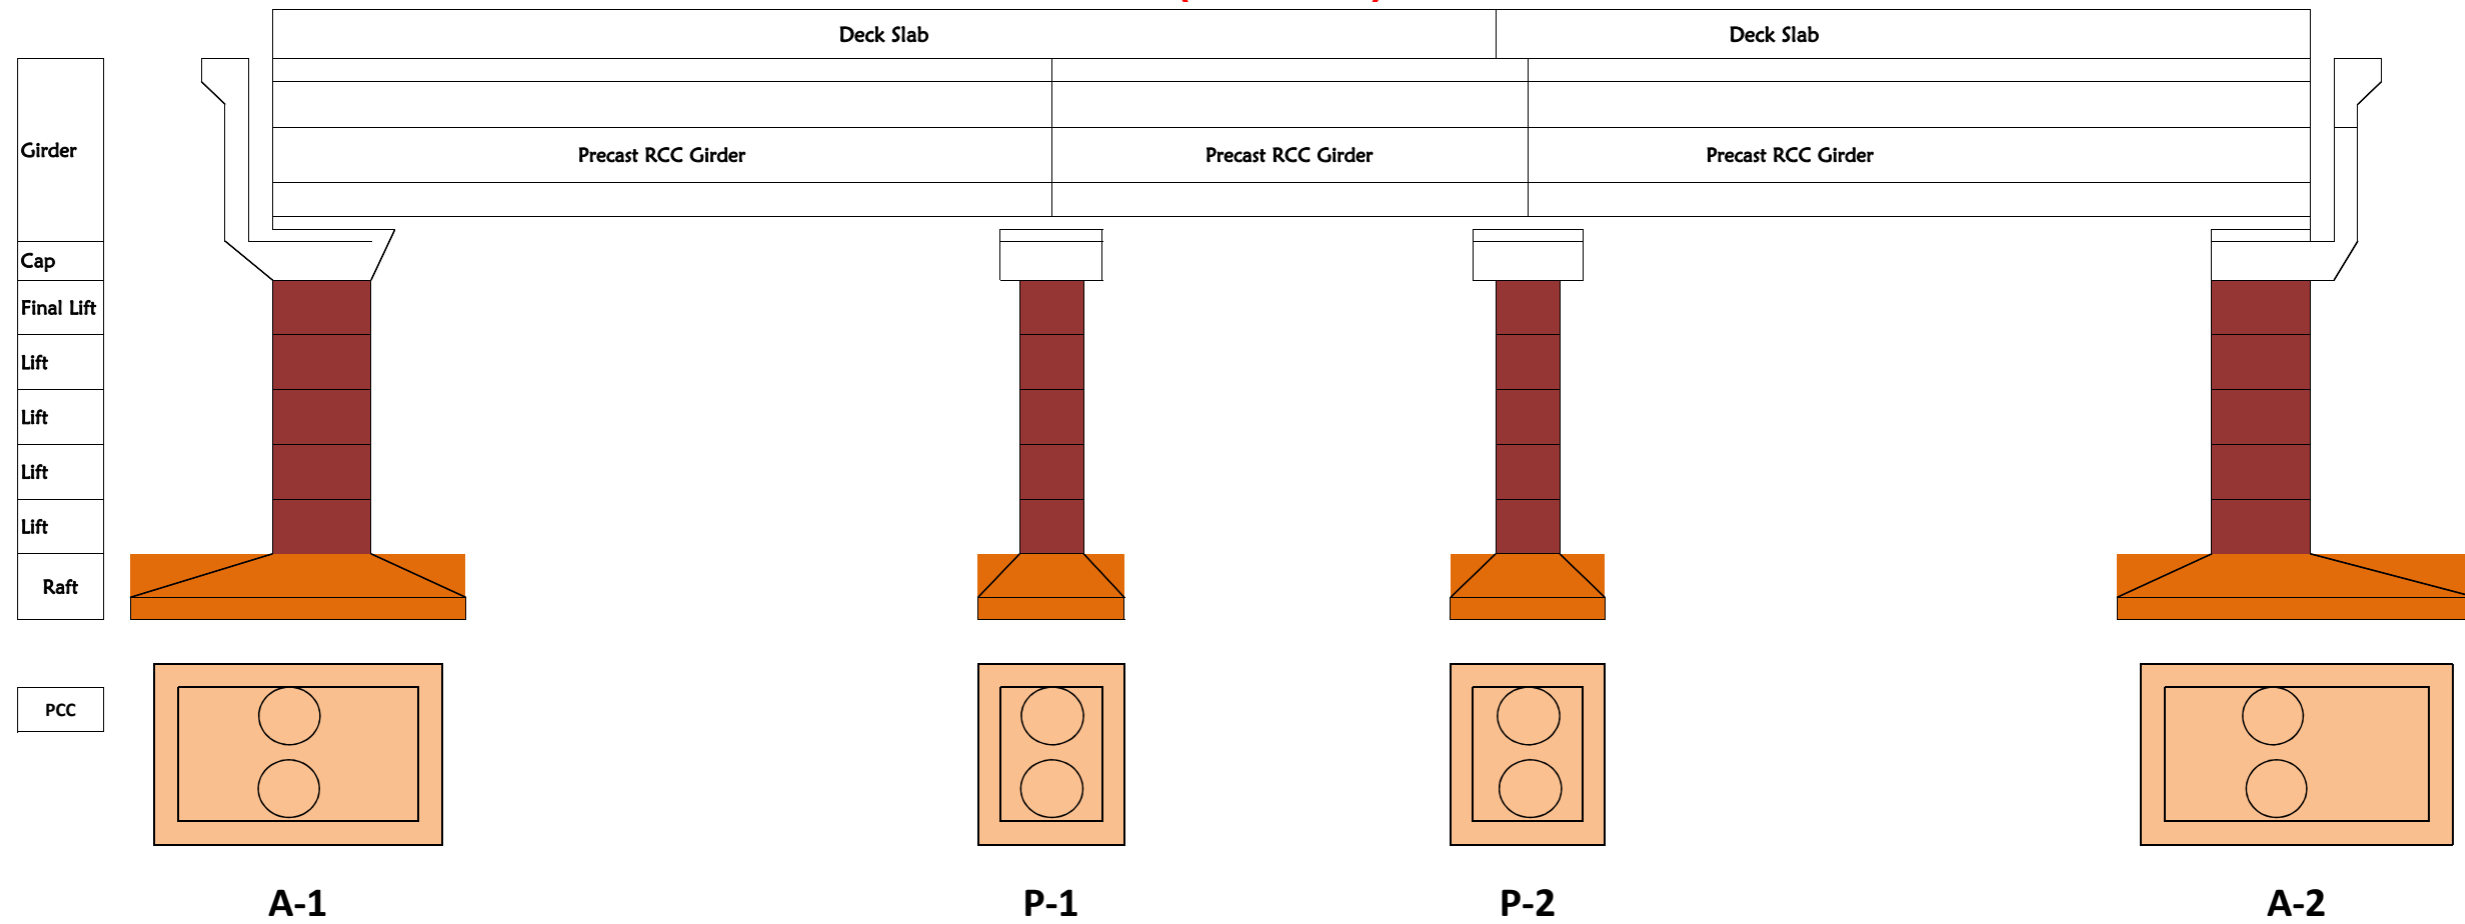


FLYOVER (58+128)LHS

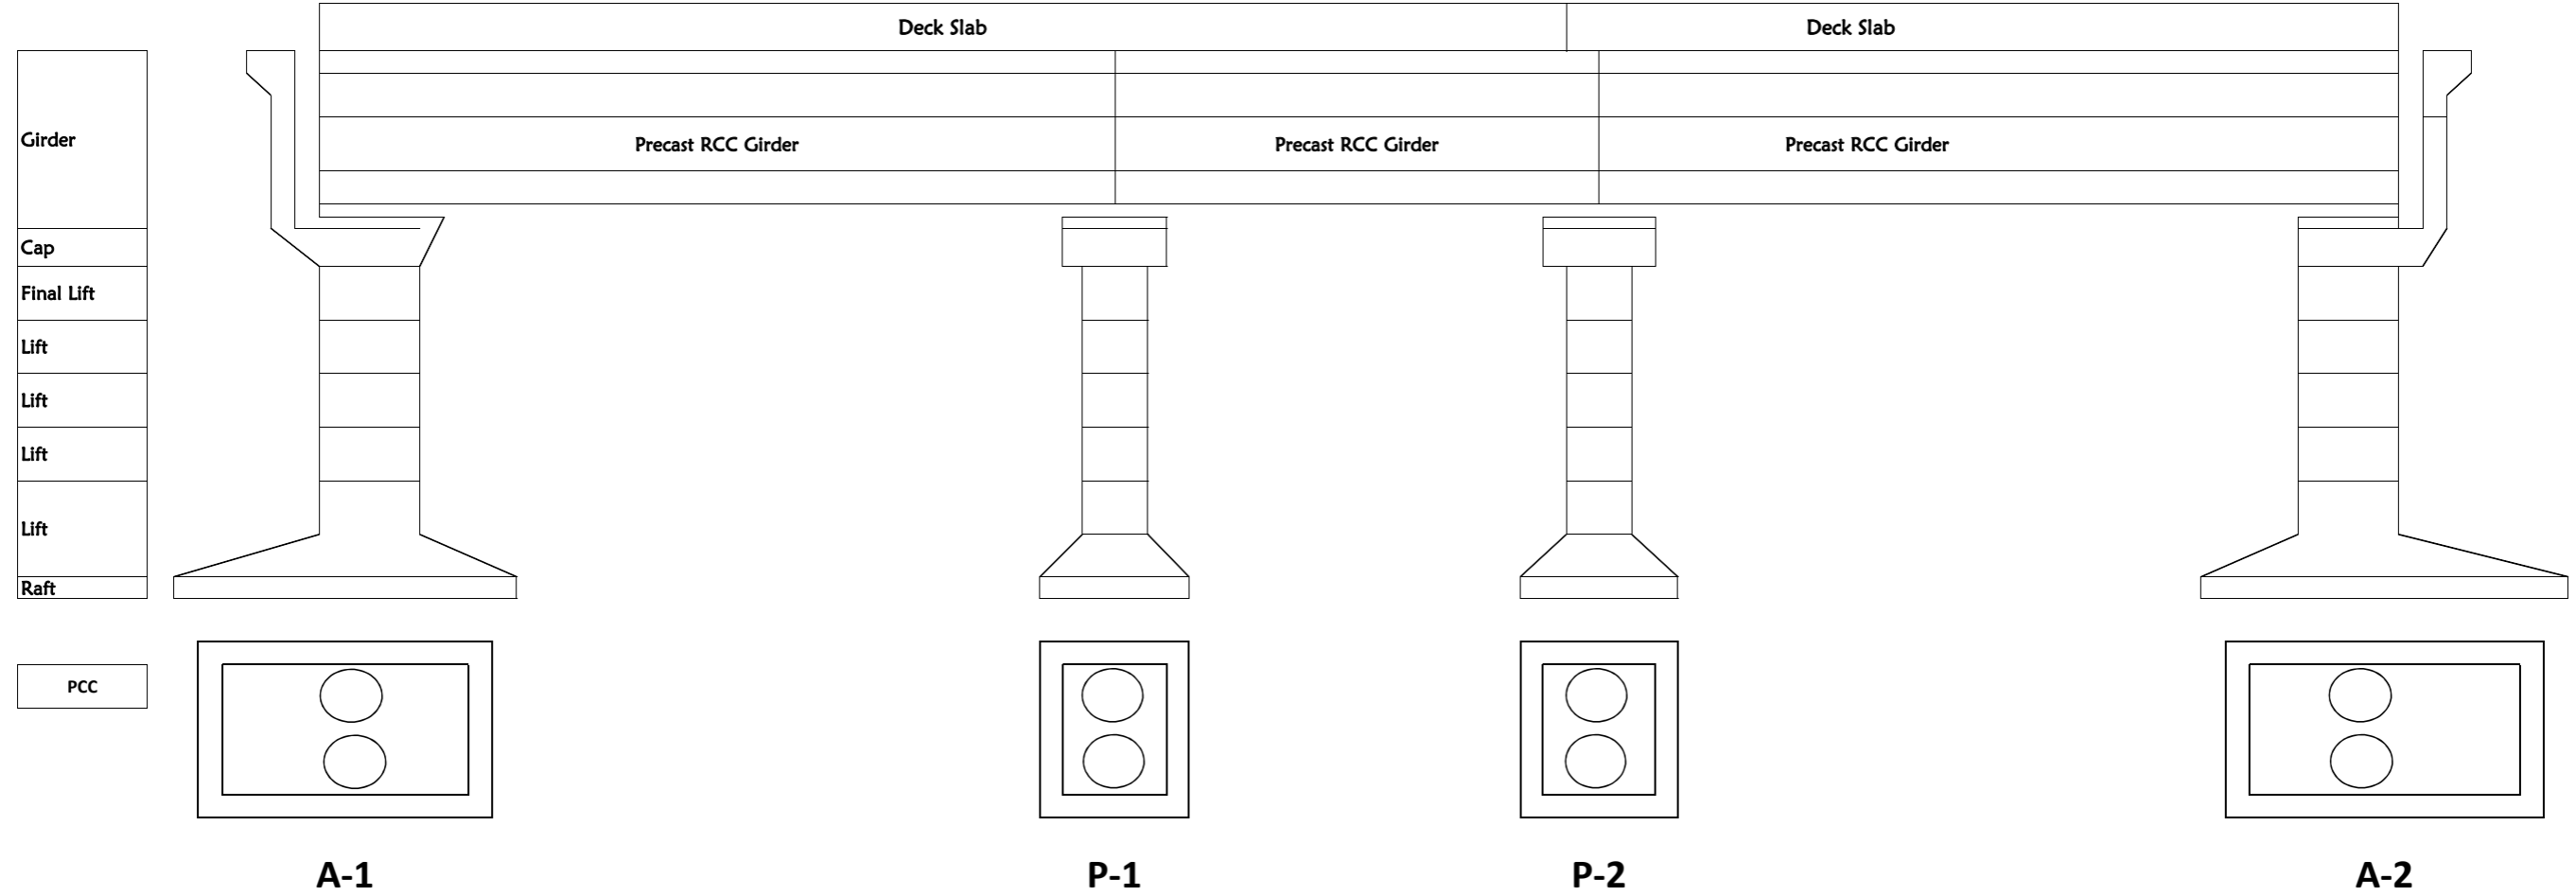

FLYOVER (58+128)LHS

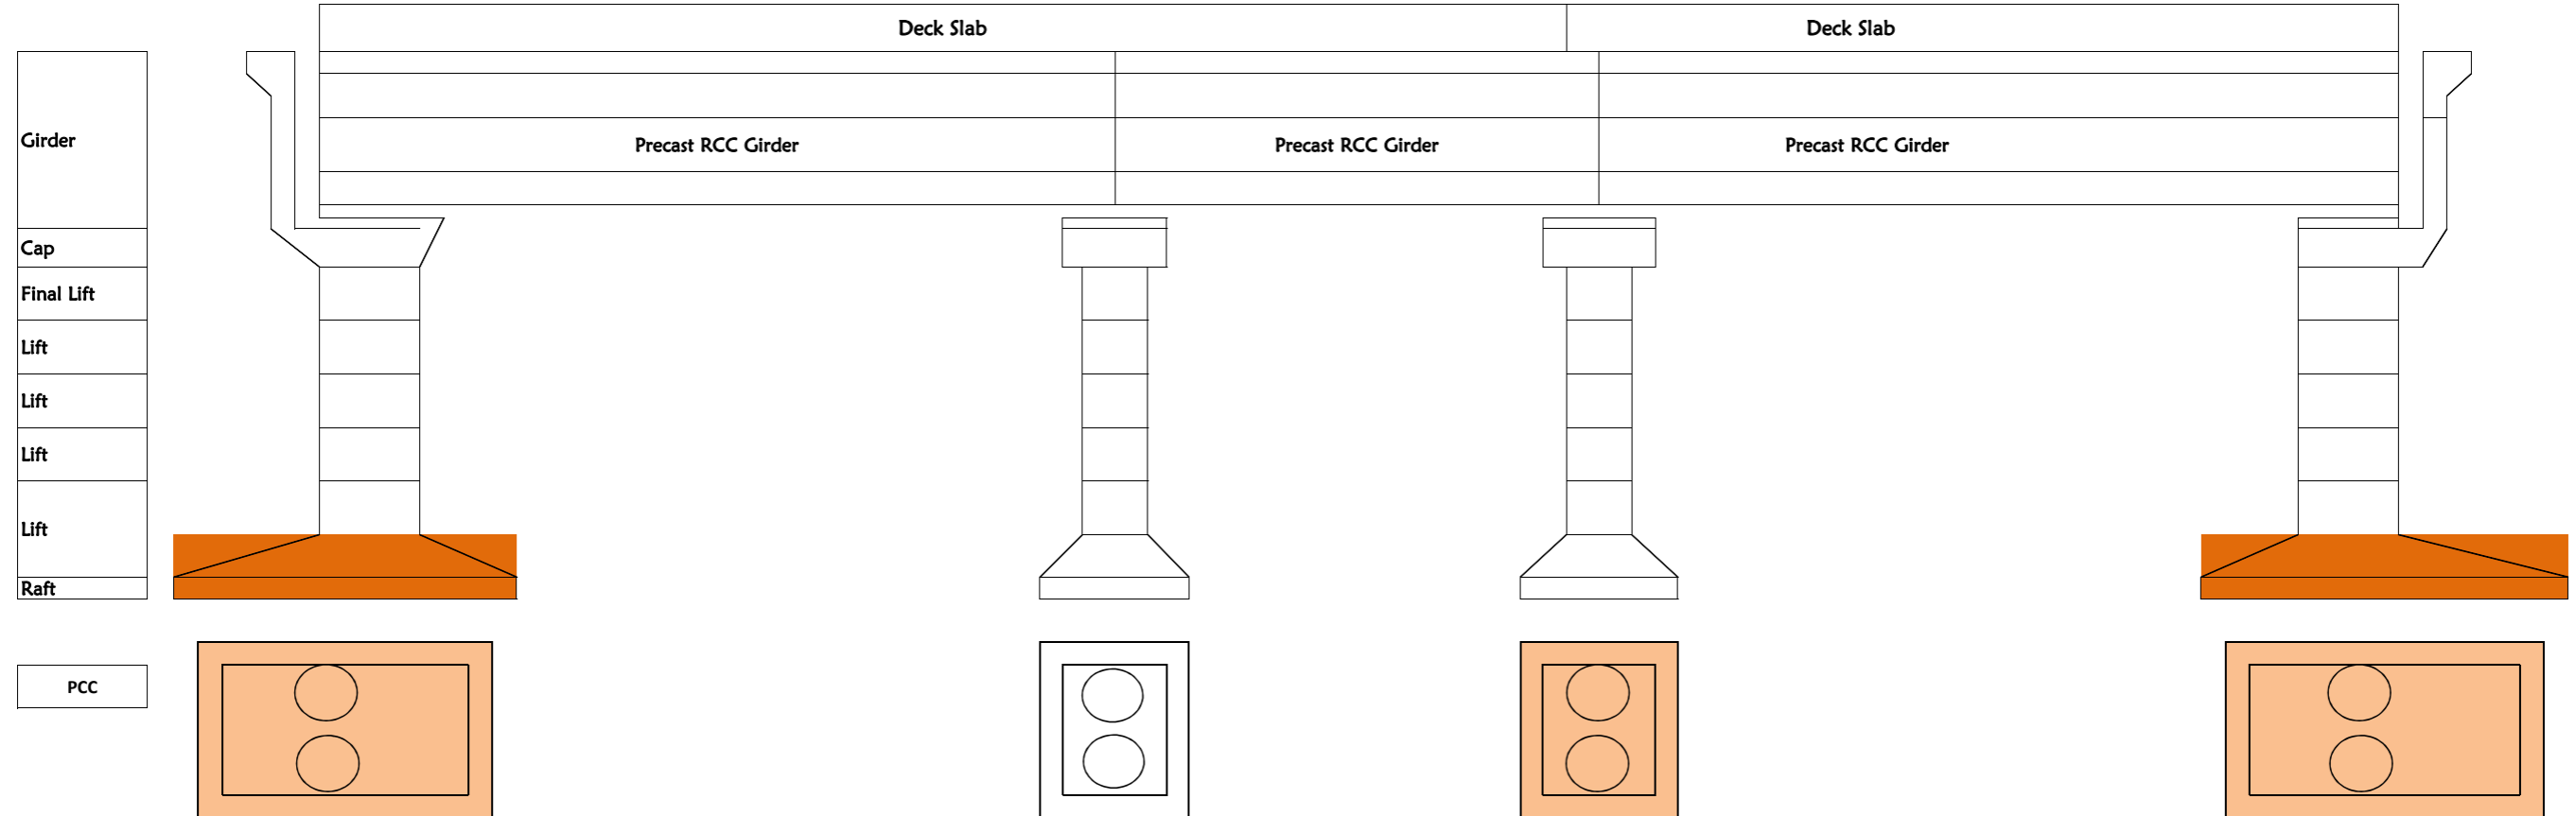


Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Pa

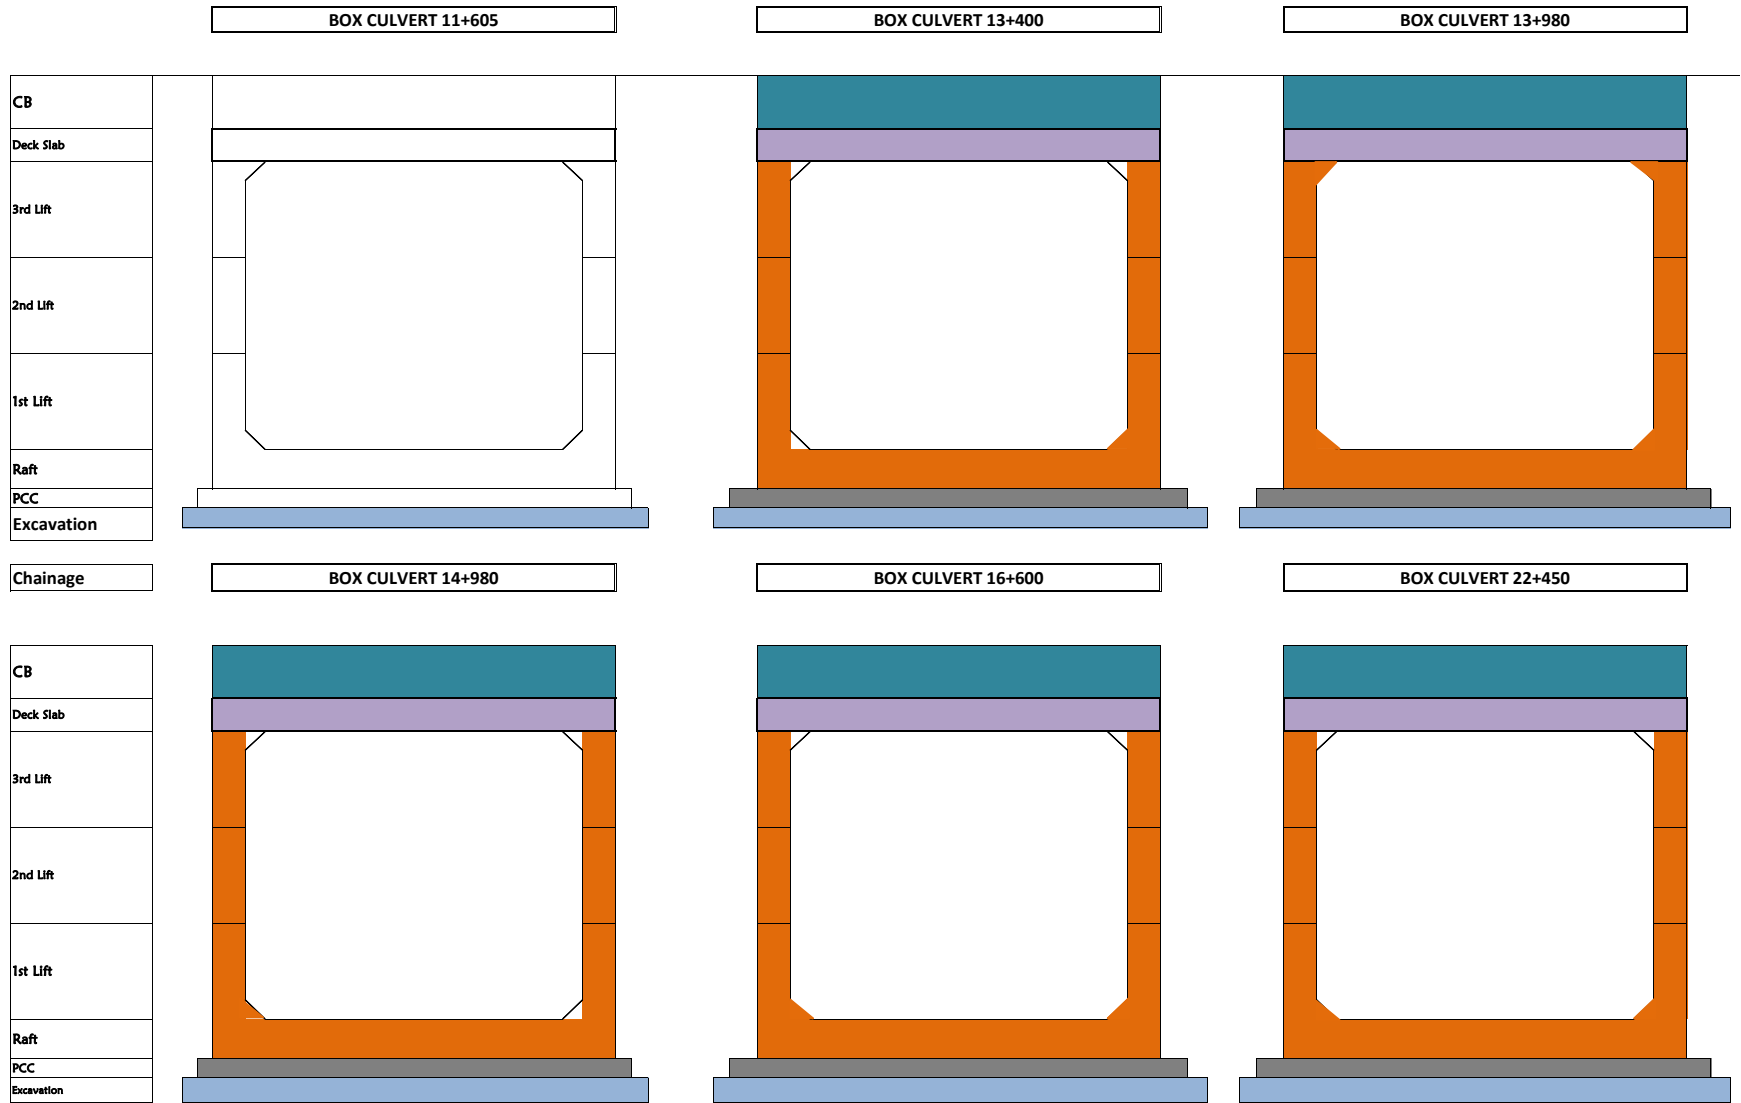


Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Pa




Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Pa

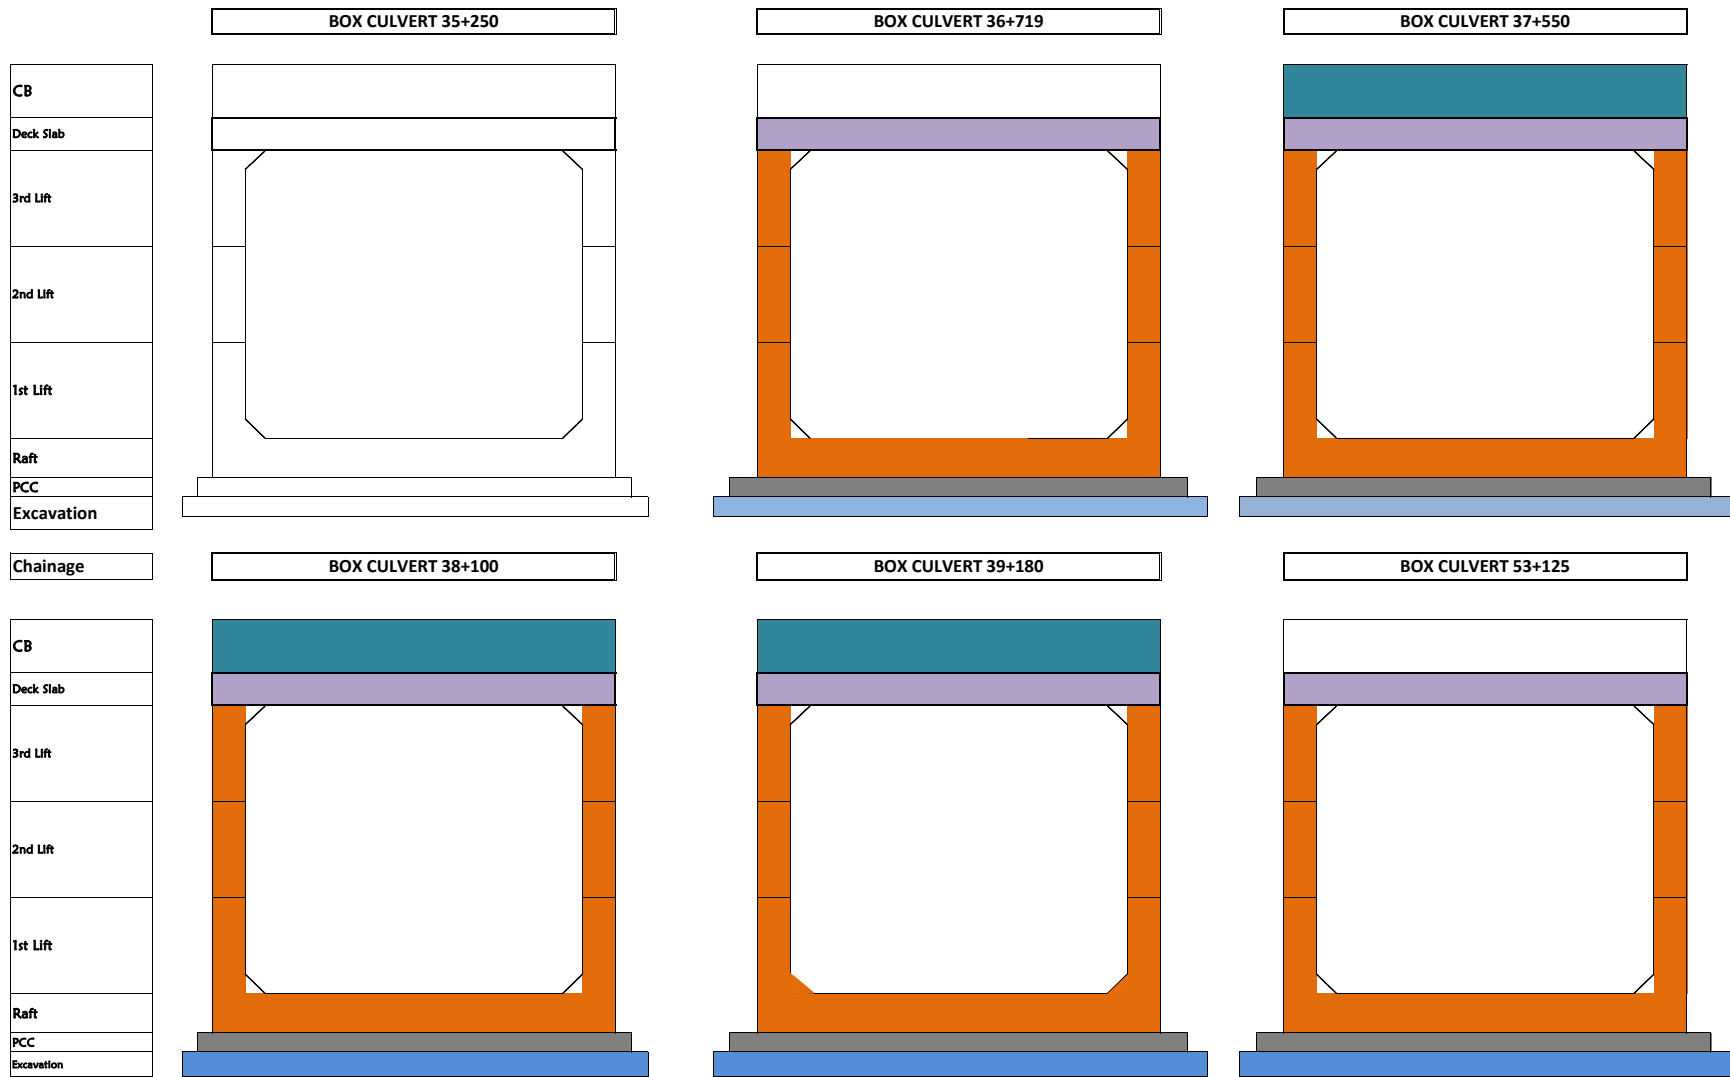


Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Pa

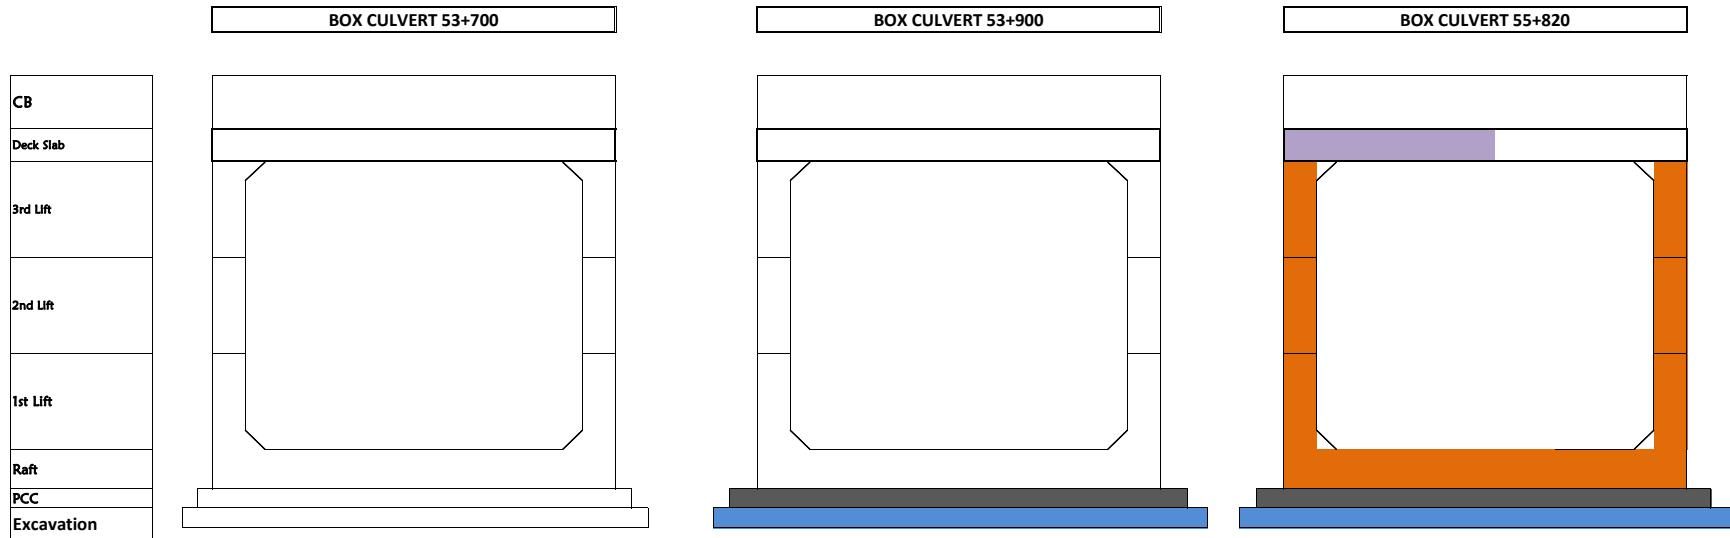

Additional / SR

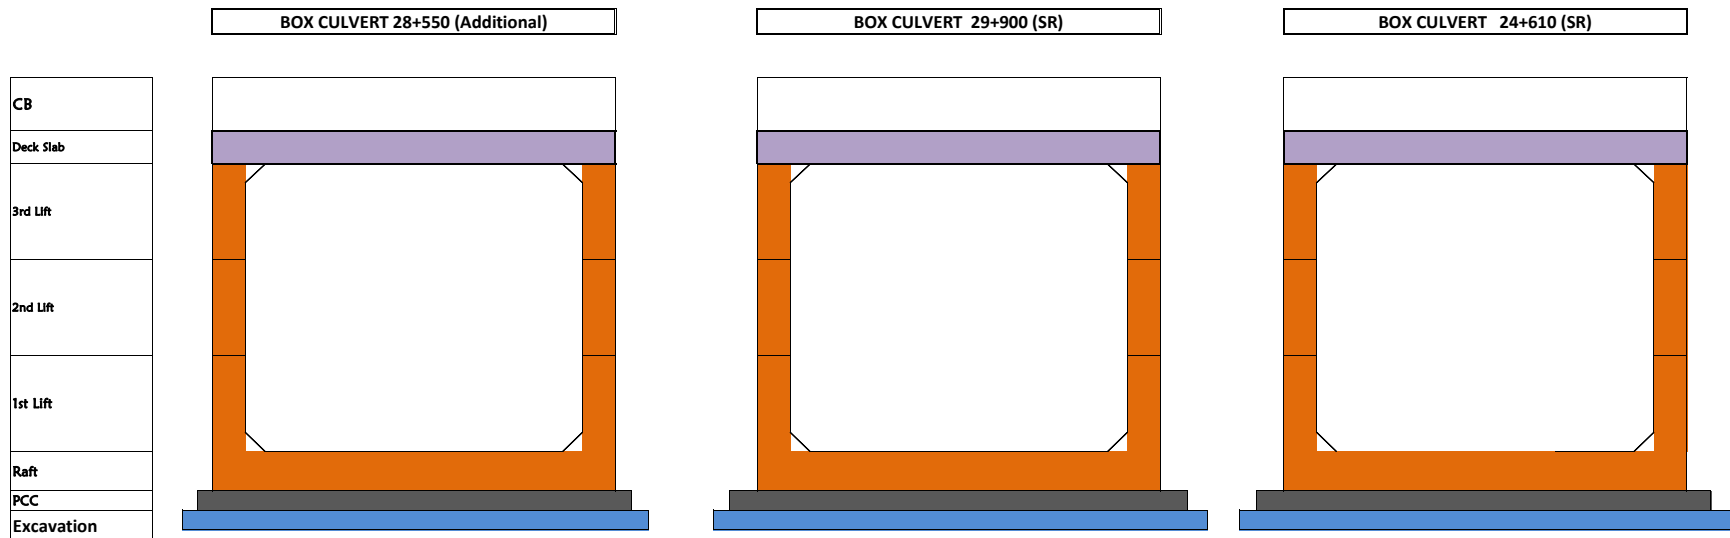







Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

FLY OVER + MAJOR BRIDGE(ELEVATED STRUCTURE- 47+450 TO 48+150)LHS

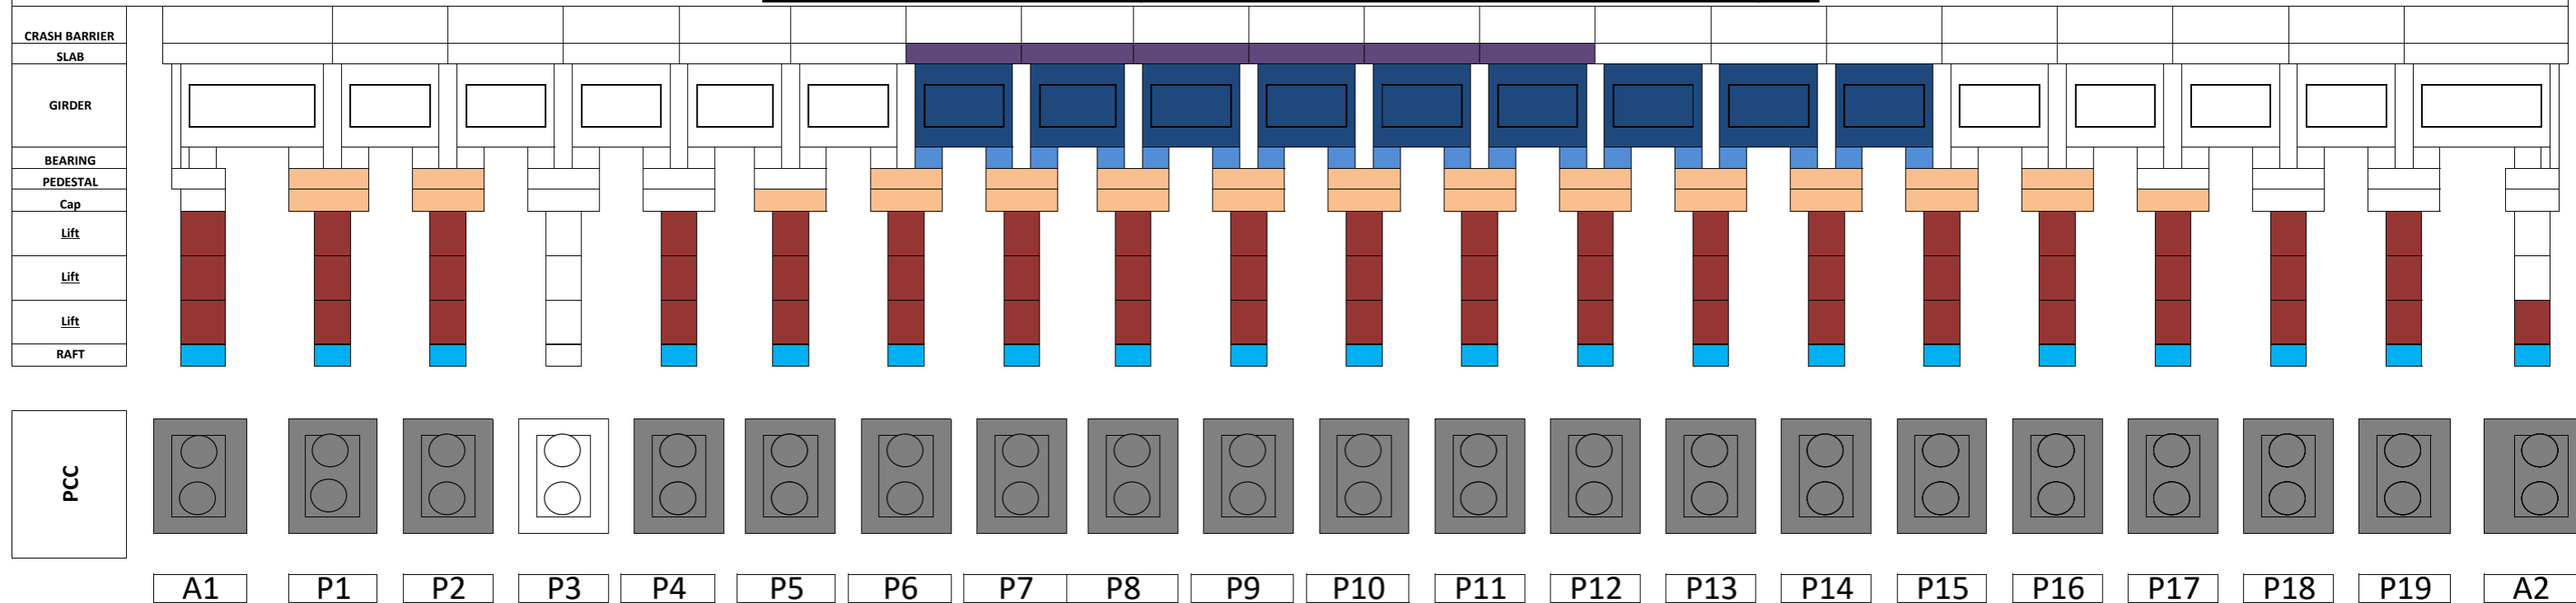



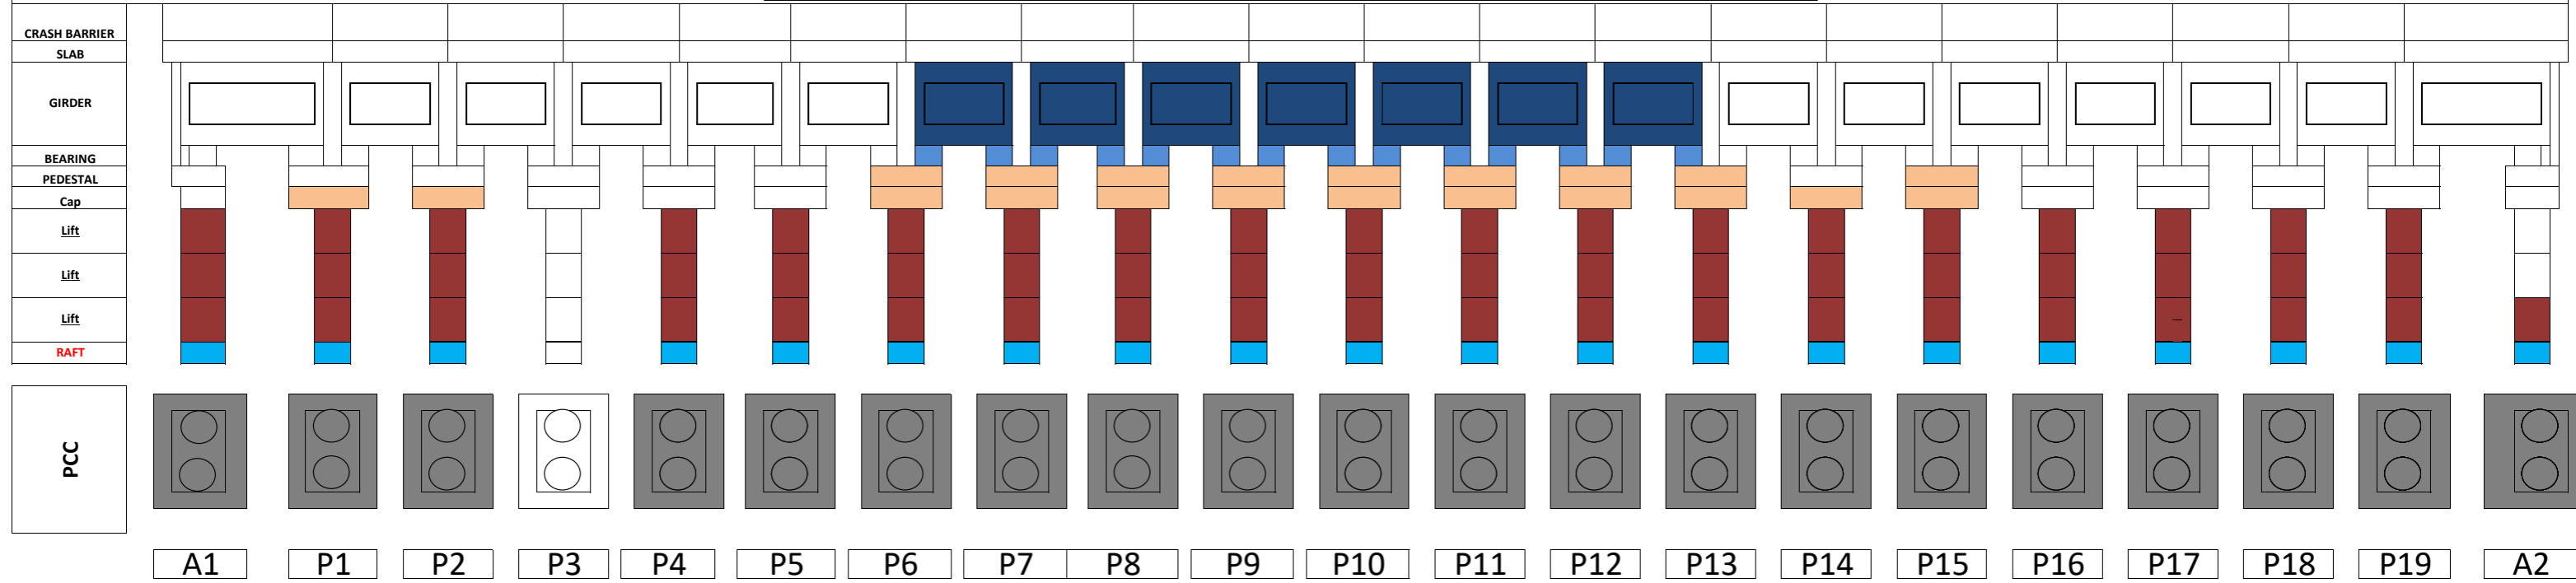








FLY OVER + MAJOR BRIDGE(ELEVATED STRUCTURE- 47+450 TO 48+150) RHS












Work Summary
 Foundation:- 40/42
 Pier:- 38/42
 Pier Cap:- 27/42
 Girders:- 109/200
 Girder Launch:- 80/200

Hindrance Details

No.	Photo	Obstruction Length (m)	LHS-Type of Hindrance	Chainage		RHS-Type of Hindrance	Obstruction Length (m)	Photo	Expected Date of Clearance	Remark's
				From	To					
1				9+860	9+896	Boundary, House & Temple	+36			Difference of compensation
2				9+980	10+020	House, Boundary wall	+40			Award approval is pending from NHAI for structure
3		+20	House	10+050	10+070					Award Approval pending
4		+10	House	10+640	10+650					Award Approval pending for structure from NHAI
5		+10	House	10+670	10+680					Compensation pending for structure
6		+800	Boundry wall, House	10+900	11+700					Compensation pending most of structure due to dispute in SDM Court
7				10+890	11+000	Compensation problem	+110			Dispute in court
8				11+300	11+350	House	+50			Compensation pending for structure
9		+60	House	12+315	12+375					Disbursement is done but not removed due to differentiation of compensation
10				15+830	15+880	Wall & House	+50			Compensation pending for structure
11		+100	Service Station	20+160	20+260					Difference of measurement of award structure is pending under NHAI
12		+150	Compensation problem	20+580	20+730	Compensation problem	+150			Disbursement ok, but Hindrance not removed from Land owner
13				20+750	20+830	Factory	+80			Difference of structure award
14		+120	Compensation problem	21+380	21+500	Compensation problem	+120			Difference of Land measurement pending from SDM, Ramganjmandi

Hindrance Details

No.	Photo	Obstruction Length (m)	LHS-Type of Hindrance	Chainage		RHS-Type of Hindrance	Obstruction Length (m)	Photo	Expected Date of Clearance	Remark's
				From	To					
15		+400	Compensation problem for Room, Bus-stand, etc	23+000	23+400					Compensation pending due to mutation opening under process at DM ,Kota
16		+50	Shop, Boundary & Land Compensation problem	23+800	23+850					Payment Disbursement pending for some structure
17				23+850	24+200	Factory	+350			Difference of Compensation claim by factory owner to LAO
18		+100	Structure, Land	24+000	24+100					Difference of Land compensation under process in LAO since 3 month
19				24+270	24+680	House ,Temple, Boundary wall, Hauz, etc.	+410			Some Villagers are unsatisfied for award done by NHAI
20		+660	Hand pump,Toilet, Verandah,Sewer tank, Boundary wall, etc	24+270	24+930					Some Villagers are unsatisfied for award done by NHAI
21				24+930	24+940	Shop, Room, Chabutra, etc	+10			Some Villagers are unsatisfied by award done by NHAI
22		+0	Compensation problem	25+550	25+800	Chabutra & Well	+10			Land Award approval pending (Length is taken in Annexure-2)
23		+0	Compensation problem	27+380	28+000	Compensation problem	+0			Forcefully Stopped the work by villagers due to Additional Land award approval pending (Length is taken in Annexure-2)
24		+85	Compensation problem	30+500	30+585	Compensation problem	+85			Compensation pending in SDM court
25		2+500	DLC problem	33+500	36+000	DLC problem	2+500			Compensation pending
26		+100	Land	41+200	41+300					Compensation pending due to High court-cases
27				42+330	42+400	Land	+70			Compensation pending due to court-cases through SDM
28		+0	Orange Garden	48+100	48+180	Orange Garden	+0			Award approval pending for Trees from RO (Length is taken in Annexure-3)

Hindrance Details

No.	Photo	Obstruction Length (m)	LHS-Type of Hindrance	Chainage		RHS-Type of Hindrance	Obstruction Length (m)	Photo	Expected Date of Clearance	Remark's
				From	To					
29		+10	House	49+960	49+970					Award pending for structure from RO
30		+700	DLC problem	51+400	52+100	DLC problem	+700			Compansation pending
31		+0	Orange Garden	54+180	54+400	Orange Garden	+0			Award approval pending for Trees from RO (Length is taken in Annexure-3)
32		+80	Garden	54+580	54+660	Garden	+80			Award approval pending for Trees from RO
33				55+500	55+600	Orange Garden	+0			Villagers forcefully stopped the work due to demanding orange trees compensation(Length is taken in Annexure-3)
34				55+600	55+700	Orange Garden	+100			Villagers forcefully stopped the work due to demanding orange trees compensation
35		+30	Garden	55+650	55+680					Award approval pending for Trees from RO
36				56+000	56+700	Orange Garden	+0			Villagers forcefully stopped the work due to demanding orange trees compensation(Length is taken in Annexure-3)
37		+70	House, Boundary wall	57+980	58+050					Award pending for structure from RO
38		+130	House	58+120	58+250					Award pending for structure from RO
39				58+060	58+150	House & Shopes	+90			Disbursement pending
Total		6+185					5+041			

Additional Award Approved on date 17.06.2019. Disbursement under progress (Ramganjmandi Section)

Annexure - 2

Sr. No.	Village	Khasra No.	Rukba	Chainage		Length (m)	Side	Description	Remarks
				From	To				
1	Kamalpura	73	0.1578	9+860	9+940	0	RHS	Govt. (Acquired by factory owner)	(Length is taken in Annexure-1)
		279/24	0.0450	10+100	10+120	20	RHS	Industrial (Private)	
		282/24	0.0100	10+120	10+135	15	RHS	Industrial (Private)	
		50/276	0.0950	10+700	10+730	30	RHS	Industrial (Private)	
2	Manpura	262	0.0150	12+350	12+400	0	LHS	Government	(Length is taken in Annexure-1)
3	Teliyakhedi	105	0.0668	15+200	15+300	+100	RHS	Government	Rest area. Tree are not in stretch of road
		106	0.9317					Private	
		107	0.2750					Private	
		112	0.0430					Private	
		25/468	0.3145	14+250	14+275	25	LHS	Private	
		30	0.0780	14+350	14+375	25		Private	
		81	0.0120	15+300	15+550	250	RHS	Private	
		82	0.0700					Government	
		83	0.2800					Private	
		97	0.0300					Private	
99	0.5200					Private			
4	Askali	210	0.0227	16+700	16+750	50	RHS	Private	
		62	0.0157	16+100	16+150	50	RHS	Private	
5	Hiriyakhedi	245	0.0504	18+500	18+550	100	Centre	Private	
		278	0.0540	18+350	18+400	100	Centre	Private	
		283	0.0175	18+200	18+250	50	LHS	Private	
		284	0.0094				LHS	Private	
		93	0.0297	17+800	17+850	50	LHS	Private	
6	Kheemuch	657	0.0120	19+710	19+760	50	RHS	Government	
		666	0.0740	20+140	20+190	50	RHS	Industrial (Private)	
7	Atraliya	211	0.0291	21+650	21+700	50	LHS	Private	
		278	0.1046	21+500	21+600	100	RHS	Private	
		560/530	0.2800	21+720	21+820	100	LHS	Private	
		570/211	0.0200					Private	
8	Pamakhedi	212	0.0553	23+140	23+150	10	RHS		
		288	0.0159	23+440	23+480	40			
		297	0.0056				Private		
		344/297	0.0022	23+485	23+515	30	RHS	Private	
		18	0.0100	22+550	22+580	30	RHS	Private	

Sr. No.	Village	Khasra No.	Rukba	Chainage		Length (m)	Side	Description	Remarks
				From	To				
9	Ummedpura	133	0.0544	25+520	25+780	260	LHS	Private	
		129	0.1985					Private	
10	Rampuriya	310/166	0.0100	26+300	26+325	50	BHS	Private	
		140	0.0100	26+400	26+425	50		Private	
11	Suket	976	0.0158	27+800	27+830		RHS	Private	
12	Beedmandi	241	0.0056	27+380	28+000	+620	LHS	Private	
		238	0.0951					Private	
		243	0.2569					Private	
		243/276	0.3212					Private	
		246	0.7000					Private	
		307/258	0.5789					Private	
		258	0.4753					Private	
		255	1.4639					Private	
		254	0.7225					Private	
		295/254	0.4600					Private	
		296/254	0.4700					Private	
		297/254	0.2300					Private	
		249	0.1659					Rajasva	
		250	0.5186					Charagah	
13	Aranyakhurd	605/246	0.0331	29+010	29+090	80	RHS	Private	
14	Basyahedi	50	0.0454	31+515	31+565	50	RHS	Private	
		153	0.0135	32+120	32+150	30	LHS	Charagah	
		436	0.1349	33+600				Govt. Land	(Length is taken in Annexure-1)
15	Aranyakalan	80	0.0118	33+640				Railway division	(Length is taken in Annexure-1)
		79	0.0512	33+620				Private	(Length is taken in Annexure-1)
		278	0.0600	34+350				Private	(Length is taken in Annexure-1)
		413	0.0060	34+180				Private	(Length is taken in Annexure-1)
		447	0.0500	35+210				Government	(Length is taken in Annexure-1)
		452	0.0100	33+500				Private	(Length is taken in Annexure-1)
16	Gola	207	0.2250	35+580				Private	(Length is taken in Annexure-1)
		205	0.1896	35+650				Private	(Length is taken in Annexure-1)
		256/209	0.0291	35+740				Private	(Length is taken in Annexure-1)
		213	0.1372	35+780				Private	(Length is taken in Annexure-1)
		217	0.0166	35+840				Private	(Length is taken in Annexure-1)
Total			11.5179			2465			

Total obstruction Length due to Land Award Approval pending (LHS):-

1.480 Km.

Total obstruction Length due to Land Award Approval pending (RHS):-

1.255 Km.

Total Obstruction Length (BHS)= [(LHS+RHS)/2]

1.368 Km.

The work has been executed upto Embankment, SG, GSB levels by giving assurance to farmers that LA compensation shall be disbursed very soon. Now They have stopped work asking compensation to be paid first & then taken up further work.

Additional award 3A & 3D pending (Jhalawar Section)										Annexure - 2	
Sr. No.	Village	Khasra No.	Chainage		Length (m)	Side	Total area	Effected area	Preacquired		Balance to be acquired
			From	To					1st	2nd	
1	Ralayata	289/607	43150	43340	190	RHS	1.675	0.6555	0.0001	0.1494	0.5060
		713/375	43750	43790	40	LHS	0.0506	0.0450	0.0264	-	0.0186
2	Jhalarpatan	55/2488	45400	45450	50	RHS	0.1644	0.1322	0.0736	0.0186	0.0400
		1980					0.0506	0.0506	0.0493	-	0.0113
3	Haripura	233/41	51580	51650	0	Centre	0.4301		0.3318	0.0136	0.0122
		317/30					0.2655	0.0029	-	-	0.0029
				Total	280					Total	0.5910
This area is to be added in the proposed additional 3A											
1	Jhalarpatan	1887	48380	48430	50	RHS					0.0520
2	Bhanwarsa	989/534	48450	48530	80	BHS		0.7100	0.4450		0.2650
					130					Total	0.3170

Total Area = 0.5910 + 0.3170 = 0.9080

Total Obstruction Length (LHS)= 0.120 Km.

Total Obstruction Length (RHS)= 0.370 Km.

Total Obstruction Length (BHS)= 0.245 Km. [(LHS+RHS)/2]

Tree Award Approved on date 22.06.2019. Disbursement in progress (Jhalawar Section)

Annexure - 3

Sr. No.	Chainage		Length	Side	Description	Remarks
	From	To				
1	36+500	36+600	100	BHS	Orange garden	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
2	36+700	36+750	50	LHS	Non Fruit Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
3	36+850	36+900	50	LHS	Non Fruit Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
4	36+950	36+975	25	LHS	Non Fruit Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
5	37+300	37+400	100	BHS	Non Fruit Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
6	37+900	38+050	150	BHS	Fruit Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
7	38+150	38+200	50	RHS	Non Fruit Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
8	38+300	38+500	200	BHS	Fruit Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
9	38+950	39+000	50	LHS	Fruit Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
10	39+200	39+250	50	RHS	Fruit Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
11	39+750	39+850	100	BHS	Fruitless Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
12	39+950	40+100	150	BHS	Fruitless Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
13	40+400	40+450	50	BHS	Fruitless Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
14	40+700	40+800	100	RHS	Fruitless Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
15	41+200	41+300	0	LHS	Highcourt Stay	Execution is stopped by Court (Length is taken in Annexure-1)
16	41+500	41+550	50	LHS	Fruitless Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019

Sr. No.	Chainage		Length	Side	Description	Remarks
	From	To				
17	41+550	41+710	160	RHS	Fruitless Tree	Tarmeem matter due to disbuesement pending
18	41+800	41+900	100	LHS	Fruitless Award pending	Execution work is continue but award approval is
19	41+920	42+000	80	BHS	Fruitless Award pending	Execution work is continue but award approval is
20	42+400	42+450	50	RHS	Fruitless Award pending	Due to SDM Court
21	44+750	44+800	50	RHS	Due to Fruitless Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
22	45+100	45+200	100	LHS	Fruitless & Fruitfill Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
23	45+600	45+700	100	BHS	Fruitless & Fruitfill Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
24	48+100	48+200	100	BHS	Fruit & Non Fruit Tree & Garden	Work is stopped due to Award pending
25	48+550	48+600	50	BHS	Non Fruit Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
26	49+300	49+400	100	LHS	Non Fruit Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
27	50+400	50+500	100	BHS	Fruit Non Fruit Tree	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
28	51+200	51+450	250	BHS	Award pending	Work is stopped
29	51+500	52+350	0	BHS	DLC matter	Work is stopped (Length is taken in Annexure-1)
30	54+250	54+400	150	BHS	Fruit & Non Fruit Tree award pending	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
31	54+500	55+300	800	BHS	Fruit & Non Fruit Tree award pending	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
32	55+500	55+600	100	RHS	Award pending from RO	Work is stopped
33	55+700	56+500	800	RHS	Orange Garden	Execution work is continue but award approval is pending from NHA1 since 11.01.2019
	Total		4365			

Total Obstruction Length (LHS)= 2.955 Km.

Total Obstruction Length (RHS)= 3.590 Km.

Total Obstruction Length (BHS)= 3.273 Km. [(LHS+RHS)/2]

The work has been executed upto Embankment, SG, GSB levels by giving assurance to farmers that LA compensation shall be disbused very soon. Now They have stopped work asking compensation to be paid first & then taken up further work.

