

National Highways Authority of India
(Ministry of Road Transport & Highways)



PATEL DARAH-JHALAWAR HIGHWAY PRIVATE LIMITED

CONSTRUCTION OF 4-LANE ROAD ON NH-12 (NEW NH-52) FROM Km. 299.000 TO Km. 346.540 (DESIGN CHAINAGE 9.860 TO 58.740) (DARAH – JHALAWAR – TEENDHAR) IN THE STATE OF RAJASTHAN UNDER NHDP PHASE-III ON HYBRID ANNUITY PROJECT.

INDEPENDENT ENGINEER

LEA ASSOCIATES SOUTH ASIA PVT. LTD

MONTHLY PROGRESS REPORT

For The Month of August-2020


Executive Summary

The old National Highway 12 runs through two big states Rajasthan and Madhya Pradesh. The total length of the old NH- 12 was 897/00 Km. The length of Old NH 12 was 408/700 Km in the state of Rajasthan. Recently MORTH has amended the number and length of the National highways. The old NH 12 in the state of Rajasthan has become the part of the New National highway 52. The New NH 52 starting from its junction with NH-7 near Sangrur in the state of Punjab connecting Narwana, Hisar in the state of Haryana, Fatehpur, Jaipur, Tonk, Kota, Aklera in the state of Rajasthan, Rajgarh, Biora, Dewas, Indore, Sendhwa in the state of Madhya Pradesh, Dhule, Aurangabad, bed, Osmanabad, Solapur in the state of Maharashtra, Bijapur, Hubli and terminating at its junction with NH-66 near Ankola in the state of Karnataka.

The Project stretch Darah-Teendharis connected to Jaipur at one end and it is connected to Bhopal at the other end. The project highway is very important highway as it connects the Capital of Rajasthan states and National capital of country through Jaipur- Delhi Highway.

The project highway is very important highway as it connects to two state Rajasthan and Madhya Pradesh. The Darah-Jhalawar-Teendhar section of National Highway has moderate traffic density. In addition to this there are few sections where alignment needs geometric improvements to maintain riding quality of highway and safe movement of vehicles. Apart from this the present alignment of NH is passing through various congested towns and villages. All of the above factors are demanding the existing 2-lane highway to be developed as 4-lane divided carriageway with bypass provisions in congested towns/ villages.

The Project Highway traverses through two districts viz. Kota and Jhalawar in Rajasthan State. The project study corridor starts at the end of ROB approach near to Darah at km 289+500 and passes through five major towns Darah, Sarvada, Dabadeh, Suket and Jhalawar, and it ends at Teendhar, Existing km 346.540 Km. Existing road width is 2 lane standard. The Existing ROW varies from 15 m to 30 m. The entire project length is under the administrative control of PIU Kota.



Project Synopsis


National Highways Authority of India plans to undertake the Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage From 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Mode (Length 48.880 Km.) – Package II.

The National Highways Authority of India (NHAI) is undertaking the up-gradation of NH-12 from Existing two lane road to four lane divided carriageway in state of Rajasthan.


The project involves up gradation of 48.88 Km from two-lane to the four-lane divided carriageway. It includes the construction of bridges, intersections, service roads, culverts and related infrastructure, and the installation of signaling systems and signboards. The project will be developed under National Highways Development Project (NHDP) Phase-III on Hybrid Annuity Mode.



Existing and Proposed alignment

SR. NO.	Existing Chainage (Km)		Length	Design Chainage (Km)		Design Length (Km)	Name of Revenue Village
	To	From		To	From		
1	299.000	299.340	0.340	9.860	10.200	0.340	KAMALPURA
2	299.340	299.740	0.400	10.200	10.600	0.400	KAMALPURA
3	299.740	300.140	0.400	10.600	11.000	0.400	KAMALPURA
4	300.140	300.440	0.300	11.000	11.300	0.300	KAMALPURA
5	300.440	300.778	0.338	11.300	11.638	0.338	KOOKARA KHURD
6	300.778	301.255	0.477	11.638	12.115	0.477	MANPURA
7	Dabadeh&Sahrawada Bypass			12.115	12.300	0.185	MANPURA
8				12.300	13.028	0.728	ZALIMPURA
9				13.028	14.200	1.172	SAHRAWADA
10				14.200	15.661	1.461	TELYA KHERI
11				15.661	17.242	1.581	ASKALI
12				17.242	19.273	2.031	HIRIYA KHERI
13				19.273	19.788	0.515	KHEEMACH
14	308.203	308.515	0.312	19.788	20.100	0.312	KHEEMACH
15	308.515	308.715	0.200	20.100	20.300	0.200	KHEEMACH
16	308.715	308.915	0.200	20.300	20.500	0.200	ATRALIYA
17	308.915	309.079	0.164	20.500	20.664	0.164	ATRALIYA
18	Atraliya Realignment			20.664	21.682	1.018	ATRALIYA
19	310.007	310.125		21.682	21.800	0.118	ATRALIYA
20	310.125	310.325		21.800	22.000	0.200	ATRALIYA
21	310.325	310.444		22.000	22.119	0.119	GORDHANPURA
22	Atraliya Realignment			22.119	22.464	0.345	GORDHANPURA & PAMA KHERI
23	310.789	311.125		22.464	22.800	0.336	PAMA KHERI




SR. NO.	Existing Chainage (Km)		Length	Design Chainage (Km)		Design Length (Km)	Name of Revenue Village
24	311.125	311.494		22.800	23.169	0.369	PAMA KHERI
25	311.494	311.625		23.169	23.300	0.131	PAMA KHERI
26	311.625	311.776		23.300	23.451	0.151	PAMA KHERI
27	311.776	312.025		23.451	23.700	0.249	PAMA KHERI
28	312.025	312.725		23.700	24.400	0.700	DEENGASI
29	312.725	312.925		24.400	24.600	0.200	DEENGASI
30	312.925	313.025		24.600	24.700	0.100	DEENGASI
31	313.025	313.125		24.700	24.800	0.100	DEENGASI
32	313.125	313.370		24.800	25.045	0.245	DEENGASI
33	313.370	313.535		25.045	25.210	0.165	DEENGASI
34				25.210	25.254	0.044	DEENGASI
35				25.254	26.124	0.870	UMMEDPURA
36				26.124	27.000	0.876	RAMPURIYA
37				27.000	27.358	0.358	SUKET
38				27.358	27.854	0.496	BEER MANDI
39				27.854	28.000	0.146	SUKET
40				28.000	29.571	1.571	ARANYA KHURD
41				29.571	31.212	1.641	SURERA
42				31.212	33.617	2.405	BANSYA HERI
43				33.617	35.565	1.948	ARANYA KALAN
44	Suket,			35.565	36.100	0.535	KALMANDI
45	Jhalawar&Jhalrapatan Bypass			36.100	38.000	1.900	HARISH PURA
46				38.000	38.537	0.537	RALAYTI
47				38.537	40.343	1.806	RALAYTA
48				40.343	41.784	1.441	JHALRAPATAN
49				41.784	44.224	2.440	MADHOPUR
50				44.224	49.800	5.576	HARIPURA
51				49.800	51.434	1.634	HARIPURA,
52				51.434	52.516	1.082	BANJARI &
53				52.516	54.200	1.684	BHANWARSA
54				54.200	54.565	0.365	BHANWARSA
55	342.895	343.673		54.565	55.343	0.778	BHANWARSA
56	343.673	347.127		55.343	58.740	3.397	BHANWARSA & ROOPAREL



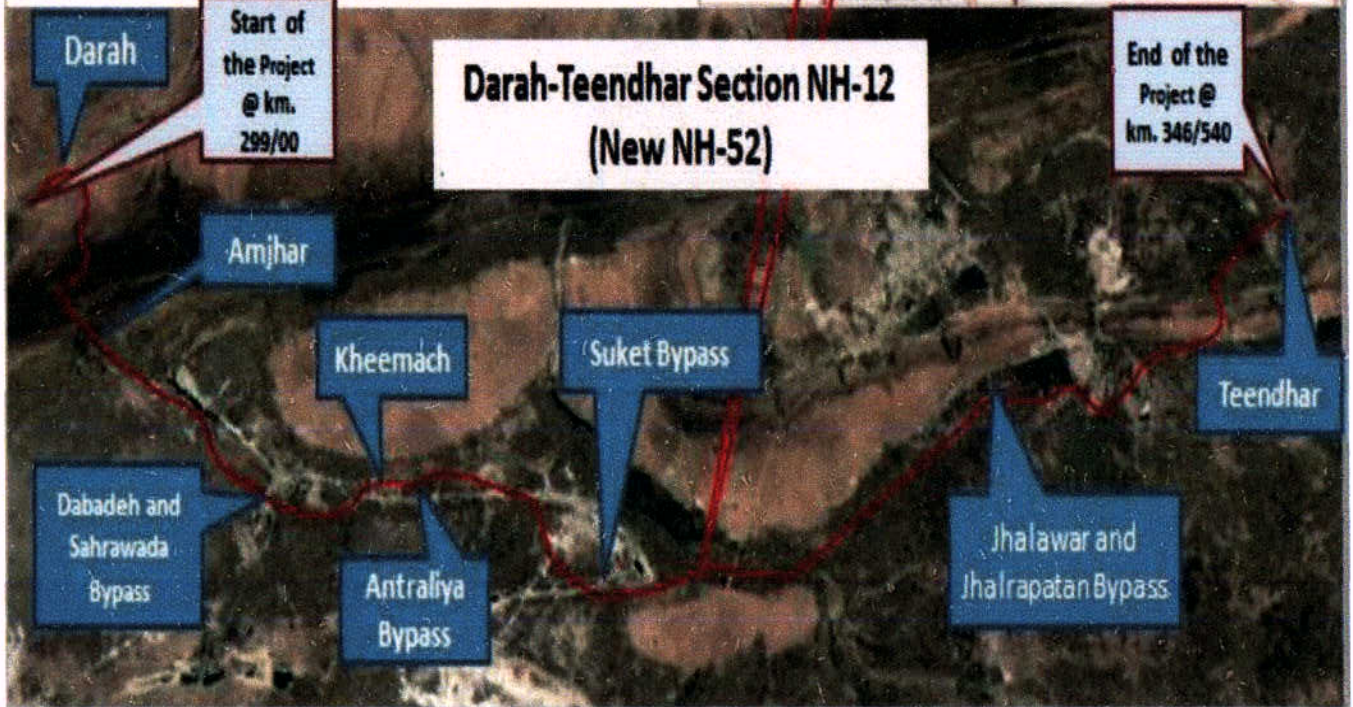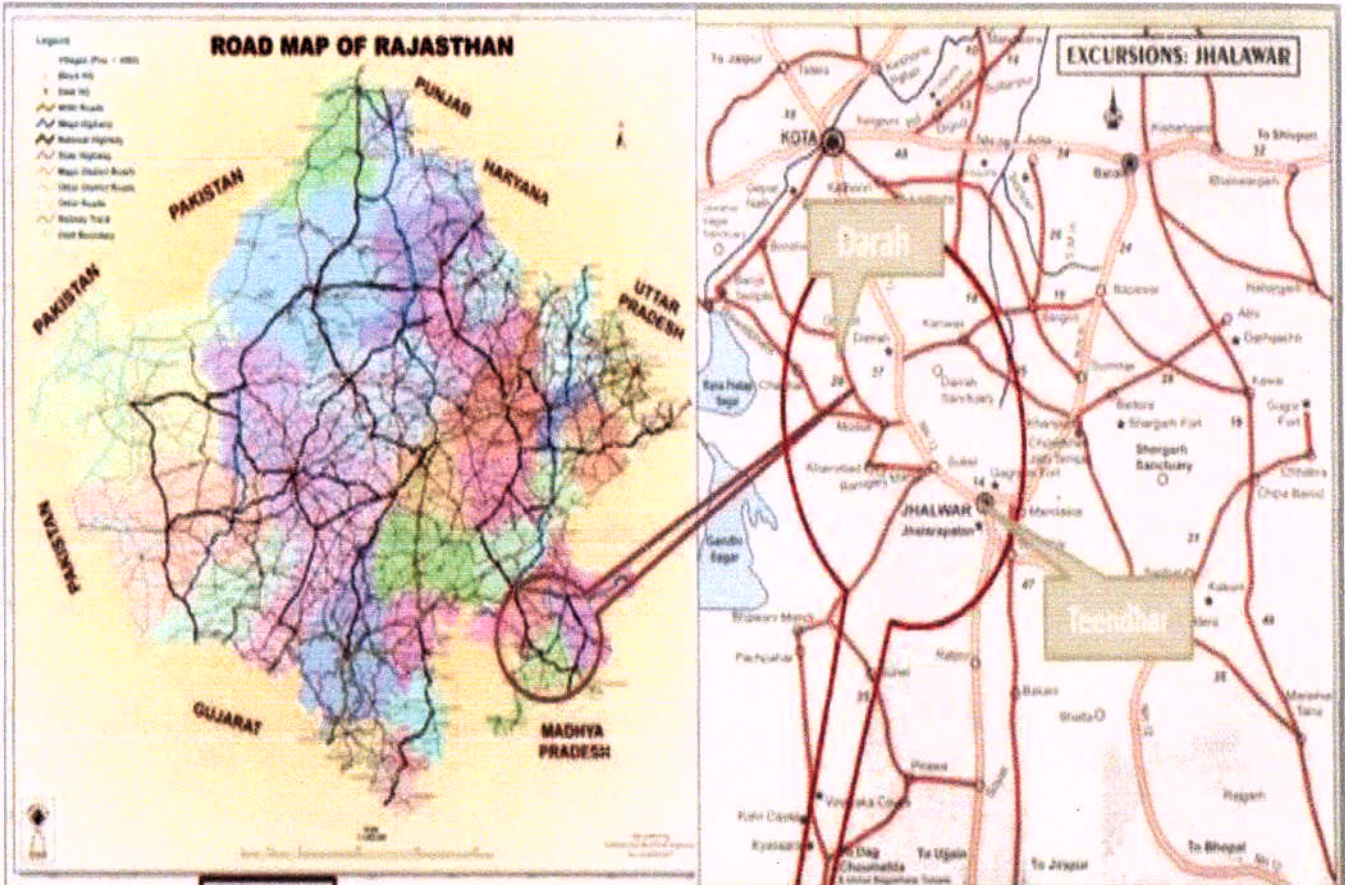

PROJECT SUMMARY


Project	Construction of 4-lane Road on NH-12 New NH-52 from Km 299.000 to 346.540 Design Chainage From 9.860 to 58.740 Darah-Jhalawar-TeendharSection in the State of Rajasthan under NHDP Phase-III Length 48.880 km Package II on Hybrid Annuity Mode.
Owner/Client	National Highways Authority of India
Concessionaire	Patel DarahJhalawar Highway Pvt. Ltd.
Independent Engineer	LEA ASSOCIATE SOUTH ASIA PVT. LTD
Project Length (In Km)	48.88 Km
Total Project Cost as per CA	1123.63 Cr.
Concession Period	15 Years
Construction Period	910 Days from the Appointed Date.
Contractual Completion Date	19 th November 2020.
Extended Completion Date	18 th July 2021.
Date of Signing of Concession Agreement	16 th November 2017
Appointed Date	24 th May 2018 (Letter ref. No. NHAI /19030/Dara-Teen/Raj/2016/1/120723 dated 09 th July 2018.



1.2 Project Overview

1.2.1 Structures

S. No.	Feature	Description
1	Major Bridge	02 Nos. – (13 x 25mtr) & (13 x 31.6mtr_3-Lane)
2	Elevated Flyover cum MJB	01 Nos. – (20 x 25mtr)
3	Flyovers/ Interchange	03 Nos. (1 Nos. – 4x25mtr.) (2 Nos. – 3 x 24mtr.)
4	ROB/ RUB	1/1 = 2 Nos.
5	Minor bridges	11 Nos. (01 no. deleted)
6	Vehicular underpass	09 Nos. – (1x24mtr)
7	Light Vehicular Underpasses	13 Nos.
8	Culverts (HP/BC/PUP) as per CA & Additional	37 Nos. (16 Nos. Pipe / 21 Nos. Box)+Additional (29 Nos Pipe, 3 nos Box and 02 Nos PUP) Total- 44 Nos Pipe and 23 nos Box Culvert
9	RE Wall	14.454 Km
10	Toll Plaza	1 No (16 Lanes)
11	Truck Lay Bys	1 (Both side)
12	Bus Shelter	5 Nos (Both side)
13	Rest Area	1no



Project Milestones

Project Milestone	Condition	Time Line	Date	Financial Progress
I	Commenced construction of Project and achieved 20% of Physical Progress	290 th Day from Appointed date	10 th March 2019	224.73 Cr.
II	Commenced construction of Project and achieved 35% of Physical Progress	430 th Day from Appointed date	28 th July 2019	393.27 Cr.
III	Commenced construction of all Project Facilities and achieved 75% of Physical Progress	690 th Day from Appointed date	13 th April 2020	842.72 Cr.
IV	Completion Of the Project	910 th Day from Appointed date	19 th Nov 2020	1123.63 Cr.

Payment Milestones

Project Milestone	Condition	Status
I	Commenced construction of Project and achieved 10% of Physical Progress	Achieved on 20 th Dec 2018
II	Commenced construction of Project and achieved 30% of Physical Progress	Achieved on 31 st August 2019
III	Commenced construction of all Project Facilities and achieved 50% of Physical Progress	Achieved on 21 st August 2020
IV	Commenced construction of all Project Facilities and achieved 75% of Physical Progress	
V	Commenced construction of all Project Facilities and achieved 90% of Physical Progress	



Progress Status as per submitted Programme

Sr. No	Item	Unit	Scope of work as per schedule - B	Planned upto Aug-2020	Progress Achieved upto July-2020	This Month Progress	Cumu in progress & Completed	Target for the month of Sept-2020	Remarks
Highway Progress (Km.)									
1	C & G	Km	46.25	46.08	46.08	0.00	46.08	0.00	
2	Embankment Top	Km	46.25	31.20	31.20	0.00	31.20	0.00	
3	Subgrade	Km	46.25	27.90	27.90	0.00	27.90	0.00	
4	G.S.B	Km	46.25	26.77	26.77	0.00	26.77	0.00	
5	D.L.C	Km	46.25	22.32	22.32	0.33	22.65	0.00	
6	P.Q.C	Km	46.25	19.50	19.50	0.00	19.50	0.00	
Structure Progress: (No.s)									
1	HPC	No	16+29=45	45	45	0	45	0	
2	BC	No	21+2=23	22	21.5	0	21.5	0.5	
3	PUP	No	2	0	0	0	0	0	
4	MNB Slab	No	22	19	19	0	19	1	
5	MJB Slab	No	39	4	3	0	3	2	
6	VUP Slab	No	18	11	8	0	8	1	
7	LVUP Slab	No	26	22	23	0	23	1	
8	Elevated Slab	No	40	31	32	3	35	2	
9	ROB Slab	No	6	0	0	0	0	0	
10	RUB Slab	No	2	0	0	0	0	0	
11	Flyover Slab	No	20	12	7	4	11	1	



1. Physical Progress Planned upto Aug -2020:- **54.35%**

(As per Revised programme Submitted on 20.06.2020)

2. Physical Progress achieved upto Aug -2020:- **51.10%**

3. Physical progress achieved in Month of Aug-2020:- **01.11%**

1.1 Summary of Progress

Summary of Progress (August 2020)

Highway Progress:

Sr. No.	Item	Unit	Scope of work	Completed / Work in progress	Balance work
1	C & G	Km	46.25	46.08	0.17
2	Embankment Top	Km	46.36	31.20	15.16
3	Sub- Grade	Km	46.36	27.90	18.46
4	GSB	Km	46.36	26.77	19.59
5	DLC (MC)	Km	46.36	22.65	24.04
6	PQC (MC)	Km	46.36	19.50	26.86
7	Embankment(SR)	Km	28.38	5.00	23.38
8	Sub- Grade(SR)	Km	28.38	4.50	23.88
9	GSB(SR)	Km	28.38	3.50	24.88
10	WMM (SR)	Km	28.38	3.50	24.88
11	DBM (SR)	Km	28.38	2.50	25.88
12	BC (SR)	Km	28.38	0.00	28.38



Structure Progress Status:-

Sl. No.	Structure Details:-	Unit	Scope	Completed	Work in progress	Balance	Remarks
1	Major Bridge	Nos	2	0	2	0	85% Achieved
2	Elevated Road	Nos	1	0	1	0	95% Achieved
3	Minor Bridge	Nos	11	9.5	0.5	0	1 no. deleted & 90% Completed
4	Box Culvert	Nos	23	22	1	0	2 nos. (Additional)
5	Pipe Culvert	Nos	45	44	1	0	29 No. (Additional)
6	Vehicular Underpass	Nos	9	4	5	0	80% Completed
7	Light Vehicular Underpass	Nos	13	12	0	1	80% Completed
8	Flyover	Nos	3	1.5	1.5	0	80% Completed
9	ROB	Nos	1	0	1	0	25% Achieved
10	RUB	Nos	1	0	1	0	20% Completed
11	Drain	Km	28.38	19	4.5	4.88	

1. Physical progress Achieved upto 31 Aug 2020- 51.10%
2. Financial Progress Achieved upto 31 Aug-2020- 56.76%(637.75 Crs)
(Financial S- Curve attached at the end)




Utility Shifting Progress

24-05-2018 is the Appointed Date for the project. 85% of the land measuring to Km 41.548 has been handed over by the Authority. As on date 99.40% is available and 0.06% (0.300 mtrs) of land is balance due to presence of structures, religious structure and other land related issues.


1. Permission for cutting of trees on Government land and forestland received. Cutting of trees in progress. Ref. no 1594 dated 03 / 05 / 2018 (Jhalawar) & 1837-44 dated 22/05/2018(Kota)
2. Electrical Utilities estimate approved in both district Kota & Jhalawar vide letter 41010 & 41011 1/2016- Kota / US – Electric- Kota and Jhalawar / Package-2/7077 dated 24th August 2018. Work for shifting of electrical utilities under progress. Work is balance in existing alignment due to presence of structure.
3. Water Pipelines Estimate is approved vide letter no. _41024 / 1 / 2016- Kota/ US - PHED- Kota / Pkg-II/ 6998 dated 16-08 2018 and 41025 / _1 / 2016- Kota / US /6997 dated 16-08-2018 Shifting work in progress. Work balance only in stretches having LA related issues.
4. Estimate of HT Lines is approved. Material received at site for execution. Survey done with department for finalizing locations of new tower. Compensation for land acquisition for HT Lines tower is in progress.

Details of numbers and length are as below: -

Sr. No.	Particulars	Total	Progress till last month	Current month	Cumulative Progress till Aug-20	Balance to be completed	Remarks
1	Electric Poles						
	Kota Section	600	592	0	592	8	Balance in kukdakhurd at CH.11+100 to 11+400 LHS, No. 04 & Dingsi at CH.24+610 to 25+000 LHS, no. 04
	Jhalawar Section	141	141	0	141	0	
	Total	741	733	0	733	8	
2	Structures (Nos.)						
	Kota Section	403	347	0	347	56	Balance in Kukdakhurd at Ch. No 11+100 to 11+700 LHS & Dingsi at Ch no. 24+610 to 24+940 LHS
	Jhalawar Section	159	158	0	158	1	CH.58+127 LHS



Sr. No.	Particulars	Total	Progress till last month	Current month	Cumulative Progress till Aug-20	Balance to be completed	Remarks
	Total	562	505	0	505	57	
3	Religious Strs (Nos.)						
	Kota Section	13	9	0	9	4	04 Nos construction inprogress at Ch. No. 09+860 RHS, 11+300 LHS, 24+600 RHS, 24+740 LHS
	Jhalawar Section	2	2	0	2	0	
	Total	15	11	0	11	4	
4	Water Utilities (km)						
	Kota Section	9.875	9.05	0	9.05	0.825	Balance in Kukdakhurd at Ch. No 11+200 to 11+690 LHS & Dingsi at Ch no. 24+610 to 24+945 LHS
	Jhalawar Section	11.125	11.125	0	11.125	0	
	Total	21	20.175	0	20.175	0.825	
5	High Tension Line						
Sr. No.	Chainage No.	Foundation		Tower Erection		String	
		LHS	RHS	LHS	RHS	LHS	RHS
1	23+100	Completed	Completed	Yet to Start	Yet to Start	Yet to Start	Yet to Start
2	27+085	Completed	Completed	Yet to Start	Yet to Start	Yet to Start	Yet to Start
3	30+800	Completed	Completed	Yet to Start	Yet to Start	Yet to Start	Yet to Start
4	41+875	Completed	Completed	Yet to Start	Yet to Start	Yet to Start	Yet to Start
5	42+075	Completed	Inprogress	Yet to Start	Yet to Start	Yet to Start	Yet to Start
6	57+075	Completed	Completed	Yet to Start	Yet to Start	Yet to Start	Yet to Start
7	33+710	Estimate charges paid by NHAI to PRVPL, Estimate are awaited					
8	42+950	Estimate charges paid by NHAI to PRVPL, Estimate are awaited					



Tree Cutting Status:-


S. No.	District	Category		Nos.	Status			Trees Cut	Balance to be cut	Remarks
					Cutting Permission	Approval Letter No.	Date			
1	Kota	Govt Trees	All	465	Yes	Revenue-III/2018/1837-44	22.05.2018	402	63	
		Private Trees	Fruit	2797	Yes	No.41002/2016-kota/L.A/Ramganjmandi/pkg-2/6243	17.04.2018	2797	0	Disbursement in progress
			Fruitless	1280	Yes			1235	45	
2	Jhalawar	Govt Trees	All	972	Yes	Revenue/18/1594,1861& 2868	03.05.2018, 25.05.2018& 06.11.2018	972	0	429 tree cutting approval vide letter no. 2868 dated 06.11.2018
		Private Trees	Fruit	1836	Yes	No.41003/2016-kota/L.A/Jhalawar/pkg-2/6242	17.04.2018	1738	98	Award finalized
			Fruitless	702	Yes			677	25	Disbursement in progress
		Forest		104	yes	F-14()2017/Jhalawar Road/FCA/1998	19.04.2018	104	0	
3	TOTAL			8156				7925	231	97%

1) Total No. of trees increased from 7727 to 8156 Nos. because of 429 trees along existing alignment added between Km.54.000 to 58.740. These trees have been cut.




Status of Conditions precedent

a	Provided Performance Security to the Authority	Released on 26.08.2019
b	Executed and procured execution of Escrow Agreement	Submitted. Vide this office letter no. PDJHPL / NHAI / FC / 039 .2018 Dt. 21-05-2018.
c	Executed and procured execution of Substitution Agreement	Submitted. Vide this office letter no. PDJHPL / NHAI / FC / 039 .2018 Dt. 21-05-2018.
d	Procure all Applicable Permits as per Schedule -E	Obtained
e	Executed Financing Agreements and delivered 3 copies duly attested by Director of the Concessionaire	Submitted. Vide this office letter no. PDJHPL / NHAI / FC / 039 .2018 Dt. 21-05-2018
f	Delivered to Authority 3 true copies of Financial Package and Financial Model duly attested by Director of the Concessionaire	Submitted. Vide this office letter no. PDJHPL / NHAI / FC / 039 .2018 Dt. 21-05-2018.
g	Delivered to Authority from Selected Bidder its respective confirmation in original of the correctness of their representations and warranties set forth in Sub Clause (k), (l) and (m) of Clause 7.1 of CA	Submitted
h	Environment Clearance	Done
i	Forest Land Clearance	Stage –II Clearance obtained
j	Wild Life Clearance	NA



Status of Railway Approvals

Proposal Description	Status	Length Impacted	Current Stage	Issues/ Comments
Rail ROB (Ch.44+158)	GAD of ROB Approved	-	Detailed design and drawing Approved by Railways.	Substructure Work in Progress.
RUB (Ch.33+585)	GAD of RUB Approved	-	Detailed design and drawing Approved by Railways. Work permission received on date 02.12.2019	Construction of Box in Progress



ISSUES OF CONCERN: -

1. (a) DLC issue from Km-

- **CH: 32+500 to 36+000:** Land payment disbursed. Payment for trees, Boundary wall is pending. Survey done in Nov-2019.
- **CH: 51+700 to 52+100:** Land payment disbursed. Payment for trees, Boundary wall is pending. Survey done in Nov-2019.

(b) Court Case Chainages : Possession of following chainages is balance because of pending cases in SDM court.


Sr no.	Chainage		Length (M)
	From	To	
1	11+100	11+700	600
2	41+200	41+300	100
	Total		700

1. Disbursement for structures in both the districts Kota & Jhalawar is under progress. Structures in Jhalawar district have been removed. The process of payment in Kota district is very slow. Structures are pending in Kamalpura, Kukda khurd & Dhingsi village. Because of non-removal of these hindrances the progress of electrical and water line shifting is affected, continuity of work fronts cannot be maintained. After disbursement of payment, it will take at-least 4-5 months for physical removal of these hindrance and shifting of utilities. The progress of L.A disbursement in Ramganjmandi (Kota district) is very poor and needs to be expedited in order to maintain the continuity of work fronts. Discontinuity of work stretches is having a direct impact on progress of work.
2. Approval of estimate for shifting of HT crossing done. Material procured at site. Survey related to crop compensation is completed by concerned authorities. Award approval is awaited from NHAI. The excavation & foundation work of HT lines has been started. And 05 nos. of foundation work for HT lines are completed out of 06 nos. & 01 no. in progress. The locations where foundation work of HT lines completed are Km. 23+100, Km. 27+085, Km. 30+800, Km. 41+875, Km. 57+830.
3. 3A of missing plots in Jhalawar district is pending, though work has been taken up in the affected stretches.
4. Disbursement of payment of religious structure within PROW is yet to be done (Jhalawar District).
5. **Award of left over structures / trees is pending for payment in Ramganjmandi tehsil (Kota District) & Jhalawar District.**
6. The details of hindrances is attached as **Annexure-I**.



QUALITY ASSURANCE & LAB MONTHLY PROGRESS REPORT
MONTH OF August-2020

Sr. No.	Name of Test	Number of Tests Conducted									Remarks
		Up To Previous Month			This Month			Total upto Date			
		Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test	
OGL & Cutting soil											
1	Free Swell Index	317	0	317	0	0	0	317	0	317	
2	Grain Size Analysis	317	0	317	0	0	0	317	0	317	
3	Plasticity Index	317	0	317	0	0	0	317	0	317	
4	Max. Dry Density	317	0	317	0	0	0	317	0	317	
5	CBR	6	0	6	0	0	0	6	0	6	
6	Density of Comp.Layer	6361	143	6504	40	0	40	6401	143	6544	
7	Moisture Cont.	0	0	0	0	0	0	0	0	0	
Borrow Area (Embankment & Subgrade)											
1	Free Swell Index	1922	42	1964	10	0	10	1932	42	1974	
2	Grain Size Analysis	1922	42	1964	10	0	10	1932	42	1974	
3	Plasticity Index	1922	42	1964	10	0	10	1932	42	1974	
4	Max. Dry Density	1941	42	1983	10	0	10	1951	42	1993	
5	CBR	421	28	449	5	0	5	426	28	454	
Earthwork Field test											
1	Density of Comp.Layer (Emb.)	58035	443	58478	620	0	620	58655	443	59098	
2	Density of Comp.Layer (Sub grade & Earthen shoulder)	8897	88	8985	120	0	120	9017	88	9105	
GSB											
1	Sieve Analysis	344	0	344	19	0	19	363	0	363	
2	Plasticity Index	341	0	341	19	0	19	360	0	360	
3	Max. Dry Density	4	0	4	0	0	0	4	0	4	
4	CBR	2	0	2	0	0	0	2	0	2	
5	Water Absorption	2	0	2	0	0	0	2	0	2	
6	AIV	3	0	3	0	0	0	3	0	3	
7	Density of Comp.Layer	1146	23	1169	68	0	68	1214	23	1237	



Sr. No.	Name of Test	Number of Tests Conducted									Remarks
		Up To Previous Month			This Month			Total upto Date			
		Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test	
WMM											
1	Sieve Analysis	23	0	23	5	0	5	28	0	28	
2	Plasticity Index	23	0	23	5	0	5	28	0	28	
3	Aggregate Impact Value	21	0	21	5	0	5	26	0	26	
4	Combined F.I & E.I.	21	0	21	5	0	5	26	0	26	
5	Max. Dry Density	0	0	0	0	0	0	0	0	0	
6	Density of Comp.Layer	67	0	67	6	0	6	73	0	73	
7	Water Absorption	0	0	0	0	0	0	0	0	0	
8	Soundness Test	0	0	0	0	0	0	0	0	0	
DBM											
1	Aggregate Impact Value	15	0	15	1	0	1	16	0	16	
2	Flakiness & Elongation	14	0	14	1	0	1	15	0	15	
3	Mix Grading	25	0	25	1	0	1	26	0	26	
4	Individual Grading	15	0	15	1	0	1	16	0	16	
5	Stability of Mix	38	0	38	1	0	1	39	0	39	
6	Binder Content & Grading Mix	26	0	26	1	0	1	27	0	27	
7	Density of Compacted layer	14	0	14	0	0	0	14	0	14	
8	Gmm Test	14	0	14	0	0	0	14	0	14	
PHYSICAL PROPERTIES OF AGGREGATE FOR CONCRETE											
1	Sieve Analysis of CA	1259	0	1259	57	0	57	1316	0	1316	
2	Sieve Analysis of FA	1206	0	1206	57	0	57	1263	0	1263	
3	Sieve Analysis of DLC	171	0	171	5	0	5	176	0	176	
4	Sieve Analysis of PQC	197	0	197	15	0	15	212	0	212	
5	Aggregate Impact Value	1348	0	1348	77	0	77	1425	0	1425	
6	Flakiness Index	1348	0	1348	77	0	77	1425	0	1425	
7	Silt Content	309	0	309	0	0	0	309	0	309	
8	Specific Gravity & WA	17	0	17	0	0	0	17	0	17	



Sr. No.	Name of Test	Number of Tests Conducted									Remarks
		Up To Previous Month			This Month			Total upto Date			
		Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test	
Concrete Mix Design (cube sets)											
1	M15 7 Days	40	0	40	0	0	0	40	0	40	
	28 Days	68	0	68	0	0	0	68	0	68	
2	M20 Kerb 7 Days	19	0	19	0	0	0	19	0	19	
	28 Days	26	0	26	0	0	0	26	0	26	
	M20 7 Days	12	0	12	0	0	0	12	0	12	
	28 Days	18	0	18	0	0	0	18	0	18	
3	M25 7 Days	67	0	67	0	0	0	67	0	67	
	28 Days	108	0	108	0	0	0	108	0	108	
4	M30 7 Days	68	0	68	0	0	0	68	0	68	
	28 Days	12	0	12	0	0	0	12	0	12	
5	M35 7 Days	141	0	141	0	0	0	141	0	141	
	28 Days	237	0	237	0	0	0	237	0	237	
6	M35 Pile 7 Days	72	0	72	0	0	0	72	0	72	
	28 Days	142	0	142	0	0	0	142	0	142	
7	M35 RE block 7 Days	45	0	45	0	0	0	45	0	45	
	28 Days	144	0	144	0	0	0	144	0	144	
8	M40 7 Days	75	0	75	0	0	0	75	0	75	
	28 Days	115	0	115	0	0	0	115	0	115	
9	M45 7 Days	59	0	59	0	0	0	59	0	59	
	28 Days	113	0	113	0	0	0	113	0	113	
10	M50 7 Days	0	0	0	0	0	0	0	0	0	
	28 Days	2	0	2	0	0	0	2	0	2	
11	M40 PQC 7 Days	152	0	152	0	0	0	152	0	152	
	28 Days	234	0	234	0	0	0	234	0	234	
12	M40 PQC Fl. Strength 7 Days	111	0	111	0	0	0	111	0	111	
	28 Days	132	0	132	0	0	0	132	0	132	
13	DLC 7 Days	101	0	101	0	0	0	101	0	101	



Sr. No.	Name of Test	Number of Tests Conducted									Remarks
		Up To Previous Month			This Month			Total upto Date			
		Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test	
14	Grouting	6	0	6	0	0	0	6	0	6	
Field Concrete (cube sets)											
1	M15 7 Days	1961	0	1961	30	0	30	1991	0	1991	
	28 Days	3008	0	3008	150	0	150	3158	0	3158	
2	M20 Kerb 7 Days	123	0	123	12	0	12	135	0	135	
	28 Days	197	0	197	21	0	21	218	0	218	
3	M25 7 Days	2860	0	2860	36	0	36	2896	0	2896	
	28 Days	3845	0	3845	155	0	155	4000	0	4000	
4	M30 7 Days	304	0	304	18	0	18	322	0	322	
	28 Days	590	0	590	55	0	55	645	0	645	
5	M35 7 Days	3349	0	3349	88	0	88	3437	0	3437	
	28 Days	8124	0	8124	296	0	296	8420	0	8420	
6	M35 Pile 7 Days	143	0	143	1	0	1	144	0	144	
	28 Days	243	0	243	8	0	8	251	0	251	
7	M35 RE block 7 Days	898	0	898	20	0	20	918	0	918	
	28 Days	2696	0	2696	35	0	35	2731	0	2731	
8	M40 7 Days	383	0	383	53	0	53	436	0	436	
	28 Days	570	0	570	230	0	230	800	0	800	
9	M45 7 Days	107	0	107	13	0	13	120	0	120	
	28 Days	281	0	281	21	0	21	302	0	302	
10	M50 7 Days	0	0	0	0	0	0	0	0	0	
	28 Days	0	0	0	0	0	0	0	0	0	
11	M40 PQC 7 Days	500	0	500	73	0	73	573	0	573	
	28 Days	430	0	430	47	0	47	477	0	477	
12	M40 PQC Flexural Strength 7 Days	518	0	518	73	0	73	591	0	591	
	28 Days	448	0	448	47	0	47	495	0	495	




Sr. No.	Name of Test	Number of Tests Conducted									Remarks
		Up To Previous Month			This Month			Total upto Date			
		Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test	
13	DLC 7 Days	409	0	409	35	0	35	444	0	444	
14	DLC FDD	799	0	799	10	0	10	809	0	809	
Cement											
1	Fineness	145	0	145	6	0	6	151	0	151	
2	Consistency	145	0	145	6	0	6	151	0	151	
3	Setting Time	145	0	145	6	0	6	151	0	151	
4	Soundness	125	0	125	6	0	6	131	0	131	
5	Compressive Strength										
	a) 3 Days	252	0	252	7	0	7	259	0	259	
	b) 7 Days	250	0	250	6	0	6	256	0	256	
	c) 28 Days	252	0	252	6	0	6	258	0	258	



EATHER REPORT (Month of August-2020)

No.	Date	Temperature C°		Humidity %		Rainfall (mm)	Climate
		Min. Temp. (°C)	Max. Temp. (°C)	Min.	Max.		
1	01-08-20	26.6	32.0	61.0	85.0	0.0	Clear
2	02-08-20	26.1	30.9	65.0	86.0	0.0	Clear
3	03-08-20	26.2	30.5	68.0	85.0	0.0	Clear
4	04-08-20	28.3	34.1	47.0	86.0	0.0	Rain at site
5	05-08-20	25.2	34.4	59.0	87.0	8.5	Cloudy/Rain
6	06-08-20	24.2	38.1	70.0	87.0	1.0	Cloudy/Rain
7	07-08-20	23.7	41.2	60.0	89.0	1.5	Cloudy/Rain
8	08-08-20	24.5	32.8	64.0	87.0	0.0	Cloudy
9	09-08-20	24.9	40.9	58.0	97.0	4.0	Cloudy/Rain
10	10-08-20	23.8	36.3	69.0	95.0	12.0	Cloudy/Rain
11	11-08-20	24.1	30.5	70.0	98.0	11.0	Cloudy/Rain
12	12-08-20	24.3	32.5	84.0	98.0	16.2	Cloudy/Rain
13	13-08-20	22.9	32.4	82.0	97.0	51.0	Cloudy/Rain
14	14-08-20	23.5	36.9	84.0	96.0	32.6	Cloudy/Rain
15	15-08-20	24.0	34.1	82.0	93.0	0.0	Cloudy
16	16-08-20	24.7	38.4	75.0	92.0	0.0	Cloudy
17	17-08-20	24.7	40.5	76.0	93.0	3.0	Cloudy/Rain
18	18-08-20	23.8	34.6	81.0	95.0	13.4	Cloudy/Rain
19	19-08-20	23.4	30.2	81.0	95.0	5.6	Cloudy/Rain
20	20-08-20	24.8	38.4	74.0	91.0	0.0	Cloudy
21	21-08-20	24.7	40.5	62.0	89.0	13.5	Cloudy/Rain
22	22-08-20	22.8	37.6	72.0	96.0	85.0	Cloudy/Rain
23	23-08-20	22.4	27.4	92.0	97.0	5.2	Cloudy/Rain
24	24-08-20	21.9	31.3	85.0	96.0	7.0	Cloudy/Rain
25	25-08-20	22.6	34.9	79.0	94.0	0.0	Cloudy

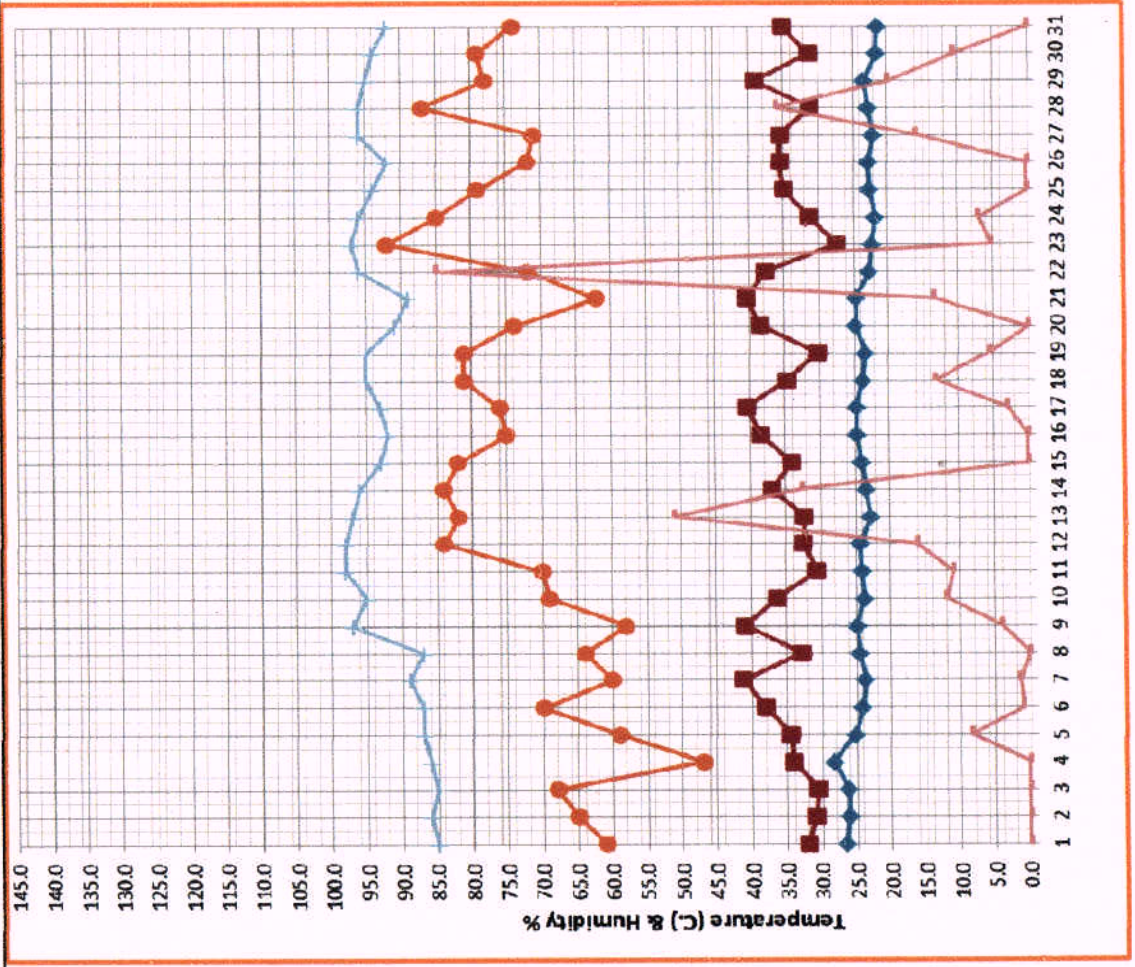


26	26-08-20	22.9	35.5	72.0	92.0	0.0	Cloudy
27	27-08-20	22.2	35.5	71.0	96.0	16.0	Cloudy/Rain
28	28-08-20	22.9	31.1	87.0	96.0	36.0	Cloudy/Rain
29	29-08-20	23.4	39.1	78.0	95.0	20.0	Cloudy/Rain
30	30-08-20	21.6	31.4	79.0	94.0	10.6	Cloudy/Rain
31	31-08-20	21.5	35.1	74.0	92.0	0.0	Sunny/Cloudy




Status of Design Mixed and source approval


Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
1	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	Submission of Mix Design	LASA/Concessionaire/D J/IE/2018/0003	21.08.2018
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-15(PCC Work) with flyash		
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-25(RCC Work) with flyash		
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-30(RCC Work) with flyash		
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-35(RCC Work) with flyash		
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-35(Pile Work with flyash		
2	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	Submission of Mix Design of Concrete from Ultratech&Mangalam Cement	LASA/Concessionaire/D J/IE/2018/0003	21.08.2018
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-35 RE Block (Ultratech&Mangalam cement)		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-35 with flyash RE Block (Ultratech&Mangalam cement)		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-15 PCC		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-25 RCC		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-30 RCC		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-35 RCC		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-35 Pile work		
3	PIL/CAMP/DJT/NHAI/2018-04/08	26.04.2018	Submission of Company profile & credential for the D.P. Wires	LASA/Concessionaire/D arah- Jhalawar/IE/2018/191	08.12.2018
4	PIL/CAMP/DJT/NHAI/2018-04/09	26.04.2018	Submission of Company profile & credential for the Shyam, Electrosteel and Premier Steel		
5	PDJHPL/NHAI/DJT/2018/019	12.03.2018	Submission of Company profile & credential for the Rashtriyaspat Nigam ltd (Vizag Steel),Nilkanth Steel Pvt.ltd. ,Steel authority of India limited (SAIL) ,Jindal steel & power limited ,Rashmi group ,Madhav Alloys Pvt.limited	LASA/Concessionaire/D J/IE/2018/17 and 58, 59 (10.09.2018)	30.08.2018
7	PIL/CAMP/DJP/N HAI/2018 -04 / 063	21.06.2018	Submission of construction material for testing.		
8	PIL/CAMP/DJP/N HAI/2018 -04 / 063	21.06.2018	Steel Dia 20mm JSW Steel (Fe-5.50D)		
10	PIL/CAMP/DJP/N HAI/2018 -04 / 063	21.06.2018	Steel - Dia 12,25 & 32mm SAIL (Fe-500D)		
10	PDJHPL/NHAI/DJT/2018/013	26.02.2018	Submission of Company profile & credential for the Birla Corporation Limited ,Mangalam Cement Limited , Wonder cement Limited . Ultrtech cement Limited ,Vadraj cement . Shree cement Limited	LASA/Concessionaire/D J/IE/2018/14	28.08.2018
11	PIL/CAMP/DJT/NHAI/2018-04/01	26.04.2018	Submission of Company profile & credential for the BASF India Ltd.for Admixture,Grout and joint Sealant , Unirock Chemicals (Admixture) , Tikitar Ltd. For Joint Sealant	LASA/Concessionaire/D J/IE/2018/016	30.08.2018



Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
PDJHPL/NHAI/DJT/2018/020	22.03.2018	Submission of Company profile & credential for Admixture and curing compound ,Kunalconchempvt.ltd.,Grout and joint Sealant ,STPLimited&Chembond Chemicals Ltd.		
PIL/CAMP/DJP/N HAI/2018 -04 /063	21.06.2018	Admixture - PC 100R (KunalIndustries)		
PDJHPL/PIU/CLO-179/2018/095	04.07.2018	DLC Flyash		
PDJHPL/PIU/CLO-179/2018/095	04.07.2018	DLC without Flyash		
PIL/CAMP/DJP/N HAI/2018 -04 /063	21.06.2018	GSB (Julmi PIL Crusher)		
PIL/CAMP/DJT/NHAI/2018-04/06	26.04.2018	Submission of Company profile & credential for the IOCL (Bitumen) ,HPCL (Bitumen) ,ESSAR (Bitumen) , GP global (Emulsions) , HINCOL (Emulsions) Total oil India pvt ltd. (Emulsions)	LASA/Concessionaire/D J/IE/2018/020 Bitumen& 19 for Emulsion	31.08.208
PIL/CAMP/DJT/NHAI/2018-04/02	26.04.2018	Submission of Company profile & credential for the SGG spun pipes	LASA/Cocessionaire/Darah- Jhalawar/IE/2018/050	07.09.2018
PIL/CAMP/DJT/NHAI/2018-04/03	26.04.2018	Submission of Company profile & credential for the TIKIDAN Danosa India	LASA/Concessionaire/Darah- Jhalawar/IE/2018/212	14.12.2018
PIL/CAMP/DJT/NHAI/2018-04/04	26.04.2018	Submission of Company profile & credential for the KANTAFLEX India Pvt.ltd. (Elastomeric & Pot bearing)	LASA/Concessionaire/Darah- Jhalawar/IE/2018/206	13.12.2018
PIL/CAMP/DJT/NHAI/2018-04/05	26.04.2018	Submission of Company profile & credential for the Dynamic Prestress (I) Pvt Ltd.	LASA/Concessionaire/Darah- Jhalawar/IE/2018/195	08.12.2018
PIL/CAMP/DJT/NHAI/2018-04/07	26.04.2018	Submission of Company profile & credential for the Amitek Infra (Thermoplastic Road Marking Paint)	LASA/Concessionaire/D J/IE/2018/018	30.08.2018
PDJHPL/NHAI/DJT/2018/021	22.03.2018	Submission of Company profile & credential for the Nakoda spun pipes		
PDJHPL/NHAI/DJT/2018/022	22.03.2018	Submission of Laboratory profile & credentials for the Star wire INDIA Pvt., Third party, Hind Heat		
PDJHPL/PIU/CLO-179/2018/047	21.06.2018	Submission of Gompany Profile &Gredential for source approval of Hercules Bridge Bearings & Bridge Expansion Joints	LASA/Concessionaire/Darah- Jhalawar/IE/2018/003	21.08.2018
PDJHPL/PIU/CLO-179/2018/096	04.07.2018	Submission of Company Profile &Gredential for Arihant Prefab	LASA/Concessionaire/Darah- Jhalawar/IE/2018/052	07.09.2018
PDJHPL/PIU/CLO-179/2018/100	05.07.2018	Submission of Gompany profile &Gredeniari for M.E. Testing Laboratory	LASA/Concessionaire/Darah- Jhalawar/IE/2018/178	04.12.2018
PDJHPL/PIU/CLO-179/2018/101	05.07.2018	Submission of Company Profile & Credential for MarutiBitumin Pvt. Ltd	LASA/Concessionaire/Darah- Jhalawar/IE/2018/054	07.09.2018
PDJHPL/PRJ/TEC/CLO-179/2018/022	02.06.2018	Submission of profite,Credentials& Basic design report on RE walls	LASA/Concessionaire/Darah- Jhalawar/IE/2018/055	07.09.2018
PDJHPL/PIU/D/2018/032	16.04.2018	Submission of Quality assurance Plan		
PDJHPL/PIU/CLO-179/2018/043	13.06.2018	Submission of Mix Design of Granular Sub-Base	LASA/Concessionaire/Darah- Jhalawar/IE/2018/155	28.11.2018
PDJHPL/PIU/CLO-179/2018/044	13.06.2018	Submission of Summary of OGL test results		
PDJHPL/PIU/CLO-179/2018/045	13.06.2018	Submission of Galibration Certificate of Batching Plant & Lab Equipments		
PDJHPL/PIU/CLO-179/2018/046	13.06.2018	Submission of Third party test reports of the material related to the project		



Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
36	PDJHPL/PIU/CLO-179/2018/056	18.06.2018	Submission of Petrographic Test Report of Coarse Aggregate		
37	PDJHPL/PIU/CLO-179/2018/108	06.07.2018	Submission of Borrow Area - 1,3,6,7,9,10,11,12,14,15,17,18,20,21,22, 23,24,26,27,29,30,31,32,33,34 & 35		
38	PDJHPL/PIU/CLO-179/2018/110	07.07.2018	Submission of Company Profile & Credential for Earthcon Systems Pvt. Ltd	LASA/Concessionaire/D arah- Jhalawar/IE/2018/049	06.09.2018
39	PDJHPL/PIU/CLO-179/2018/111	07.07.2018	Submission of Construction Design (Geogrid Reinforced Soil Wall)	LASA/Concessionaire/D arah- Jhalawar/IE/2018/063	15.09.2018
40	PDJHPL/PIU/CLO-179/2018/122	10.07.2018	Testing for C & O Value of soil samples of Borrow area No. 1 & 22		
41	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	Submission of Mix-Design	LASA/Concessionaire/D arah- Jhalawar/IE/2018/003	21.08.2018
42	PDJHPL/PIU/CLO-179/2018/133	16.07.2018	Submission of Trial Patch Report of GSB & DLC		
43	PDJHPL/IE/ICO-181/2018/241	28.08.2018	Submission of Company Profile & Credential OF Maruti Rub Plast Pvt. Ltd.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/088	15/10/2018
44	PDJHPL/IE/ICO-181/2018/242	28.08.2018	Submission of Company Profile & Credential Of Tar Products Pvt. Ltd.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/053	07/09/2018
45	PDJHPL/NHAI/DJT/013/2018	28.08.2018	Submission of Company Profile & Credentials for Birla Corporation, Mangalam Cement, Wonder Cement, Ultratech Cement, Vadraj Cement & Shree Cement.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/014	28/08/2018
46	PDJHPL/IE/ICO-181/2018/260	07.09.2018	Submission of Company Profile & Credential Of Sanfield (India) Ltd.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/072	28/09/2018
47	PDJHPL/IE/ICO-181/2018/286	18.09.2018	Submission of Company Profile & Credential for RAMA TMT Bars	LASA/Concessionaire/D arah- Jhalawar/IE/2018/074	28/09/2018
48	PDJHPL/IE/ICO-181/2018/287	18.09.2018	Submission of Company Profile & Credential for SHYAM Steel	LASA/Concessionaire/D arah- Jhalawar/IE/2018/073	28/09/2018
49	PDJHPL/IE/ICO-181/2018/318	29.09.2018	Submission of Company Profile & Credential of Sanfield (India) Ltd.-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/078	03.10.2018
50	PDJHPL/IE/ICO-181/2018/348	09.10.2018	Submission of Company Profile & Credentials of Katalinepaints.-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/091	15/10/2018
51	PDJHPL/IE/ICO-181/2018/353	10.10.2018	Submission of Third party testing of RE wall concrete block in km. 23+600-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/130	13.11.2018
52	PDJHPL/IE/ICO-181/2018/362	12.10.2018	Submission of Company Profile & Credentials of PNT designs Pvt. Ltd.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/126	13.11.2018
53	PDJHPL/IE/ICO-181/2018/367	13.10.2018	Submission of GSB Mix design for approvals	LASA/Concessionaire/D arah- Jhalawar/IE/2018/111	29/10/2018
54	PDJHPL/IE/ICO-181/2018/381	18.10.2018	Submission of Filter media Mix-design -reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/217	13.11.2018
55	PDJHPL/IE/ICO-181/2018/408	26.10.2018	Submission of Company Profile and Credential of M/s Deevin Seismic Systems Pvt. Ltd. for Expansion Joints-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/127	13.11.2018




 Patel Jhalawar Highway

Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
56	PDJHPL/IE/ICO-181/2018/429	02/11/2018	Submission of DLC Mix Design Confirmatory Reports-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/163	03.12.2018
57	PDJHPL/IE/ICO-181/2018/450	17/11/2018	Submission of Company profile & Credetials of M/s Deevin Seismic Systems Pvt. Ltd. for Expansion joints - reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/199	12.12.2018
58	PDJHPL/IE/ICO-181/2018/451	17/11/2018	Submission of third party test report of construction materials-reg		
59	PDJHPL/IE/ICO-181/2018/452	17/11/2018	Submission of Company profile & Credential of JK Lakshmi Cement Ltd-reg	LASA/Concessionaire/D arah -Jhalawar/IE/2018/148	26/11/2018
60	PDJHPL/IE/ICO-181/2018/453	17/11/2018	Submission of company Profile & Credentials of Supreme Bitumen India Pvt. Ltd.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/162	03.12.2018
61	PDJHPL/IE/ICO-181/2018/454	17/11/2018	Resubmission of Company Profile & Credentials of M/s Hind Heat Treatment & Testing House-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/158	30.11.2018
62	PDJHPL/IE/ICO-181/2018/455	17/11/2018	Submission of Company Profile & Credentials of M/s Yash Enterprises-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/177	04.12.2018
63	PDJHPL/IE/ICO-181/2018/460	20/11/2018	Submission of Company Profile & Credentials of M/s Electrotherm India Ltd. -	LASA/Concessionaire/D arah- Jhalawar/IE/2018/190	08.12.2018
64	PDJHPL/IE/ICO-181/2018/461	20/11/2018	Submission of Mix Design of WMM-reg	LASA/Concessionaire/D arah -Jhalawar/IE/2018/152	27/11/2018
66	PDJHPL/IE/ICO-181/2018/473	22/11/2018	Submission of Concrete Mix Design Done only with Wonder & Ultratech Cement-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/211	15.12.2018
67	PDJHPL/IE/ICO-181/2018/475	22/11/2018	Submission of Concrete Mix Design Using Fly ash with Wonder & Ultratech Cements-reg		
68	PDJHPL/IE/ICO-181/2018/479	23/11/2018	Submission of PQC M-40 Design Using Fly ash with Ultratech Cement-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/176	04.12.2018
69	PDJHPL/IE/ICO-181/2018/480	23/11/2018	Submission of Company Profile & Credentials of M/s KunalConchem Pvt. Ltd.-reg	LASA/Concessionaire/D arah -Jhalawar/IE/2018/147	26/11/2018
70	PDJHPL/IE/ICO-181/2018/510	30/11/2018	Submission of PQC M-40 Design with Ultratech Cement.		
71	PDJHPL/IE/ICO-181/2018/511	30/11/2018	Submission of Company Profile & Credentials of M/s. Normat India Pvt.Ltd	LASA/Concessionaire/D arah- Jhalawar/IE/2018/207	13/12/2018
72	PDJHPL/IE/ICO-181/2018/521	03/12/2018	Submission of Julmi Crusher Aggregate Test Reports-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/196	10/12/2018
73	PDJHPL/IE/ICO-181/2018/522	03/12/2018	Submission of Fine Aggregate Test Report of Kalisindh River-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/197	10/12/2018
74	PDJHPL/IC/ICO-181/2018/542	08/12/2018	Submission of company profile & credential of M/s HI-TECH Engineering Solutions - reg		
75	PDJHPL/IC/ICO-181/2018/599	21/12/2018	Submission of Test Report of Spun pipes for NP-4 pipe - reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/226	24/12/2018
76	PDJHPL/IC/ICO-181/2018/620	31/12/2018	Submission of Inspection Report of Elastomeric Bearing Testing (KANTAFLEX) - reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/247	04.01.2019
77	PDJHPL/IC/ICO-181/2018/626	02/01/2019	Submission of Chemical Composition Test Report of Steel.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/288	24/01/2019
78	PDJHPL/IC/ICO-181/2019/638	05/01/2019	Submission of PQC (M-40) Mix Design with Ultratech Cement.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/252	11/01/2019



Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
PDJHPL/IC/ICO-181/2019/639	05/01/2019	Submission of PQC (M-40) Mix Design using Flyash with Ultratech Cement.	LASA/Concessionaire/Darah-Jhalawar/IE/2018/250	10/01/2019
PDJHPL/IC/ICO-181/2019/643	07/01/2019	Submission of Company Profile and Credentials of Molecule ConchemPvt.Ltd	LASA/Concessionaire/Darah-Jhalawar/IE/2018/273	21.01.2019
PDJHPL/IC/ICO-181/2019/653	10/01/2019	Submission of Test Report of T.M.T Bars from Electrotherm (India) Ltd.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/297	04/02/2019
PDJHPL/IC/ICO-181/2019/665	15/01/2019	Submission of Third Party Test Report of Reinforcement Steel (Hind Heat Treatment)	LASA/Concessionaire/Darah-Jhalawar/IE/2019/292	28/01/2019
PDJHPL/IC/ICO-181/2019/666	15/01/2019	Review of Mix Design of PQC (M-40) with Ultratech Cement & Unirock Plasticizers.		
PDJHPL/IC/ICO-181/2019/672	16/01/2019	Review of Mix Design of PQC (M-40) with Ultratech Cement, Flyash & Unirock Plasticizers.		
PDJHPL/IC/ICO-181/2019/685	21/01/2019	Submission of Company Profile and Credentials of Choksey Chemicals Pvt.Ltd.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/289	28/01/2019
PDJHPL/IC/ICO-181/2019/686	21/01/2019	Submission of Company Profile and Credentials of J.K Cement Ltd.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/290	28/01/2019
PDJHPL/IC/ICO-181/2019/713	31/01/2019	Submission of Test Report of POT/PTFE Bearings for Flyover+Major Bridge 47+650 to 48+150 (Dynamic Prestress Pvt. Ltd).	LASA/Concessionaire/Darah-Jhalawar/IE/2019/304	06/02/2019
PDJHPL/IC/ICO-181/2019/732	06/02/2019	Submission of PQC Trial patch Report from Ch.28+400 to 28+147(LHS) - reg		
PDJHPL/IC/ICO-181/2019/753	12/02/2019	Submission of Company Profile & Credentials of OomsAvenhorn Holding India Pvt. Ltd. & Ooms Polymer Modified Bitumen Pvt. Ltd.-reg	LASA/Concessionaire/Darah-Jhalawar/IE/2019/307	18/02/2019
PDJHPL/IC/ICO-181/2019/761	14/02/2019	Submission of Company Profile & Credential of Unirock Chemicals Pvt. Ltd.-reg	LASA/Concessionaire/Darah-Jhalawar/IE/2019/308	18/02/2019
PDJHPL/IC/ICO-181/2019/788	20/02/2019	Submission of Company Profile & Credential of MSP Group for procurement of Dowel Bars - reg		
PDJHPL/IC/ICO-181/2019/798	25/02/2019	Submission of Company Profile & Credetial of M/s Sika India - reg	LASA/NHAI/Darah-Jhalawar/IE/2019/350	16.03.2019
PDJHPL/IC/ICO-181/2019/804	26/02/2019	Submission of Company Profile & Credential of M/s STP Ltd - reg	LASA/NHAI/Darah-Jhalawar/IE/2019/351	16.03.2019
PDJHPL/IC/ICO-181/2019/812	28/02/2019	Submission of Company Profile & Credetial of MSP steel & Power Ltd - reg.		
PDJHPL/IC/ICO-181/2019/833	07/03/2019	Submission of Company Profile & Credetial of Chembond Chemicals - reg	LASA/Concessionaire/Darah-Jhalawar/IE/2019/352	16.03.2019
PDJHPL/IC/ICO-181/2019/962	23/04/2019	Submission of Company Profile & Credetial of FortuneLtd -reg		
PDJHPL/IC/ICO-181/2019/967	25/04/2019	Submission of Company Profile & Credetial of BalajeeLohaLtd -reg		
PDJHPL/IC/ICO-181/2019/1018	09/05/2019	Submission of Company Profile & Credetial of Essar Steel -reg		
PDJHPL/IC/ICO-181/2019/1019	09/05/2019	Submission of Company Profile & Credetial of BostikPvtLtd -reg	LASA/Concessionaire/Darah-Jhalawar/IE/2019/415	16/05/2019
PDJHPL/IC/ICO-181/2019/1031	11/05/2019	Submission of Methodology of Pile Load Test of Routine Pile @ 57+127 (MJB)		
PDJHPL/IC/ICO-181/2019/1048	16/05/2019	Submission of Methodology of Pile Load Test of Routine Pile @ 36+070 (MJB)	LASA/Concessionaire/Darah-Jhalawar/IE/2019/429	24/05/2019
PDJHPL/IC/ICO-181/2019/1074	25/05/2019	Submissio of Plate Load Test Report Conducted at 36+070 (MJB) & 58+128 (Flyover).		



Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
103	PDJHPL/IC/ICO-181/2019/1083	28/05/2019	Submission of Initial Load Test Report Conducted on Test Pile .		
104	PDJHPL/IC/ICO-181/2019/1088	30/05/2019	Submission of Company Profile & Credetial of Nuvoco Vistas Corp. Ltd -reg	LASA/Concessionaire/Darah-Jhalawar/IE/2019/583	27/09/2019
105	PDJHPL/IC/ICO-181/2019/1098	03/06/2019	Submission of Kerb (M-20) with Ultratech Cement without Flyash.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/446	10/06/2019
106	PDJHPL/IC/ICO-181/2019/1099	03/06/2019	Submission of SPT Test Report for Ch.36+070 (MJB)		
107	PDJHPL/IC/ICO-181/2019/1100	03/06/2019	Submission of Bore Log Test Report @ 36+070 (MJB) & 58+128 (Flyover).		
108	PDJHPL/IC/ICO-181/2019/1189	30/06/2019	Submission of Company Profile & Credential of STECOL (Essar TMT Brand)		
109	PDJHPL/IC/ICO-181/2019/1369	07/09/2019	Submission of Company Profile & Credential of VADOL Corporation	LASA/Concessionaire/Darah-Jhalawar/IE/2019/587	28/09/2019
110	PDJHPL/IC/ICO-181/2019/1379	10/09/2019	Change in Company name Deevin Engineering Consulting group to DECG International.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/596	05/10/2019
110	PDJHPL/IC/ICO-181/2019/1402	18/09/2019	Submission of Company Profile & Credential of J Sons Engg Corporation	LASA/Concessionaire/Darah-Jhalawar/IE/2019/594	03/10/2019
111	PDJHPL/IC/ICO-181/2019/1437	30/09/2019	Submission of Company Profile & Credential of Shree Cement Limited	LASA/Concessionaire/Darah-Jhalawar/IE/2019/595	04/10/2019
112	PDJHPL/IC/ICO-181/2019/1564	21/11/2019	Submission of Inspection Report of Elastomeric Bearing Testing (KANTAFLEX India Pvt. Limited) for MJB 36+070	LASA/Concessionaire/Darah-Jhalawar/IE/2019/666	27/11/2019
113	PDJHPL/IC/ICO-181/2019/1574	23/11/2019	Submission of Company Profile & Credential of Electrosteel Steels Limited	LASA/Concessionaire/Darah-Jhalawar/IE/2019/671	29/11/2019
114	PDJHPL/IC/ICO-181/2019/1605	30/11/2019	Submission of company profile & credential of M/s Sika India Pvt. Ltd.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/699	12/12/2019
115	PDJHPL/IC/ICO-181/2019/1619	05/12/2019	Submission of Plate Load Test Report of BC (53+700).		
116	PDJHPL/IC/ICO-181/2019/1620	05/12/2019	Submission of Plate Load Test Report of VUP (Km 54+550).		
117	PDJHPL/IC/ICO-181/2019/1621	05/12/2019	Submission of Inspection Test Report of POT/ PTFE Bearing (Dynamic Prestress) of Elevated @ Km 47+830 & MJB @ Km 57+127.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/700	12/12/2019
118	PDJHPL/IC/ICO-181/2019/1654	14/12/2019	Submission of Company Profile and Credential of M/s BASF India Limited (for Admixture).	LASA/Concessionaire/Darah-Jhalawar/IE/2020/719	02/01/2020
119	PDJHPL/IC/ICO-181/2019/1665	17/12/2019	Submission of Factory Visit and TMT inspection Test Report of M/s Electrosteel Steels Limited for TMT Bars and Third Party Test Report.		
120	PDJHPL/IC/ICO-181/2019/1684	21/12/2019	Submission of Test Report of Strands of DP Wires.		
121	PDJHPL/IC/ICO-181/2019/1698	26/12/2019	Submission of Inspection Test Report of POT/ PTFE Bearing (Dynamic Prestress) of Flyover @ Km 46+957, Km 50+095, Km 58+128.	LASA/NHAI/Darah-Jhalawar/IE/2020/798	20/02/2020
122	PDJHPL/IC/ICO-181/2019/1700	26/12/2019	Submission of High Strain Dynamic Pile Load Test Reort of MJB @ Km 36+070.		
123	PDJHPL/IC/ICO-181/2019/1743	08/01/2020	Submission of Mix Design of DBM with VG-40 Grade.		
124	PDJHPL/IC/ICO-181/2019/1745	08/01/2020	Submission of Concrete Mix design with Nuvoco Cement & Sika Admixture & Without Flyash.		




Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
125	PDJHPL/IC/ICO-181/2019/1753	11/01/2020	Submission of Test Report of Core Sample of Retaining Wall Raft.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/754	22/01/2020
126	PIL/PRJ/TECH/ODO-189/2020/1755	11/01/2020	Submission of Company Profile & Credential of HMM Infra Ltd.		
127	PDJHPL/IC/ICO-181/2020/1766	16/01/2020	Submission of Company Profile & Credential of GOEL TMT.		
128	PDJHPL/IC/ICO-181/2020/1770	17/01/2020	Submission of Test Report of Steel of MJB @ Ch 57+127, LVUP @ Ch 23+065.	LASA/NHAI/Darah-Jhalawar/IE/2020/766	30/01/2020
129	PDJHPL/IC/ICO-181/2020/1799	30/01/2020	Submission of Plate Load Test Report of ROB @ 44+158.		
130	PDJHPL/IC/ICO-181/2020/1810	30/01/2020	Submission of Environmental Monitoring Test Report for the year 2020.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/754	05/02/2020
131	PDJHPL/IC/ICO-181/2020/1842	07/02/2020	Submission of Company Profile & Credential of TATA Steel Ltd for Procurement of LRPC Strands		
132	PDJHPL/IC/ICO-181/2020/1886	19/02/2020	Submission of Independent Laboratory Test Reports of Geogrid of Strata Geosystems (India) Pvt. Ltd		
133	PDJHPL/IC/ICO-181/2020/2158	29/07/2020	Submission of Company Profile and Credential of J.K Prestressing Co. for Jack use in Girder prestressing work of MJB @ Km 57+127.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/963	07/08/2020
134	PDJHPL/IC/ICO-181/2020/2166	31/07/2020	Submission of Company Profile & Credential of BG Trade Infra for Procurement of Plastic for Bituminous Mixs.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/959	04/08/2020
135	PDJHPL/IC/ICO-181/2020/2231	25/08/2020	Submission of Company Profile & Credential of JSW Steel Ltd for TMT Steel.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1009	03/09/2020



Status of submitted Drawings

S.No	Type of Structure	Scope in Nos	No. of Drawing Submitted	Vide Letter No.	Date	Proof Check	Remarks	
1	Pipe Culvert	16	R0-16 Nos.	PDJHPL/PIU/D/016/2018	27.02.2018	NIL	Approved (13 Nos)	
				PDJHPL/PIU/CLO-179/2018/146	23.07.2018	NIL		
				R1-8 Nos.	PDJHPL/PIU/CLO-179/2018/146	23.07.2018		NIL
2	Box Culvert	21	R0-20 Nos.	PDJHPL/PIU/D/016/2018	27.02.2018	NIL	Approved (11 Nos)	
				PDJHPL/PIU/CLO-179/2018/093	04.07.2018	NIL		
				PDJHPL/PIU/CLO-179/2018/041	12.06.2018	NIL		
				PDJHPL/PIU/CLO-179/2018/037	07.06.2018	NIL		
				R1-20 Nos.	PDJHPL/PIU/CLO-179/2018/093	04.07.2018		NIL
				PDJHPL/PIU/CLO-179/2018/137	18.07.2018	NIL		
				PDJHPL/PIU/CLO-179/2018/138	18.07.2018	NIL		
				PDJHPL/PIU/CLO-179/2018/228	22.08.2018	NIL		
				PDJHPL/PIU/CLO-179/2018/388	18.10.2018	NIL		
				PDJHPL/PIU/CLO-179/2018/463	20.11.2018	NIL		
PDJHPL/IC/ICO-181/2019/1349	03.09.2019	NIL						
3	Minor Bridge	11	R0-10 Nos.	PDJHPL/PIU/D/016/2018	27.02.2018	NIL	Approved (08 Nos)	
				PDJHPL/PIU/CLO-179/2018/146	23.07.2018	NIL		
				PDJHPL/PIU/CLO-189/2018/191	09.08.2018	NIL		
				R1-05 Nos	PDJHPL/PIU/CLO-179/2018/037	07.06.2018		NIL
				PDJHPL/IE/ICO-181/2018/317	29.09.2018	NIL		
				Compliance	PDJHPL/IE/ICO-181/2018/487	23.11.2018		NIL
				PDJHPL/IE/ICO-181/2018/488	26.11.2018	NIL		
				PDJHPL/IC/ICO-181/2018/562	11.12.2018	NIL		
				PDJHPL/IC/ICO-181/2018/582	17.12.2018	NIL		
				R1 - 01 Nos	PDJHPL/IC/ICO-181/2018/816	01.03.2019		
PDJHPL/IC/ICO-181/2019/1298	13.08.2019		Approved					
PDJHPL/IC/ICO-181/2019/1349	03.09.2019		Approved					
4	Major Bridge	2	R0-02 Nos	PDJHPL/PIU/D/034/2018	19.04.2018	NIL		
				R1-03Nos	PDJHPL/PIU/CLO-179/2018/037 01 Nos. (Letter -119 date- 09.07.2018) (Proof Checked)	07.06.2018	1 set	
				PDJHPL/PIU/CLO-179/2018/072	25.06.2018		Approved	
				PDJHPL/IE/ICO-181/2018/272	12.09.2018		Approved	
				PDJHPL/HO/DJT/IE/578/2018	15.12.2018	1 set	Approved	
5	Elevated Road	1	R1-01 Nos	PDJHPL/PIU/CLO-179/2018/037 01 Nos. (Letter -119 date- 09.07.2018) (Proof Checked)	07.06.2018	1 set	Approved	
6	VUP	9	R0-09 Nos	PDJHPL/PIU/D/018/2018	12.03.2018			
				PDJHPL/PIU/D/014/2018	27.02.2018			
				Letter No- 041 (IIT Certified Copy)	12.06.2018	1 set	Approved (06 Nos)	



S.No	Type of Structure	Scope in Nos	No. of Drawing Submitted	Vide Letter No.	Date	Proof Check	Remarks
			R1-06 Nos	Letter No- 041 (IIT Certified Copy) (Letter -158 date- 28.07.2018)	12.06.2018	1 set	
				(Letter -188 date- 08.08.2018)	08.08.2018		
			R2-04 Nos.	PDJHPL/IC/ICO-181/583	17.12.2018		
				PDJHPL/IC/ICO-181/632	03.01.2019		Approved (12 Nos)
7	LVUP	13	R0-13 Nos	PDJHPL/PIU/D/016/2018	27.02.2018	NIL	
				PDJHPL/PIU/CLO-179/2018/067	22.06.2018	NIL	
			R1-06 Nos	PDJHPL/PIU/CLO-179/2018/067	22.06.2018	NIL	
				PDJHPL/IC/ICO-181/2019/811	28/02/2019		
8	FlyOver	3	R0-03Nos	PDJHPL/PIU/D/034/2018	19.04.2018	1 set	Approved (01 Nos)
			R1-03 Nos	PDJHPL/PIU/CLO-179/2018/115	09.07.2018	NIL	
			R2-03 Nos	PDJHPL/IC/ICO-181/2018/431	03.11.2018	2 set	
9	ROB	1	R1-01 Nos	PDJHPL/PIU/CLO-179/2018/118 01 Nos. (Letter-118 date- 09.07.2018) Proof Checked)	09.07.2018	1 set	Approved
				PDJHPL/IC/ICO-181/2018/550	10.12.2018	2 set	
			R2-02 Nos	PDJHPL/IC/ICO-181/2019/1570	22.11.2019	02 set	Approved
10	RUB	1	R1-01 Nos	PDJHPL/PIU/TEC/CLO- 179/2018/019 Hard Copy of Trecing Paper Drawing	31.05.2018	1 set	Approved
1	Plan & Profile	48.88 Km	R0-01 Nos	PDJHPL/PIU/CLO-179/2018/106	06.07.2018	NIL	
				PDJHPL/IC/ICO-181/2018/364	12.10.2018	NIL	
			R1-01 Nos	PDJHPL/IC/ICO-181/2018/474	22.11.2018	NIL	
				PDJHPL/HO/DJT/IE/001/2019	07.01.2019	NIL	
				PDJHPL/HO/DJT/IE/007/2019	19.01.2019		Approved upto 48.88 Km
2	TOLL PLAZA		R0-01 Nos	PDJHPL/IC/ICO-181/2018/316	29.09.2018		Approved
3	POT/PTEF Bearing		46+950, 50+095, 58+128	PDJHPL/IC/ICO-181/2018/430	03.11.2018		Approved
	Pin, Free, Metallic guided Bearing		57+127	PDJHPL/IC/ICO-181/2019/1465	11.10.2019		Approved
	Elastomeric Bearing		30+078, 41+102, 49+330	PDJHPL/IC/ICO-181/1511	02.11.2019		Approved
	Strip Seal Expansion Joint		12+125, 15+725, 19+965, 25+100, 27+025, 30+075, 36+070, 41+095, 49+330, 54+550,	PDJHPL/IC/ICO-181/2019/1714, PDJHPL/IC/ICO-181/2019/1715, PDJHPL/IC/ICO-181/2020/1767	30/12/2019 16/01/2020		
				PDJHPL/IC/ICO-181/2020/1777	18/01/2020		Approved



S.No	Type of Structure	Scope in Nos	No. of Drawing Submitted	Vide Letter No.	Date	Proof Check	Remarks
			47+830,				
	Signage Plan		48.88 Km	PDJHPL/IC/ICO-181/2019/1699	26/12/2019		
	Junction Drawing		48.88 Km	PDJHPL/IC/ICO-181/2019/1618	05/12/2019		
	Friction Slab Drawing			PDJHPL/IC/ICO-181/2019/1671	18/12/2019		Approved
4	Pavement Design			PDJHPL/HO/DJT/IE/008/2019	19.01.2019		Approved
5	RE wall		VUP (12+125) & 12+450 (LVUP)	PDJHPL/IC/ICO-181/2018/658	12/01/2019		
			LVUP (15+725)	PDJHPL/PIU/CLO-189/2018/200	11/08/18		
			LVUP (17+353)	PDJHPL/PIU/CLO-189/2018/201	11/08/18		
			VUP (19+970)	PDJHPL/IC/ICO-181/2018/659	12/01/2019		
			LVUP (21+183)	PDJHPL/IC/ICO-181/2018/660	12/01/2019		
			LVUP (23+065)	PDJHPL/IC/ICO-181/2018/661	12/01/2019		
			LVUP (23+687)	PDJHPL/IC/ICO-181/2018/662	12/01/2019		
			LVUP (24+547) & VUP (25+100)	PDJHPL/PIU/CLO-189/2018/202	11/08/18		
			LVUP (27+029)	PDJHPL/PIU/CLO-189/2018/203	11/08/18		
			LVUP (37+050)	PDJHPL/PIU/CLO-189/2018/204	11/08/18		
			LVUP (38+545)	PDJHPL/PIU/CLO-189/2018/205	11/08/18		
			ROB (44+158) (R0)	PDJHPL/PIU/CLO-189/2019/1164	21/05/2019		
			LVUP (42+258)	PDJHPL/PIU/CLO-189/2018/537	07/12/2018		Approved
			VUP (49+330) (R0)	PDJHPL/IE/ICO-181/2018/534	07/12/2018		
			VUP (49+330) (R1)	PDJHPL/IE/ICO-181/2018/603	24/12/2018		
			VUP (49+330) (R2)	PDJHPL/IC/ICO-181/2019/760	14/02/2019		Approved
			Flyover (50+099) (R0)	PDJHPL/IE/ICO-181/2018/535	07/12/2018		Approved
			Flyover (50+099) (R1)	PDJHPL/IE/ICO-181/2018/602	24/12/2018		
			Flyover (50+099) (R2)	PDJHPL/IC/ICO-181/2019/759	14/02/2019		
			LVUP (51+762)	PDJHPL/OC/ICO-179/2019/1001	03/05/2019		Approved
			VUP (41+102) & LVUP (41+465) (R0)	PDJHPL/IE/ICO-181/2018/536	07/12/2018		Approved
			VUP (41+102) & LVUP (41+465) (R1)	PDJHPL/IC/ICO-181/2019/719	01/02/2019		
			LVUP (42+263) (R0)	PDJHPL/IE/ICO-181/2018/537	07/12/2018		



S.No	Type of Structure	Scope in Nos	No. of Drawing Submitted	Vide Letter No.	Date	Proof Check	Remarks
			LVUP (42+263) (R1)	PDJHPL/IC/ICO-181/2019/720			Approved
			LVUP (45+875) (R0)	PDJHPL/IC/ICO-189/2019/1000	03/05/2019		Approved
			Design & Drawing for Sandy Soil	PDJHPL/IE/ICO-181/2018/548	10/12/2018		
			Bus Bay	PDJHPL/IC/ICO-181/2020/1821	03/02/2020		Approved
			Strip Seal Expansion Joint (DECG) for Flyover @ Km 46+950 & Km 58+128.	PDJHPL/IC/ICO-181/2020/2127	17/07/2020		Approved
			Approach Slab & Terminal Slab	PDJHPL/IC/ICO-181/2020/2178	05/08/2020		
			Drainage Spout	PDJHPL/IC/ICO-181/2020/2184	07/08/2020		Approved
			Bus Shelter	PDJHPL/IC/ICO-181/2020/2233	26/08/2020		



Mobilization of Manpower


Name of the Employee	Designation	Department
P.Gangadhar	General Manager (EPC)	Technical
Milind Pande	Project Incharge	Technical
Atul Kumar Mishra	Sr. Project Manager	Technical
Shubhash Kumar	Sr.Manager	Mechanical
Praveen Kahar	Manager	Liasion
Balram Singh Shekhawat	Manager	Liasion
Bhagwan Jha	Manager	Purchase
Subhash Singh	Dy. Project Manager	Technical (Highway)
Ranjay Kumar Anju	Dy. Project Manager	Planning & Billing
Ramesh Chandra Barad	Dy. Manager (HR & Admin)	HR & Admin
Ritesh Verma	Dy. Manager (HR & Admin)	HR & Admin
Mahesh Pandey	Dy. Project Manager	Highway
SajjanLal Sharma	Dy. Project Manager	Structure
Sanjay Gaur	Dy. Project Manager	QA/QC
Rajesh Rawal	Dy. Project Manager	QA/QC
Bal Krishna Rath	Dy. Project Manager	Structure
Kuldeep Singh	Sr.Surveyor	Survey
Ravi Kishore Pandey	Sr.Accountant	Finance & Accounts
Rajan Upadhyay	Dy. Project Manager	Health & Safety
HR & ADMIN DEPARTMENT		
Asst Manager (S &V)	01 Nos	HR & Admin
Sr. Executive	01 Nos	HR & Admin
Sr.Officer(S & V)	03 Nos	HR & Admin
Officer (S & V)	03 Nos	HR & Admin
Executive	01 Nos	HR & Admin
Jr.Executive	01 Nos	HR & Admin
Security violation	02 Nos	HR & Admin
Office Boy	06 Nos	HR & Admin
PLANNING & BILLING DEPARTMENT		
Sr.Engineer	03 Nos	Planning & Billing
Engineer	02 Nos	Planning & Billing
Asst. Engineer	02 Nos	Planning & Billing
QA/QC DEPARTMENT		
Sr. Engineer	01 Nos	QA/QC
Lab Asst.	01 Nos	QA/QC
Sr.Lab Technician	02 Nos	QA/QC
Lab Technician	07 Nos	QA/QC
Jr.Lab Technician	01 Nos	QA/QC
Engineer	03 Nos	QA/QC
Jr.Engineer	03 Nos	QA/QC



HIGHWAY DEPARTMENT		
Sr. Engineer	03 Nos	Highway
Engineer	03 Nos	Highway
Asst. Engineer	08 Nos	Highway
Jr.Engineer	06 Nos	Highway
Engineer Trainee	02 Nos	Highway
Jr. Supervisor	01 Nos	Highway
Supervisor	11 Nos	Highway
STRUCTURE DEPARTMENT		
Sr. Engineer	05 Nos	Structure
Engineer	06 Nos	Structure
Asst. Engineer	04 Nos	Structure
Jr.Engineer	04 Nos	Structure
Engineer Trainee	01 Nos	Structure
Sr.Supervisor	06 Nos	Structure
Supervisor	03 Nos	Structure
Jr.Supervisor	03 Nos	Structure
SURVEY DEPARTMENT		
Sr. Surveyor	01 Nos	Survey
Surveyor	10 Nos	Survey
Jr.Surveyor	04 Nos	Survey
STORE DEPARTMENT		
Jr. Executive	05 Nos	Store
Executive	08 Nos	Store
WEIGH BRIDGE		
Jr.Executive	13 Nos	Weigh Bridge
PURCHASE DEPARTMENT		
Dy.Manager	01 Nos	Purchase
Sr.Executive	01 Nos	Purchase
Executive	01 Nos	Purchase
HEALTH & SAFETY DEPARTMENT		
Sr.Executive	01 Nos	Health & Safety
Engineer	01 Nos	Health & Safety
Executive	01 Nos	Health & Safety
IT DEPARTMENT		
Sr.Executive	01 Nos	IT
Executive	01 Nos	IT
MECHANICAL DEPARTMENT		
Sr.Supervisor	01 Nos	Mechanical
Sr. Engineer	03 Nos	Mechanical
Engineer	01 Nos	Mechanical
Asst. Engineer	06 Nos	Mechanical
Executive	01 Nos	Mechanical
Asst. Mechanic	03 Nos	Mechanical
Fitter	01 Nos	Mechanical




Tyre Fitter	04 Nos	Mechanical
Jr.Engineer	03 Nos	Mechanical
Jr.Executive	03 Nos	Mechanical
Engineer Trainee	01 Nos	Mechanical
Supervisor	10 Nos	Mechanical
Driver	125 Nos	Mechanical
Operator / Helper/ Mechanic	105 Nos	Mechanical
SPV DEPARTMENT		
Sr.Executive	01 Nos	SPV



Mobilization of Resources (Plant and Machineries)

S.No	Name of Machinery / Equipments	TOTAL	Remarks
1	Excavator	32	
2	Hywa/Tipper	174	
3	Soil Compactor	19	
4	Dozer	0	
5	Water Tanker	22	
6	Diesel Dispenser	6	
7	Grader	15	
8	Loader	10	
9	Back Hoe	6	
10	Transit Mixer	21	
11	Crusher	3	
12	Concrete Batching Plant	5	
13	Weigh Bridge	7	
14	WMM Plant	1	
15	Hydra Crane	8	
16	Hot Mix Plant	1	
17	Concrete Pump	2	
18	Sand Classifier	2	
19	Tractor	13	
20	Tower Light	17	
21	DG Set	17	
22	Light Vehicle	34	
23	Trailer	4	
24	JCB	6	
25	Boom Placer	2	
26	Tandem Roller	6	
27	Baby Roller	2	
28	Mobile Service Van	2	
29	DLC Paver	3	
30	Automatic PQC Paver	1	
31	Kerb Paver	2	
32	Chilling Plant	1	
33	Bus	1	
34	Fork Lift	3	
35	Block Casting Machine	1	
36	Ambulance Van	1	
	Total	450	



Site Progress Photo



9+860 to
9+950

Rolling work of Median opening in
progress

Median



50+580 to 50+720

Rolling work of DLC for
median opening in progress

Median





16+520

Tree Plantation work in progress


Median



29+170

Concrete work of Median Cross
drain wall in progress

Median





9+860 to
9+950

DLC work for Median opening
in progress

Median



28+530

Tree Plantation work in
progress

Median





LVUP @ 23+687

Casting Work of Slab Complete


RHS



FOB @
46+950

Concrete work of Diaphragm
P1-P2 span in progress

RHS





MJB @ 36+070

Steel & shuttering checking of slab P12-A2 in progress

RHS



FOB @ 46+9950

Reinforcement work of P3 pier cap in progress

LHS





Camp-2	Concrete pouring work of crash barrier completed.	---
--------	---	-----



Elevated @ 47+830	Concrete pouring work of crash barrier completed.	LHS
----------------------	---	-----





Ahu River @ 36+070	Pile Steel checking with Lasa BE	---
-----------------------	----------------------------------	-----



ROB @ 44+158	ROB Pier Concrete Pouring	---
-----------------	---------------------------	-----



Elevated @
47+830


Concrete pouring work of crash
barrier completed.



28+700

Median Cross drain pcc work
in progress

Median





MNB @
12+380

Casting work of MNB SLAB
completed

BHS



FOB @ 16+060


Concrete Pouring
Work of Pier P-3

LHS




Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Pa


BOX CULVERT 13+980

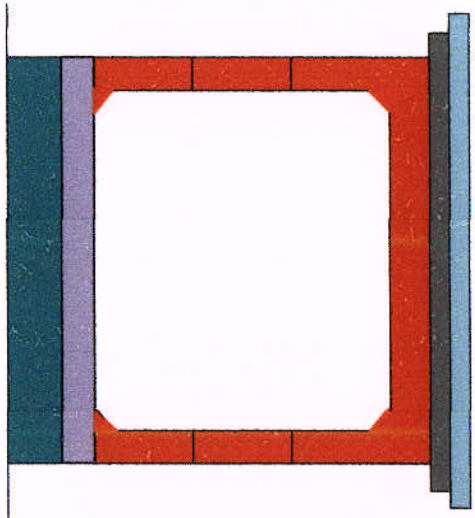

BOX CULVERT 13+400

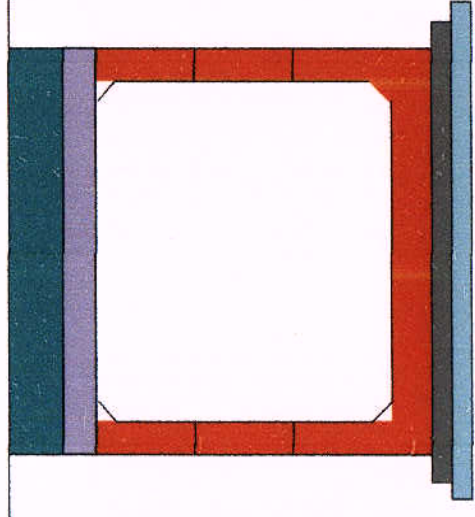


BOX CULVERT 11+605

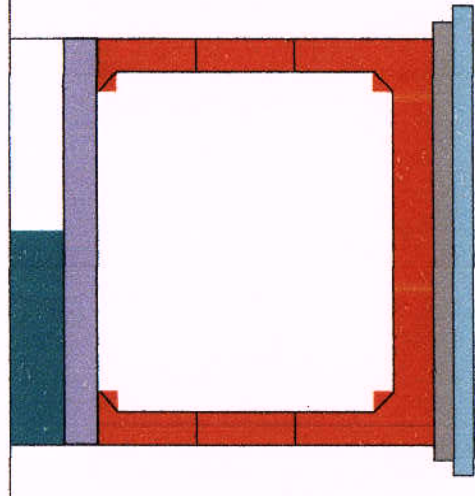


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation


BOX CULVERT 22+450

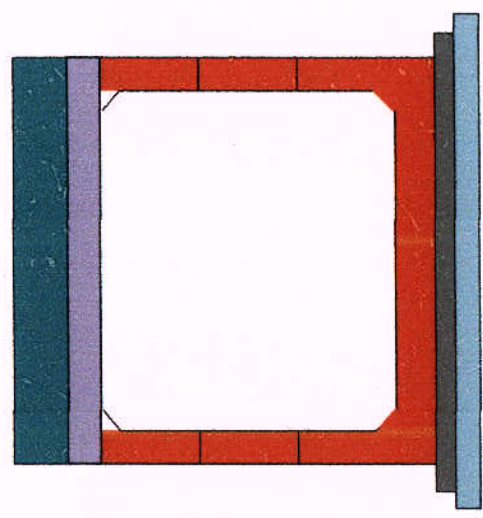

BOX CULVERT 16+600

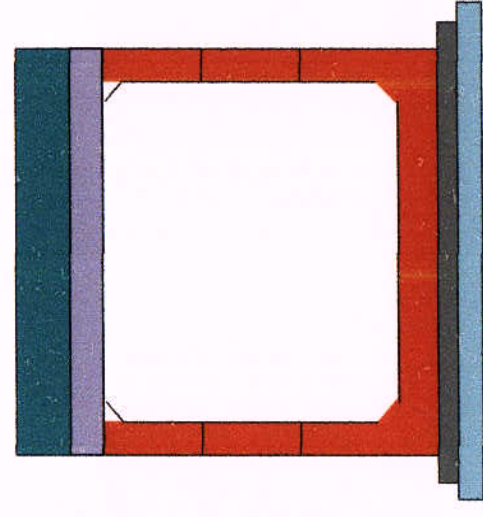

BOX CULVERT 14+980

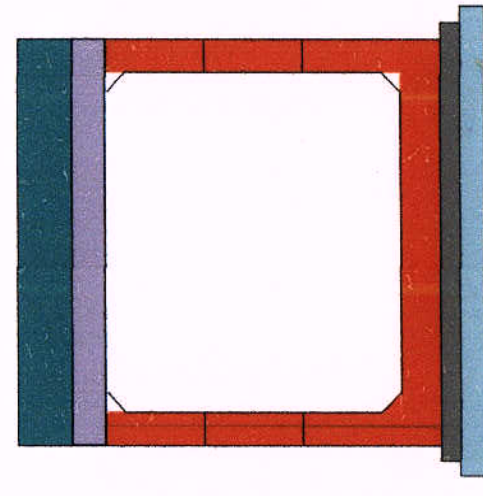


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation

Chainage



Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Pa

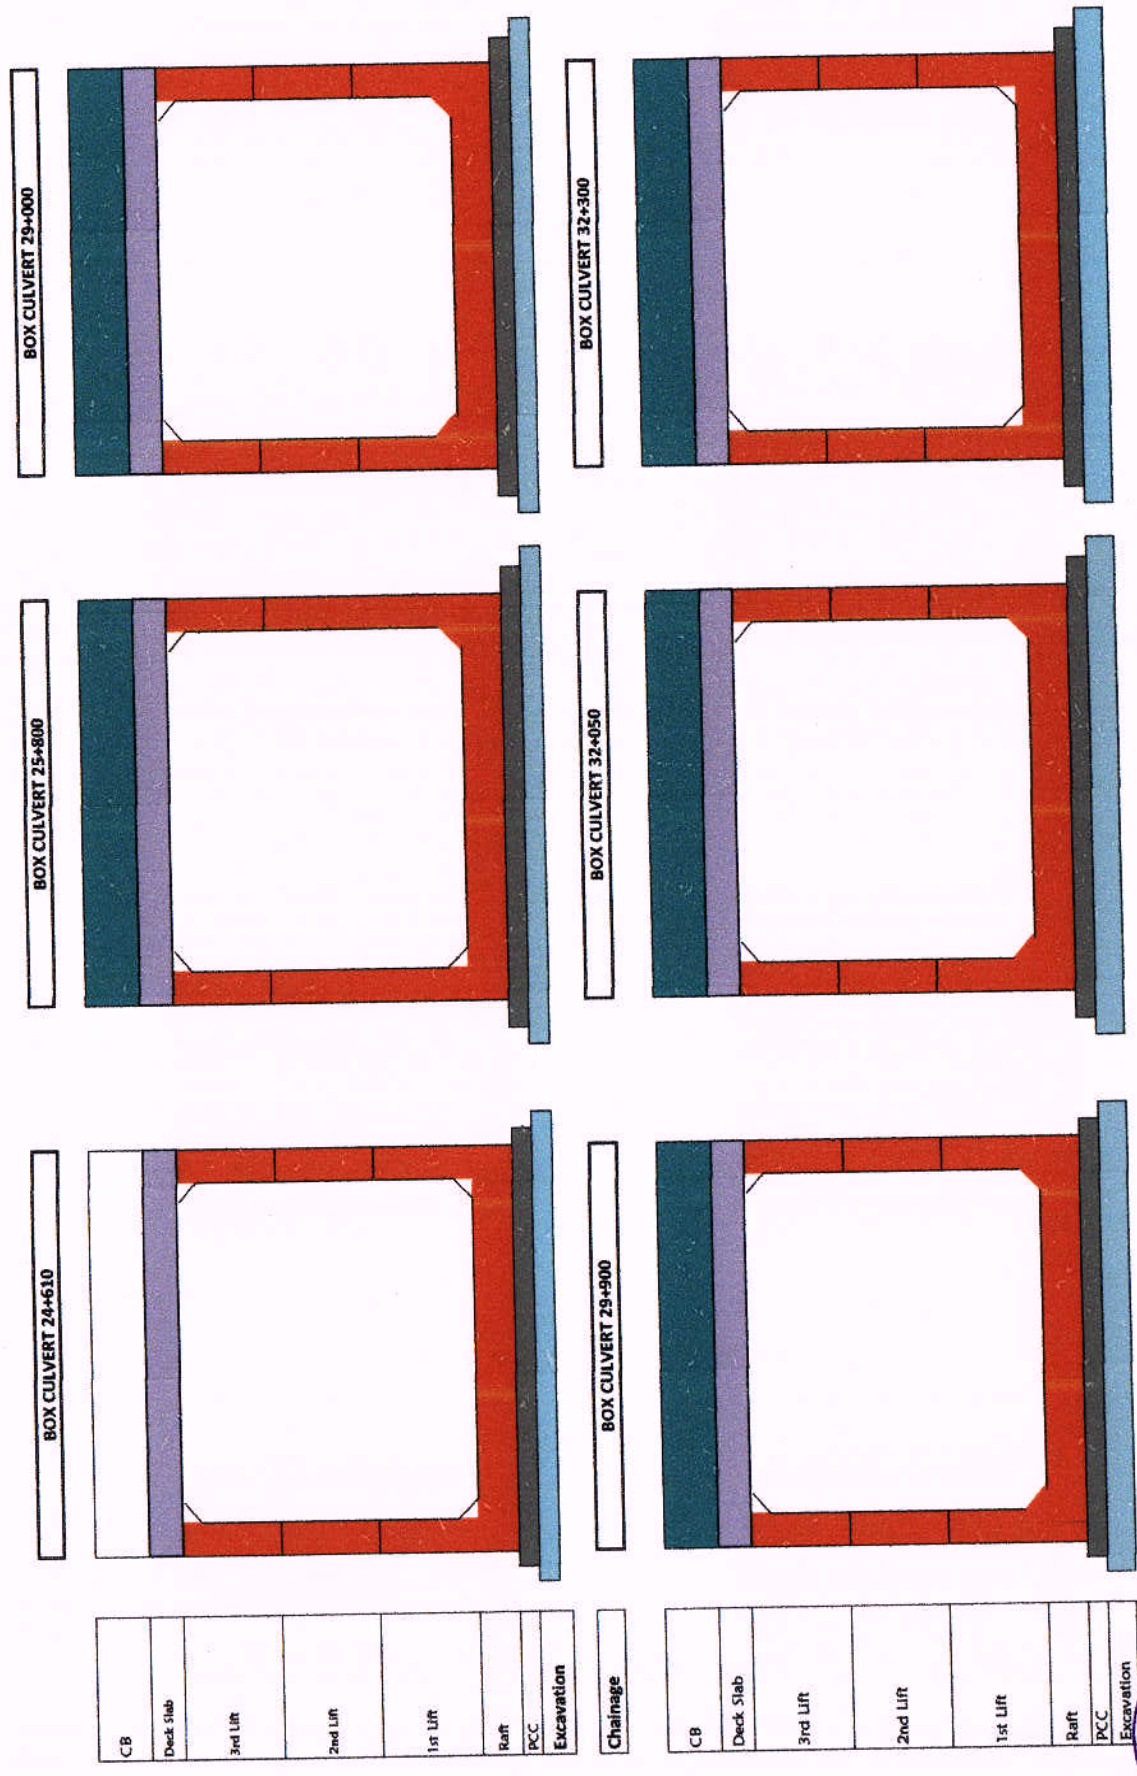




CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation

Chainage




CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation



Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teenchar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Pa

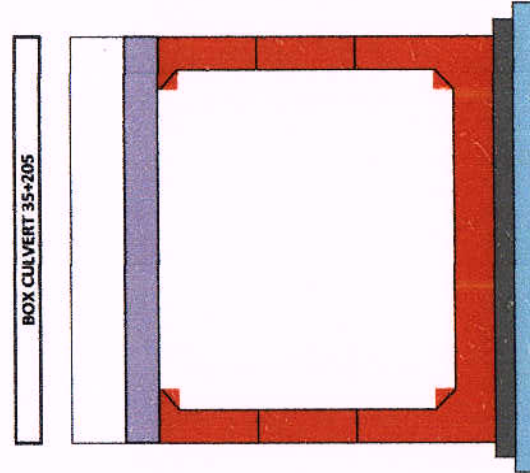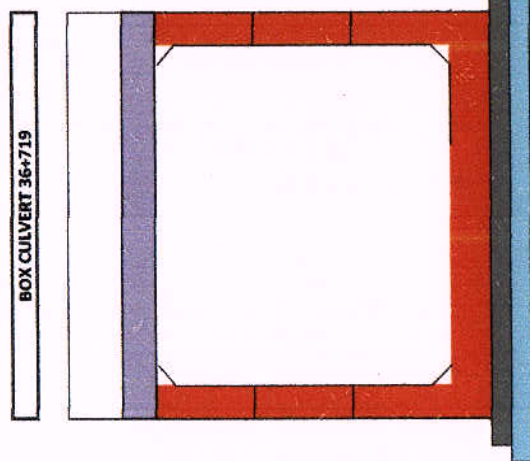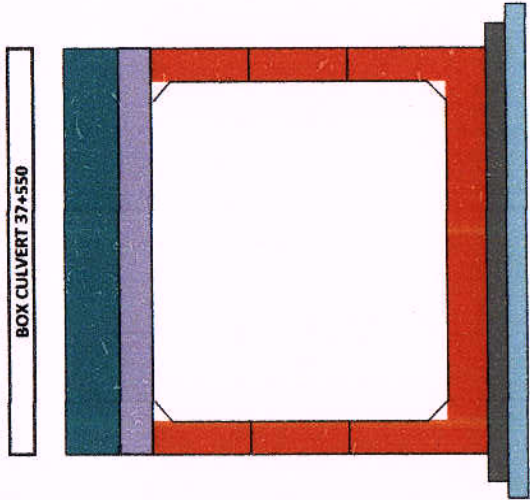

CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation

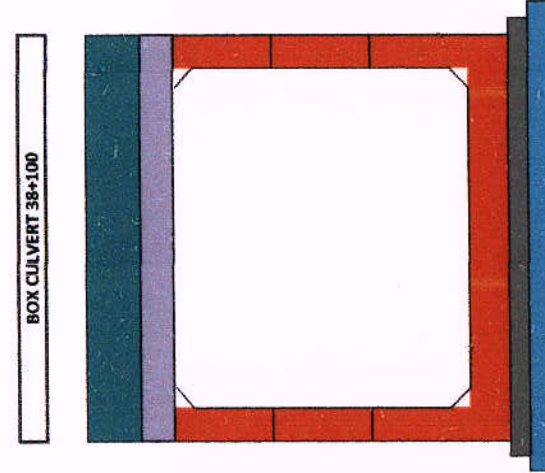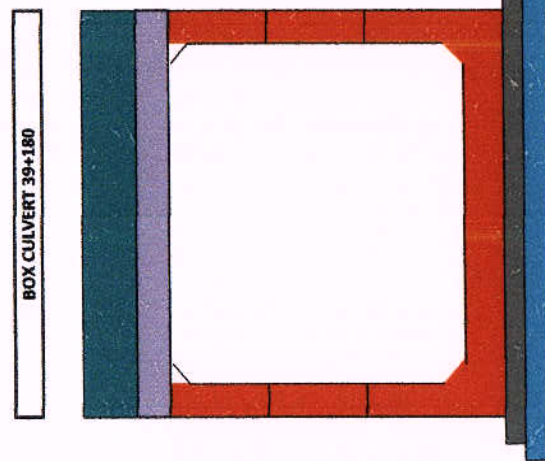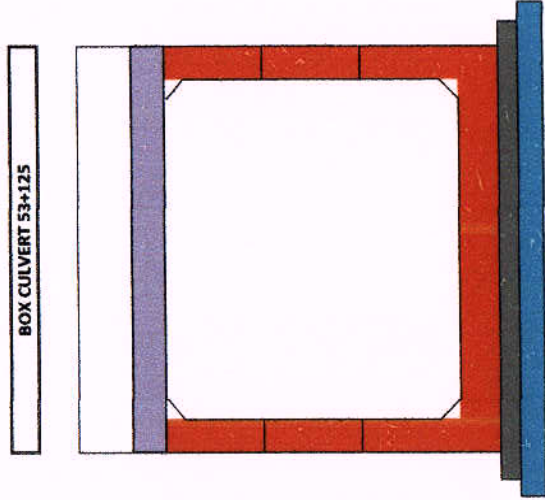


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation


Chainage






Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Pa

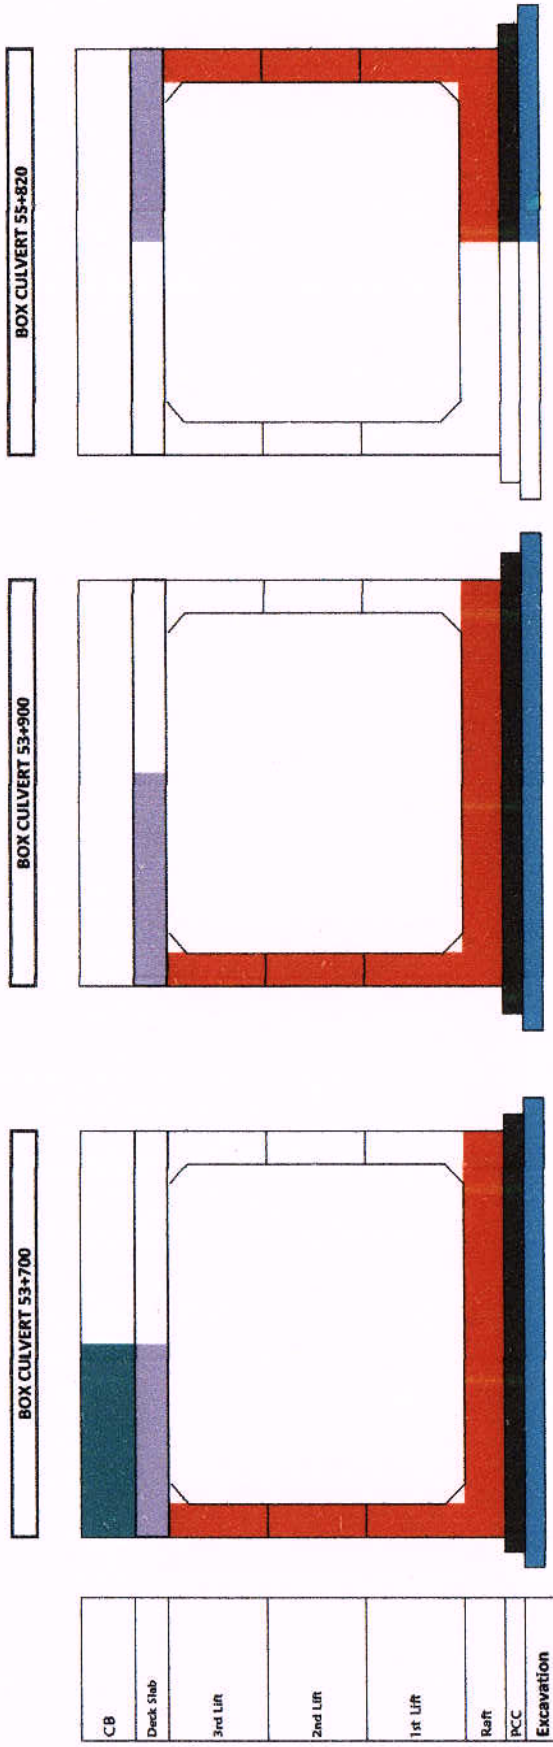

Additional / SR

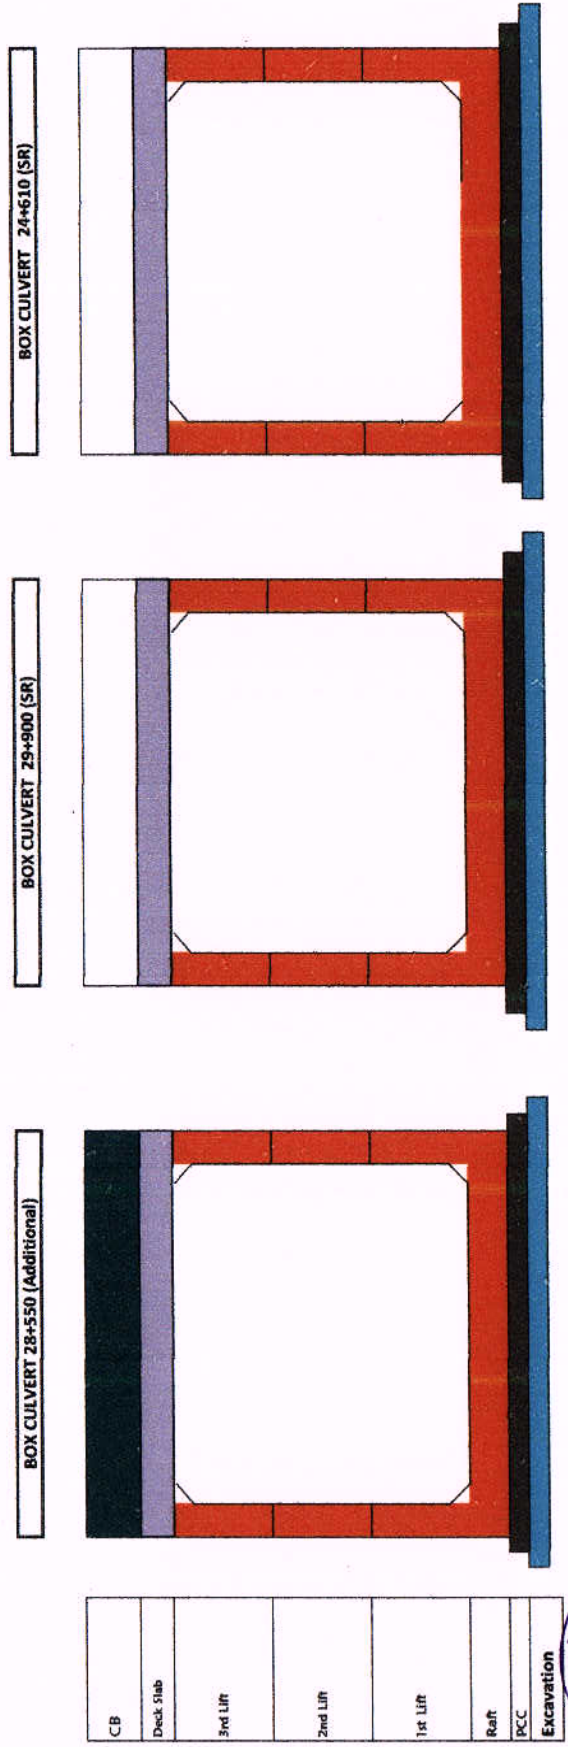

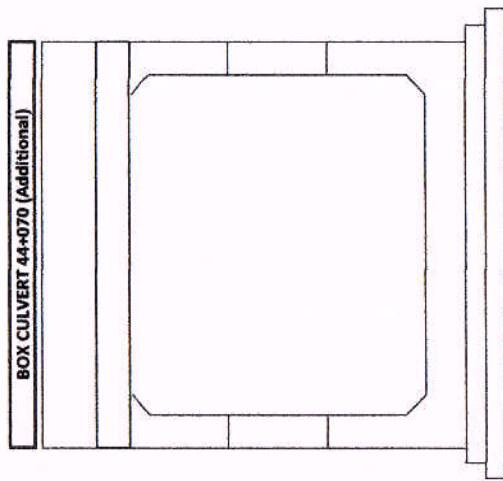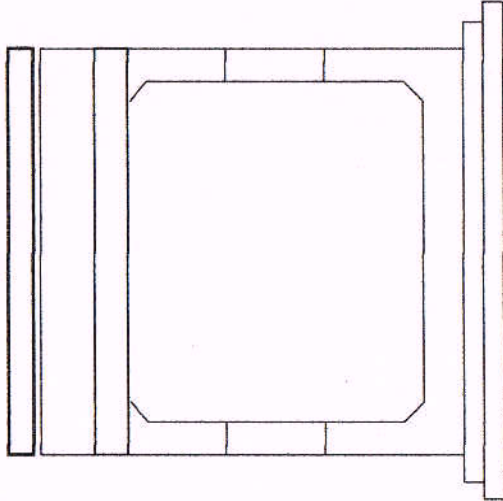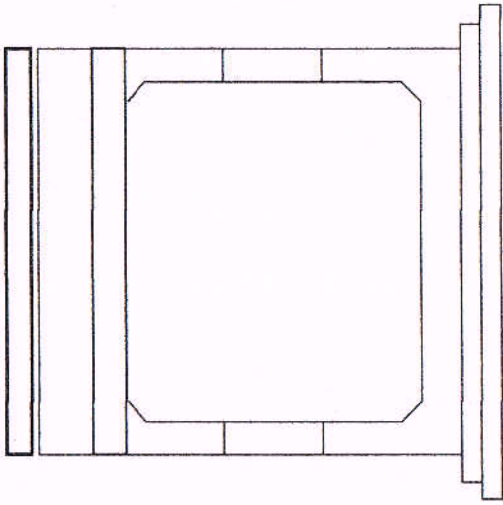


BOX CULVERT 44+070 (Additional)

CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation




N...NO... BR...JGL AT ...M. 2+300 LHS

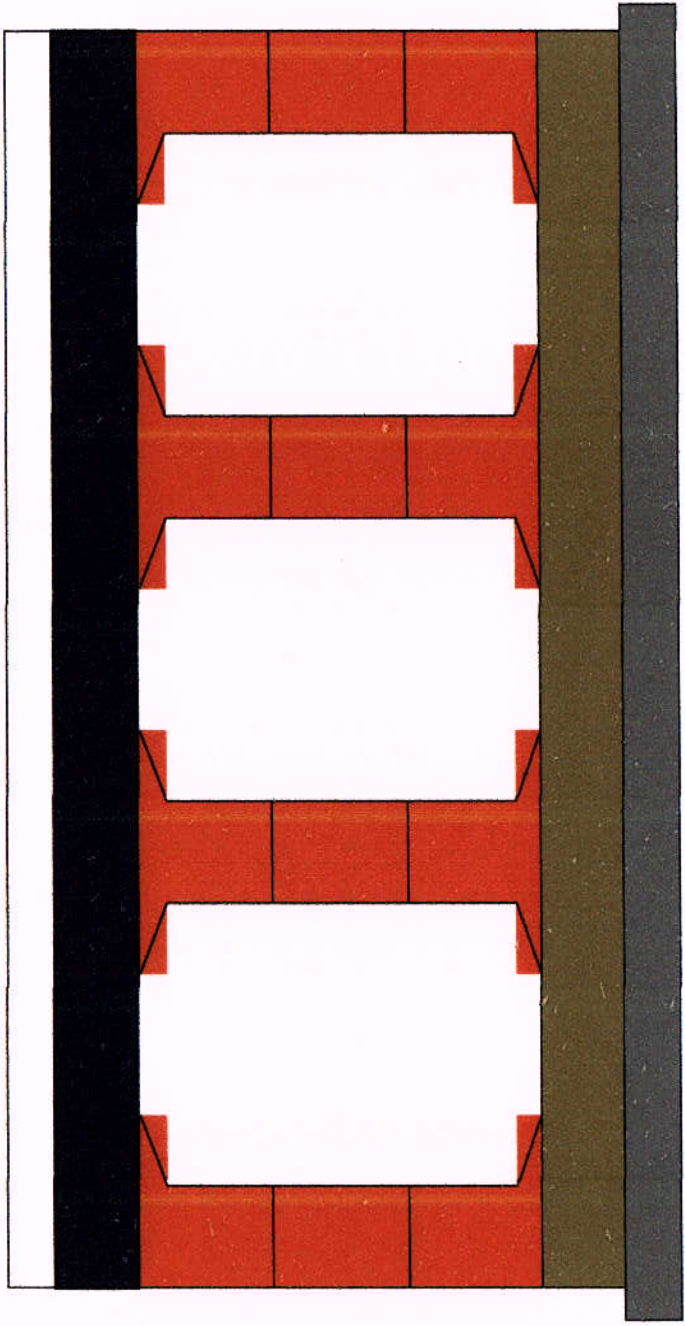

CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC


MINOR BRIDGE AT KM. 12+380 LHS

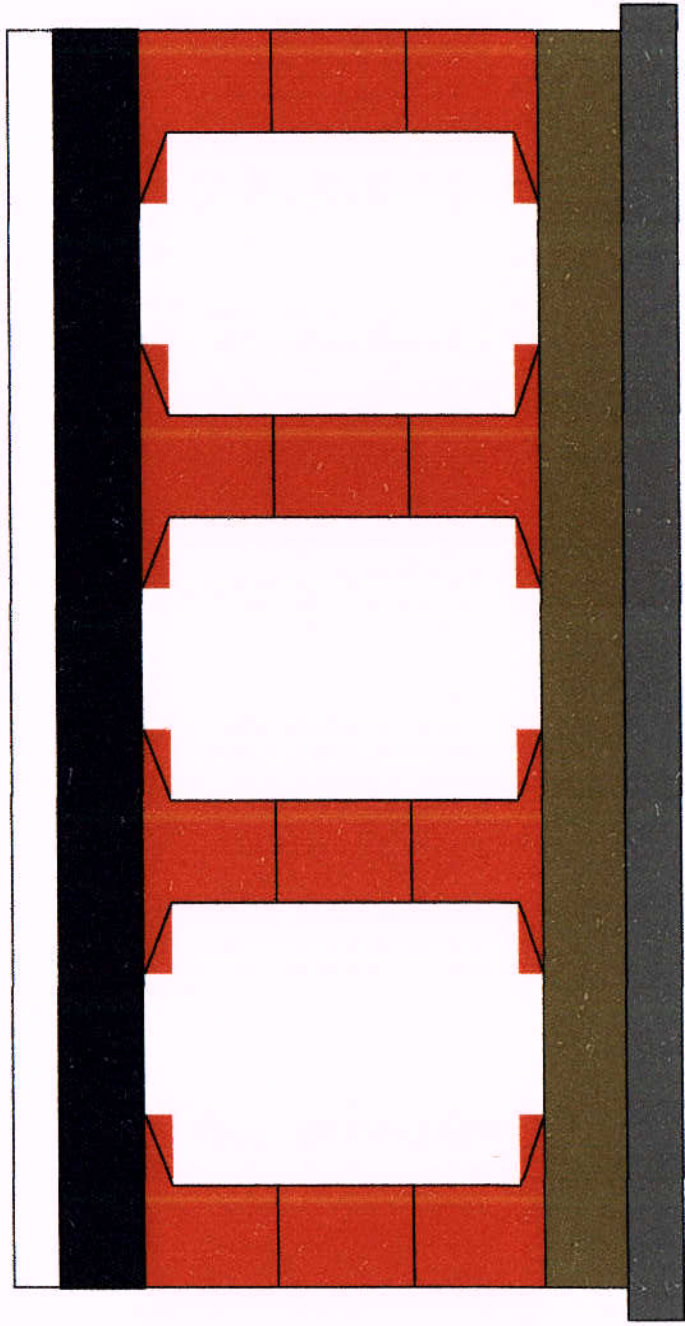

CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC




MINOR BRIDGE AT KM. 12+380 R.H.S Service Road

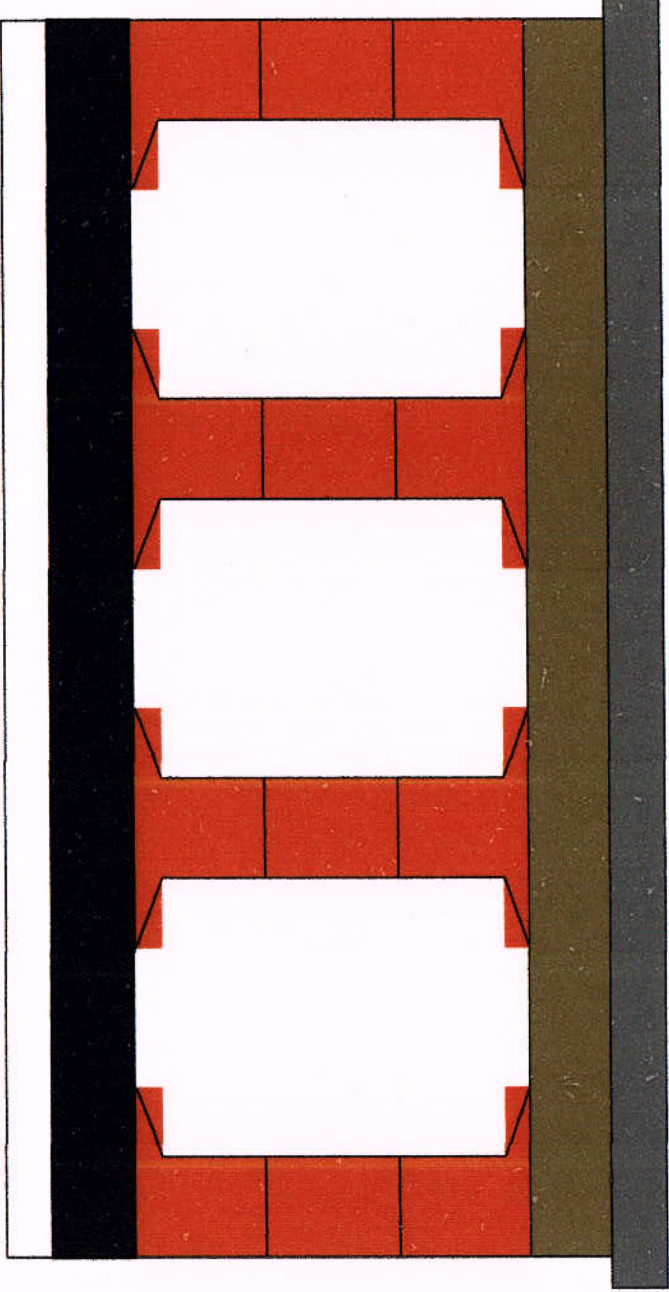

CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC


MINOR BRIDGE AT KM. 12+380 LHS Service Road

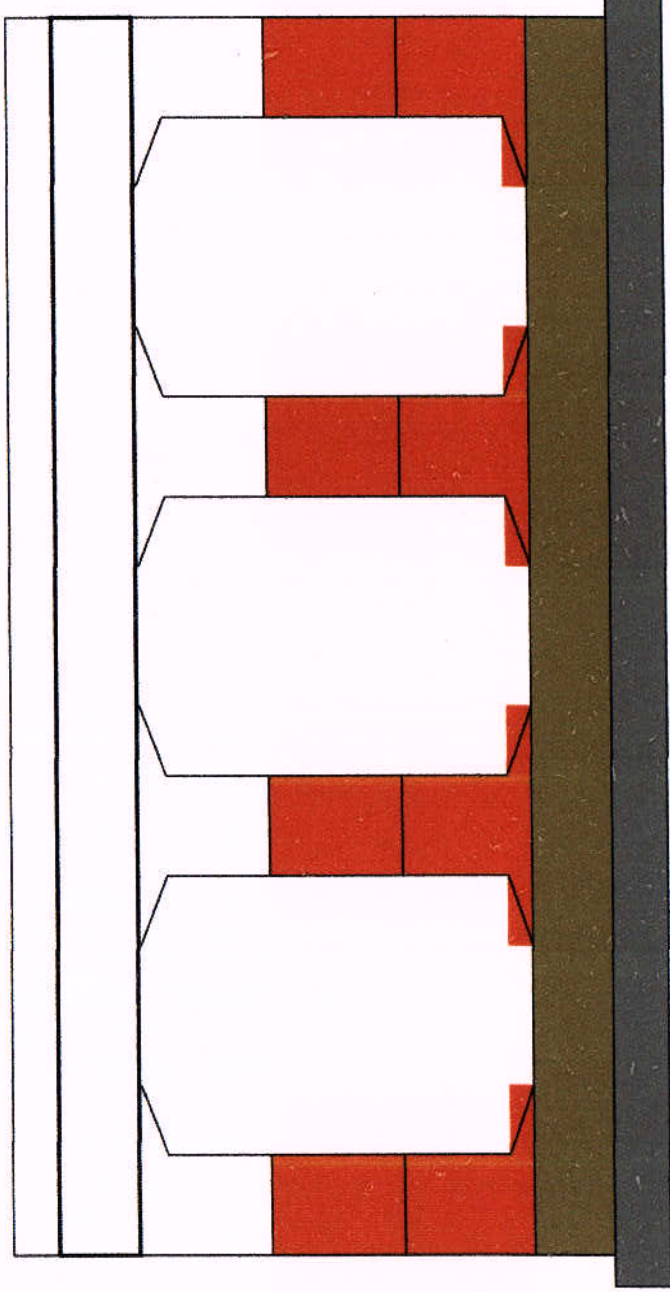

CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC




MINOR BRIDGE AT KM. 16+060 (Main Carriage Way) RHS

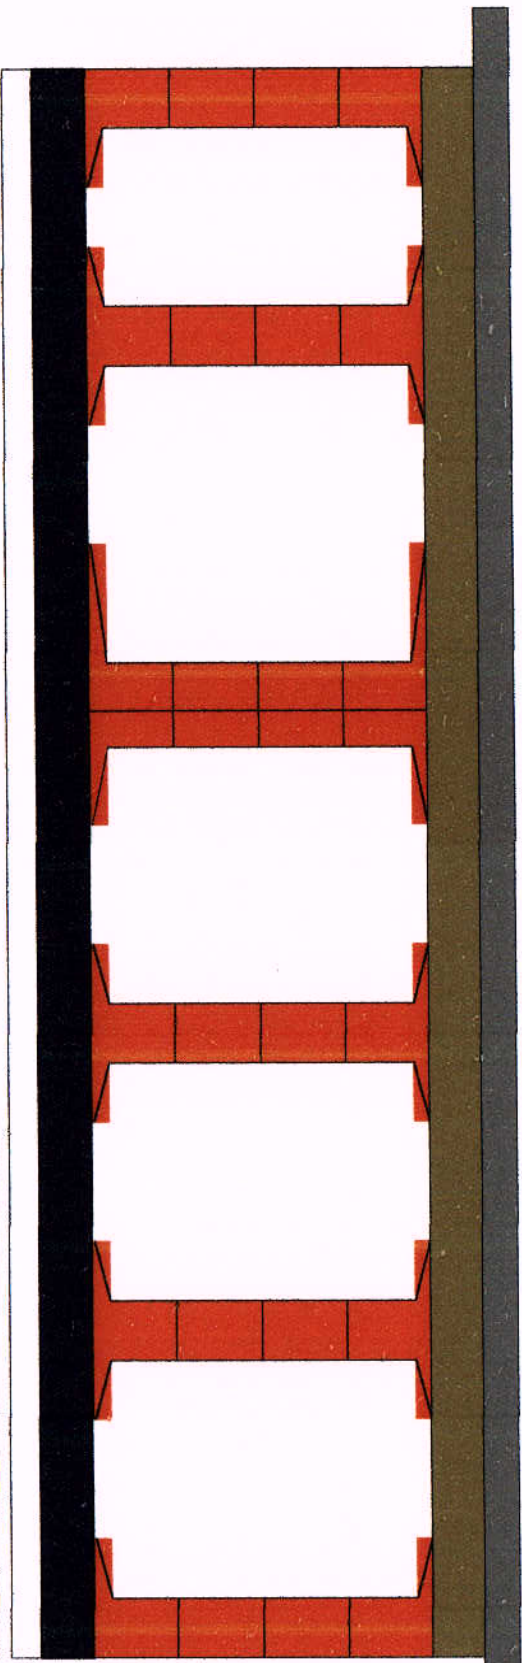


CB
4th Lift
3rd Lift
2nd Lift
1st Lift
Raft
PCC


Project: Construction of 4-lane Road on NH-12 (New NH-52) from Km 395.000 to 346.540 (Design Challenge from 360 to 340) (Dorah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project (Length 48.880 Km.) - Package II

MINOR BRIDGE AT KM. 16+060 (Main Carriage Way) LHS

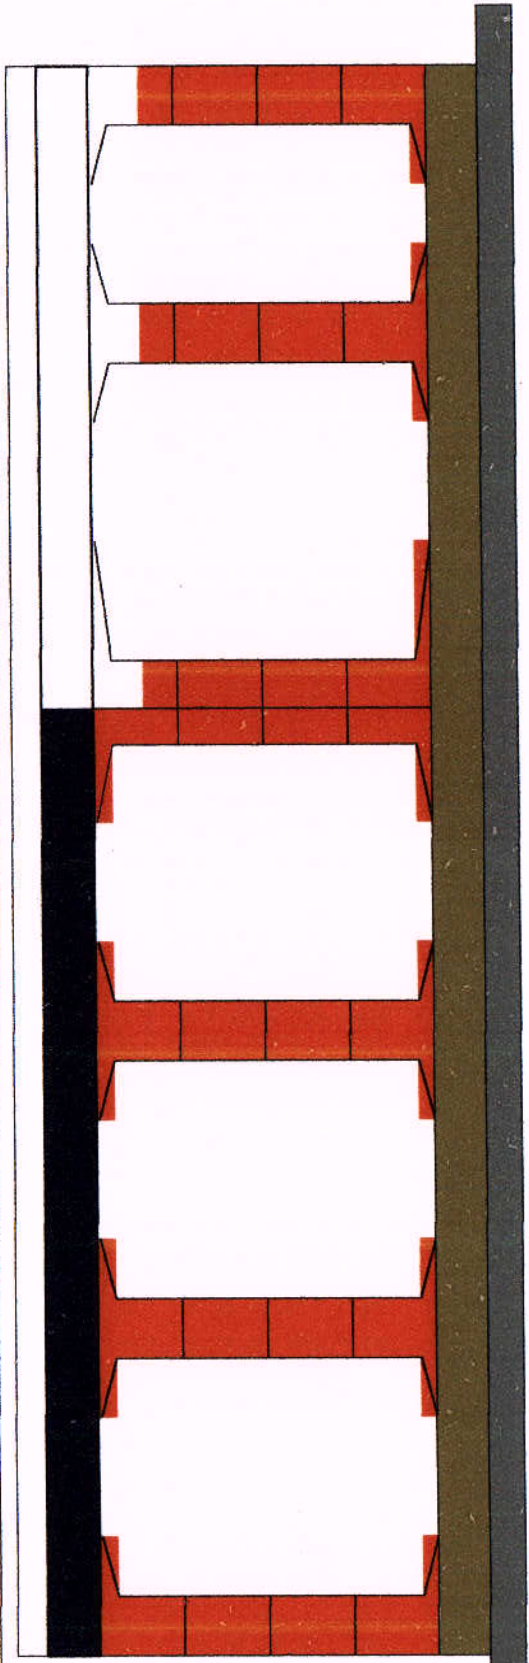


CB
4th Lift
3rd Lift
2nd Lift
1st Lift
Raft
PCC

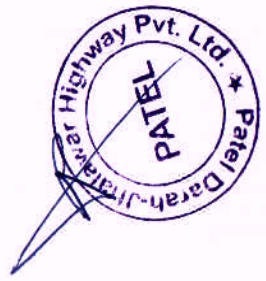

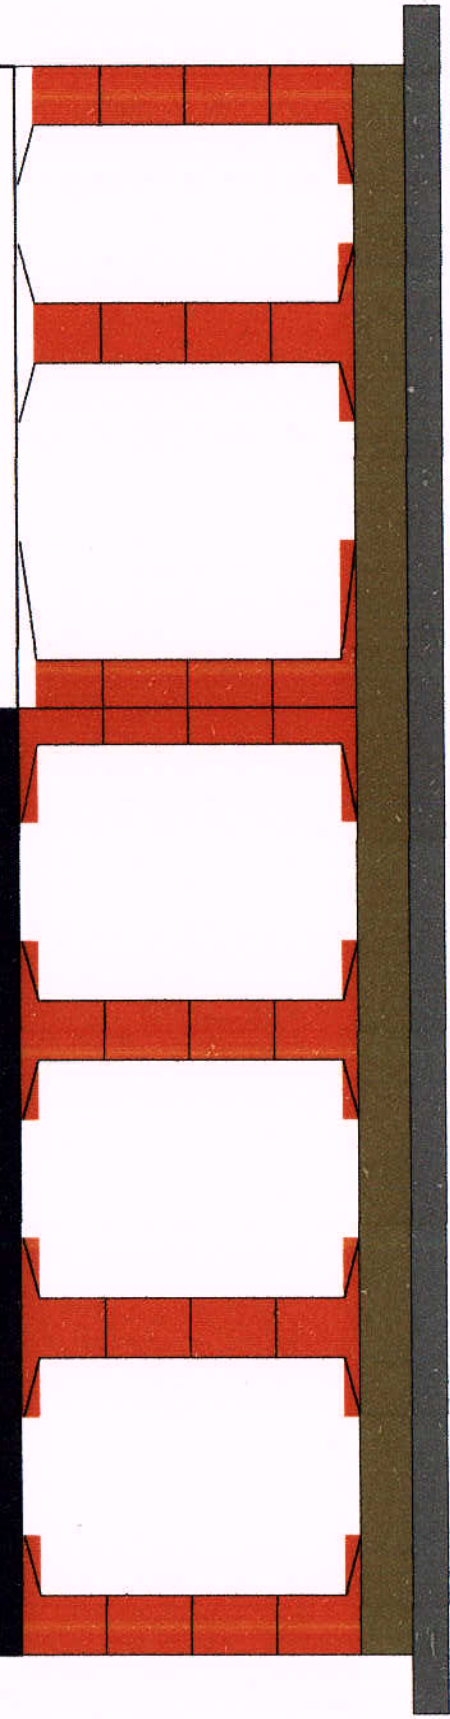


MINOR BRIDGE AT KM. 16+060 (Service Road) LHS

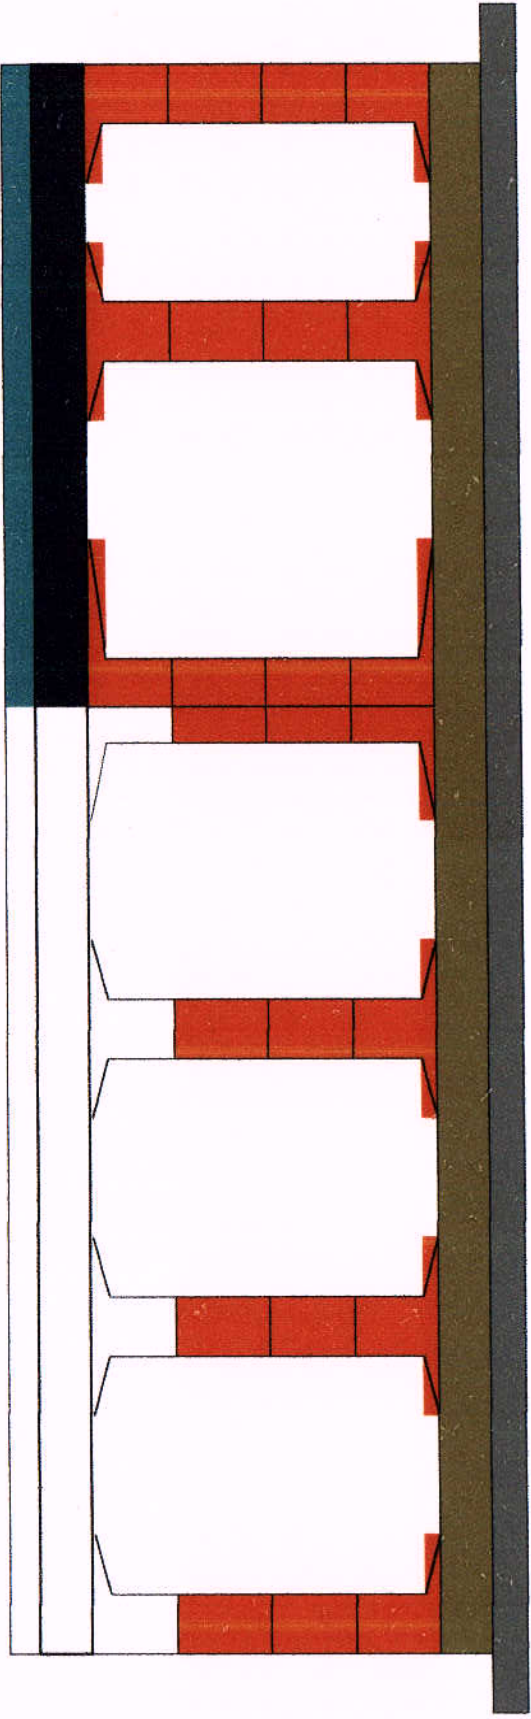


4th Lift
3rd Lift
2nd Lift
1st Lift
Raft
PCC

CB
4th Lift
3rd Lift
2nd Lift
1st Lift
Raft
PCC




N...NO... BR...JGL AT ...M. 17+880 LHS

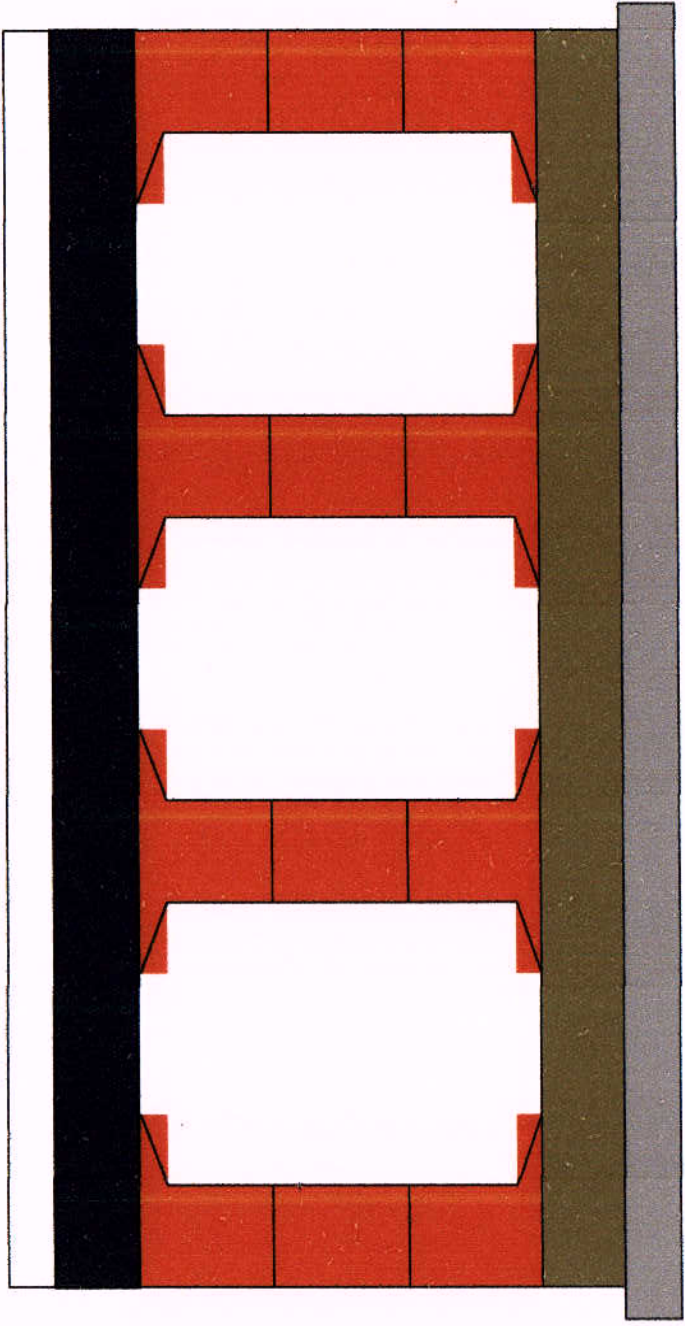

CB					
	3rd Lift				
	2nd Lift				
	1st Lift				
	Raft				
	PCC				


MINOR BRIDGE AT KM. 17+880 LHS

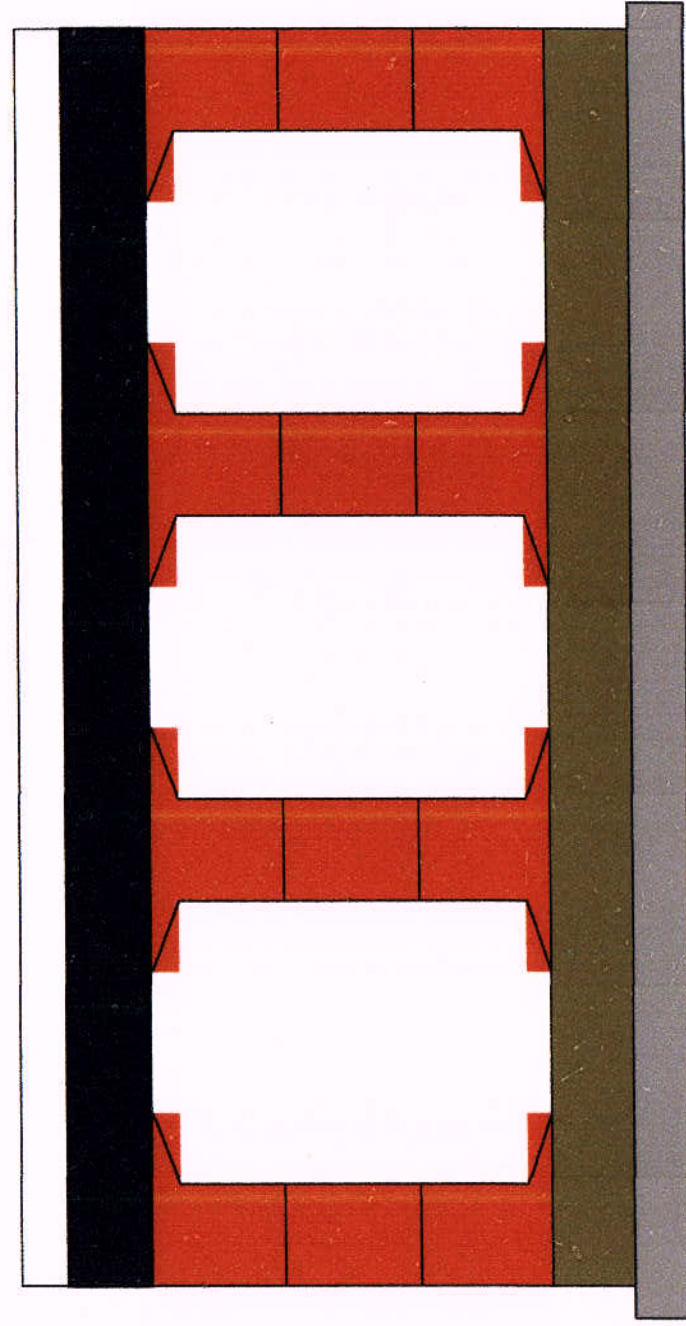

CB					
	3rd Lift				
	2nd Lift				
	1st Lift				
	Raft				
	PCC				




MINOR BRIDGE AT KM. 29+600 LHS

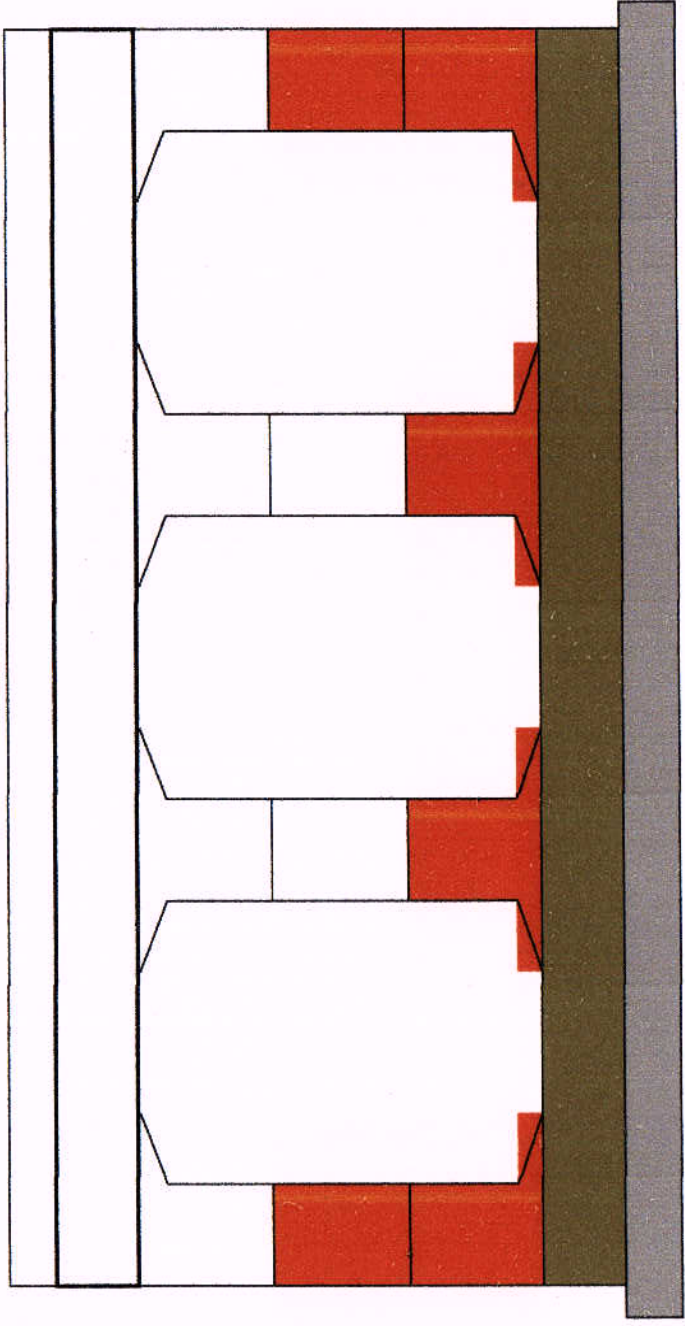

CB						
3rd Lift						
2nd Lift						
1st Lift						
Raft						
PCC						


MINOR BRIDGE AT KM. 29+600 LHS

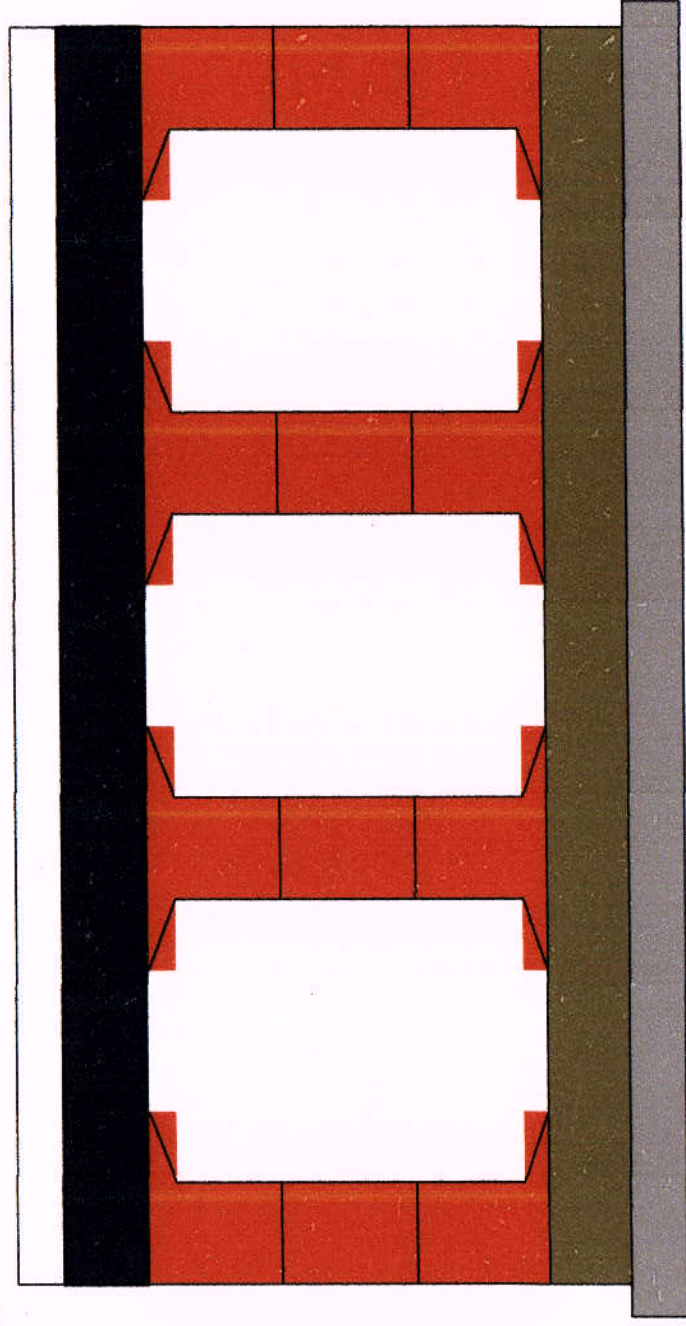

CB						
3rd Lift						
2nd Lift						
1st Lift						
Raft						
PCC						




MINOR BRIDGE A. KM. 33+000 RHS

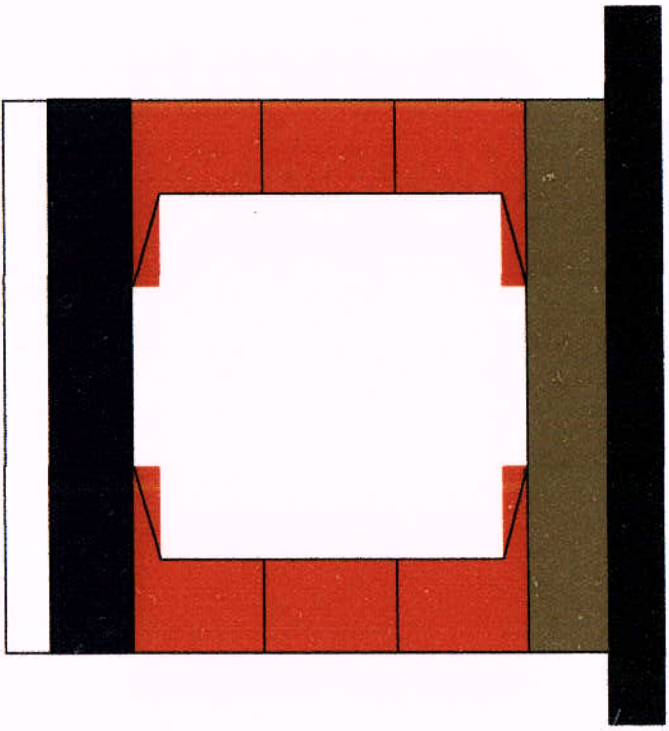

CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC


MINOR BRIDGE AT KM. 33+000 LHS

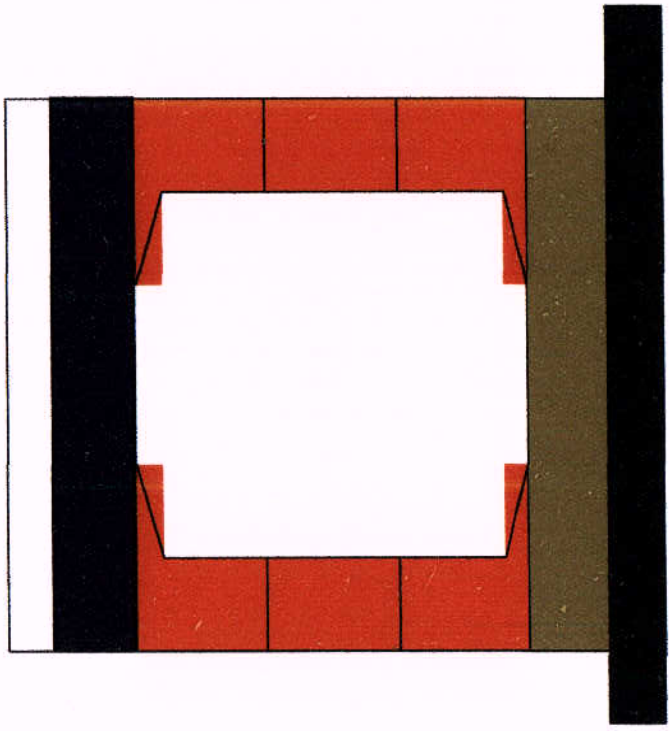

CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC



Patel Darah-Jhalawa Highway Pvt. Ltd. ★
PATEL

MINOR BRIDGE AT KM. 34-360 RH.

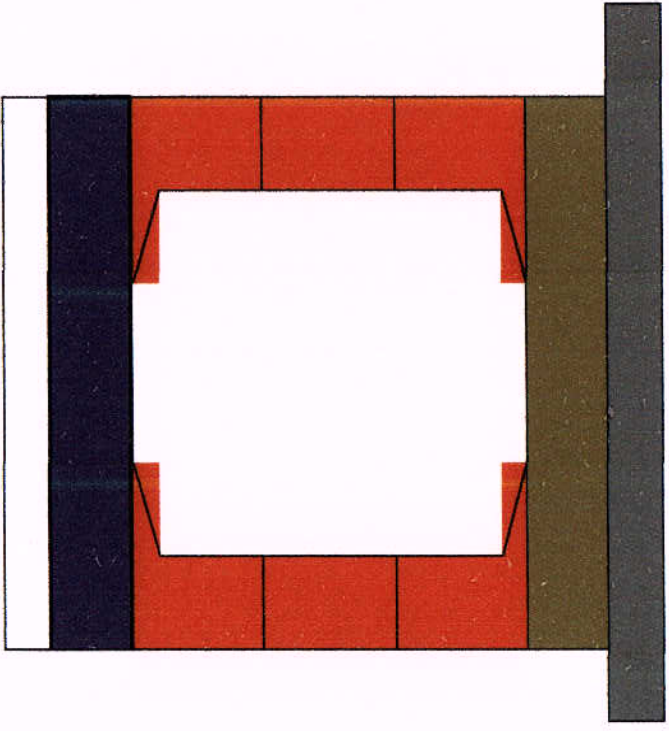



CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC

MINOR BRIDGE AT KM. 34+360 LHS

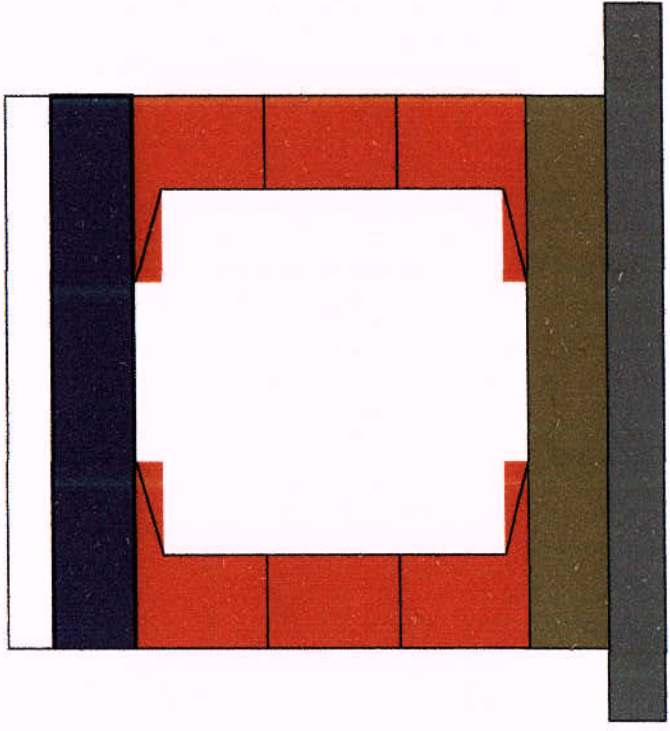


CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC

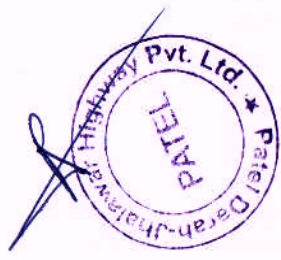

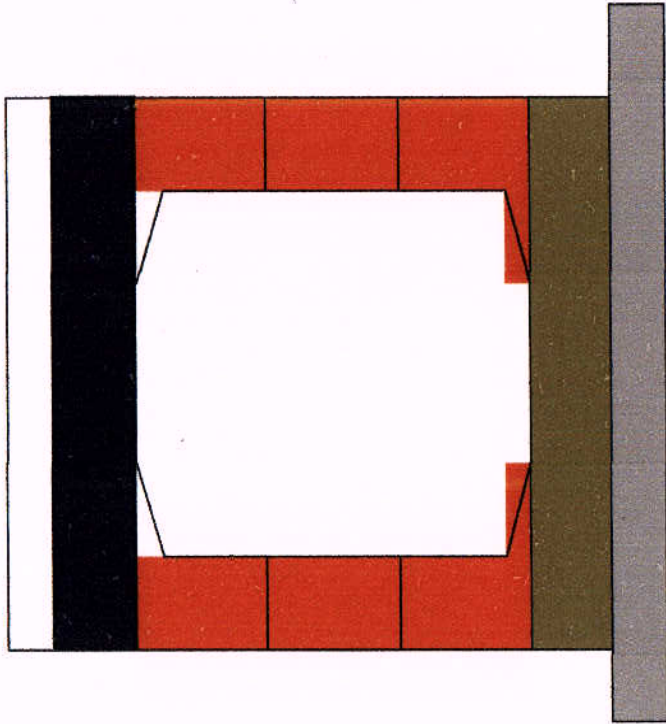


CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC

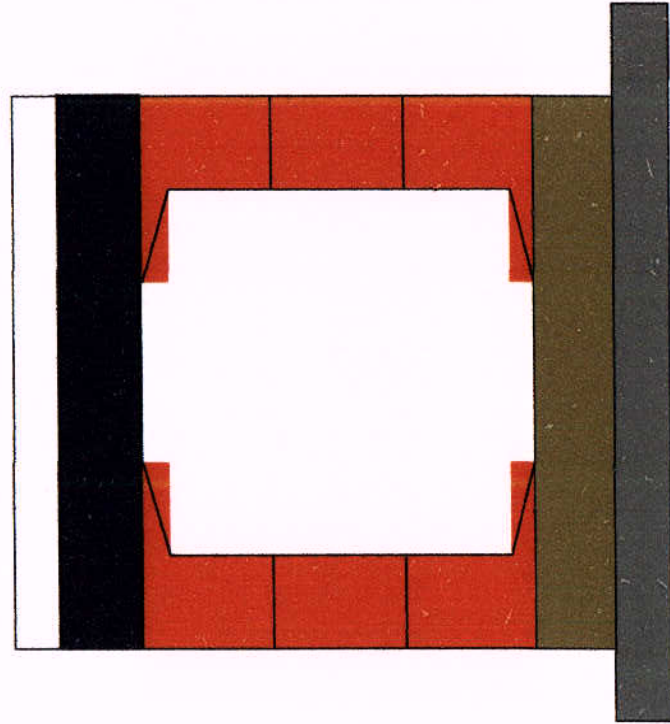

CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC




MINOR BRIDGE AT KM. 49+785 (Main Carriage Way) RHS

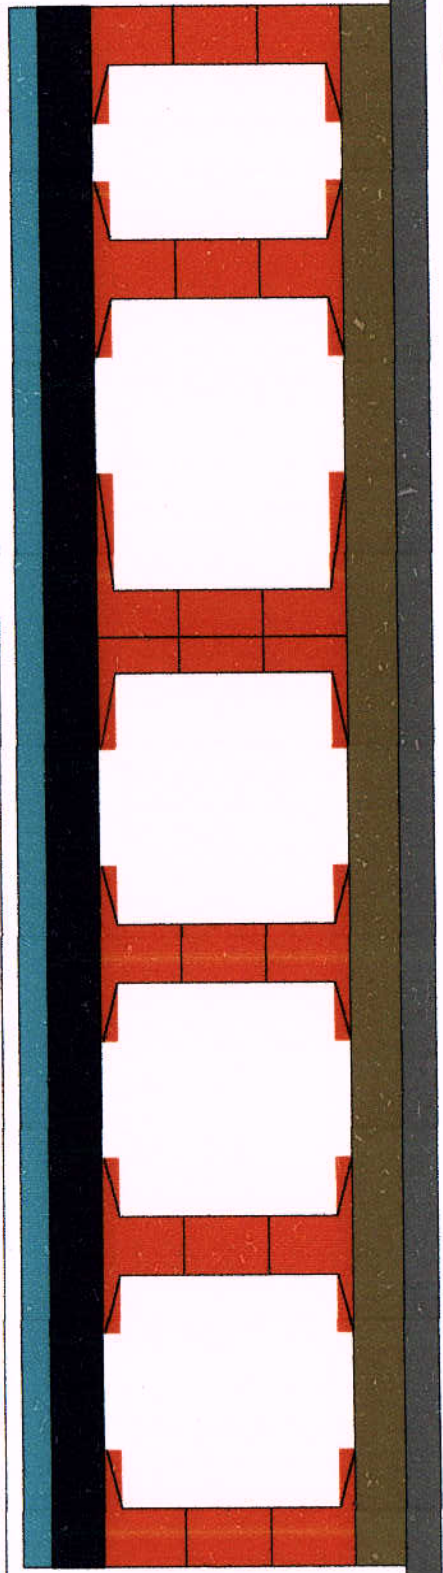


CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC

Project - Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chaiage from 9.860 to 38.740) (Durah-Jhalawar-Jeendhar section) in the State of Rajasthan under MIDP Phase-III on Hybrid Annuity Project (Length 48.880 Km) - Package II


MINOR BRIDGE AT KM. 49+785 (Main Carriage Way) LHS

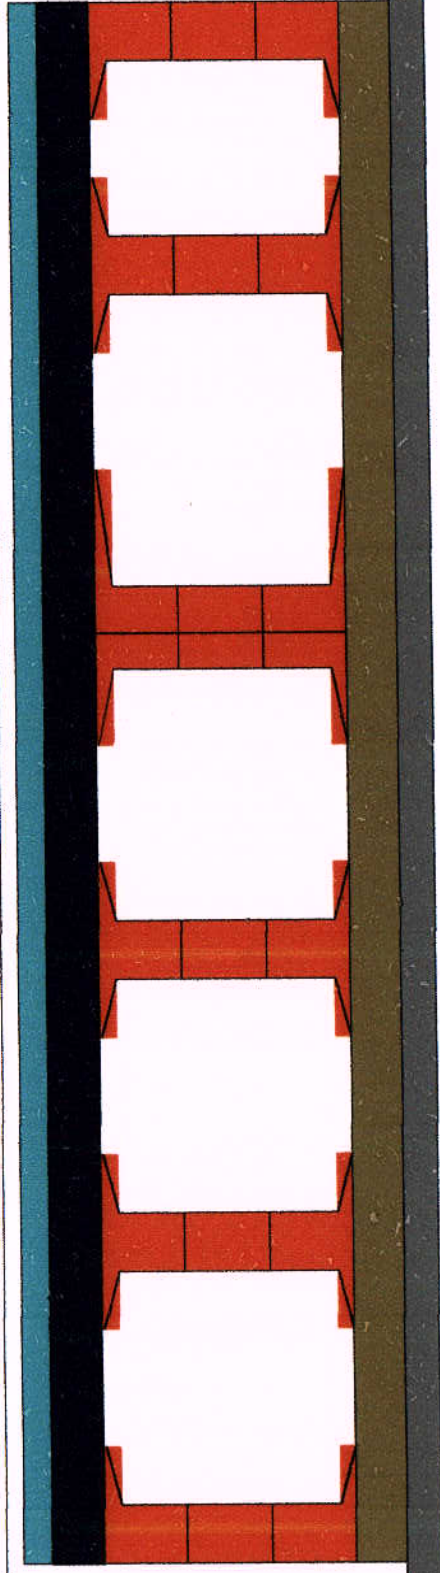

CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC




NO. 1100 IT K. 89+7 (Ser. a Ro. RHE)

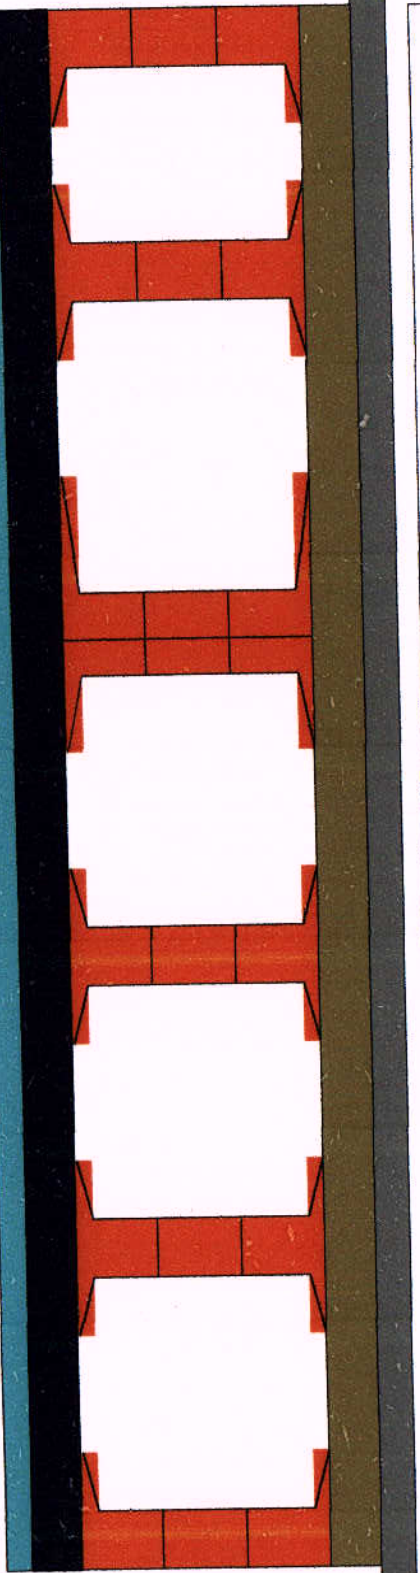

CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC


MINOR BRIDGE AT KM. 49+785 (Service Road) LHS

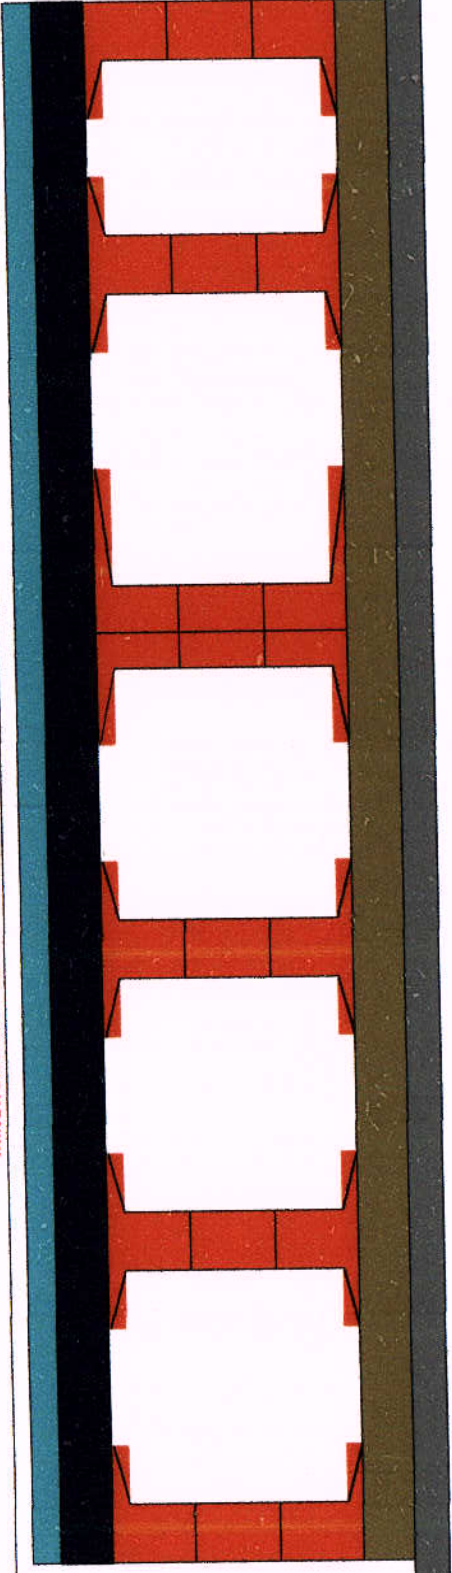

CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC




MINOR BRIDGE A. KM. 54+040 RHS

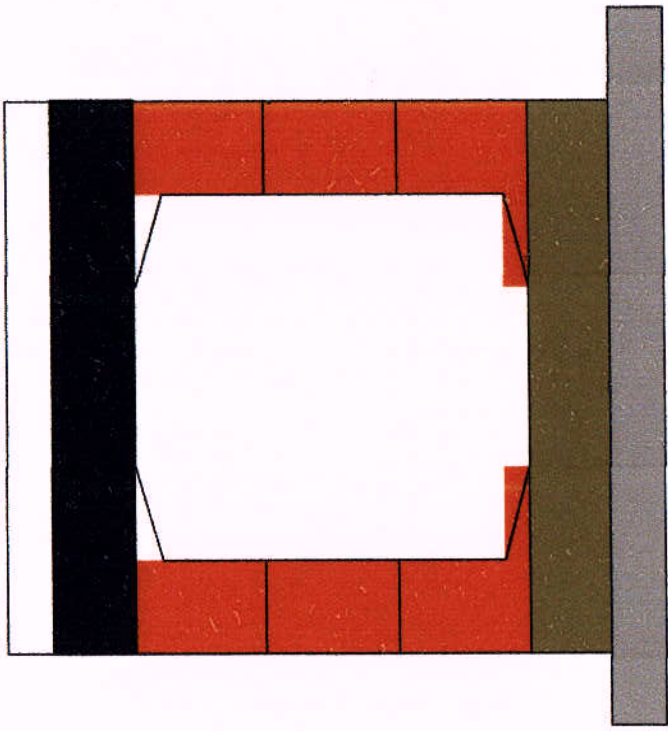

CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC


MINOR BRIDGE AT KM. 54+040 LHS

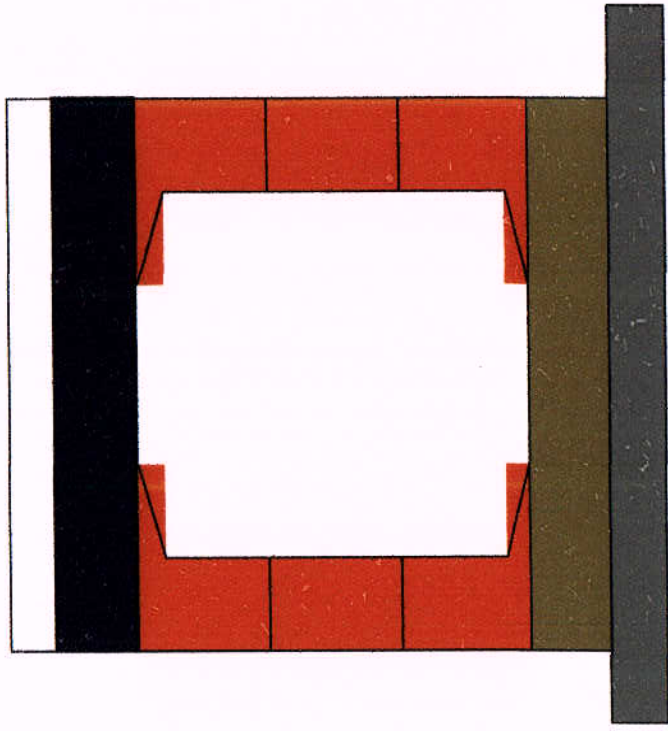

CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC




MINOR BRIDGE AT KM. 54+370 LHS

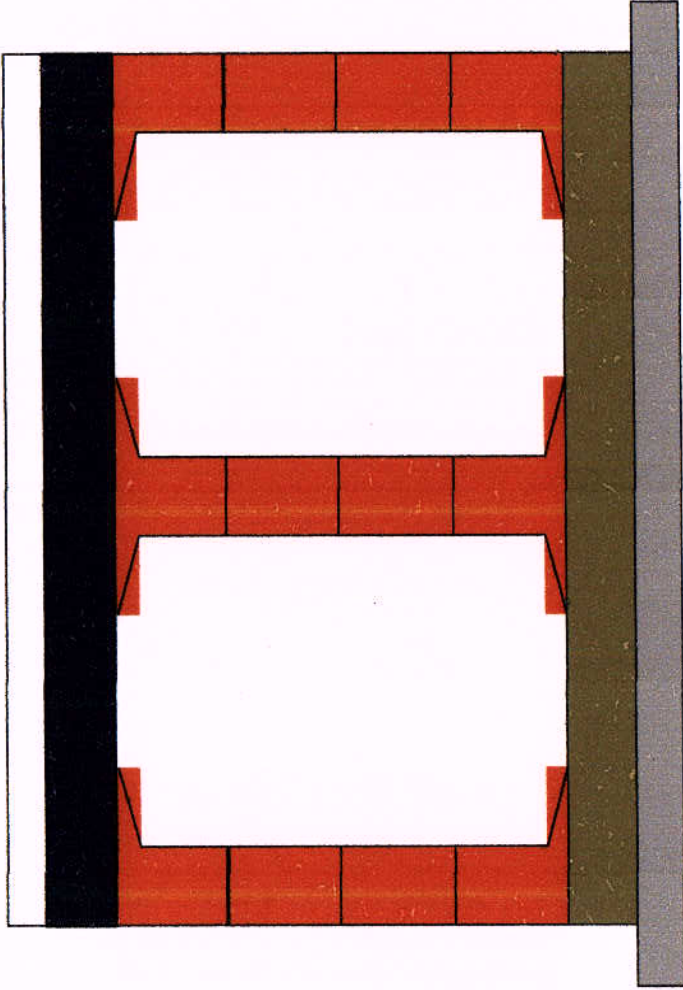

CB
Slab
4th Lift
3rd Lift
2nd Lift
1st Lift
Raft
PCC


MINOR BRIDGE AT KM. 54+070 LHS

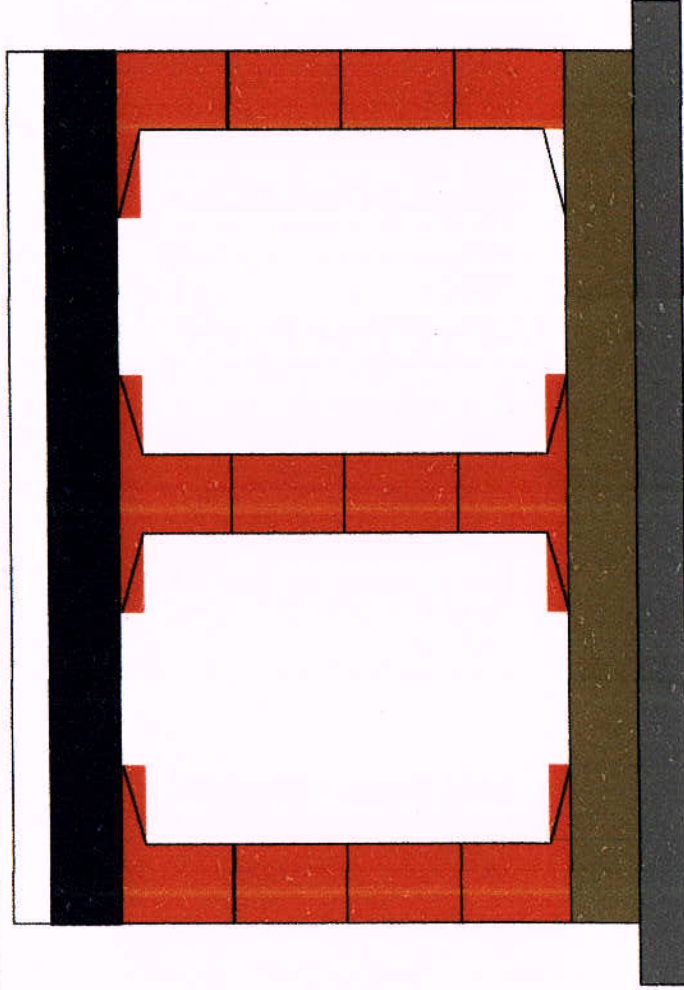

CB
Slab
4th Lift
3rd Lift
2nd Lift
1st Lift
Raft
PCC



VEHICULAR UNDERPASS AT 12+125 A1/A2RHS

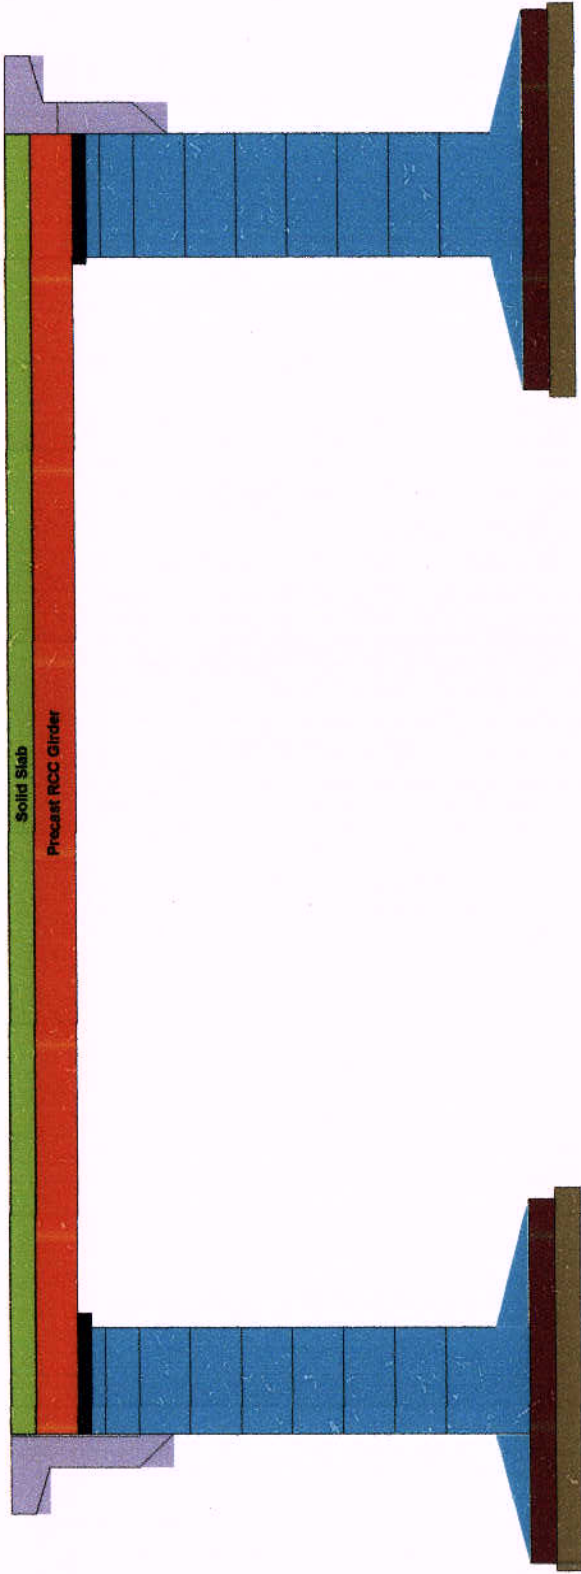

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

VEHICULAR UNDERPASS AT 12+125A1/A2 LHS



Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC







Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Reaft
PCC

VEHICULAR UNDERPASS AT 15+725 A1/A2 LHS




Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Reaft
PCC


 Darah-Jharkhand Highway Pvt. Ltd.
PATEL

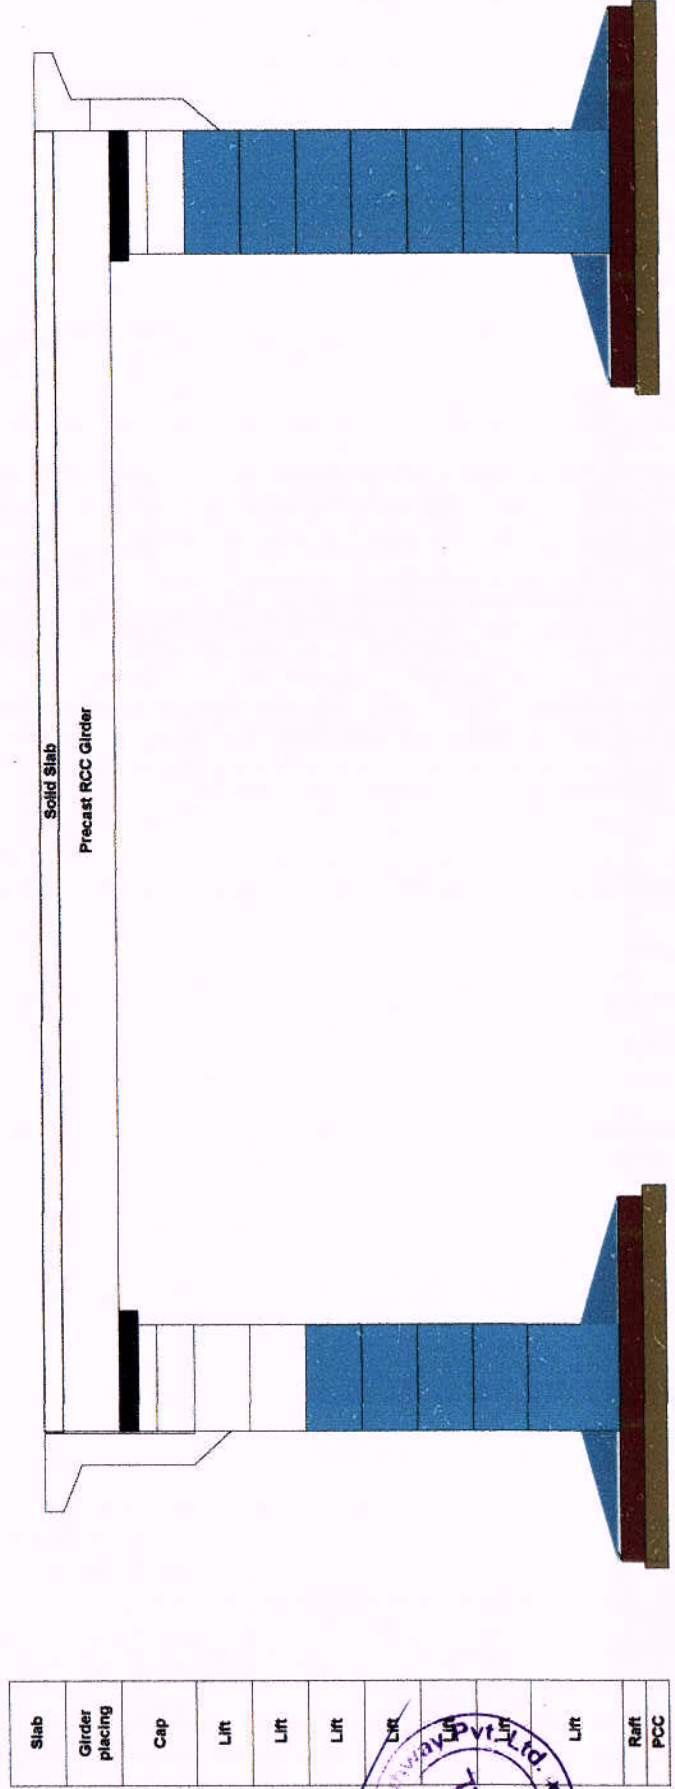


VEHICULAR UNDERPASS AT 25+100 A1/A2 RHS

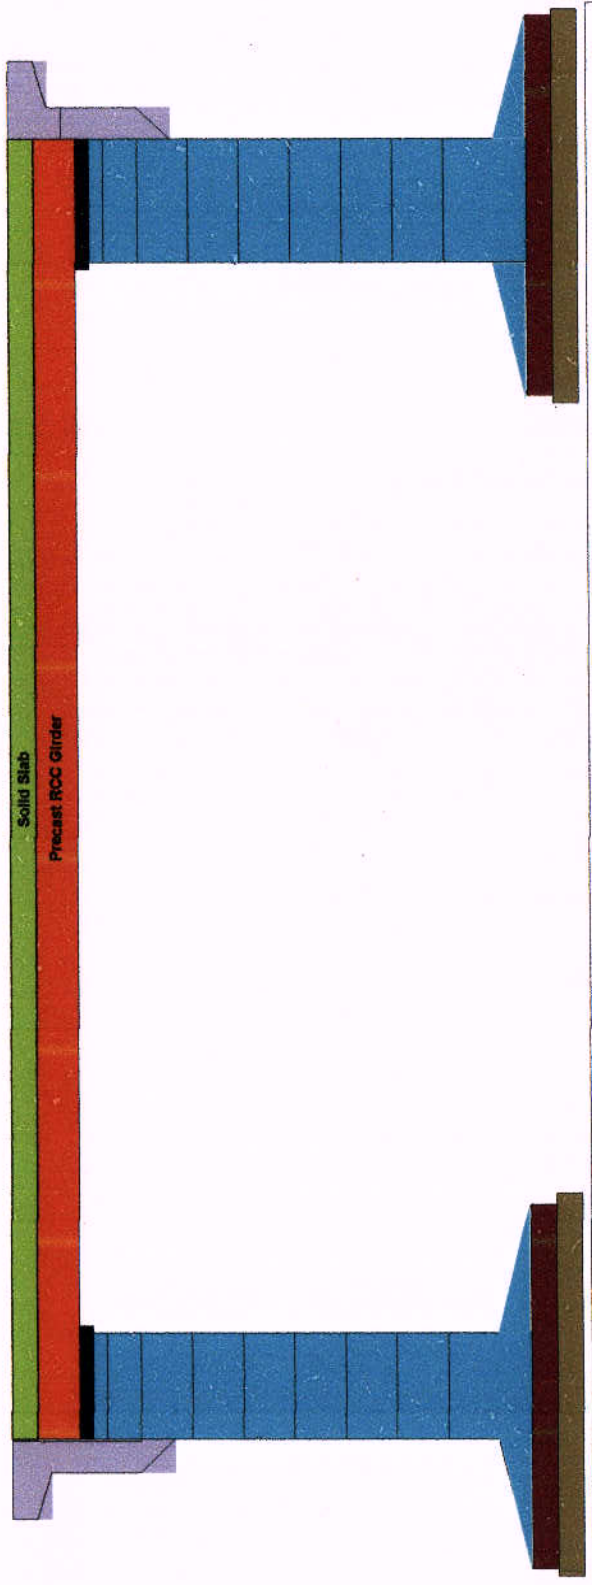

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

VEHICULAR UNDERPASS AT 25+100 A1/A2 LHS

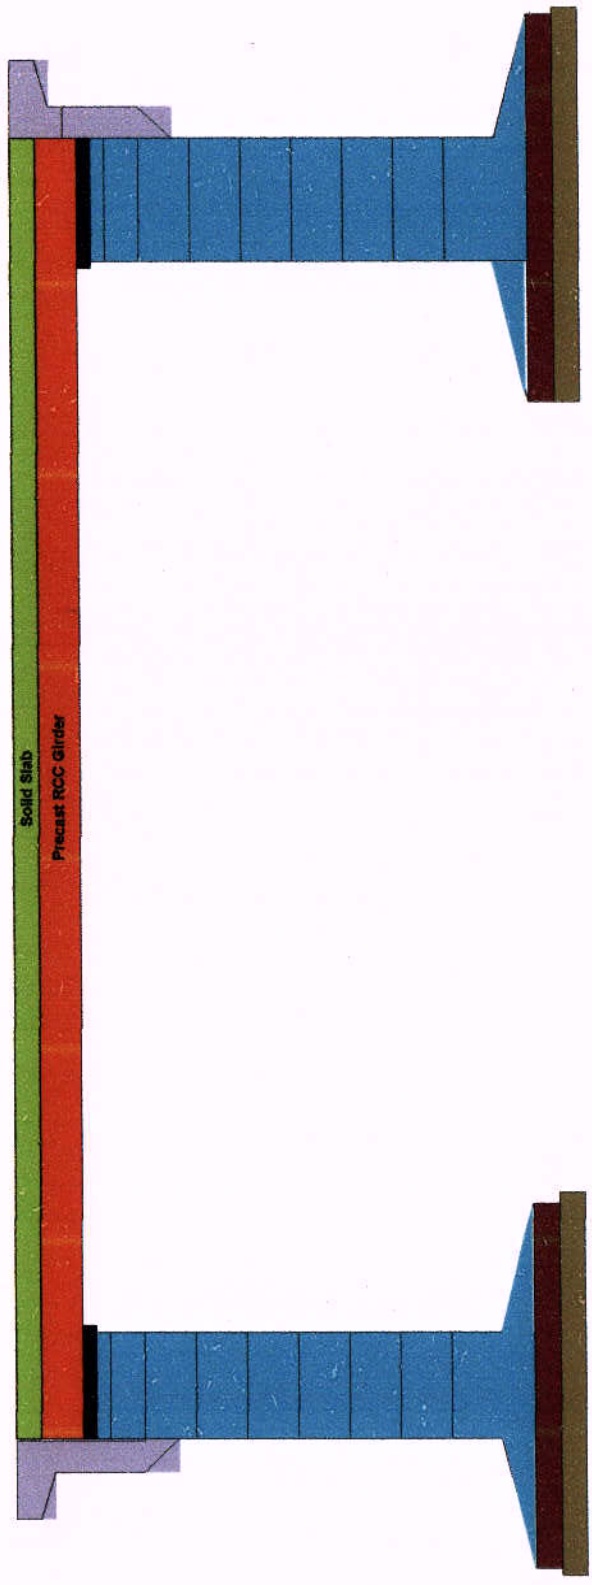

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC







Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

VEHICULAR UNDERPASS AT 27+029 A1/A2 LHS



Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC



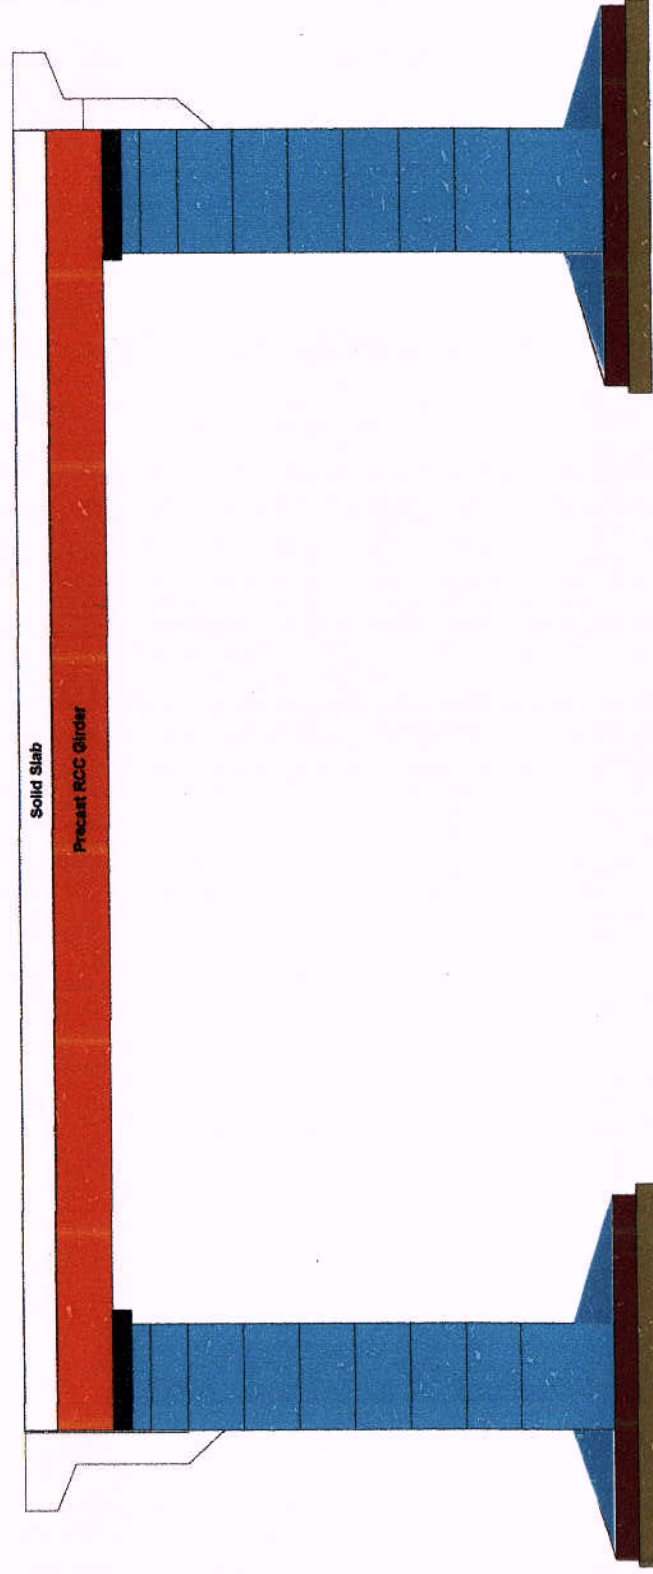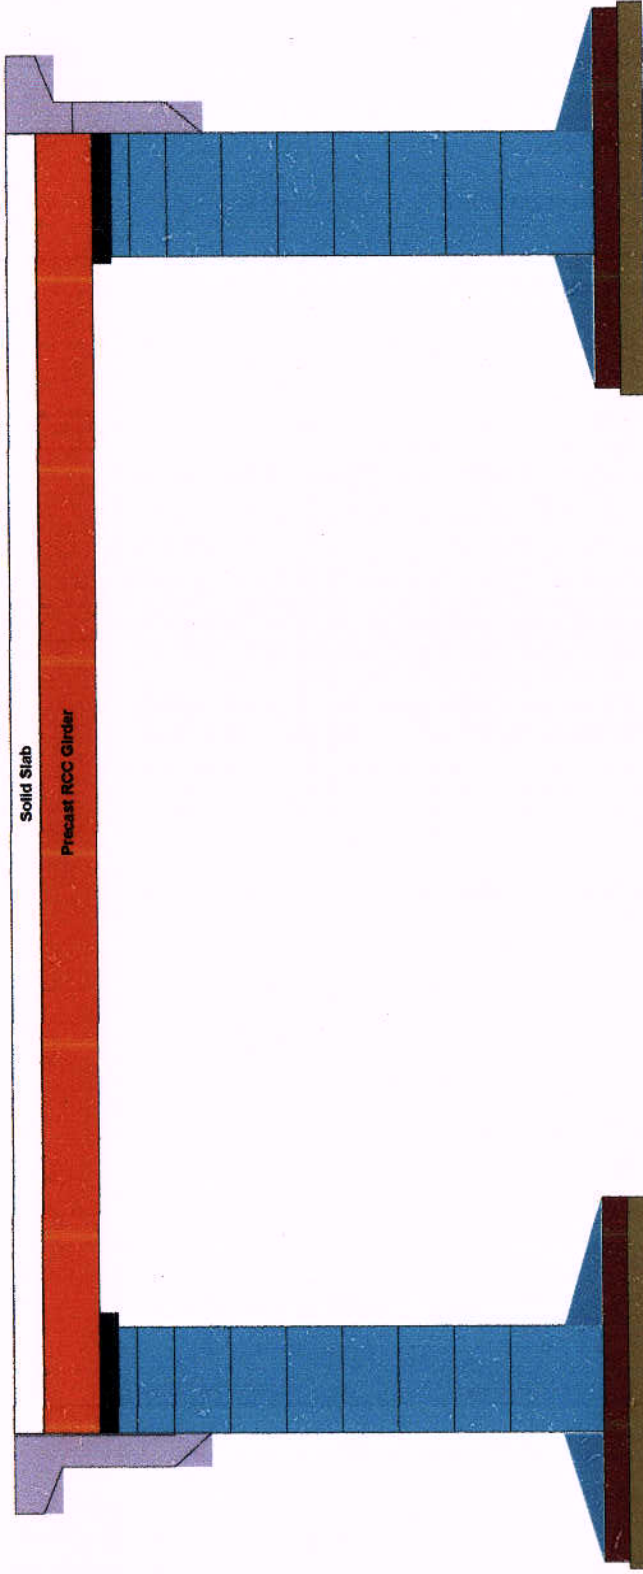

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC



Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC




VEHICULAR UNDERPASS AT 41+095 A1/A2 LHS



VEHICULAR UNDERPASS AT 41+095 A1/A2RHS

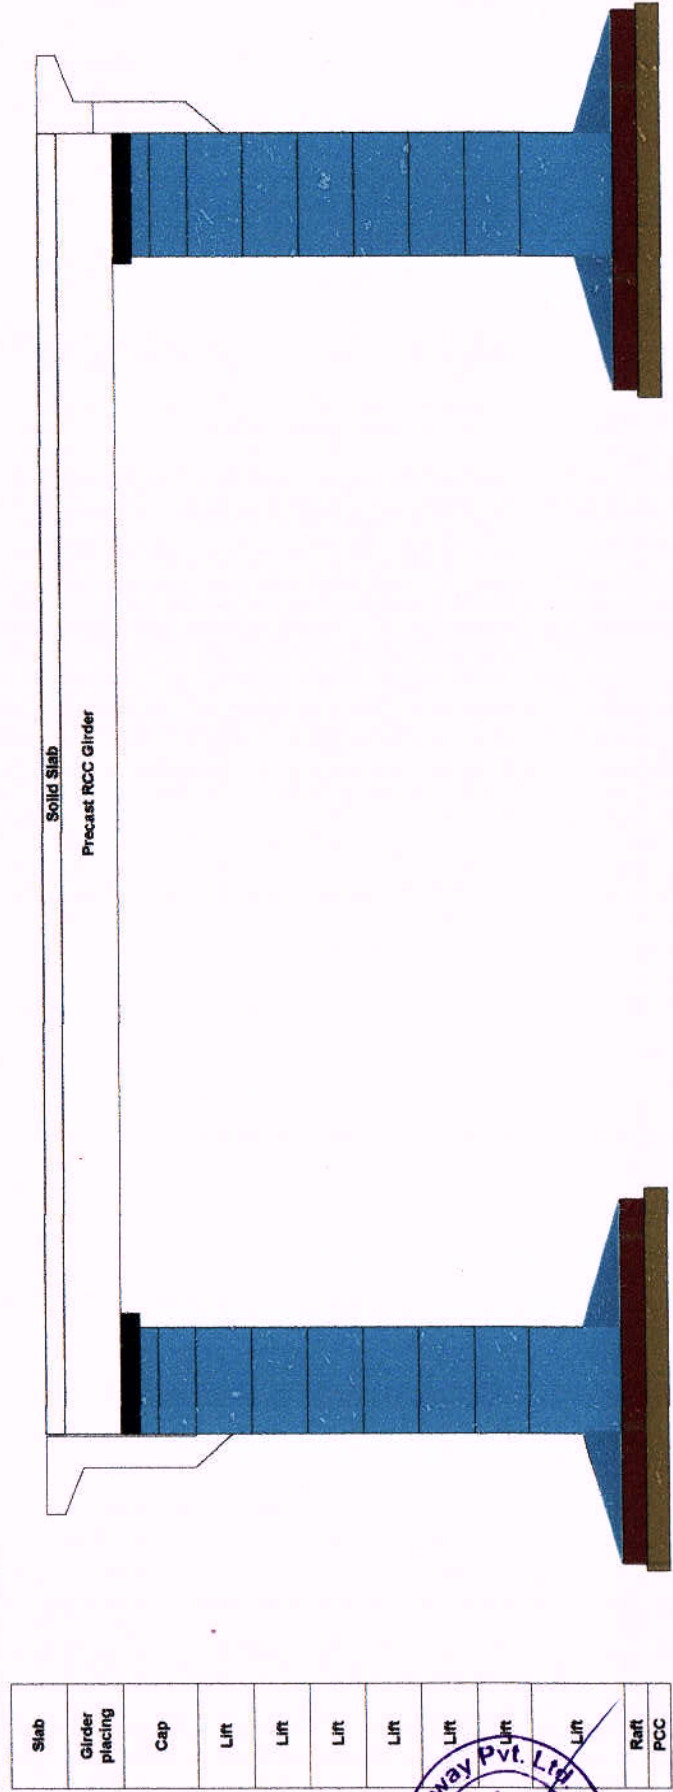

VEHICULAR UNDERPASS AT 49+330A1/ A2 LHS

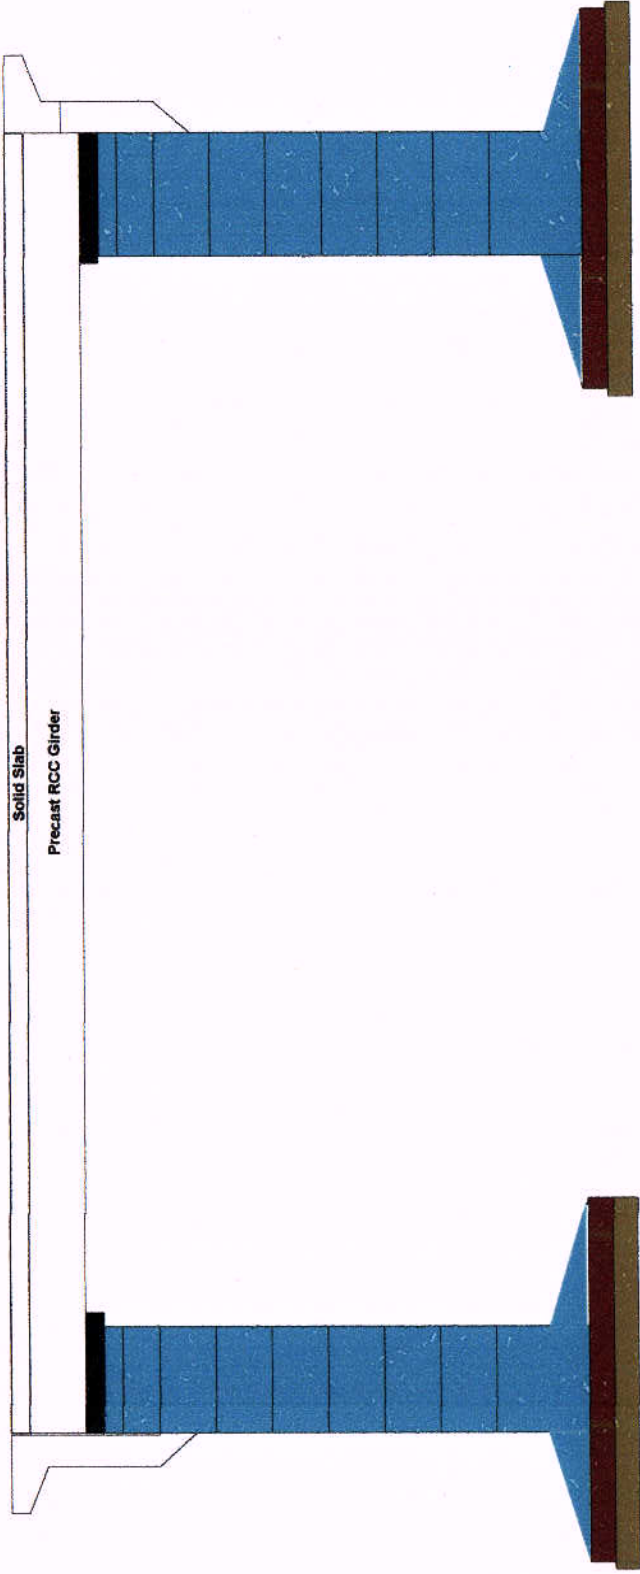


Solid Slab

Precast RCC Girder

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Reft
PCC

VEHICULAR UNDERPASS AT 49+330 A1 /A2RHS

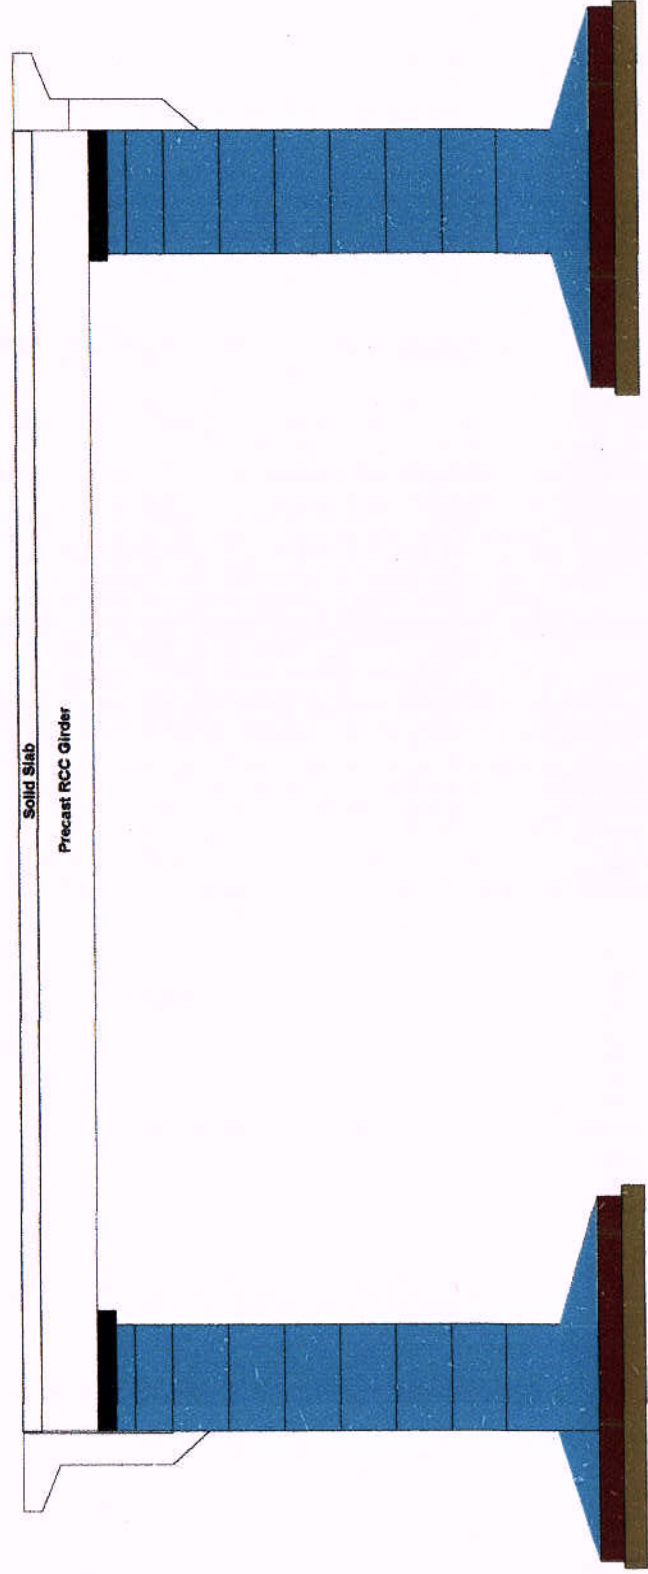


Solid Slab

Precast RCC Girder

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Reft
PCC



VEHICULAR UNDERPASS AT 54+550 A1/A2 LHS

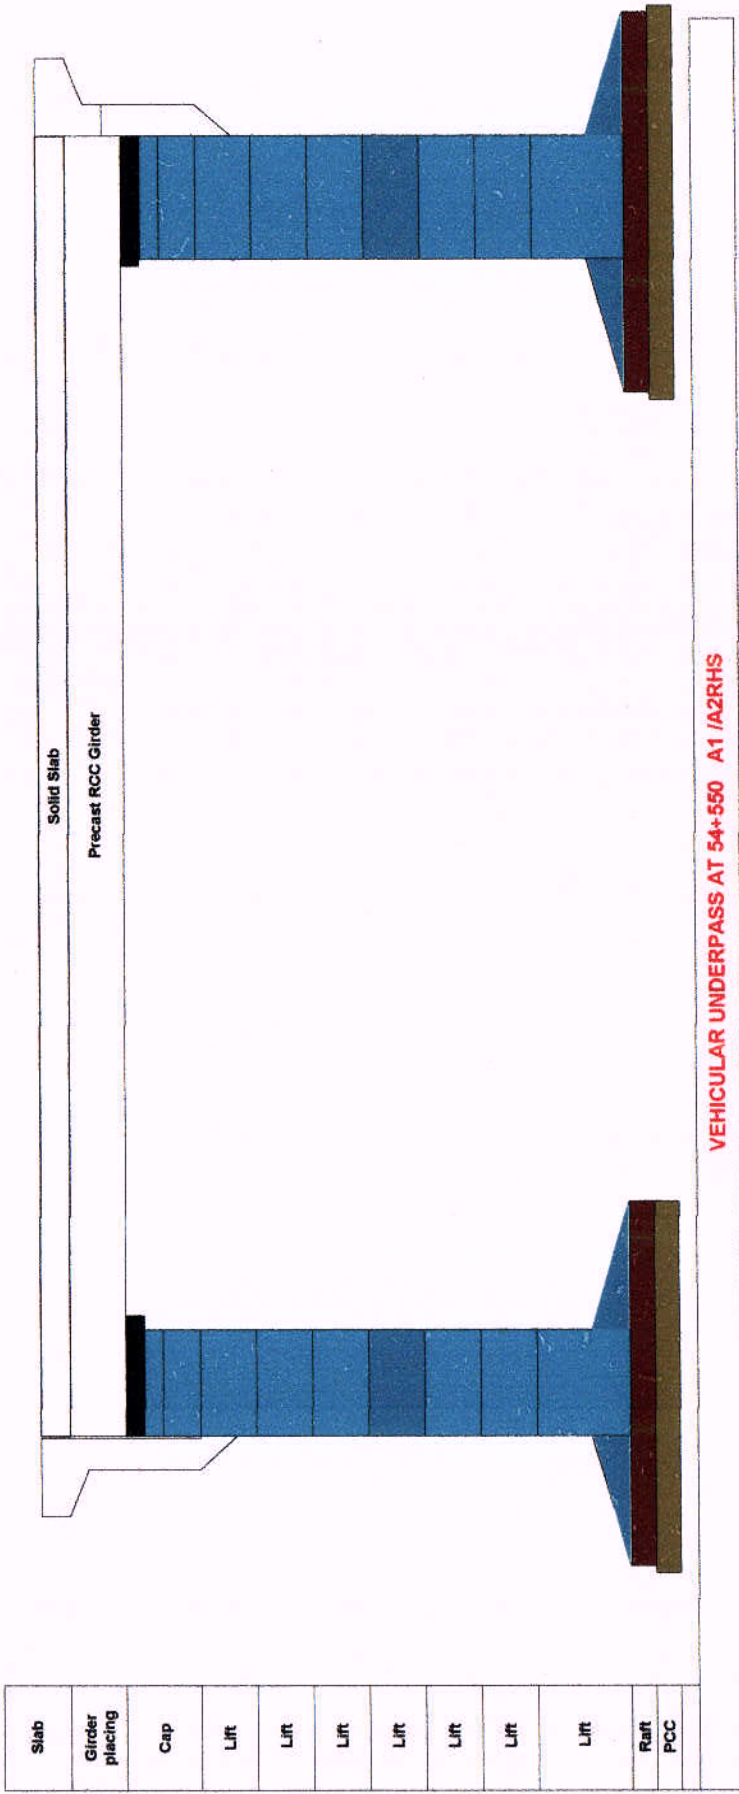

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

VEHICULAR UNDERPASS AT 54+550 A1/A2 RHS






Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC




Project:-Construction of 4-lane Road on NH-12 (New NH-62) from Km 299.000 to 346.640 (Design Chainage from 9.980 to 88.740) (Darrah-Jhalwar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

Chainage
CB
Duct, sub
UR
UR
UR
UR
Reft
PCC
Excavation

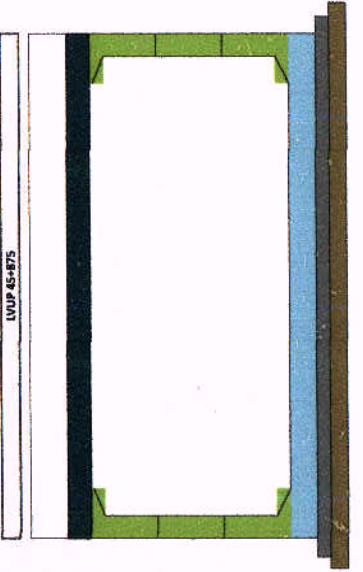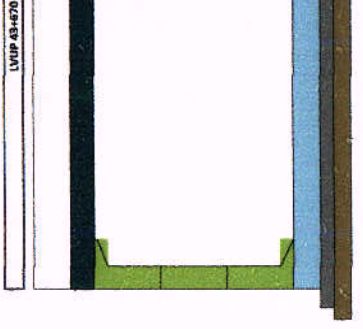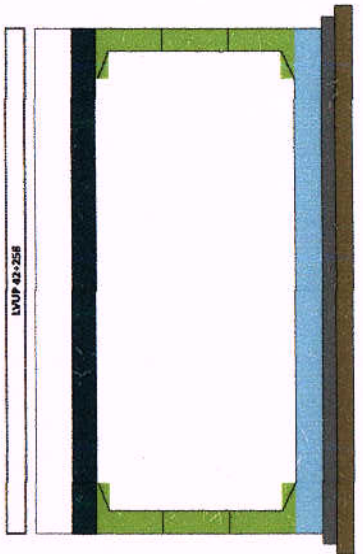


Chainage
CB
Duct, sub
UR
UR
UR
UR
Reft
PCC
Excavation

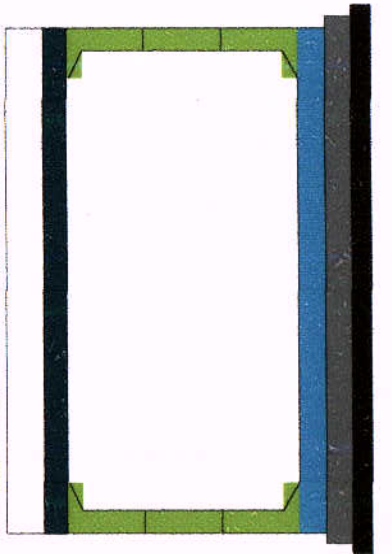


Patel Daraj-Jhalawar Highway Private Limited
Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

RUB CH. 33+585 LHS.

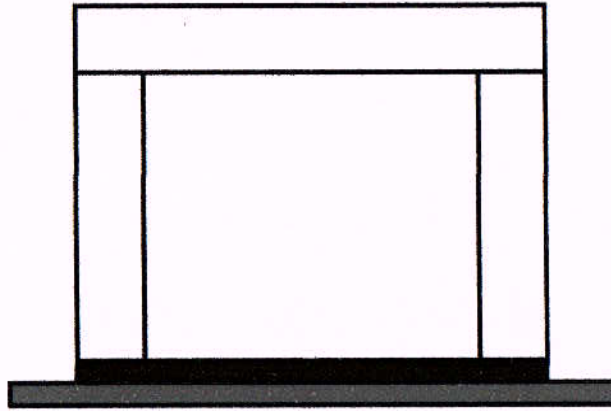

RUB CH. 33+585 RHS.

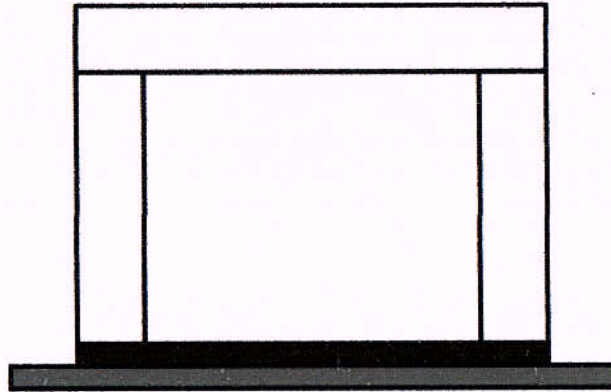


Patel Daraj-Jhalawar Highway Private Limited




Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -

Package II



ROB at 44+158

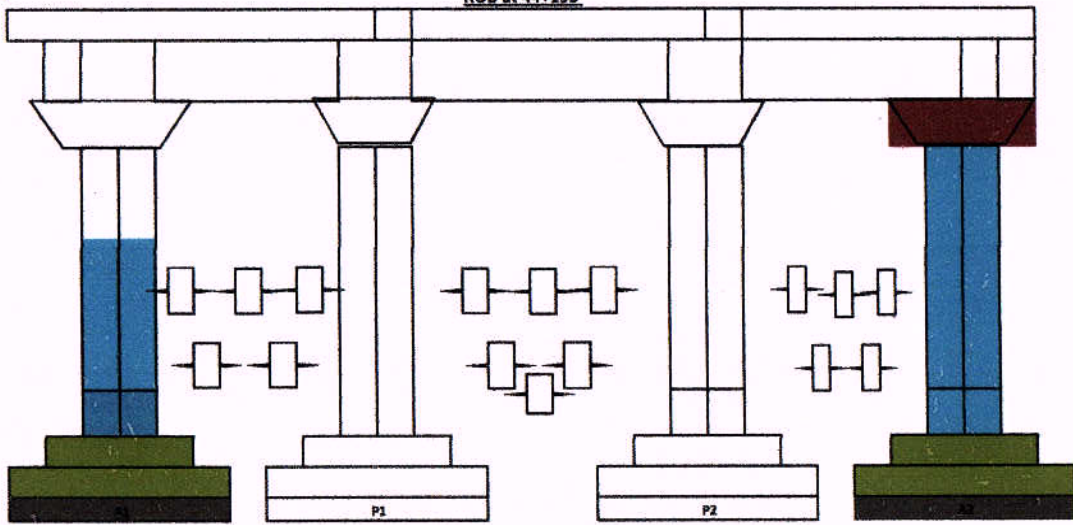



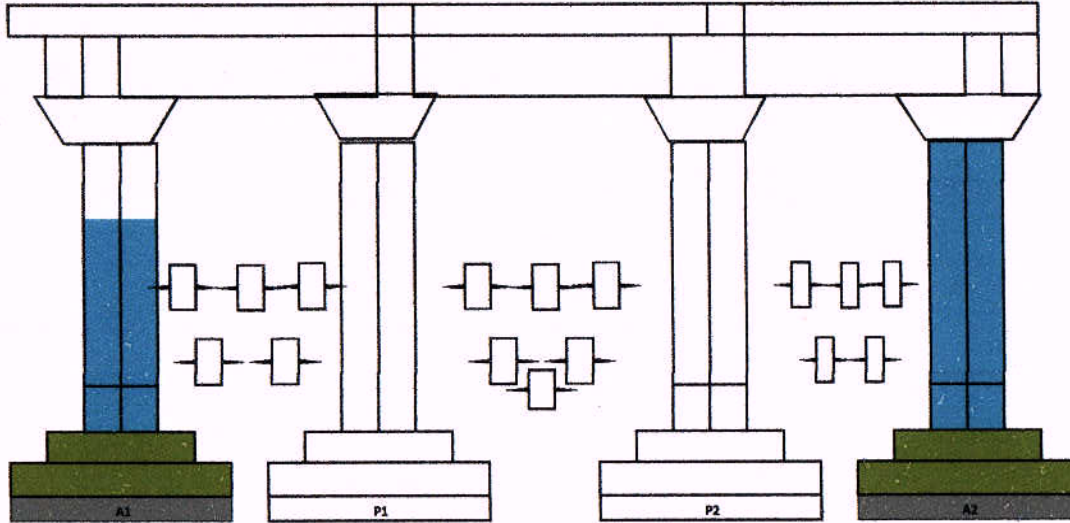






LHS




RHS



Hindrance Details									
Photo	Obstruction Length (m)	LHS-Type of Hindrance	Chainage		RHS-Type of Hindrance	Obstruction Length (m)	Photo	Expected Date of Clearance	Remark's
			From	To					
			9+980	10+020	House, Boundary wall				Award approval is pending from NHAI. PQC is completed but ROW are affected.
		House	10+640	10+650					Award approval is pending from NHAI. PQC is completed but ROW are affected. Measurement done in July-2019.
		House	10+670	10+680					Award approval is pending from NHAI. PQC is completed but ROW are affected. Measurement done in July-2019.
		Well	10+685	10+690					Award approval is pending from NHAI. PQC is completed but ROW are affected. Measurement done in July-2019.
			10+890	11+000	Compensation problem				Dispute in DM court. PQC is completed but ROW are affected.
		Boundry wall, House	11+100	11+700					Stay order by civil court. PQC inprogress but ROW are affected.
			11+330	11+350	Mango Tree				Award approval pending from NHAI.
	+30	House	12+315	12+345					Award approval is pending from NHAI.
	+50	Shop, Boundary & Land Compensation problem	23+800	23+850					Well & Tubewell difference award prepared by CALA and send to NHAI for approval.
	+100	Structure, Land	24+000	24+100					Difference of Agriculture / commercial Land compensation are prepared & send to NHAI for approval.
			24+470	24+520	House ,Temple, Boundary wall, Hauz, etc.	+50			Some Villagers are unsatisfied for award done by NHAI. Community Land disbursement of compensation pending from LAO.
	+80	Hand pump,Toilet, Verandah,Sewer tank, Boundary wall, etc	24+500	24+580					Some Villagers are unsatisfied for award done by NHAI. Community Land disbursement of compensation pending from LAO.
	+80	Hand pump,Toilet, Verandah,Sewer tank, Boundary wall, etc	24+850	24+930					Some Villagers are unsatisfied for award done by NHAI. Community Land disbursement of compensation pending from LAO.
			26+150	26+200	Mango & lemon Tree	+50			Nandsingh Madhavsingh Awasthi under process between LAO & NHAI




Hindrance Details

No.	Photo	Obstruction Length (m)	LHS-Type of Hindrance	Chainage		RHS-Type of Hindrance	Obstruction Length (m)	Photo	Expected Date of Clearance	Remark's
				From	To					
15			DLC issue	32+500	36+000	DLC issue				Supplementary fruits , non fruits & boundary wall survey done but award pending between LAO & NHAI.
16		+100	Land	41+200	41+300					Compansation pending due to High court stay. Rekha Lalwani NHAI Letter No. 7500 dated 06.11.2018
17			DLC issue	51+700	52+100	DLC issue				Supplementary fruits , non fruits & boundary wall survey done but award pending between LAO & NHAI.
Total		+440					+100			
Total : (LHS + RHS)/2				0.270						




KEY PLAN OF THE PROJECT

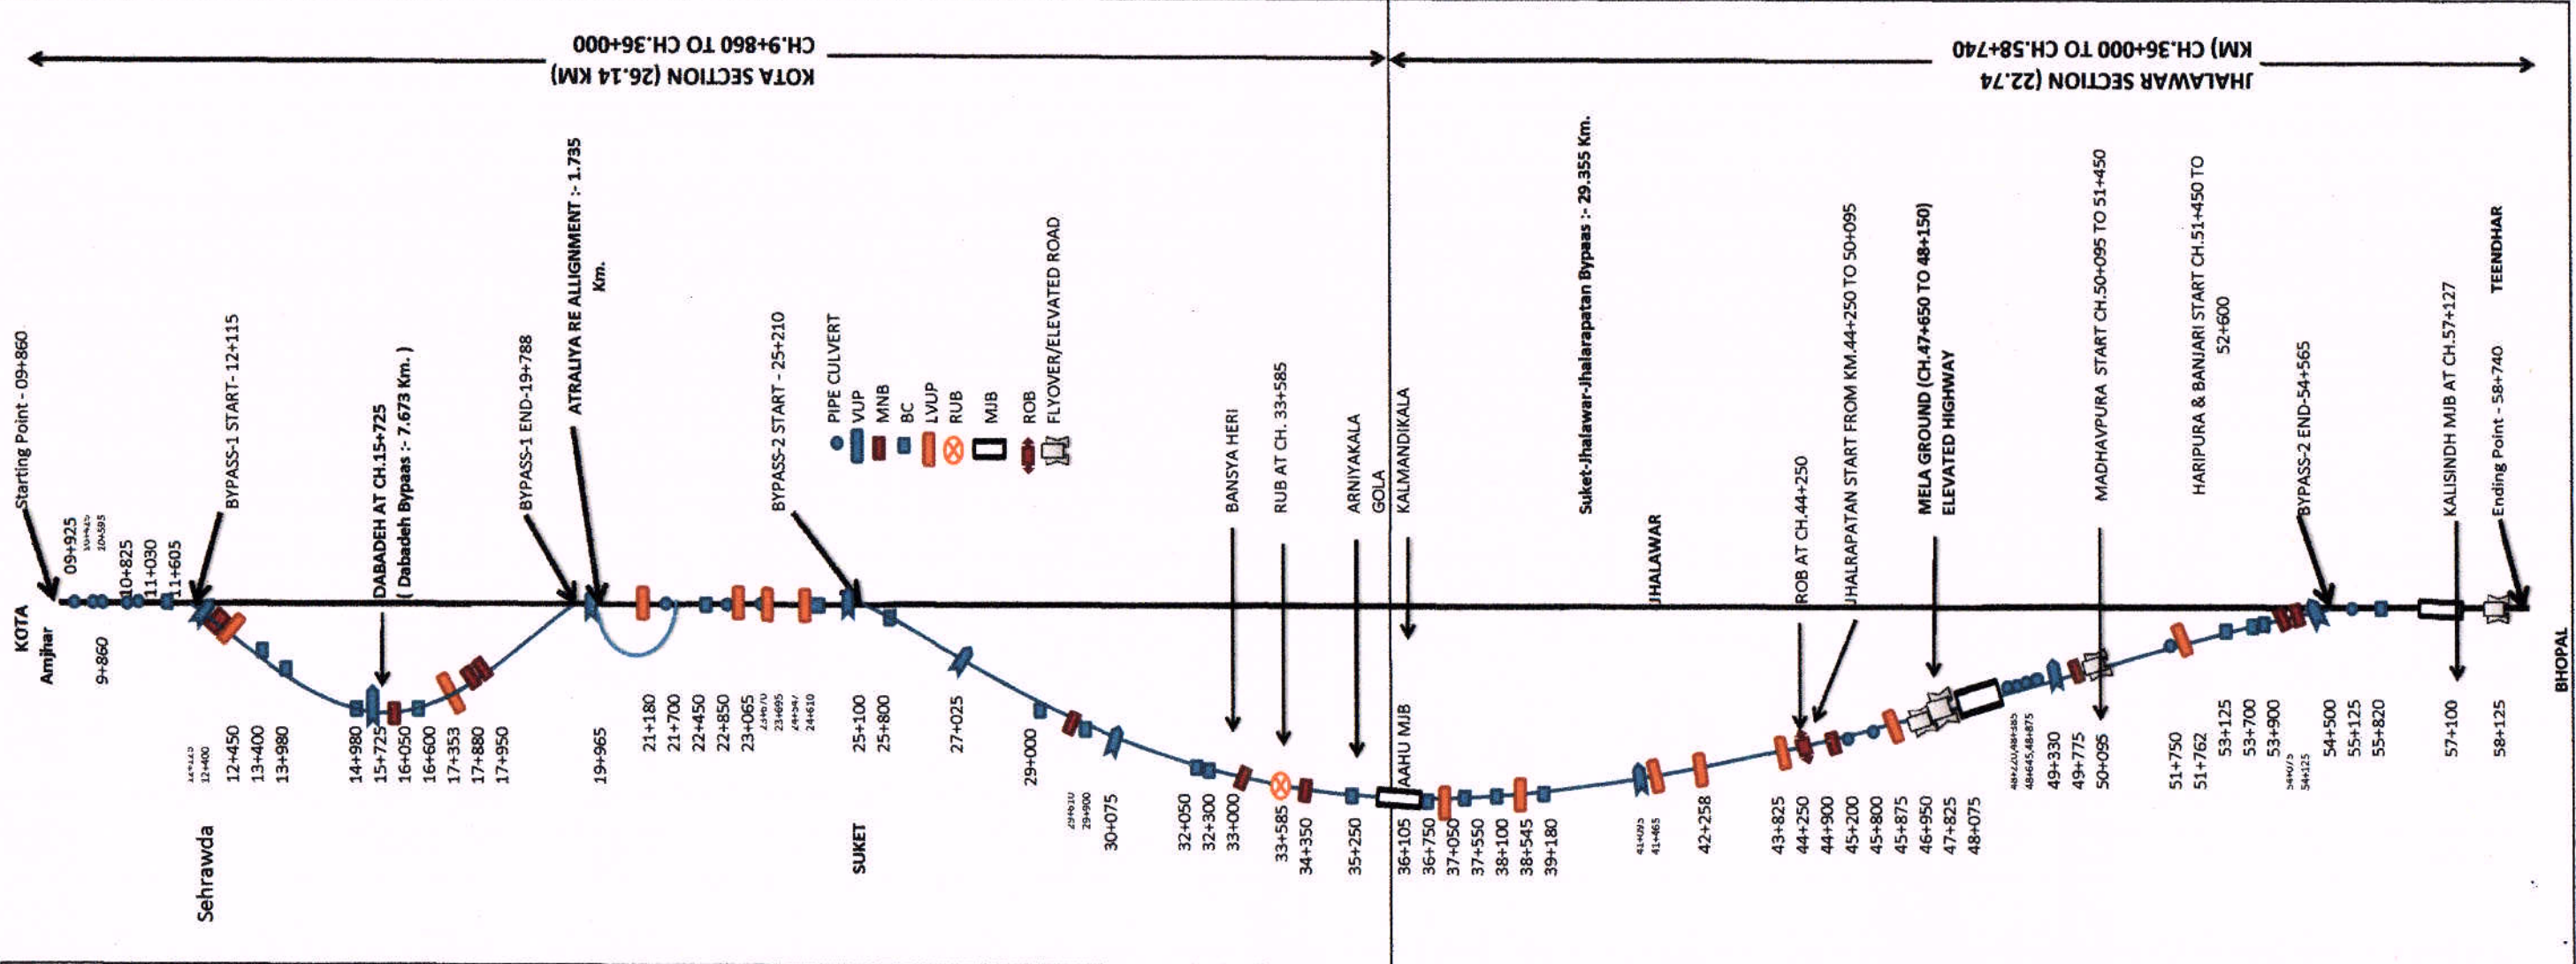




S- CURVE OF FINANCIAL PROGRESS AS PER SUBMITTED PROGRAMME

MONTH	Dev. Period	Jun-18	Jul-18	Aug-18	Sep-18	Oct-18	Nov-18	Dec-18	Jan-19	Feb-19	Mar-19	Apr-19	May-19	Jun-19	Jul-19	Aug-19	Sep-19	Oct-19	Nov-19	Dec-19	Jan-20	Feb-20	Mar-20	Apr-20	May-20	Jun-20	Jul-20	Aug-20	Sep-20	Oct-20	Nov-20	Dec-20	Jan-21	Feb-21	Mar-21	Apr-21	May-21	Jun-21	Jul-21	Aug-21	Sep-21	
PLANNED (MONTHLY)	22.60	25.56	17.37	22.79	14.34	18.41	24.74	29.81	30.39	24.30	29.31	17.05	29.71	36.10	25.60	19.42	14.98	19.52	37.01	39.72	35.29	39.27	17.50	1.92	0.01	6.48	6.60	4.92	7.37	32.49	33.63	35.84	45.65	60.64	63.42	61.84	61.58	56.64	25.79	13.16	14.69	
PLANNED (CUMULATIVE)	22.60	48.16	65.54	88.33	102.67	121.08	145.82	175.63	206.02	230.32	259.62	276.67	306.38	342.48	368.09	387.50	402.48	422.00	459.01	498.72	534.01	573.28	590.79	592.70	592.71	599.19	605.99	610.90	618.28	650.77	684.39	720.23	765.88	826.51	889.93	951.77	1,013.35	1,070.00	1,095.79	1,108.95	1,123.64	
Achieved (MONTHLY)	20.08	22.77	15.55	20.27	12.81	16.39	22.12	26.49	27.01	21.79	26.11	15.15	26.41	32.07	24.23	18.03	14.07	18.05	34.58	34.03	61.64	41.36	35.65	-	1.35	8.36	16.15	25.24														
Achieved (CUMULATIVE)	20.08	42.85	58.39	78.66	91.47	107.86	129.98	156.47	183.48	205.27	231.38	246.53	272.94	305.01	329.24	347.27	361.34	379.39	413.97	448.00	509.64	551.00	586.65	588.65	588.00	596.36	612.51	637.75														

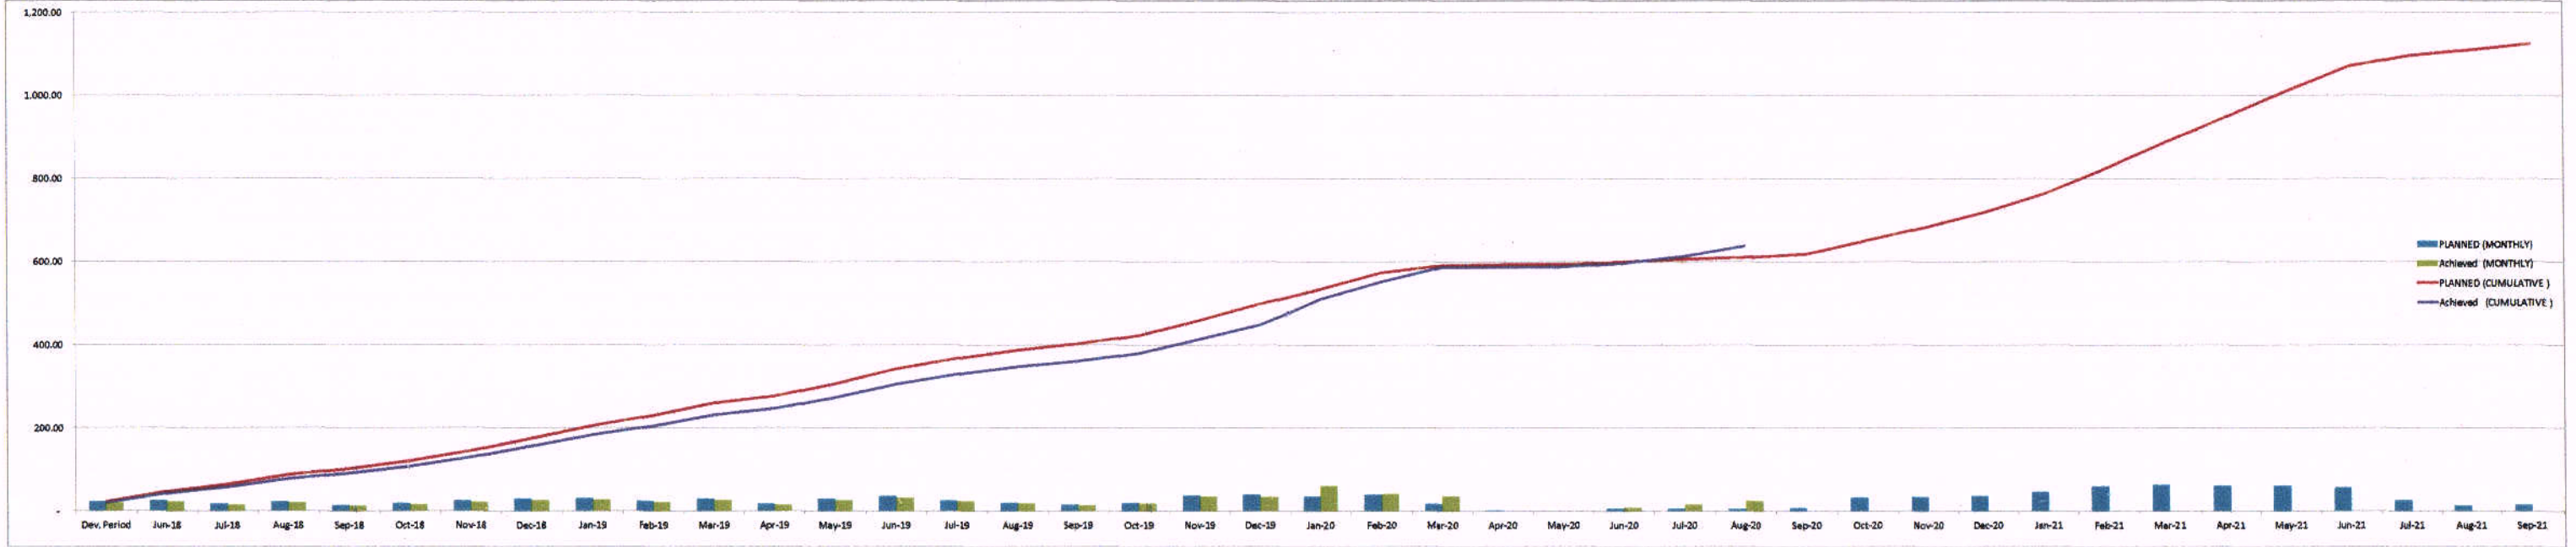

Strip Chart
Darah-Jhalawar-Teendhar section

Index	C & G	EMB	SG	GSB	DLC	PQC
	Length 47.320Km	Length 31.20Km	Length 27.90Km	Length 26.770Km	Length 22.688Km	Length 19.506Km

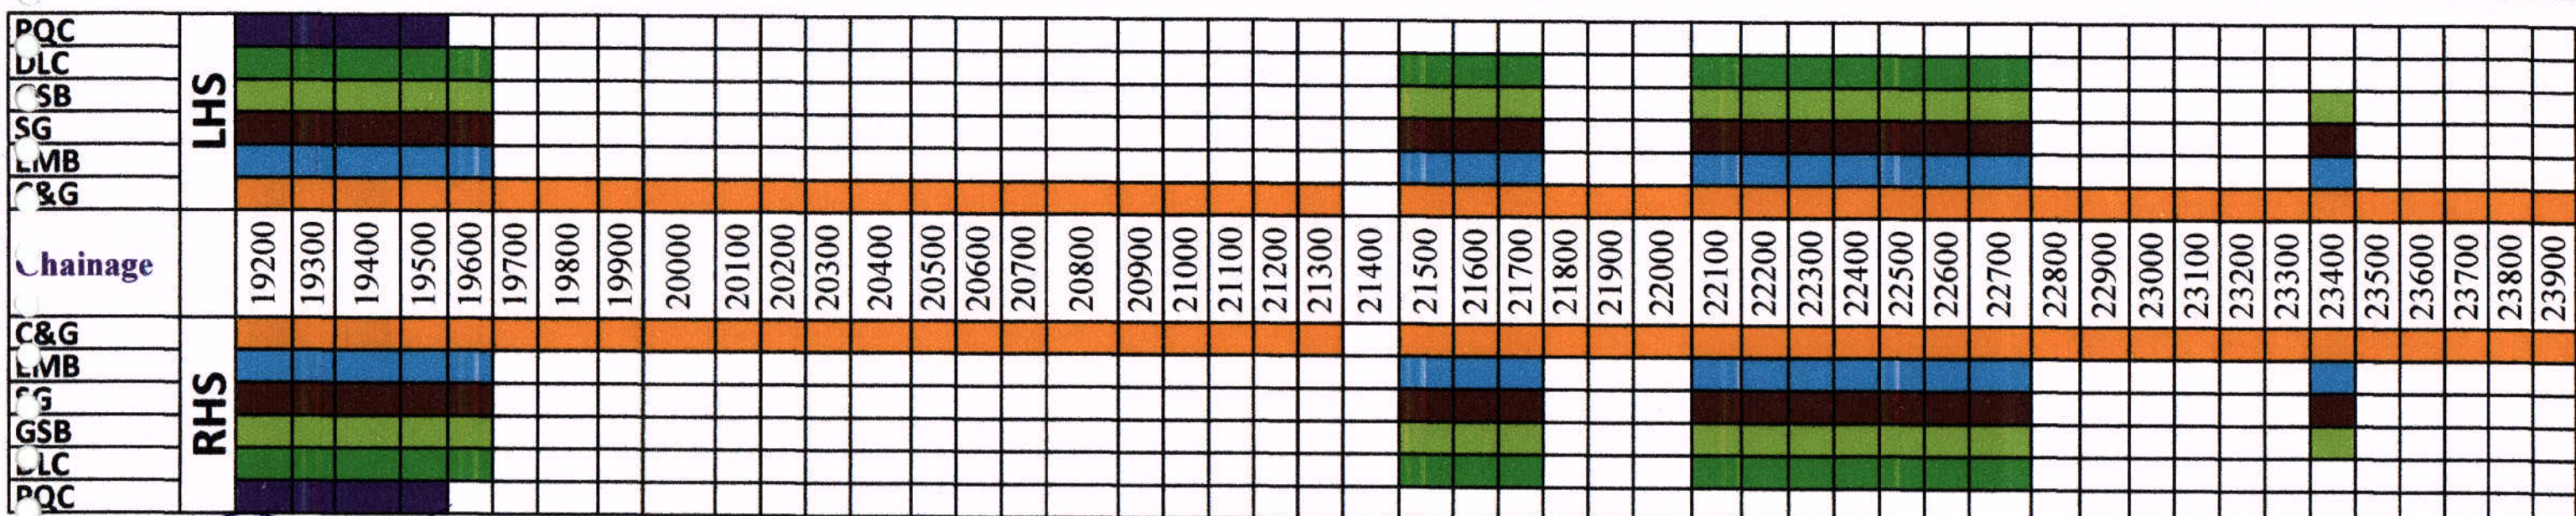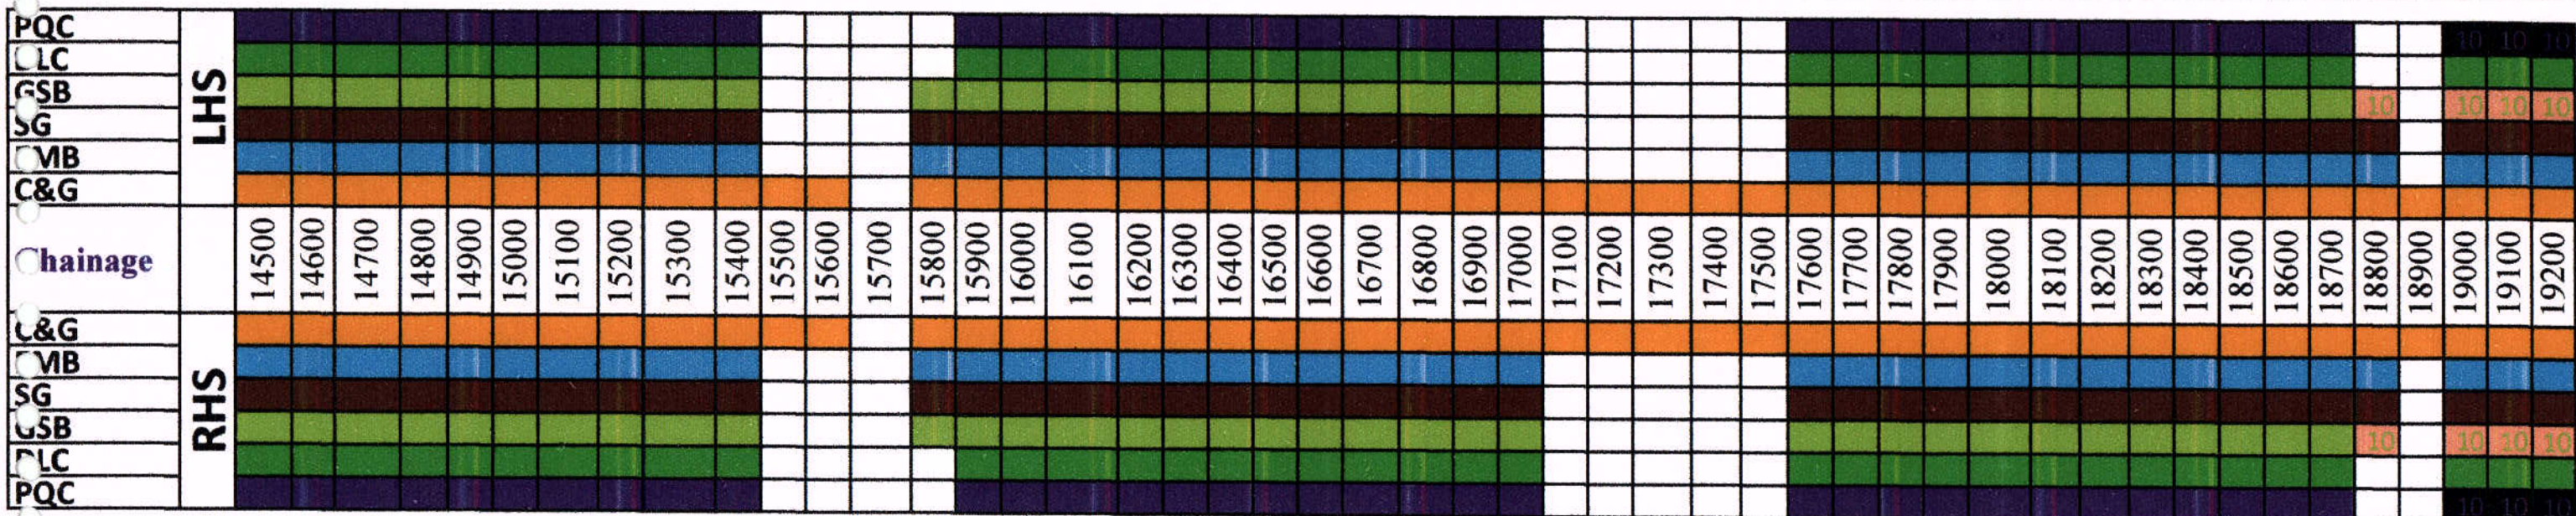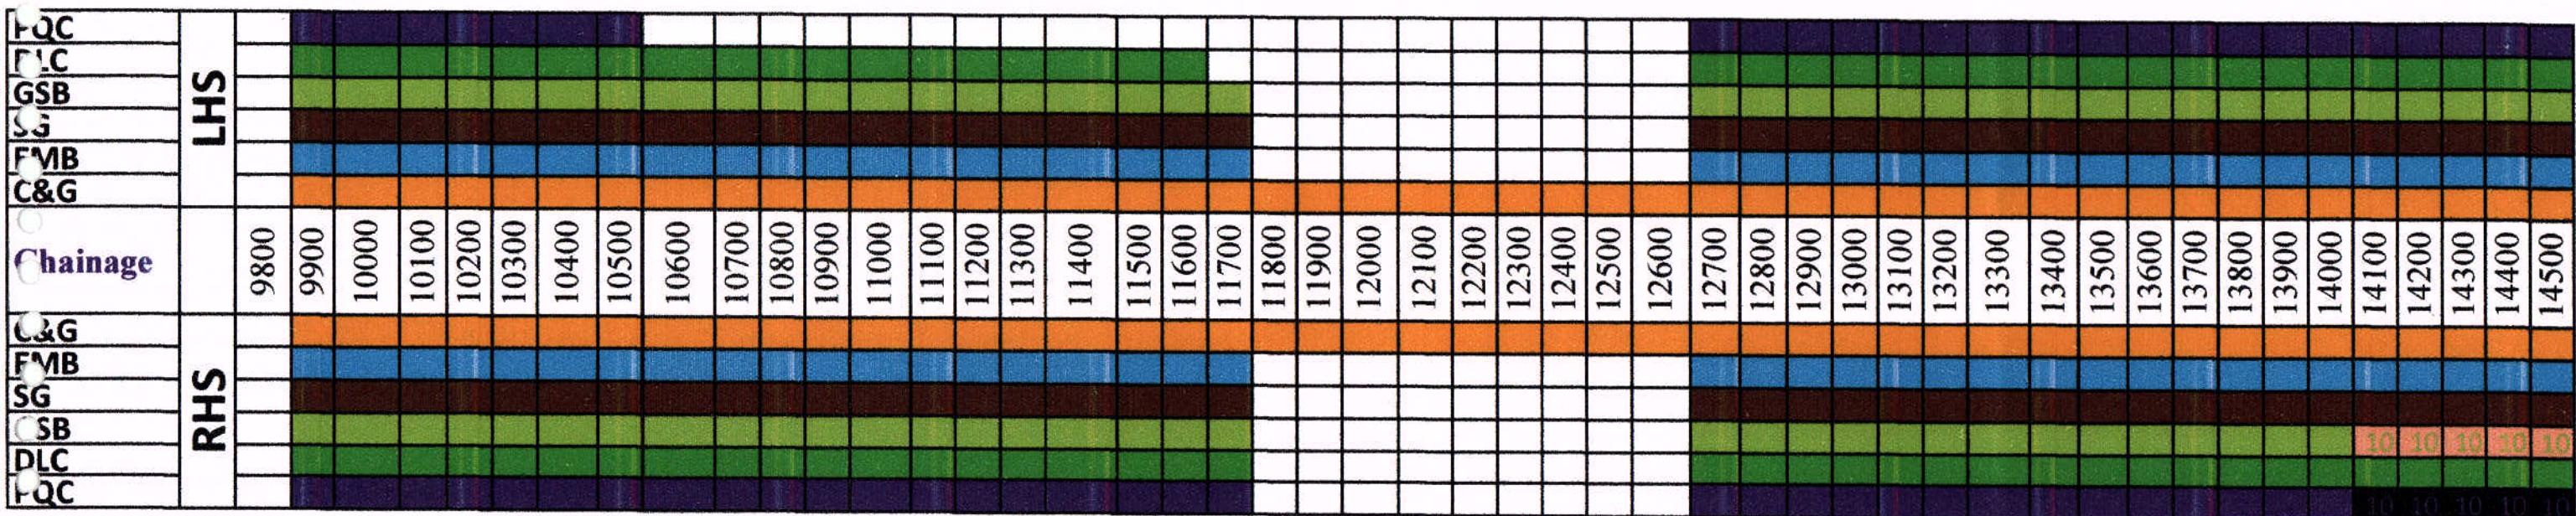

Index	C & G	
	Length	47.320Km

EMB	
Length	31.20Km

SG	
Length	27.90Km

GSB	
Length	26.770Km

DLC	
Length	22.688Km

PQC	
Length	19.506Km

PQC	LHS	
DLC		
GSB		
SG		
LMB		
C&G		
Chainage		23900
C&G	RHS	
LMB		
SG		
GSB		
DLC		
PQC		
Chainage		28600

PQC	LHS	
DLC		
GSB		
SG		
EMB		
C&G		
Chainage		28600
C&G	RHS	
EMB		
SG		
GSB		
DLC		
PQC		
Chainage		33300

PQC	LHS	
DLC		
GSB		
SG		
EMB		
C&G		
Chainage		33300
C&G	RHS	
EMB		
SG		
GSB		
DLC		
PQC		
Chainage		38000



Index	C & G	
	Length	47.320Km

EMB	
Length	31.20Km

SG	
Length	27.90Km

GSB	
Length	26.770Km


DLC	
Length	22.688Km

PQC	
Length	19.506Km


QC	LHS	
DLC		
GSB		
G		
MB		
&G		
Chainage		38000 38100 38200 38300 38400 38500 38600 38700 38800 38900 39000 39100 39200 39300 39400 39500 39600 39700 39800 39900 40000 40100 40200 40300 40400 40500 40600 40700 40800 40900 41000 41100 41200 41300 41400 41500 41600 41700 41800 41900 42000 42100 42200 42300 42400 42500 42600 42700
&G	RHS	
MB		
G		
SB		
LC		
QC		

QC	LHS	
DLC		
GSB		
G		
MB		
&G		
Chainage		42700 42800 42900 43000 43100 43200 43300 43400 43500 43600 43700 43800 43900 44000 44100 44200 44300 44400 44500 44600 44700 44800 44900 45000 45100 45200 45300 45400 45500 45600 45700 45800 45900 46000 46100 46200 46300 46400 46500 46600 46700 46800 46900 47000 47100 47200 47300 47400
&G	RHS	
MB		
G		
SB		
DLC		
QC		


QC	LHS	
DLC		
GSB		
G		
MB		
&G		
Chainage		47400 47500 47600 47700 47800 47900 48000 48100 48200 48300 48400 48500 48600 48700 48800 48900 49000 49100 49200 49300 49400 49500 49600 49700 49800 49900 50000 50100 50200 50300 50400 50500 50600 50700 50800 50900 51000 51100 51200 51300 51400 51500 51600 51700 51800 51900 52000 52100
&G	RHS	
MB		
G		
SB		
DLC		
QC		




FLYOVER (46+957)LHS

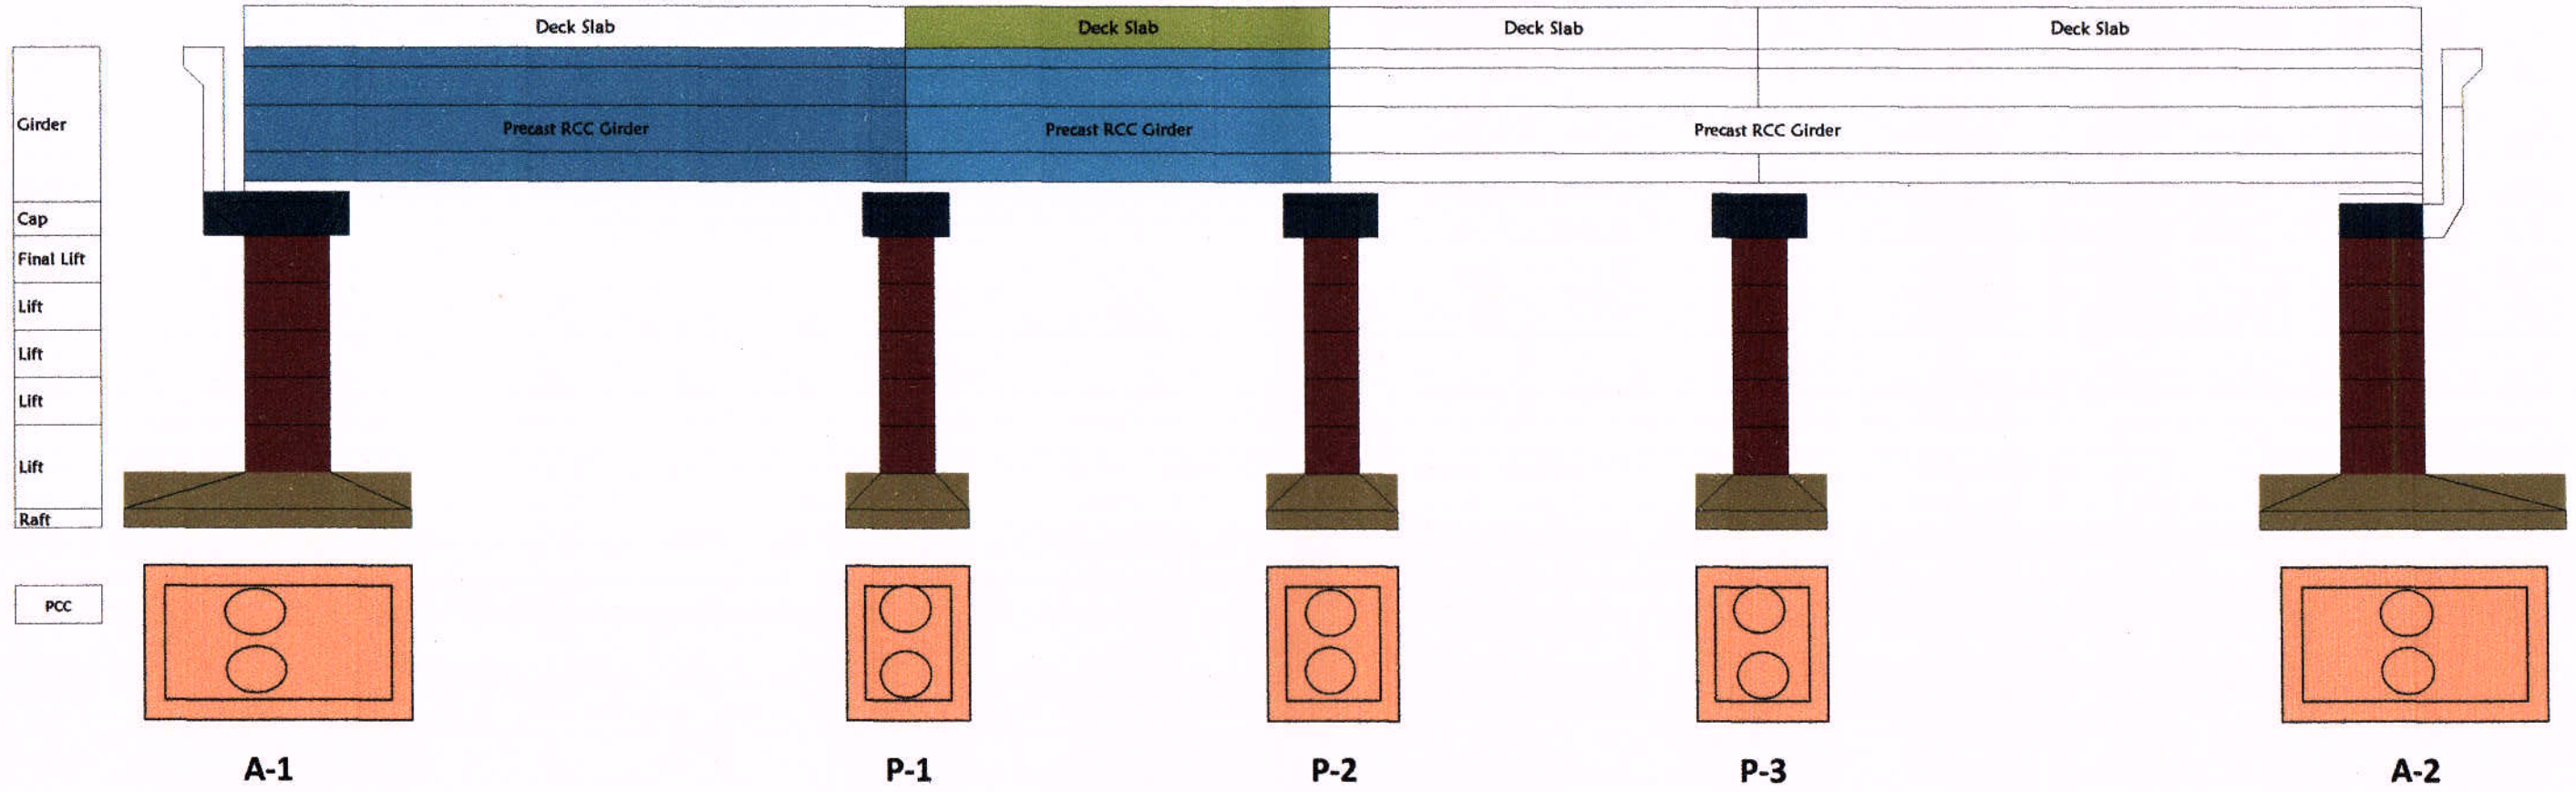


FLYOVER (46+957)RHS

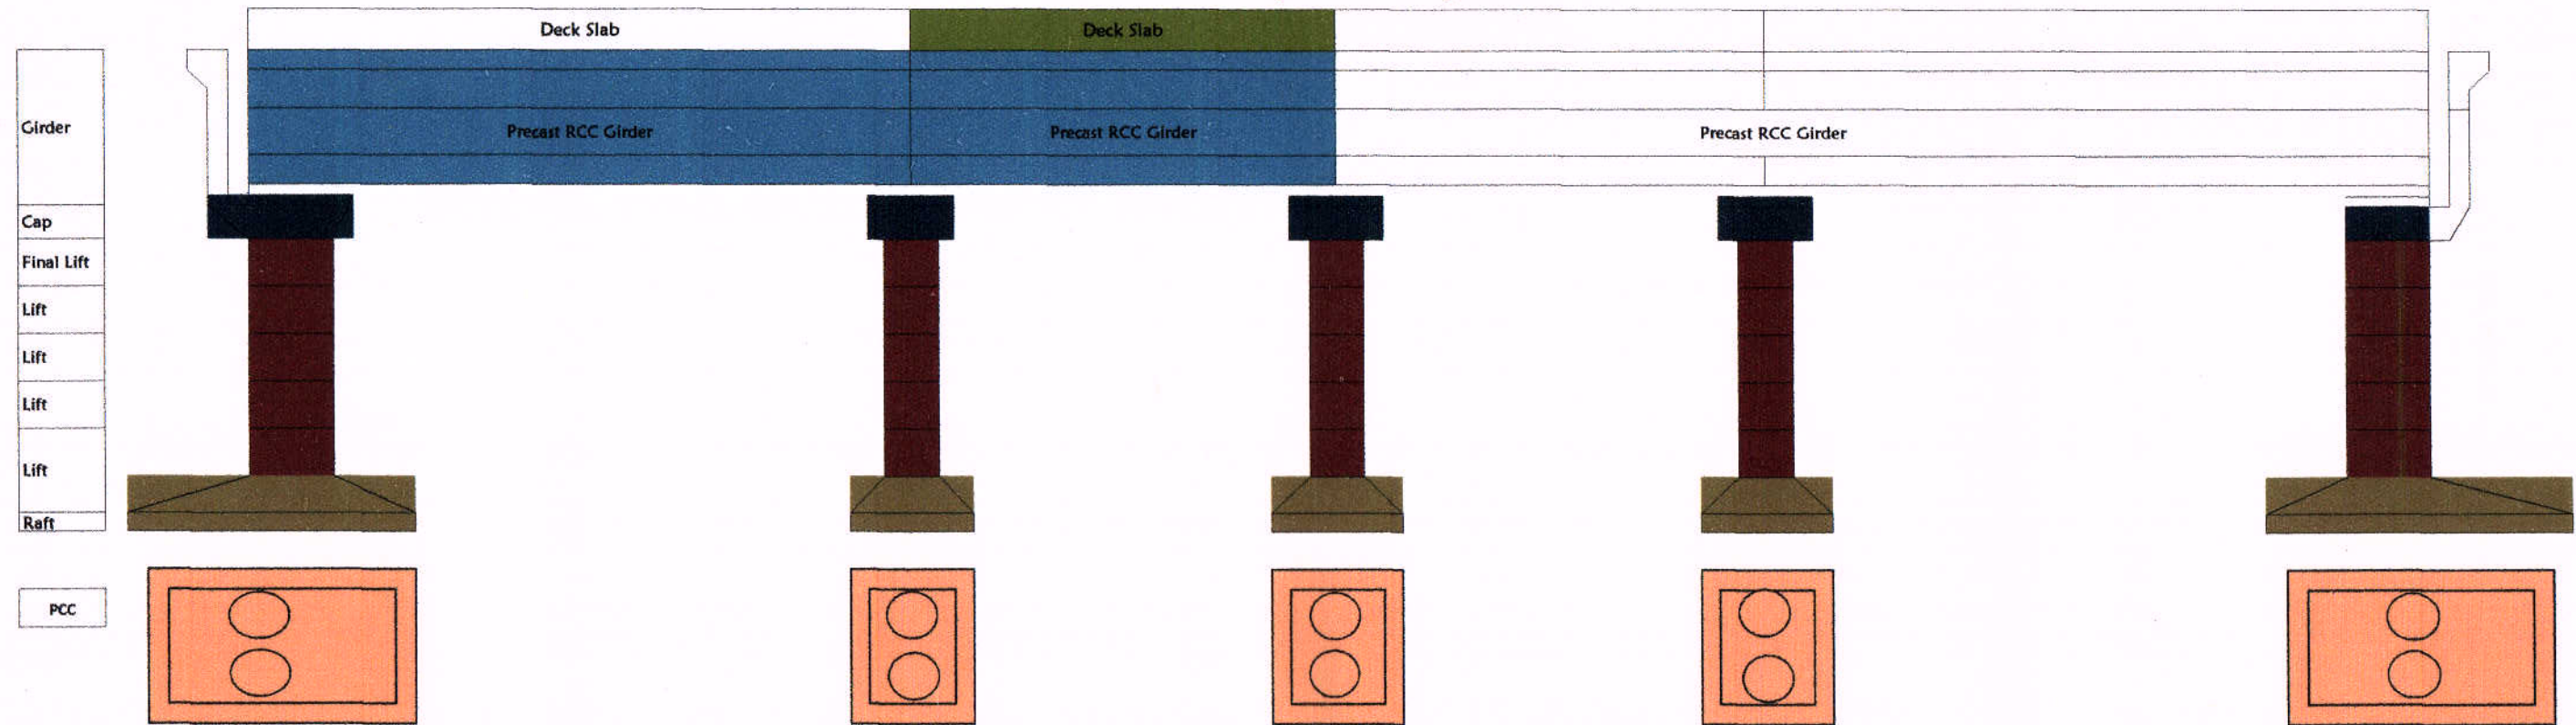


FLYOVER (50+095)RHS

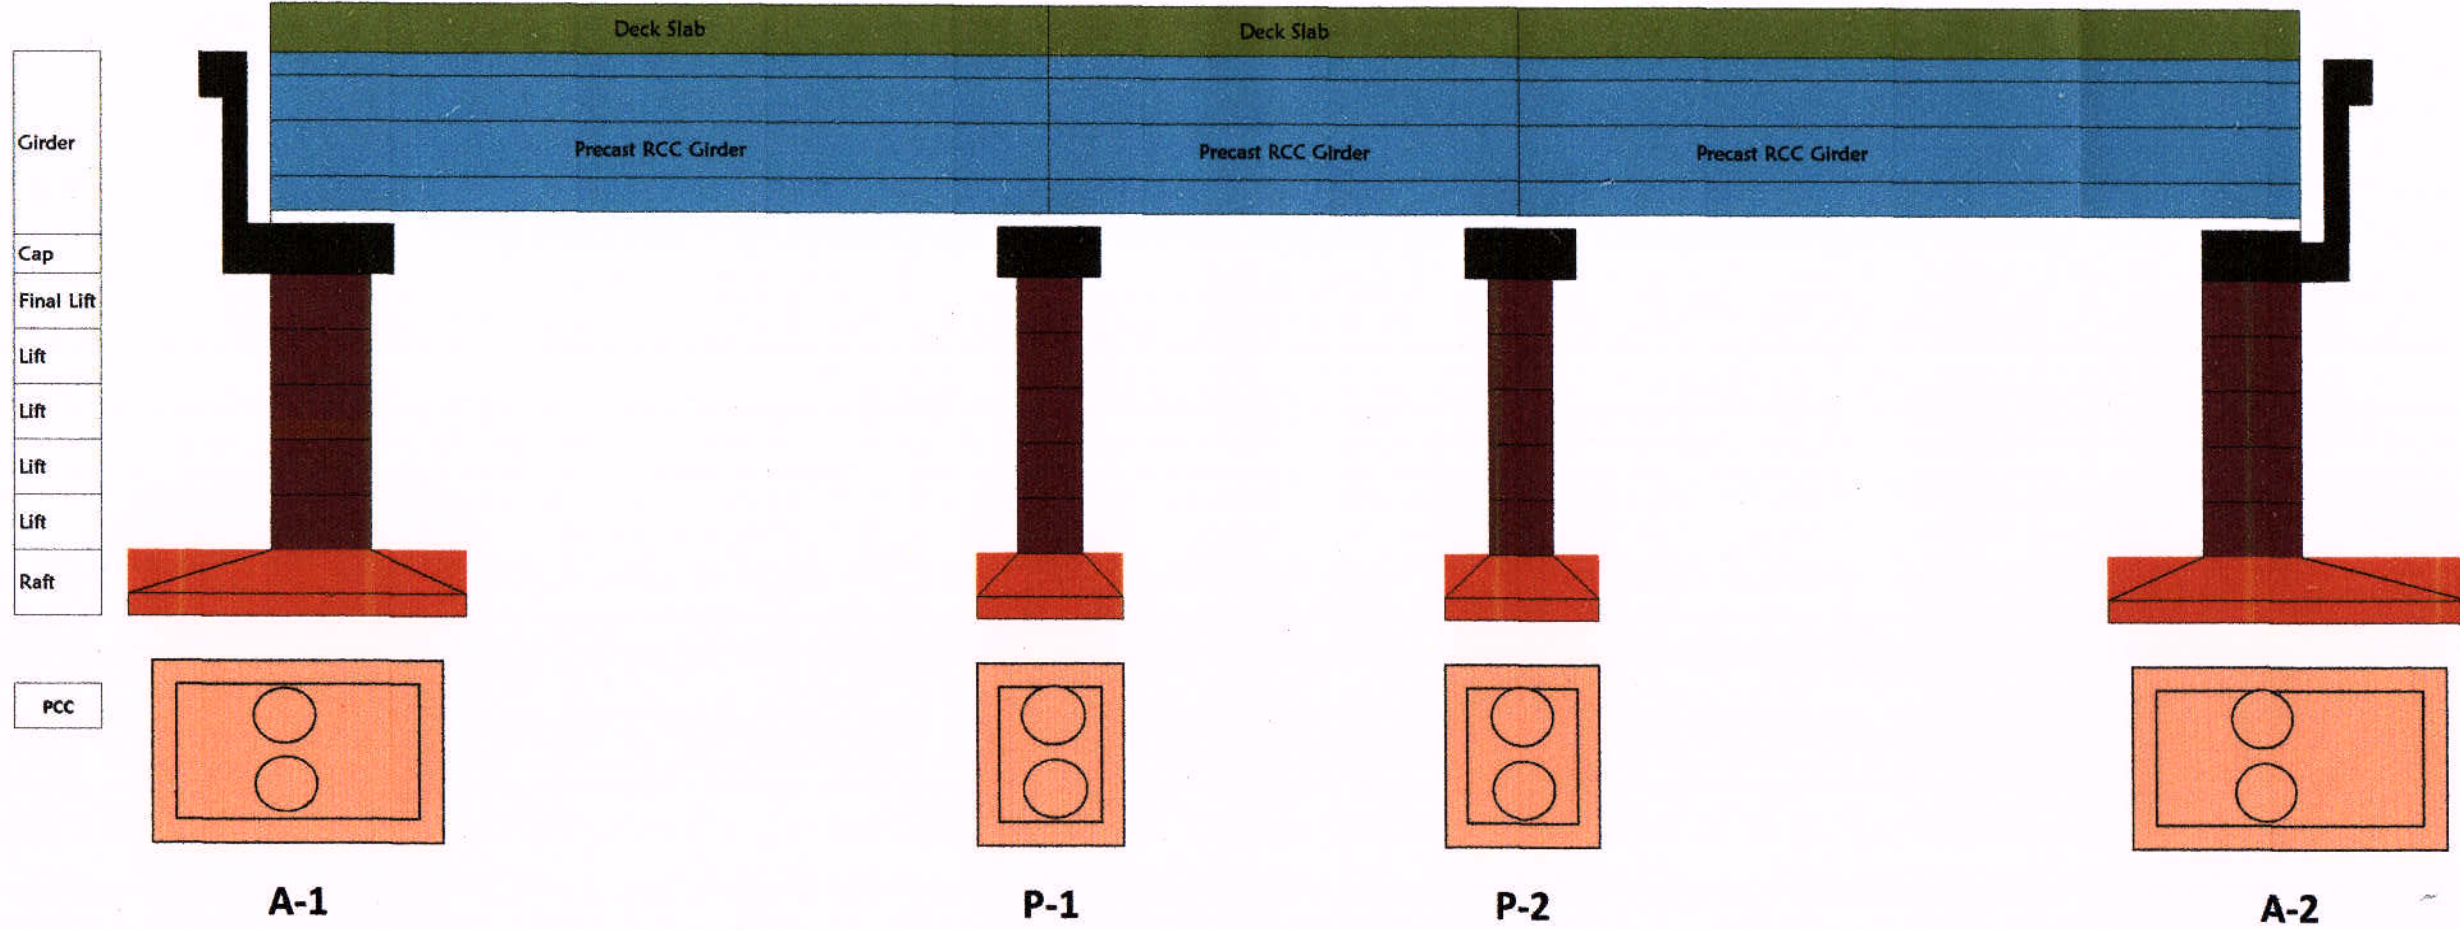


FLYOVER (50+095)LHS

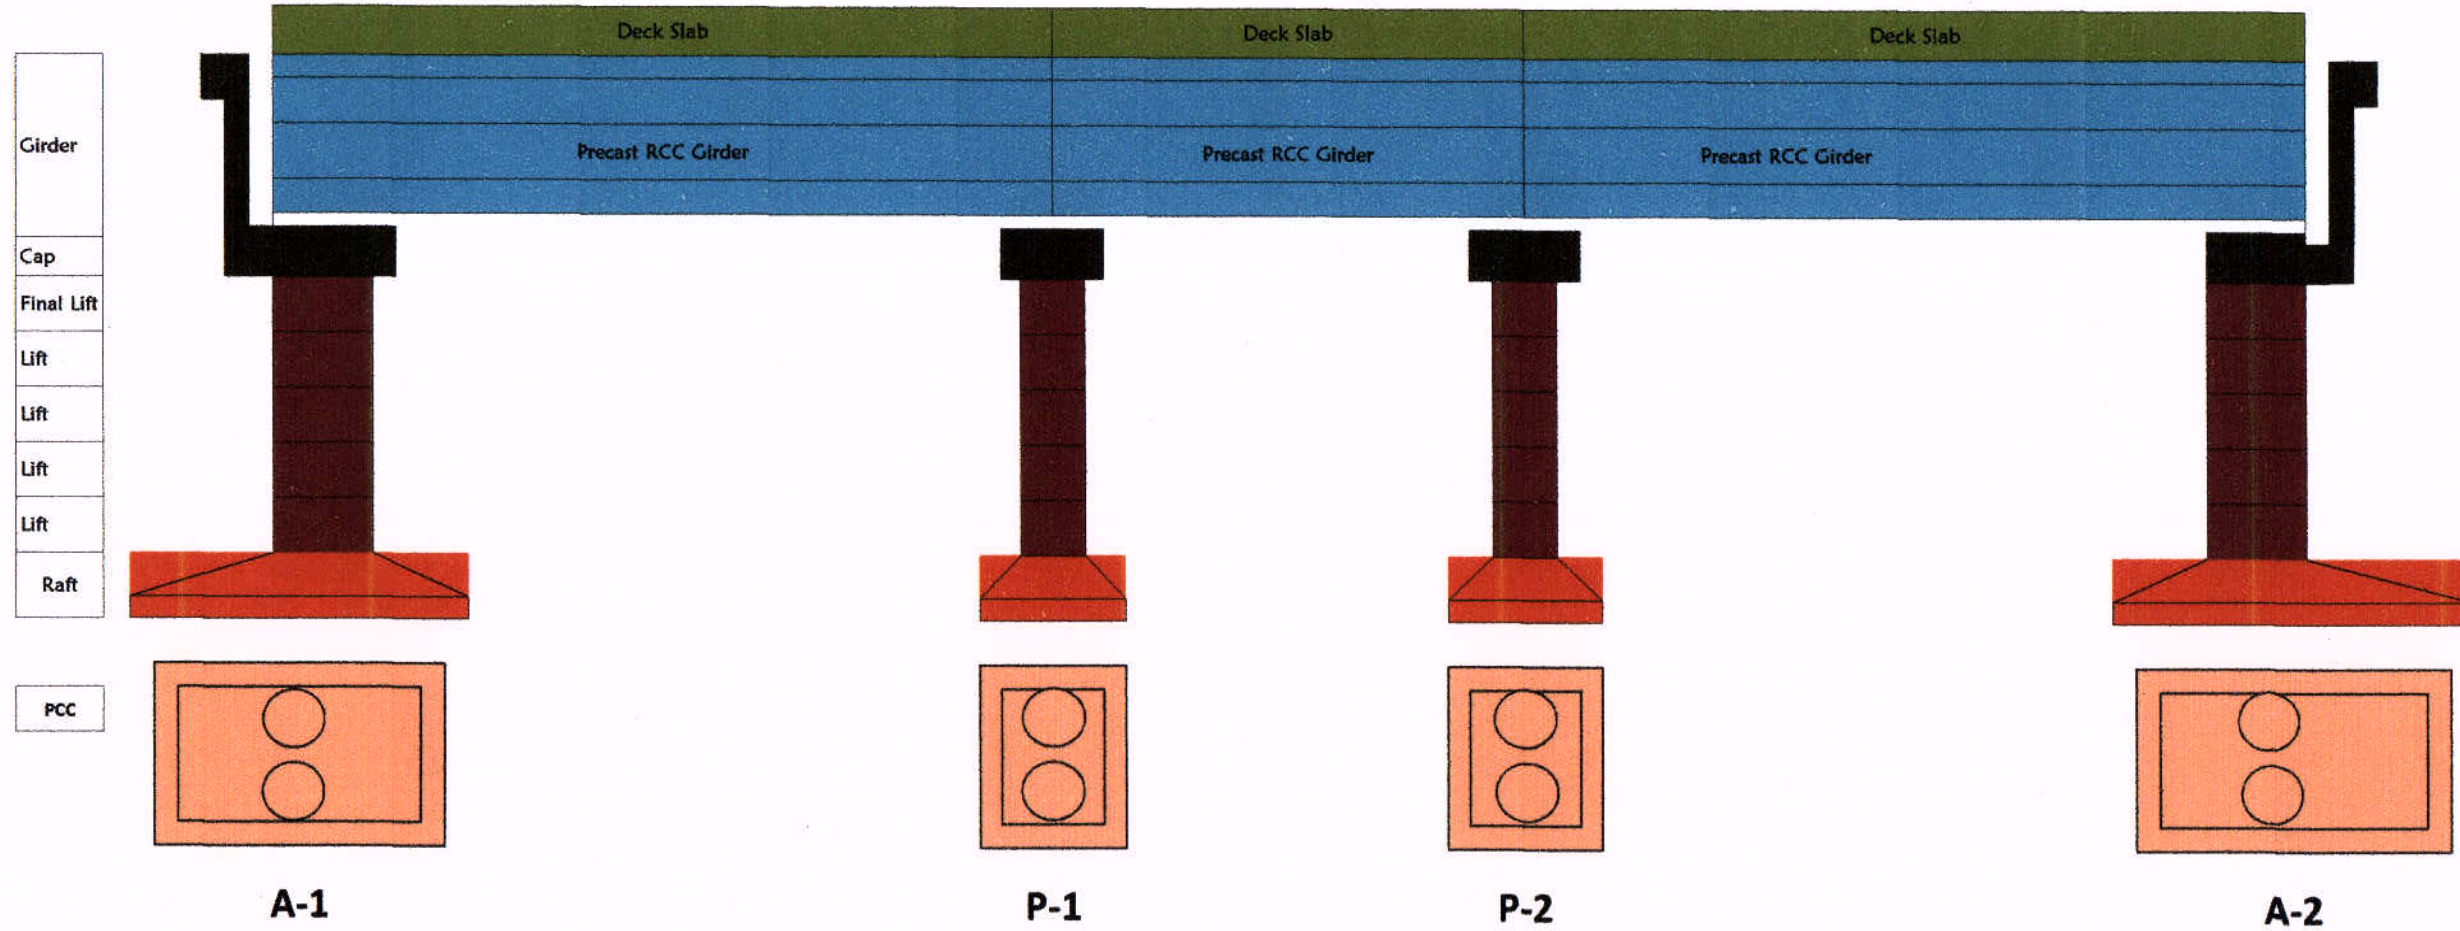


FLYOVER (58+128)RHS

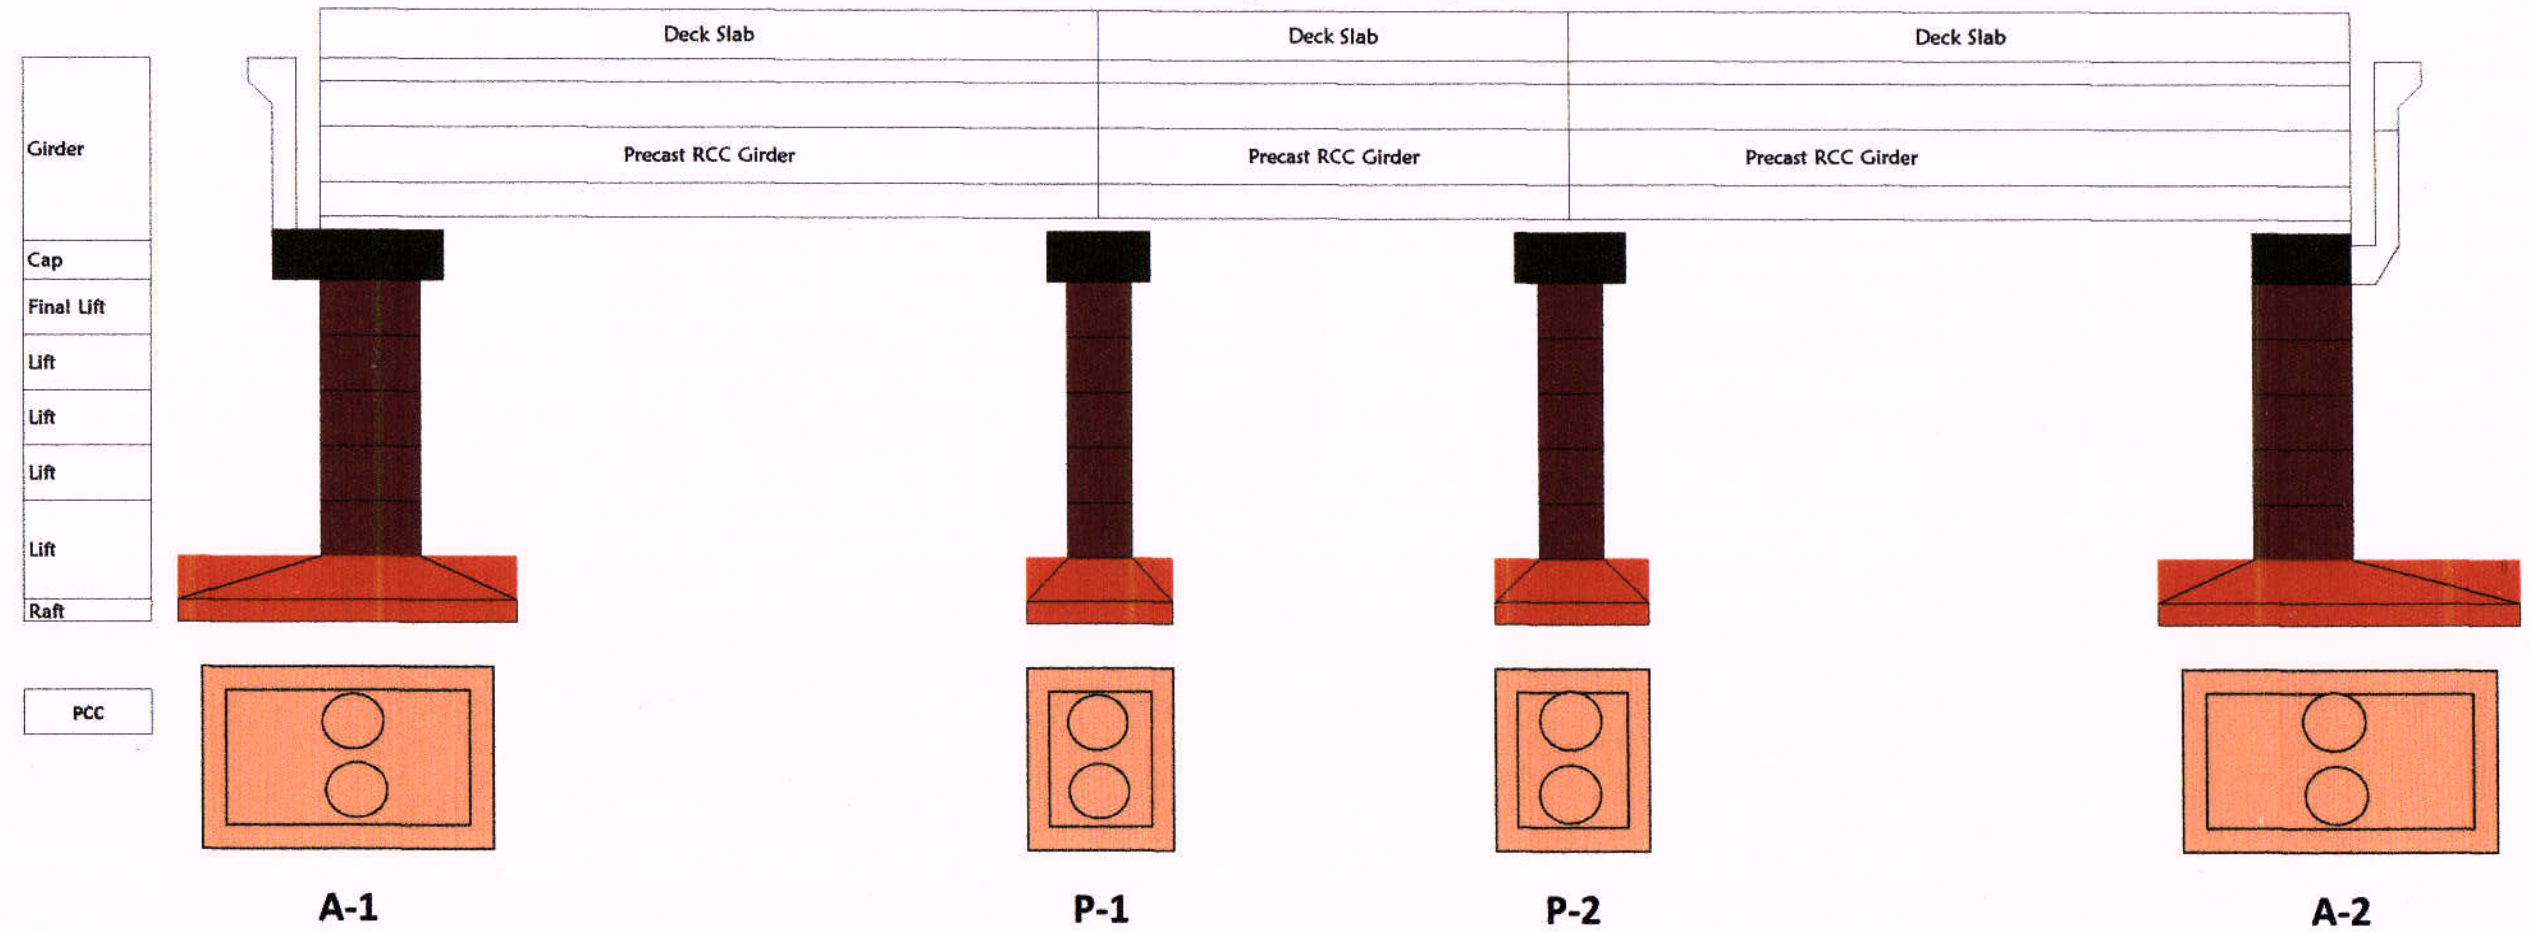


FLYOVER (58+128)LHS

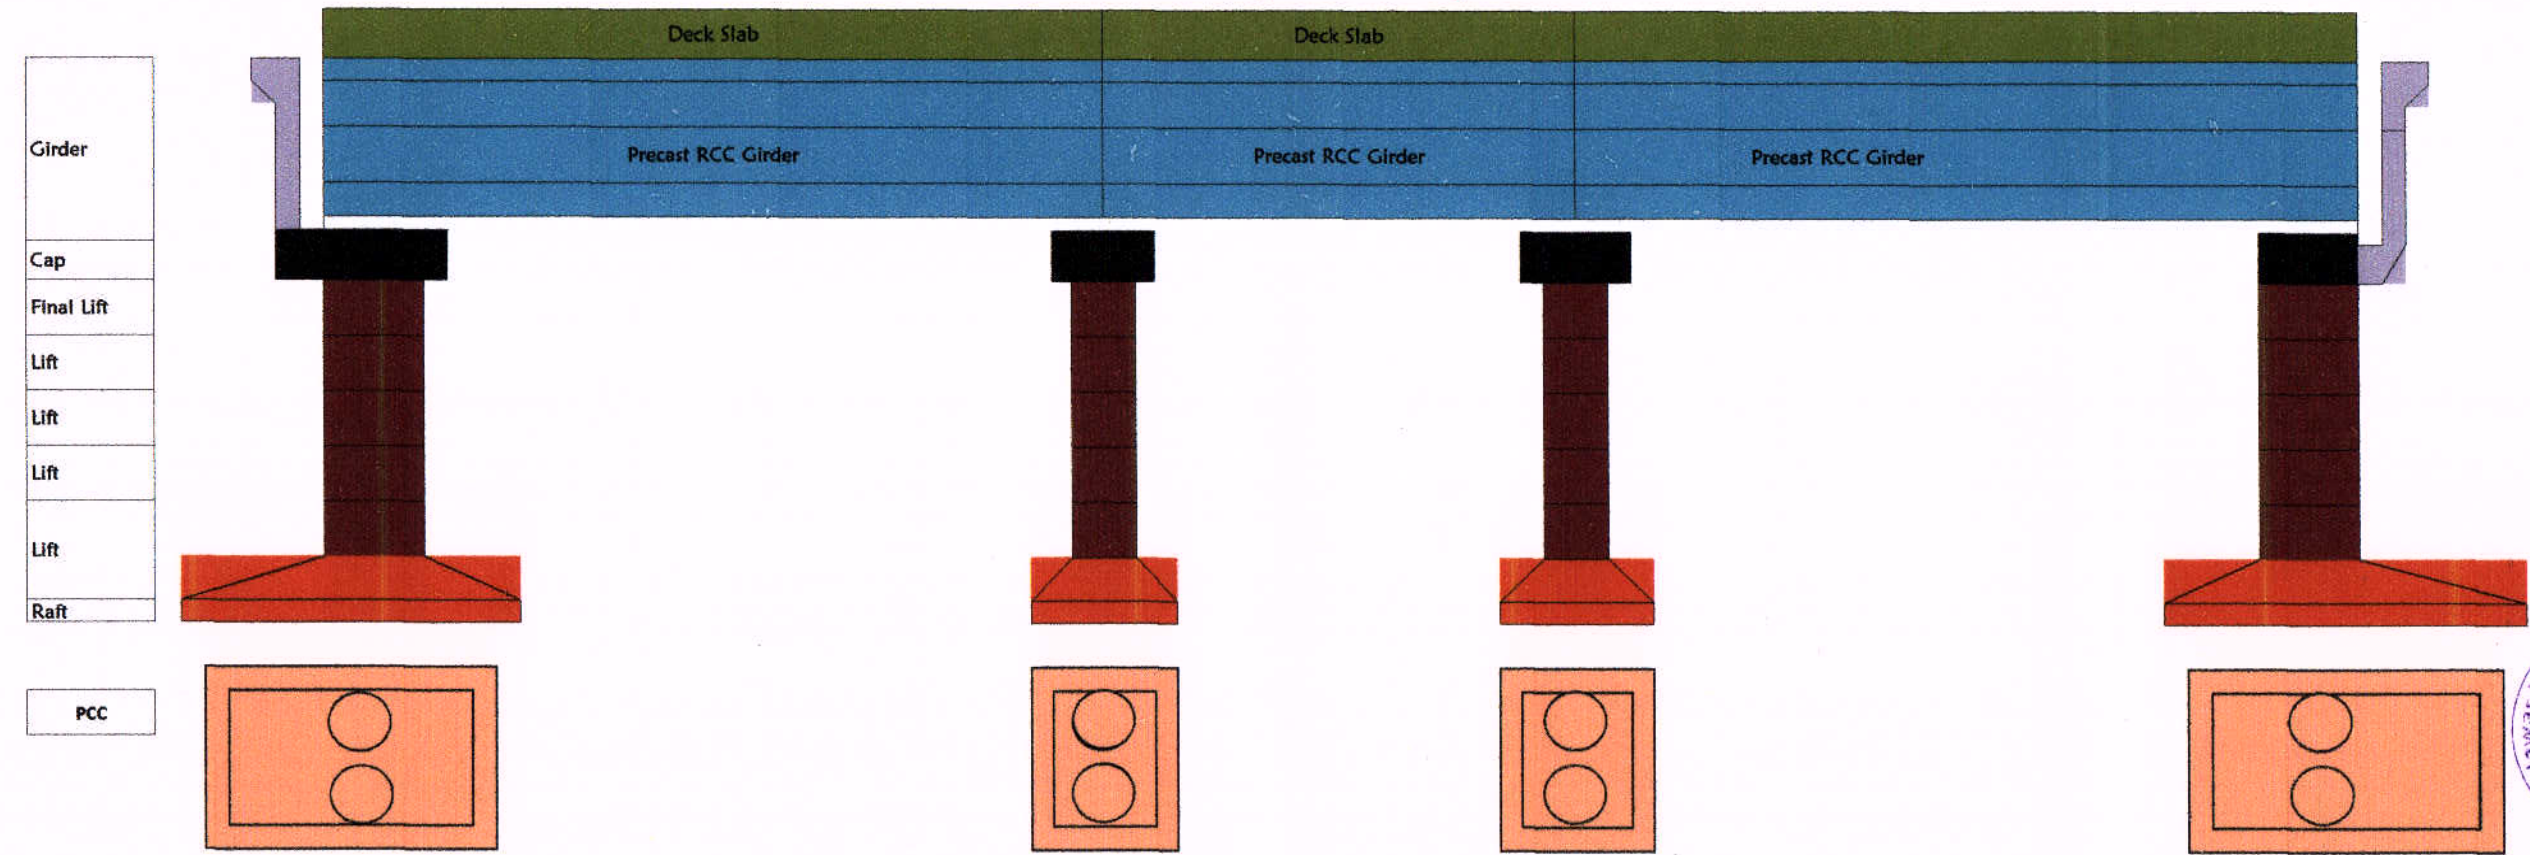

MAJOR BRIDGE AT 36+070 (AHU RIVER) LHS

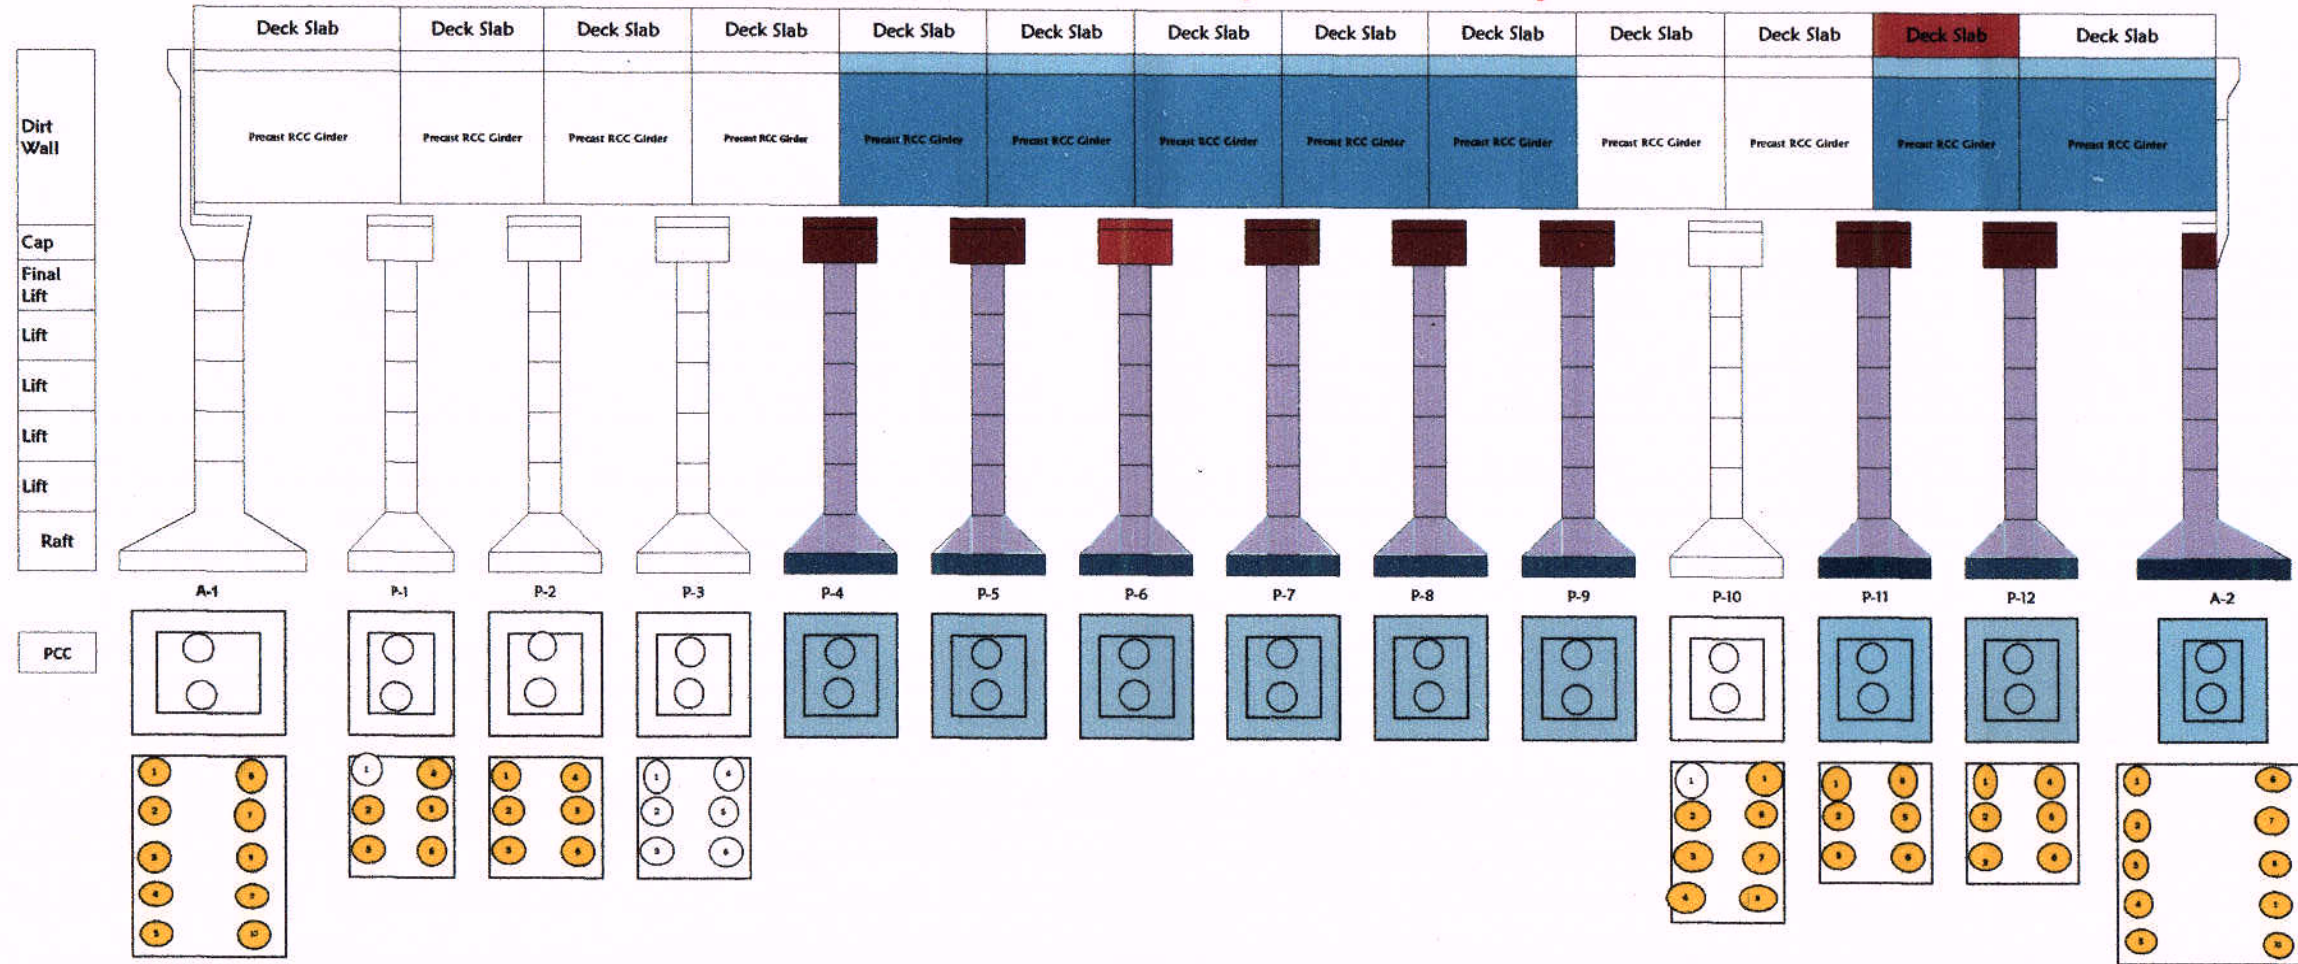

MAJOR BRIDGE AT 36+070 (AHU RIVER) RHS

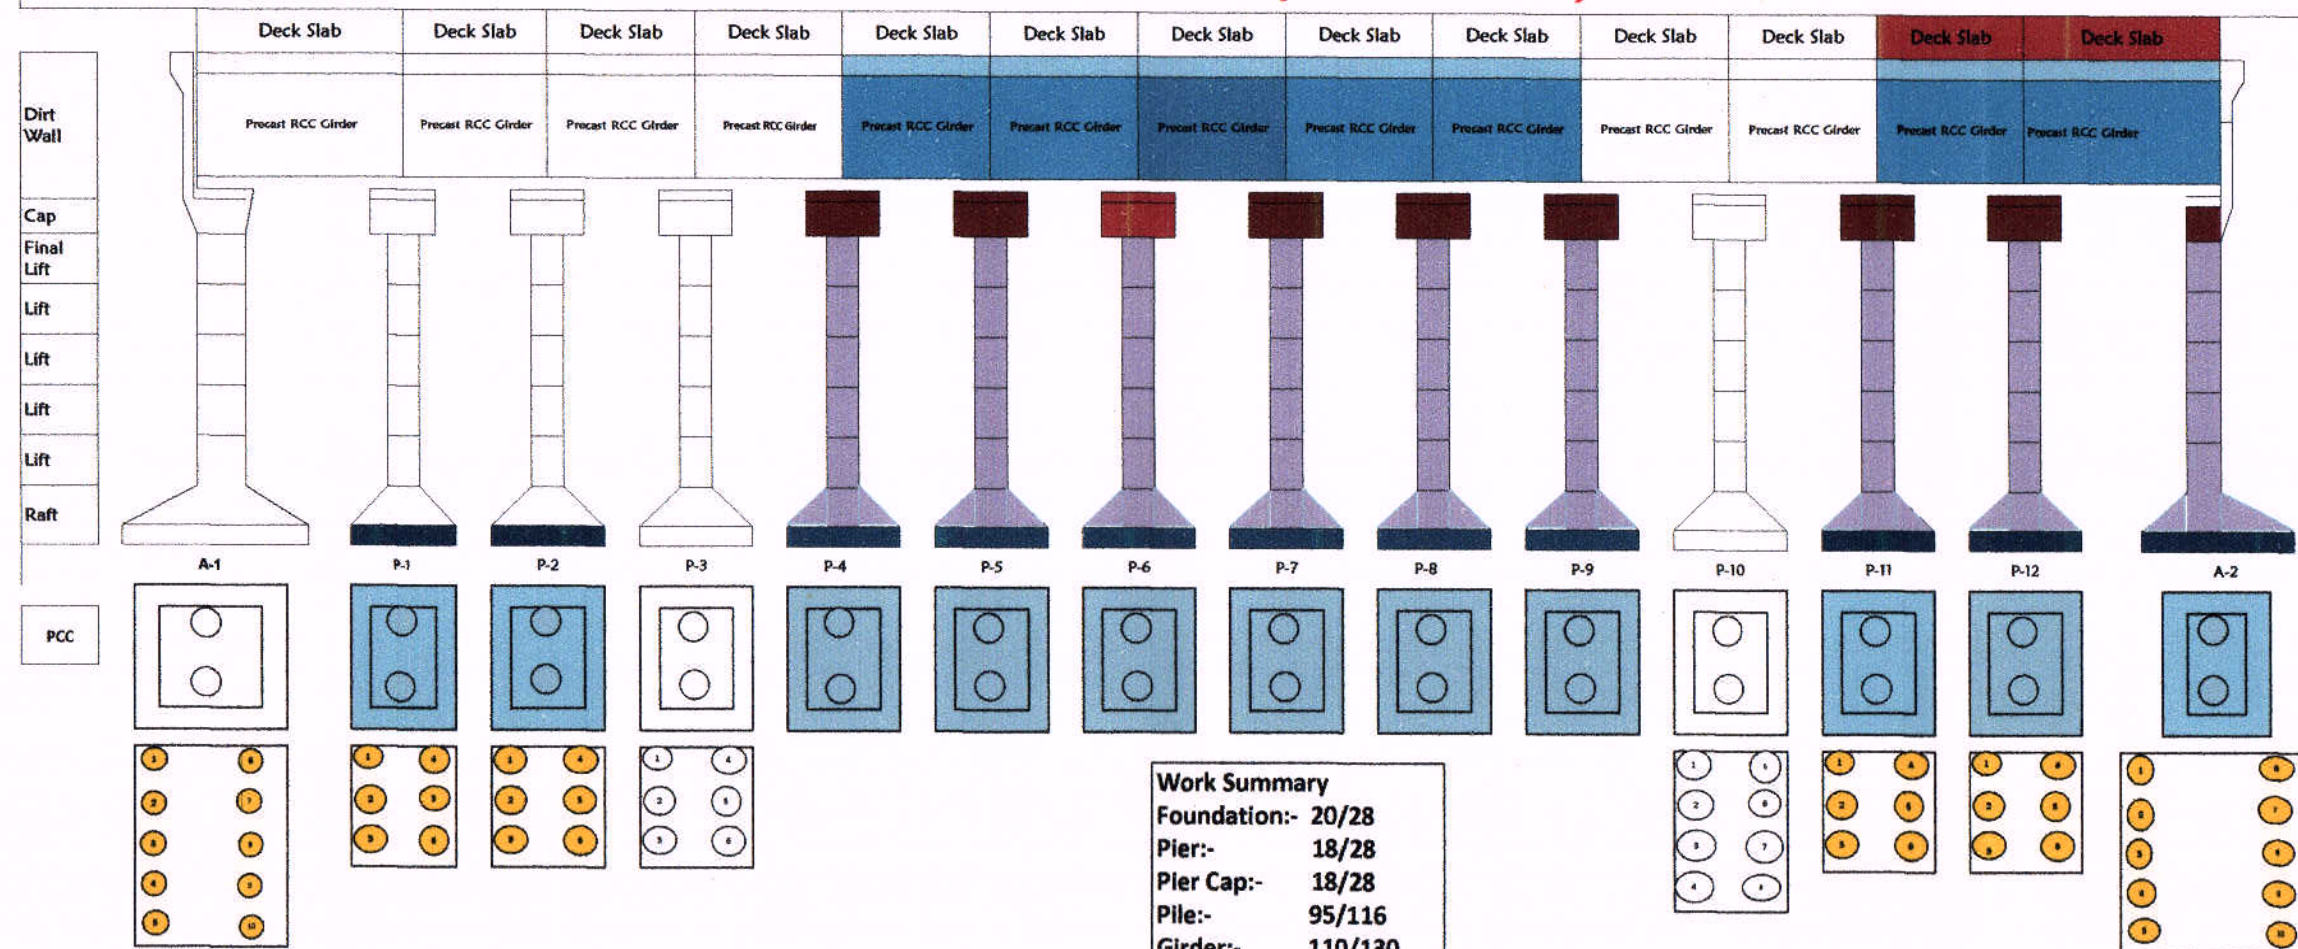


Work Summary	
Foundation:-	20/28
Pier:-	18/28
Pier Cap:-	18/28
Pile:-	95/116
Girder:-	110/130
Slab:-	02/26



MAJOR BRIDGE AT 57+127


- lab
- Dirt Wall
- Cap
- nal Lift
- h Lift
- h Lift
- h Lift
- 3rd Lift
- 2nd Lift
- 1st Lift
- Pile Cap
- PCC

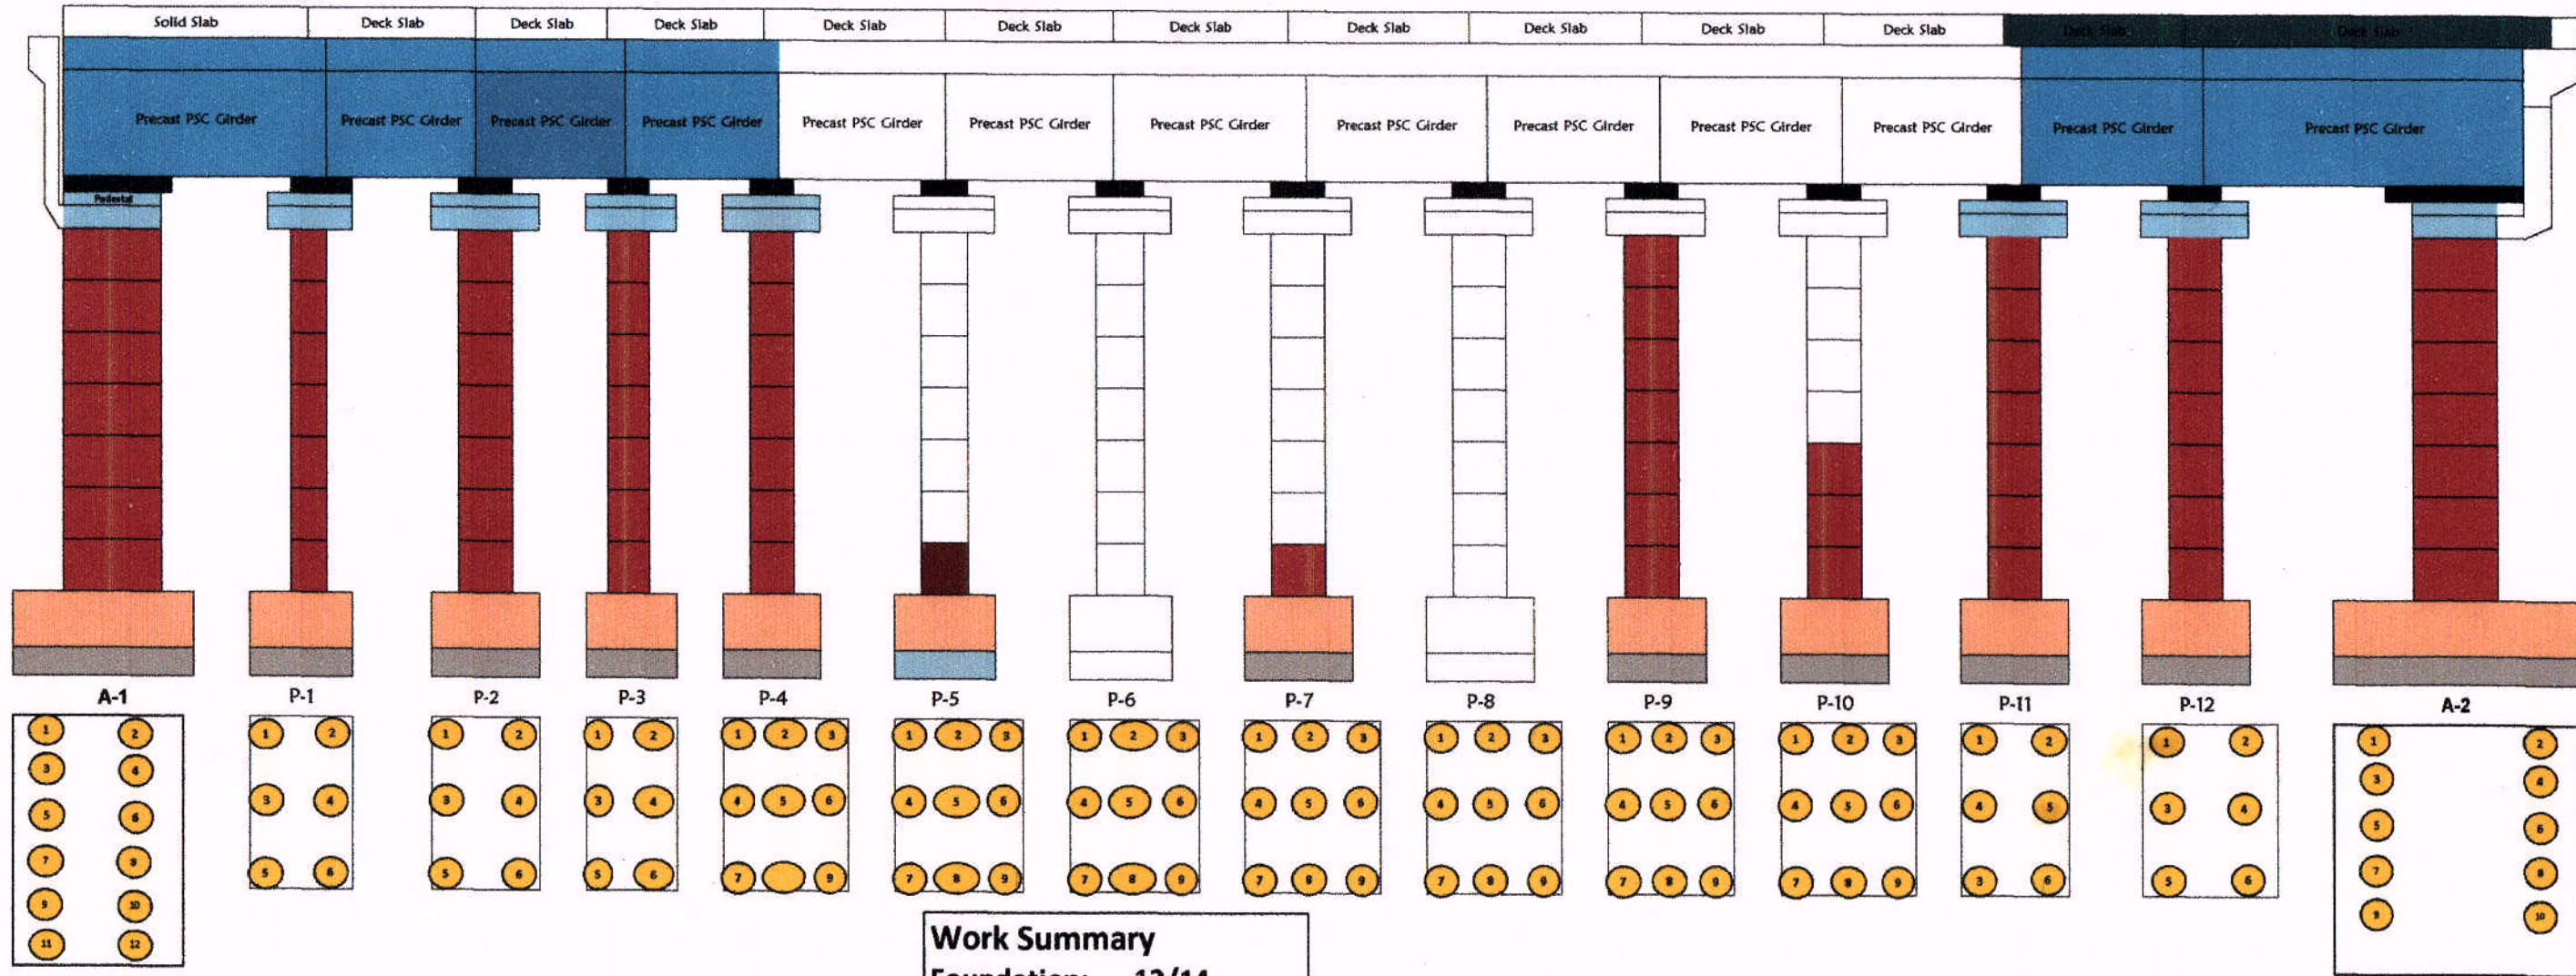


Work Summary
 Foundation:- 12/14
 Pile:- 115/115
 Pile Cap:- 12/14
 Pier:- 09/14
 Pier Cap:- 08/14
 Girer Casting:- 61/65



FLY OVER + MAJOR BRIDGE(ELEVATED STRUCTURE- 47+450 TO 48+150)LHS

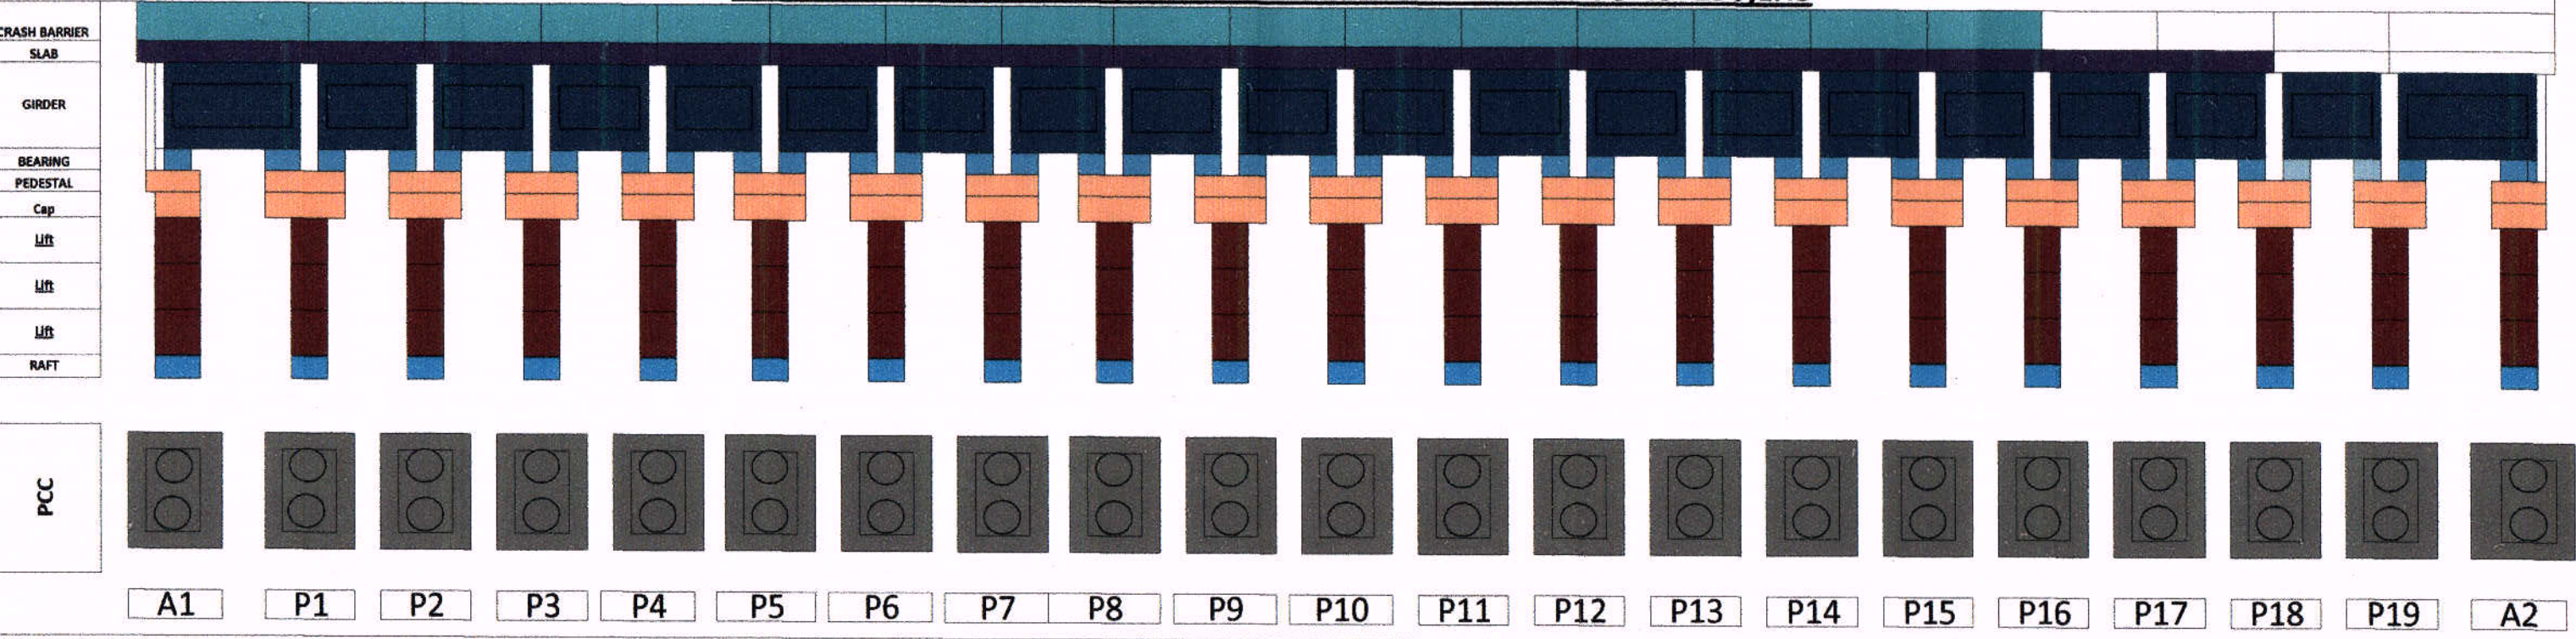

FLY OVER + MAJOR BRIDGE(ELEVATED STRUCTURE- 47+450 TO 48+150) RHS

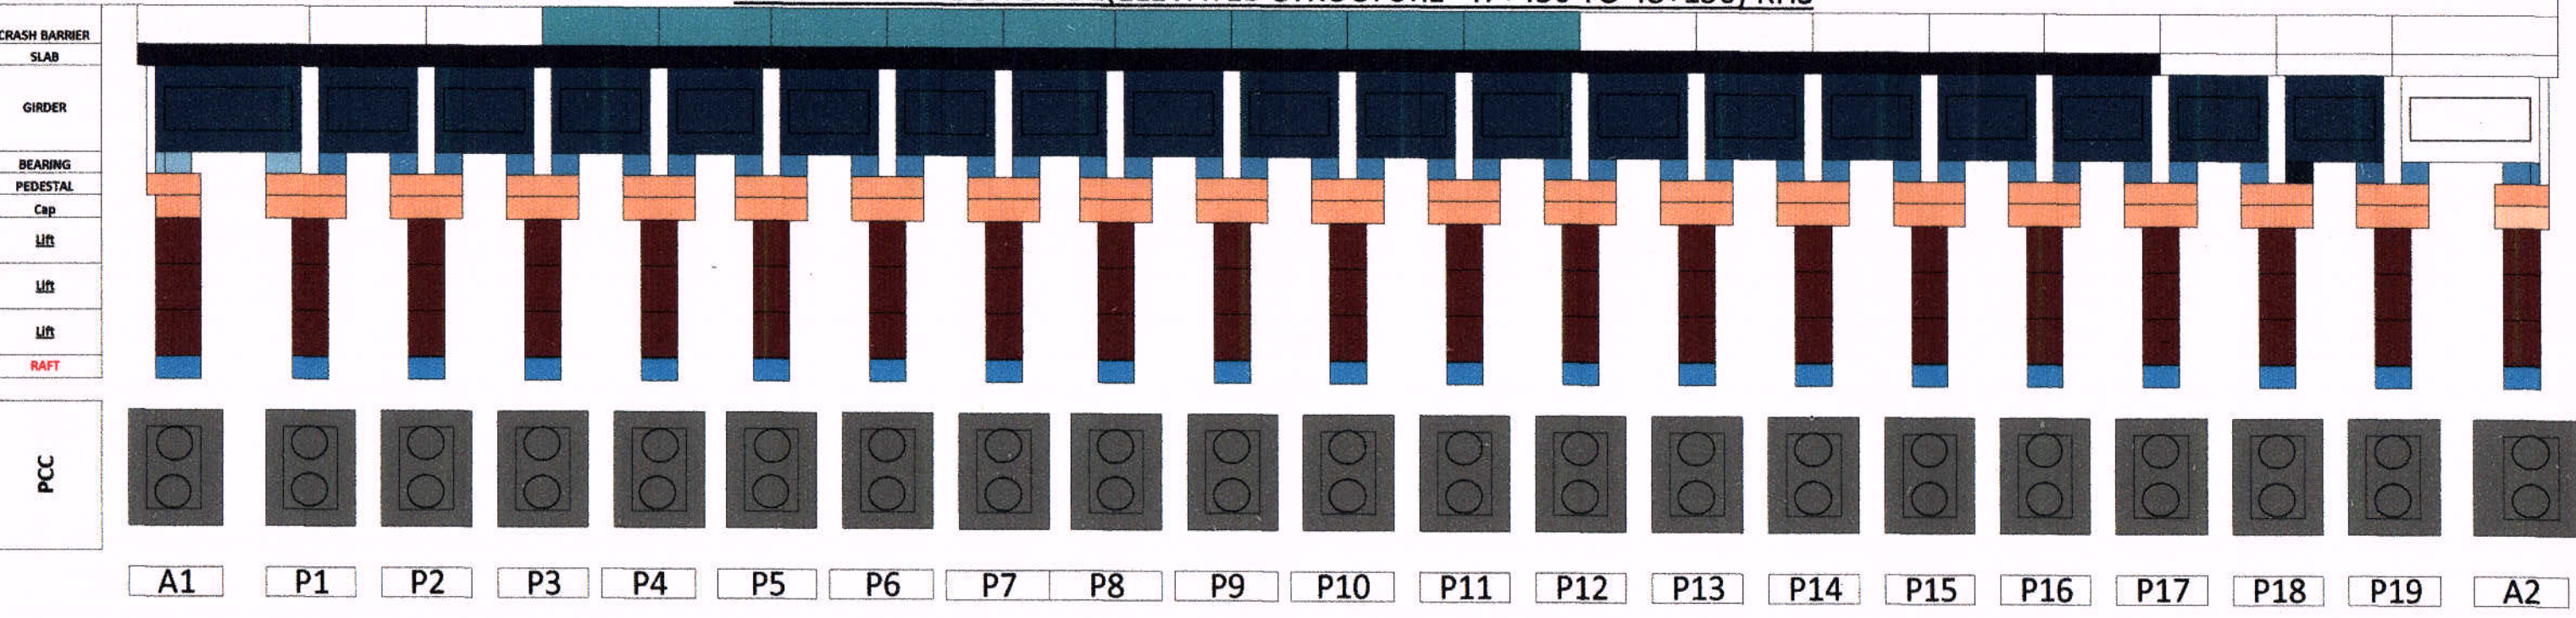

Work Summary
 Foundation:- 42/42
 Pier:- 42/42
 Pier Cap:- 42/42
 Girders:- 200/200
 Girder Launch:- 195/200

