


National Highways Authority of India
(Ministry of Road Transport & Highways)

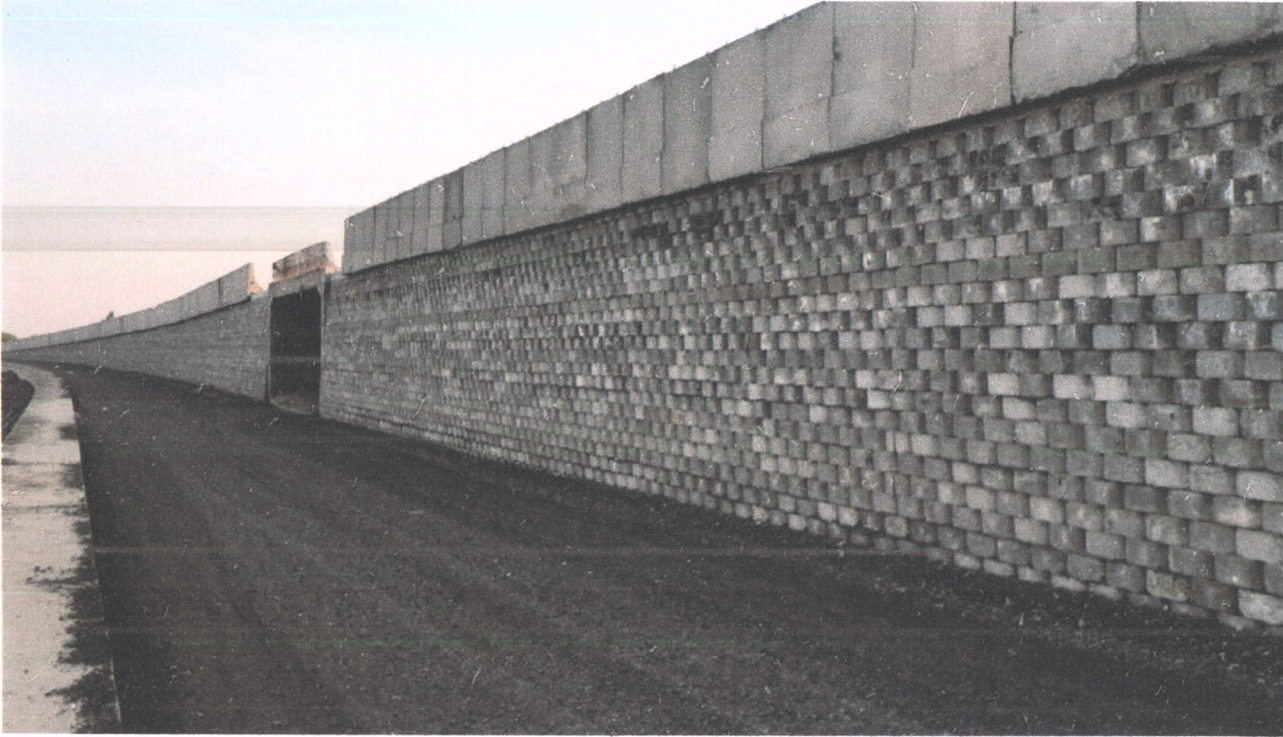

PATEL DARAH-JHALAWAR HIGHWAY PRIVATE LIMITED

CONSTRUCTION OF 4-LANE ROAD ON NH-12 (NEW NH-52) FROM Km. 299.000 TO Km. 346.540 (DESIGN CHAINAGE 9.860 TO 58.740) (DARAH – JHALAWAR – TEENDHAR) IN THE STATE OF RAJASTHAN UNDER NHDP PHASE-III ON HYBRID ANNUITY PROJECT.

INDEPENDENT ENGINEER

LEA ASSOCIATES SOUTH ASIA PVT. LTD

MONTHLY PROGRESS REPORT

For The Month of January-2021

INDEX

S.No	Description of Item	Page No
1	Executive Summary	4
1.1	Project Synopsis	5-6
1.2	Map of Project	7
1.3	Key Plan of Project	8
2	Project Summary	9
2.1	Project Overview	10
2.1.1	Structures Detail	10
2.1.2	Project Milestones	11
3	Project Progress	12-14
4	Utility Shifting Progress	15-16
5	Tree Cutting Status	17
6	Status of Condition Precedent	18
7	Status of Railway Approval	19
8	Issues of Concern	20
9	LAB MPR	21-27
10	Status of Mix Design & Source Approval	28-35
11	Status of Submitted Drawings	36-44
11.1	RE Wall Drawings Status	44-47
11.2	Bearing Drawings Status	49

11.3	Plan & Profile and Miscellaneous Drawings	49-50
12	Mobilization of Manpower	51-53
13	Mobilization of Resources	54
14	Site Progress Photographs	55-71
15	S-Curve	72
16	Highway Stripchart	73-76
17	Structures Pictorial	77-114
18	Hindrance Details	115

1. Executive Summary

The old National Highway 12 runs through two big states Rajasthan and Madhya Pradesh. The total length of the old NH- 12 was 897/00 Km. The length of Old NH 12 was 408/700 Km in the state of Rajasthan. Recently MORTH has amended the number and length of the National highways. The old NH 12 in the state of Rajasthan has become the part of the New National highway 52. The New NH 52 starting from its junction with NH-7 near Sangrur in the state of Punjab connecting Narwana, Hisar in the state of Haryana, Fatehpur, Jaipur, Tonk, Kota, Aklera in the state of Rajasthan, Rajgarh, Biora, Dewas, Indore, Sendhwa in the state of Madhya Pradesh, Dhule, Aurangabad, bed, Osmanabad, Solapur in the state of Maharashtra, Bijapur, Hubli and terminating at its junction with NH-66 near Ankola in the state of Karnataka.

The Project stretch Darah-Teendhar is connected to Jaipur at one end and it is connected to Bhopal at the other end. The project highway is very important highway as it connects the Capital of Rajasthan states and National capital of country through Jaipur- Delhi Highway.

The project highway is very important highway as it connects to two state Rajasthan and Madhya Pradesh. The Darah-Jhalawar-Teendhar section of National Highway has moderate traffic density. In addition to this there are few sections where alignment needs geometric improvements to maintain riding quality of highway and safe movement of vehicles. Apart from this the present alignment of NH is passing through various congested towns and villages. All of the above factors are demanding the existing 2-lane highway to be developed as 4-lane divided carriageway with bypass provisions in congested towns/ villages.

The Project Highway traverses through two districts viz. Kota and Jhalawar in Rajasthan State. The project study corridor starts at the end of ROB approach near to Darah at km 289+500 and passes through five major towns Darah, Sarvada, Dabadeh, Suket and Jhalawar, and it ends at Teendhar, Existing km 346.540 Km. Existing road width is 2 lane standard. The Existing ROW varies from 15 m to 30 m. The entire project length is under the administrative control of PIU Kota.



1.1 Project Synopsis


National Highways Authority of India plans to undertake the Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage From 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Mode (Length 48.880 Km.) – Package II.

The National Highways Authority of India (NHAI) is undertaking the up-gradation of NH-12 from Existing two lane road to four lane divided carriageway in state of Rajasthan.


The project involves up gradation of 48.88 Km from two-lane to the four-lane divided carriageway. It includes the construction of bridges, intersections, service roads, culverts and related infrastructure, and the installation of signaling systems and signboards. The project will be developed under National Highways Development Project (NHDP) Phase-III on Hybrid Annuity Mode.

Existing and Proposed alignment


SR. NO.	Existing Chainage (Km)		Length	Design Chainage (Km)		Design Length (Km)	Name of Revenue Village
	To	From		To	From		
1	299.000	299.340	0.340	9.860	10.200	0.340	KAMALPURA
2	299.340	299.740	0.400	10.200	10.600	0.400	KAMALPURA
3	299.740	300.140	0.400	10.600	11.000	0.400	KAMALPURA
4	300.140	300.440	0.300	11.000	11.300	0.300	KAMALPURA
5	300.440	300.778	0.338	11.300	11.638	0.338	KOOKARA KHURD
6	300.778	301.255	0.477	11.638	12.115	0.477	MANPURA
7	Dabadeh&Sahrawada Bypass			12.115	12.300	0.185	MANPURA
8				12.300	13.028	0.728	ZALIMPURA
9				13.028	14.200	1.172	SAHRAWADA
10				14.200	15.661	1.461	TELYA KHERI
11				15.661	17.242	1.581	ASKALI
12				17.242	19.273	2.031	HIRIYA KHERI
13				19.273	19.788	0.515	KHEEMACH
14	308.203	308.515	0.312	19.788	20.100	0.312	KHEEMACH
15	308.515	308.715	0.200	20.100	20.300	0.200	KHEEMACH
16	308.715	308.915	0.200	20.300	20.500	0.200	ATRALIYA
17	308.915	309.079	0.164	20.500	20.664	0.164	ATRALIYA
18	Atraliya Realignment			20.664	21.682	1.018	ATRALIYA
19	310.007	310.125		21.682	21.800	0.118	ATRALIYA
20	310.125	310.325		21.800	22.000	0.200	ATRALIYA
21	310.325	310.444		22.000	22.119	0.119	GORDHANPURA
22	Atraliya Realignment			22.119	22.464	0.345	GORDHANPURA & PAMA KHERI
23	310.789	311.125		22.464	22.800	0.336	PAMA KHERI
24	311.125	311.494		22.800	23.169	0.369	PAMA KHERI
25	311.494	311.625		23.169	23.300	0.131	PAMA KHERI



SR. NO.	Existing Chainage (Km)		Length	Design Chainage (Km)		Design Length (Km)	Name of Revenue Village
26	311.625	311.776		23.300	23.451	0.151	PAMA KHERI
27	311.776	312.025		23.451	23.700	0.249	PAMA KHERI
28	312.025	312.725		23.700	24.400	0.700	DEENGASI
29	312.725	312.925		24.400	24.600	0.200	DEENGASI
30	312.925	313.025		24.600	24.700	0.100	DEENGASI
31	313.025	313.125		24.700	24.800	0.100	DEENGASI
32	313.125	313.370		24.800	25.045	0.245	DEENGASI
33	313.370	313.535		25.045	25.210	0.165	DEENGASI
34				25.210	25.254	0.044	DEENGASI
35				25.254	26.124	0.870	UMMEDPURA
36				26.124	27.000	0.876	RAMPURIYA
37				27.000	27.358	0.358	SUKET
38				27.358	27.854	0.496	BEER MANDI
39				27.854	28.000	0.146	SUKET
40				28.000	29.571	1.571	ARANYA KHURD
41				29.571	31.212	1.641	SURERA
42				31.212	33.617	2.405	BANSYA HERI
43				33.617	35.565	1.948	ARANYA KALAN
44	Suket,			35.565	36.100	0.535	KALMANDI
45	Jhalawar&Jhalrapatan Bypass			36.100	38.000	1.900	HARISH PURA
46				38.000	38.537	0.537	RALAYTI
47				38.537	40.343	1.806	RALAYTA
48				40.343	41.784	1.441	JHALRAPATAN
49				41.784	44.224	2.440	MADHOPUR
50				44.224	49.800	5.576	HARIPURA
51				49.800	51.434	1.634	HARIPURA,
52				51.434	52.516	1.082	BANJARI &
53				52.516	54.200	1.684	BHANWARSA
54				54.200	54.565	0.365	BHANWARSA
55	342.895	343.673		54.565	55.343	0.778	BHANWARSA
56	343.673	347.127		55.343	58.740	3.397	BHANWARSA & ROOPAREL




KEY PLAN OF THE PROJECT

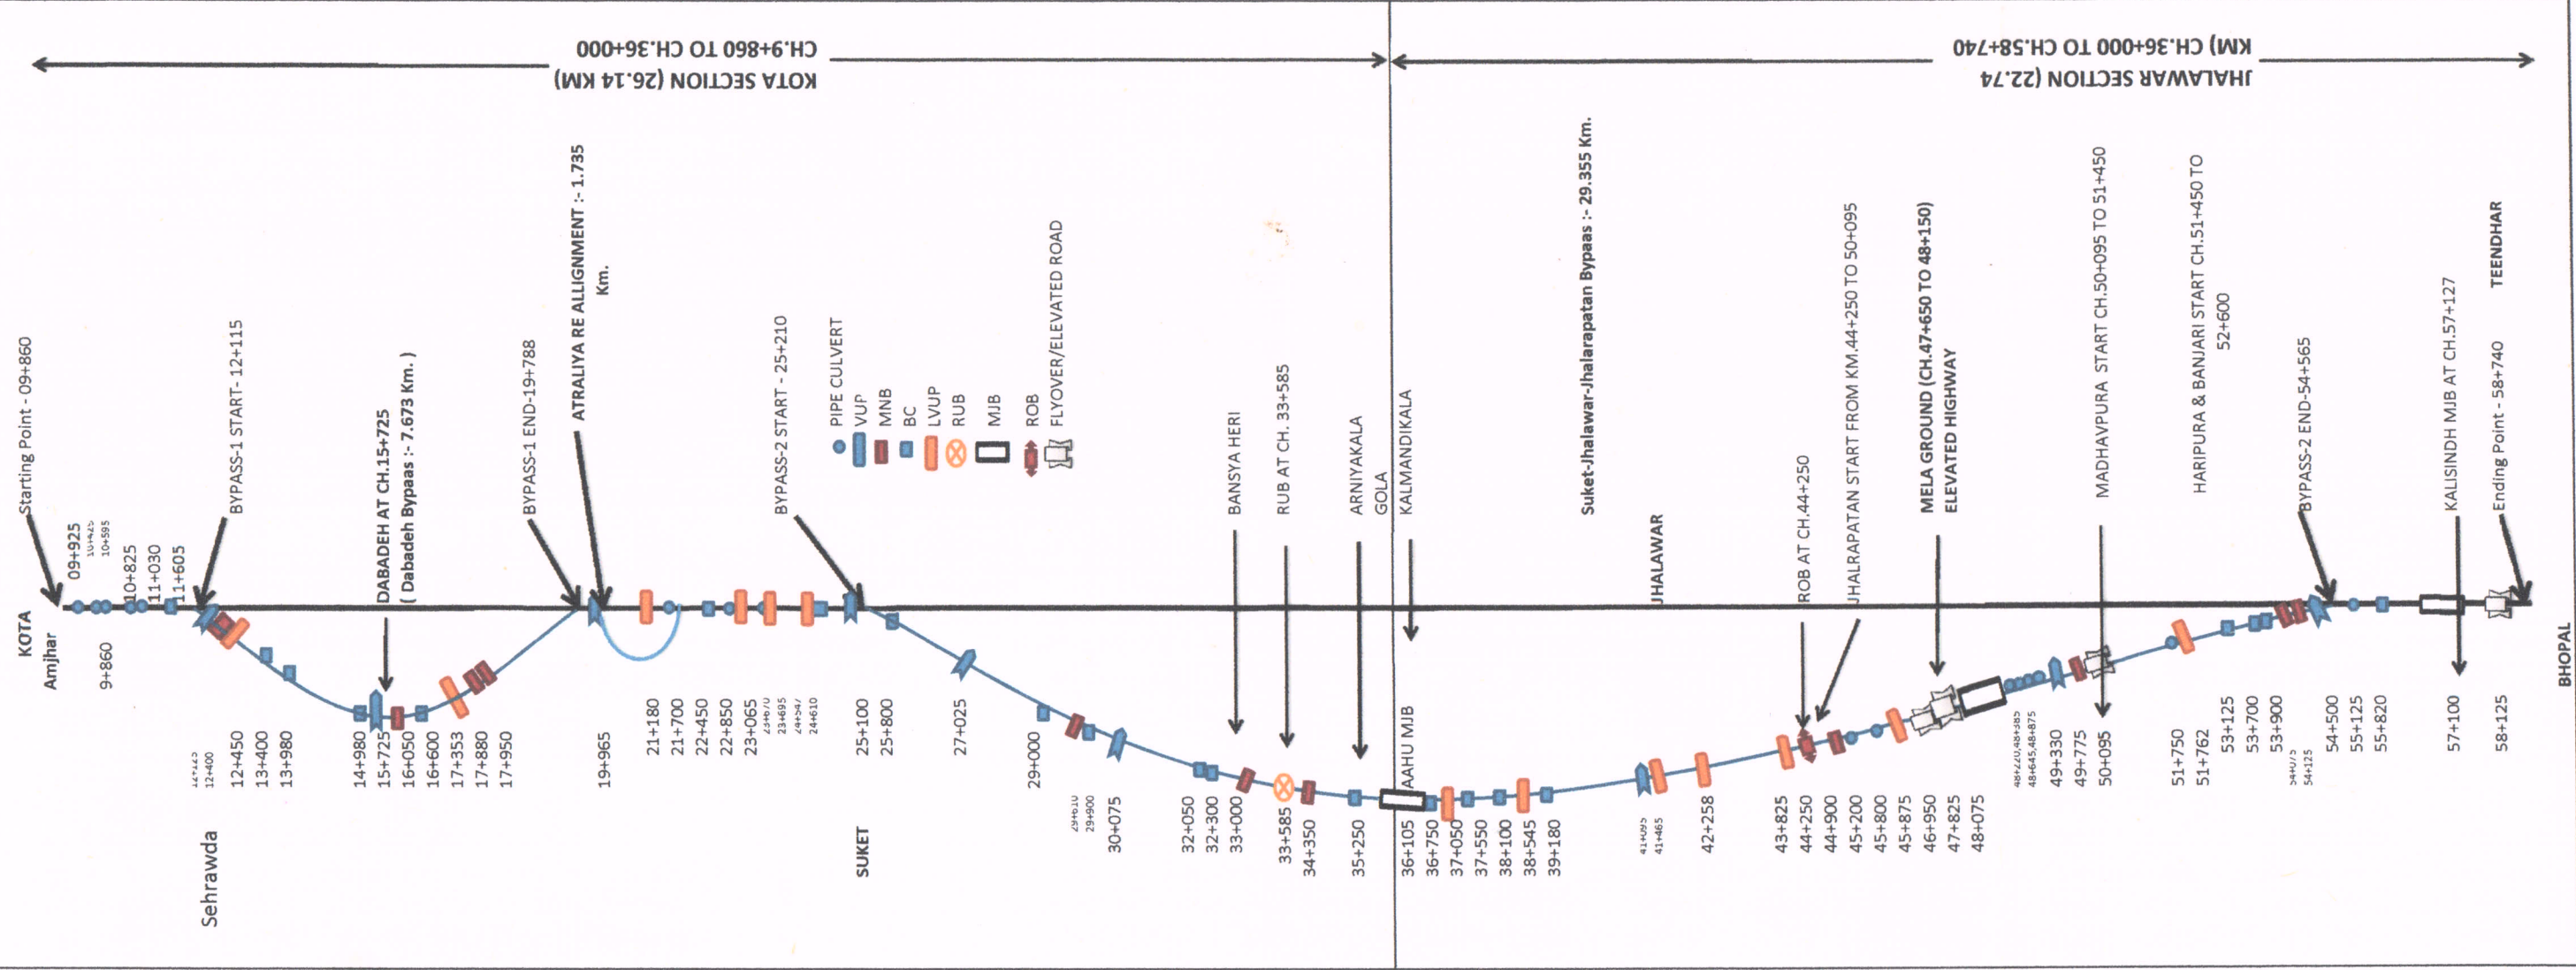

2. PROJECT SUMMARY

Project	Construction of 4-lane Road on NH-12 New NH-52 from Km 299.000 to 346.540 Design Chainage From 9.860 to 58.740 Darah-Jhalawar-TeendharSection in the State of Rajasthan under NHDP Phase-III Length 48.880 km Package II on Hybrid Annuity Mode.
Owner/Client	National Highways Authority of India
Concessionaire	Patel DarahJhalawar Highway Pvt. Ltd.
Independent Engineer	LEA ASSOCIATE SOUTH ASIA PVT. LTD
Project Length (In Km)	48.88 Km
Total Project Cost as per CA	1123.63 Cr.
Concession Period	15 Years
Construction Period	910 Days from the Appointed Date.
Contractual Completion Date	19 th November 2020.
Extended Completion Date	Yet to finalized
Date of Signing of Concession Agreement	16 th November 2017
Appointed Date	24 th May 2018 (Letter ref. No. NHAI /19030/Dara-Teen/Raj/2016/1/120723 dated 09 th July 2018.



2.1 Project Overview

2.1.1 Structures

S. No.	Feature	Description
1	Major Bridge	02 Nos. – (13 x 25mtr) & (13 x 31.6mtr_3-Lane)
2	Elevated Flyover cum MJB	01 Nos. – (20 x 25mtr)
3	Flyovers/ Interchange	03 Nos. (1 Nos. – 4x25mtr.) (2 Nos. – 3 x 24mtr.)
4	ROB/ RUB	1/1 = 2 No.
5	Minor bridges	As per CA -11 Nos. (01 no. deleted as per site condition)
6	Vehicular underpass	09 Nos. – (1x24mtr)
7	Light Vehicular Underpasses	13 Nos.
8	Culverts (HP/BC/PUP) as per CA & Additional	37 Nos. (16 Nos. Pipe & 21 Nos. Box)+Additional (31 Nos Pipe, 2 nos Box and 03 Nos PUP) Total- 47 Nos Pipe and 23 nos Box Culvert
9	RE Wall	14.454 Km
10	Toll Plaza	1 No (16 Lanes)
11	Truck Lay Bys	1 (Both side)
12	Bus Shelter	5 Nos (Both side)
13	Rest Area	1no

2.1.2 Project Milestones

Project Milestone	Condition	Time Line	Date	Financial Progress
I	Commenced construction of Project and achieved 20% of Physical Progress	290 th Day from Appointed date	10 th March 2019	224.73 Cr.
II	Commenced construction of Project and achieved 35% of Physical Progress	430 th Day from Appointed date	28 th July 2019	393.27 Cr.
III	Commenced construction of all Project Facilities and achieved 75% of Physical Progress	690 th Day from Appointed date	13 th April 2020	842.72 Cr.
IV	Completion Of the Project	910 th Day from Appointed date	19 th Nov 2020	1123.63 Cr.

Payment Milestones

Project Milestone	Condition	Status
I	Commenced construction of Project and achieved 10% of Physical Progress	Achieved on 20 th Dec 2018
II	Commenced construction of Project and achieved 30% of Physical Progress	Achieved on 31 st August 2019
III	Commenced construction of all Project Facilities and achieved 50% of Physical Progress	Achieved on 21 st August 2020
IV	Commenced construction of all Project Facilities and achieved 75% of Physical Progress	
V	Commenced construction of all Project Facilities and achieved 90% of Physical Progress	

3. Progress Status

Progress Status as per submitted Programme									
Sr.	Item	Unit	Scope of work as per schedule -B	Planned upto Jan-2021	Progress Achieved upto Dec-2020	This Month Progress	Cumulative in progress & Completed	Target for the month of Feb-2021	Remarks
No									
Highway Progress (Km.)									
1	C & G	Km	46.25	46.25	46.08	0.00		0	
2	Embankment Top	Km	46.25	35.00	35.2	1.00	36.20	2	
3	Subgrade	Km	46.25	31.76	33.8	1.00	34.80	1.98	
4	G.S.B	Km	46.25	29.50	31.9	0.50	32.40	2.97	
5	D.L.C	Km	46.25	27.69	27.77	0.50	28.27	3.46	
6	P.Q.C	Km	46.25	24.86	24.58	2.00	26.58	3.46	
Structure Progress: (No.s)									
1	HPC	No	16+31=47	45	45.00	0.00	45.00	0	
2	BC	No	21+2=23	22.5	22.00	0.50	22.50	0.5	
3	PUP Slab	No	6	0	0.00	0.00	0.00	2	
4	MNB Slab	No	22	20.5	20.00	0.50	20.00	0	
5	MJB Slab	No	39	11	15.00	4.00	19.00	4	
6	VUP Slab	No	18	15	11.00	0.00	11.00	2	
7	LVUP Slab	No	26	26	24.00	0.00	24.00	0	
8	Elevated Slab	No	40	40	40.00	0.00	40.00	0	
9	ROB Slab	No	6	0	0.00	0.00	0.00	0	
10	RUB Slab	No	10	5	4	0.00	4	1	
11	Flyover Slab	No	20	20	20	0.00	20	0	

1. Physical Progress Planned upto Jan -2021:- **65.68 %**

(As per Revised programme Submitted on 20.06.2020)

2. Physical Progress achieved upto Jan -2021:- **63.19%**

3. Physical progress achieved in Month of Jan-2021:- **02.80%**



Summary of Progress (January 2021)
Highway Progress:

Sr. No.	Item	Unit	Scope of work	Completed / Work in progress	Balance work
1	C & G	Km	46.25	46.08	0.17
2	Embankment Top	Km	46.36	36.20	8.16
3	Sub- Grade	Km	46.36	34.80	11.56
4	GSB	Km	46.36	32.40	13.96
5	DLC (MC)	Km	46.36	28.27	18.09
6	PQC (MC)	Km	46.36	26.58	19.78
7	Embankment(SR)	Km	28.38	22.50	5.88
8	Sub- Grade(SR)	Km	28.38	17.17	11.21
9	GSB(SR)	Km	28.38	14.36	14.02
10	WMM (SR)	Km	28.38	12.70	15.68
11	DBM (SR)	Km	28.38	11.97	16.41
12	BC (SR)	Km	28.38	00.00	28.38



Structure Progress Status:-

Sl. No.	Structure Details:-	Unit	Scope	Completed	Work in progress	Balance	Remarks
1	Major Bridge	Nos	2	0	2	0	85% Achieved
2	Elevated Road	Nos	1	0	1	0	95% Achieved
3	Minor Bridge	Nos	11	10	0	0	1 no. deleted & 90% Completed
4	Box Culvert	Nos	23	22	1	0	2 nos. (Additional)
5	Pipe Culvert	Nos	47	45	0	2	31 No. (Additional)
6	Vehicular Underpass	Nos	9	6.5	2.5	0	85% Completed
7	Light Vehicular Underpass	Nos	13	12	0	1	80% Completed
8	Flyover	Nos	3	3	0	0	Completed
9	ROB	Nos	1	0	1	0	25% Achieved
10	RUB	Nos	1	0	1	0	20% Completed
11	Drain	Km	28.38	22	4	2.38	

1. Physical progress Achieved upto Jan 2021- 63.19%
2. Financial Progress Achieved upto Jan 2021- 67.45% (757.906 Crs)
(Financial S- Curve attached at the end)
3. Financial Progress Planned upto Jan-2021- 64.10%




4. Utility Shifting Progress

24-05-2018 is the Appointed Date for the project. 85% of the land measuring to Km 41.548 has been handed over by the Authority. As on date 99.62% is available and 0.38% (0.185 mtrs) of land is balance due to presence of structures, religious structure and other land related issues.

1. Permission for cutting of trees on Government land and forestland received. Cutting of trees in progress. Ref. no 1594 dated 03 / 05 / 2018 (Jhalawar) &1837-44 dated 22/05/2018(Kota)
2. Electrical Utilities estimate approved in both district Kota &Jhalawar vide letter 41010 & 41011 1/2016- Kota / US – Electric- Kota and Jhalawar / Package-2/7077 dated 24th August 2018. Work for shifting of electrical utilities under progress.Work is balance in existing alignment due to presence of structure.
3. Water Pipelines Estimate is approved vide letter no. _41024 / 1 / 2016- Kota/ US - PHED- Kota / Pkg-II/ 6998 dated 16-08 2018 and 41025 / _1 / 2016- Kota / US /6997 dated 16-08-2018 Shifting work in progress. Work balance only in stretches having LA related issues.
4. Estimate of HT Lines is approved. Material received at site for execution. Survey done with department for finalizing locations of new tower. Foundation & Tower erection work in progress.

Details of numbers and length are as below: -


<u>Utility Shifting</u>							
Sr. No.	Particulars	Total	Progress till last month	Current month	Cumulative Progress till Jan-21	Balance to be completed	Remarks
1	Electric Poles						
	Kota Section	600	596	0	596	4	Balance in kukdakhurd at CH.11+100 to 11+400 LHS, No. 04
	Jhalawar Section	141	141	0	141	0	
	Total	741	733	0	737	4	
2	Structures (Nos.)						
	Kota Section	403	378	00	378	25	Balance in Kukdakhurd at Ch. No 11+100 to 11+700 LHS.
	Jhalawar Section	159	159	0	159	0	
	Total	562	517	0	537	25	



Utility Shifting

Sr. No.	Particulars	Total	Progress till last month	Current month	Cumulative Progress till Jan-21	Balance to be completed	Remarks
3	Religious Strs (Nos.)						
	Kota Section	13	10	0	10	3	03 Nos construction in progress at Ch. No. 09+860 RHS, 11+300 LHS, 35+960 Median
	Jhalawar Section	2	2	0	2	0	
	Total	15	12	0	12	3	
4	Water Utilities (km)						
	Kota Section	9.875	9.05	0	9.05	0.825	Balance in Kukdakhurd at Ch. No 11+200 to 11+690 LHS & Dingsi at Ch no. 24+610 to 24+945 LHS
	Jhalawar Section	11.125	11.125	0	11.125	0	
	Total	21	20.175	0	20.175	0.825	
5	High Tension Line						
Sr. No.	Chainage No.	Foundation		Tower Erection		String	
		LHS	RHS	LHS	RHS	LHS	RHS
1	23+100	Completed	Completed	To be taken up	To be taken up	To be taken up	To be taken up
2	27+085	Completed	Completed	To be taken up	To be taken up	To be taken up	To be taken up
3	30+800	Completed	Completed	To be taken up	To be taken up	To be taken up	To be taken up
4	41+875	Completed	Completed	To be taken up	To be taken up	To be taken up	To be taken up
5	42+075	Completed	Completed	To be taken up	To be taken up	To be taken up	To be taken up
6	57+075	Completed	Completed	Completed	Completed	To be taken up	To be taken up
7	33+710	Estimate charges paid by NHA to PRVPL, Estimate are awaited					
8	42+950	Estimate charges paid by NHA to PRVPL, Estimate are awaited					

Note:- Awaiting for Shut Down Permission




5 Tree Cutting Status:-

Status of Tree Cutting:

Sr. No.	District	Category	Total Nos.	Status of Cutting permission	Cumulative No. of Cutting upto this month	Balance	Approval Letter No.	Remark	
1	Kota	Govt Trees	All	465	Yes	439	26	Revenue-III/2018/1837-44 dated 22.05.2018	Need not to be cut out of construction width
		Pvt. Trees	Fruit Bearing	2882	Not required	2797	85	No.41002/2016 - kota/L.A/Ramganjmandi/pkg-2/6243 dated 17.04.2018	Disbursement in progress Award of 365 Nos (85 fruit+280 non fruit) trees approved vide letter No. 175 dated 21.01.2020
			Non fruit Bearing	1560	Not required	1560	0		
2	Jhalawar	Govt Trees	All	972	Yes	972	0	Revenue/18/1594 dated 03.05.2018 & 1861 dated 25.05.2018	429 tree cutting approval vide letter no. 2868 dated 06.11.2018
		Pvt. Trees	Fruit Bearing	1836	Not required	1836	0	No.41003/2016 - kota/L.A/Jhalawar/pkg-2/6242 dated 17.04.2018	
			Non fruit Bearing	702	Not required	702	0		
		Forest		104	Yes	104	0	F-14()2017/Jhalawar Road/FCA/1998 dated 19.04.2018	
		Total Trees		8521		8410	111		99%

Note:- Private trees can be cut immediately after payment disbursement.

- 1) Total No. of trees increased from 7727 to 8521 Nos. because of (a) 429 trees along existing alignment added in Jhalawar District (b) 365 Nos (85 fruits+ 280 nonfruits) trees added in Kota District




6. Status of Conditions precedent

a	Provided Performance Security to the Authority	Released on 26.08.2019
b	Executed and procured execution of Escrow Agreement	Submitted. Vide this office letter no. PDJHPL / NHAI / FC / 039 .2018 Dt. 21-05-2018.
c	Executed and procured execution of Substitution Agreement	Submitted. Vide this office letter no. PDJHPL / NHAI / FC / 039 .2018 Dt. 21-05-2018.
d	Procure all Applicable Permits as per Schedule -E	Obtained
e	Executed Financing Agreements and delivered 3 copies duly attested by Director of the Concessionaire	Submitted. Vide this office letter no. PDJHPL / NHAI / FC / 039 .2018 Dt. 21-05-2018
f	Delivered to Authority 3 true copies of Financial Package and Financial Model duly attested by Director of the Concessionaire	Submitted. Vide this office letter no. PDJHPL / NHAI / FC / 039 .2018 Dt. 21-05-2018.
g	Delivered to Authority from Selected Bidder its respective confirmation in original of the correctness of their representations and warranties set forth in Sub Clause (k), (l) and (m) of Clause 7.1 of CA	Submitted
h	Environment Clearance	Done
i	Forest Land Clearance	Stage –II Clearance obtained
j	Wild Life Clearance	NA

7. Status of Railway Approvals

Proposal Description	Status	Length Impacted	Current Stage	Issues/ Comments
Rail ROB (Ch.44+158)	GAD of ROB Approved	-	Detailed design and drawing Approved by Railways.	Substructure Work in Progress.
RUB (Ch.33+585)	GAD of RUB Approved	-	Detailed design and drawing Approved by Railways. Work permission received on date 02.12.2019	Soil Nailing work in Progress




8. ISSUES OF CONCERN: -

1. (a) DLC issue from Km-
 - **CH: 32+500 to 36+000:** Land payment disbursed. Some Villagers are unsatisfied for fruit & non-fruit tree award done by NHAI.

(b) Court Case Chainages : Possession of following chainages is balance because of pending cases in SDM court.


Sr no.	Chainage		Length (M)	Remarks
	From	To		
1	11+100	11+700	600	
2	35+900	35+940	40	Hearing Postponed to 8 th Feb'21
	Total		640	

1. Disbursement for structures in both the districts Kota & Jhalawar is under progress. Structures in Jhalawar district have been removed. The process of payment in Kota district is very slow. Structures are pending in Kamalpura & Kukda khurd village. Because of non-removal of these hindrances the progress of electrical and water line shifting is affected, continuity of work fronts cannot be maintained. After disbursement of payment, it will take at-least 4-5 months for physical removal of these hindrance and shifting of utilities. Discontinuity of work stretches is having a direct impact on progress of work.
2. Approval of estimate for shifting of EHV crossing done. Material procured at site. Survey related to crop compensation is completed by concerned authorities. Award approval is awaited from NHAI. The excavation & foundation work of EHV lines has been started. And 06 nos. of foundation work for EHV lines are completed out of 06 nos. The locations where foundation work of EHV lines completed are Km. 23+100, Km. 27+085, Km. 30+800, Km. 41+875, 42+075 & Km. 57+075. Also 1 no. of tower erection work completed. 02 Nos EHV tower approvals are awaited from concerned department & authority.
3. 3A of missing plots in Jhalawar district is pending, though work has been taken up in the affected stretches.
4. Disbursement of payment of religious structure within PROW is yet to be done (Jhalawar District).
5. Award of left over structures / trees is pending for payment in Ramganjmandi tehsil (Kota District) & Jhalawar District.
6. **The Works of Major Bridge (Ahu river bridge) at A-1 side i.e A-1, P-1, P-2, P-3 in the village boundary of Gola are affected and works are not progressing (held up) because of land Acquisition Issues since 20.10.2020.**
7. Independent Engineer recommended the Extension of Time (EOT) to Authority vide Letter No. 1343 dated 18.11.2020 for revised schedule completion date as 07.09.2021.
8. Authority has granted 180 days of Extension of Time due to COVID -19 vide NHAI, PIU, Kota letter No. 41041/1/2018-Kota/IE-LASA/General/Pkg-II/2172 dated 29th Dec 2020.
9. Independent Engineer recommended the Change of Scope (COS) and forwarded to the Authority vide Letter No. 1175 dated 10.12.2020 for approval.
10. The details of hindrances is attached as **Annexure-I**.




9. QUALITY ASSURANCE & LAB MONTHLY PROGRESS REPORT
MONTH OF January-2021


Sr. No.	Name of Test	Number of Tests Conducted									Remarks
		Up To Previous Month			This Month			Total upto Date			
		Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test	
OGL & Cutting soil											
1	Free Swell Index	317	0	317	0	0	0	317	0	317	
2	Grain Size Analysis	317	0	317	0	0	0	317	0	317	
3	Plasticity Index	317	0	317	0	0	0	317	0	317	
4	Max. Dry Density	317	0	317	0	0	0	317	0	317	
5	CBR	6	0	6	0	0	0	6	0	6	
6	Density of Comp.Layer	6781	143	6924	19	0	19	6800	143	6943	
7	Moisture Cont.	0	0	0	0	0	0	0	0	0	
Borrow Area (Embankment & Subgrade)											
1	Free Swell Index	2254	42	2296	156	0	156	2410	42	2452	
2	Grain Size Analysis	2274	42	2316	156	0	156	2430	42	2472	
3	Plasticity Index	2274	42	2316	160	0	160	2434	42	2476	
4	Max. Dry Density	2278	42	2320	160	0	160	2438	42	2480	
5	CBR	491	28	519	51	0	51	542	28	570	
Earthwork Field test											
1	Density of Comp.Layer (Emb.)	84115	482	84597	16796	12	16808	100911	494	101405	
2	Density of Comp.Layer (Sub grade & Earthen shoulder)	13725	115	13840	1300	0	1300	15025	115	15140	
GSB											
1	Sieve Analysis	473	0	473	106	0	106	579	0	579	
2	Plasticity Index	470	0	470	106	0	106	576	0	576	
3	Max. Dry Density	4	0	4	0	0	0	4	0	4	
4	CBR	2	0	2	0	0	0	2	0	2	
5	Water Absorption	2	0	2	0	0	0	2	0	2	
6	AIV	3	0	3	0	0	0	3	0	3	
7	Density of Comp. Layer	1491	23	1514	268	0	268	1759	23	1782	
WMM											




Sr. No.	Name of Test	Number of Tests Conducted									Remarks
		Up To Previous Month			This Month			Total upto Date			
		Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test	
1	Sieve Analysis	91	0	91	30	0	30	121	0	121	
2	Plasticity Index	91	0	91	30	0	30	121	0	121	
3	Aggregate Impact Value	71	0	71	18	0	18	89	0	89	
4	Combined F.I & E.I.	70	0	70	24	0	24	94	0	94	
5	Max. Dry Density	0	0	0	0	0	0	0	0	0	
6	Density of Comp.Layer	510	0	510	244	0	244	754	0	754	
7	Water Absorption	0	0	0	0	0	0	0	0	0	
8	Soundness Test	0	0	0	0	0	0	0	0	0	
DBM											
1	Aggregate Impact Value	46	0	46	7	0	7	53	0	53	
2	Flakiness & Elongation	45	0	45	7	0	7	52	0	52	
3	Mix Grading	60	0	60	7	0	7	67	0	67	
4	Individual Grading	18	0	18	0	0	0	18	0	18	
5	Stability of Mix	102	0	102	27	0	27	129	0	129	
6	Binder Content & Grading Mix	61	0	61	14	0	14	75	0	75	
7	Density of Compacted layer	123	0	123	20	0	20	143	0	143	
8	Gmm Test	46	0	46	14	0	14	60	0	60	
PRIME COAT											
1	Quality Of Binder (Viscosity)	5	0	5	1	0	1	6	0	6	
2	Rate of Spray of Binder	97	0	97	21	0	21	118	0	118	
TACK COAT											
1	Quality Of Binder	1	0	1	1	0	1	2	0	2	
2	Rate of Spray of Binder	114	0	114	21	0	21	135	0	135	
PHYSICAL PROPERTIES OF AGGREGATE FOR CONCRETE											
1	Sieve Analysis of CA	1549	0	1549	60	0	60	1609	0	1609	
2	Sieve Analysis of FA	1466	0	1466	60	0	60	1526	0	1526	
3	Sieve Analysis of DLC	204	0	204	18	0	18	222	0	222	
4	Sieve Analysis of PQC	280	0	280	18	0	18	298	0	298	



Sr. No.	Name of Test	Number of Tests Conducted									Remarks
		Up To Previous Month			This Month			Total upto Date			
		Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test	
5	Aggregate Impact Value	1728	0	1728	96	0	96	1824	0	1824	
6	Flakiness Index	1728	0	1728	96	0	96	1824	0	1824	
7	Silt Content	309	0	309	0	0	0	309	0	309	
8	Specific Gravity & W A	17	0	17	0	0	0	17	0	17	
Concrete Mix Design (cube sets)											
1	M15 7 Days	40	0	40	0	0	0	40	0	40	
	28 Days	68	0	68	0	0	0	68	0	68	
2	M20 Kerb 7 Days	19	0	19	0	0	0	19	0	19	
	28 Days	26	0	26	0	0	0	26	0	26	
	M20 7 Days	12	0	12	0	0	0	12	0	12	
	28 Days	18	0	18	0	0	0	18	0	18	
3	M25 7 Days	67	0	67	0	0	0	67	0	67	
	28 Days	108	0	108	0	0	0	108	0	108	
4	M30 7 Days	68	0	68	0	0	0	68	0	68	
	28 Days	12	0	12	0	0	0	12	0	12	
5	M35 7 Days	144	0	144	0	0	0	144	0	144	
	28 Days	258	0	258	0	0	0	258	0	258	
6	M35 Pile 7 Days	72	0	72	0	0	0	72	0	72	
	28 Days	142	0	142	0	0	0	142	0	142	
7	M35 RE block 7 Days	45	0	45	0	0	0	45	0	45	
	28 Days	144	0	144	0	0	0	144	0	144	
8	M40 7 Days	75	0	75	0	0	0	75	0	75	
	28 Days	115	0	115	0	0	0	115	0	115	
9	M45 7 Days	59	0	59	0	0	0	59	0	59	
	28 Days	113	0	113	0	0	0	113	0	113	
10	M50 7 Days	0	0	0	0	0	0	0	0	0	
	28 Days	2	0	2	0	0	0	2	0	2	
11	M40 PQC 7 Days	164	0	164	0	0	0	164	0	164	
	28 Days	268	0	268	0	0	0	268	0	268	



Sr. No.	Name of Test	Number of Tests Conducted									Remarks
		Up To Previous Month			This Month			Total upto Date			
		Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test	
12	M40 PQC Fl. Strength 7 Days	129	0	129	0	0	0	129	0	129	
	28 Days	149	0	149	0	0	0	149	0	149	
13	DLC 7 Days	101	0	101	0	0	0	101	0	101	
14	Grouting	6	0	6	0	0	0	6	0	6	
Field Concrete (cube sets)											
1	M15 7 Days	2375	0	2375	138	0	138	2513	0	2513	
	28 Days	3613	0	3613	200	0	200	3813	0	3813	
2	M20 Kerb 7 Days	266	0	266	52	0	52	318	0	318	
	28 Days	308	0	308	103	0	103	411	0	411	
3	M25 7 Days	3347	0	3347	208	0	208	3555	0	3555	
	28 Days	4514	0	4514	191	0	191	4705	0	4705	
4	M30 7 Days	521	0	521	34	0	34	555	0	555	
	28 Days	980	0	980	130	0	130	1110	0	1110	
5	M35 7 Days	3958	0	3958	93	0	93	4051	0	4051	
	28 Days	9443	0	9443	247	0	247	9690	0	9690	
6	M35 Pile 7 Days	208	0	208	0	0	0	208	0	208	
	28 Days	361	0	361	0	0	0	361	0	361	
7	M35 RE block 7 Days	940	0	940	0	0	0	940	0	940	
	28 Days	2847	0	2847	0	0	0	2847	0	2847	
8	M40 7 Days	861	0	861	82	0	82	943	0	943	
	28 Days	1538	0	1538	204	0	204	1742	0	1742	
9	M45 7 Days	208	0	208	0	0	0	208	0	208	
	28 Days	764	0	764	5	0	5	769	0	769	
10	M50 7 Days	0	0	0	0	0	0	0	0	0	
	28 Days	0	0	0	0	0	0	0	0	0	
11	M40 PQC 7 Days	780	0	780	67	0	67	847	0	847	
	28 Days	775	0	775	117	0	117	892	0	892	




Sr. No.	Name of Test	Number of Tests Conducted									Remarks
		Up To Previous Month			This Month			Total upto Date			
		Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test	
12	M40 PQC Flexural Strength 7 Days	798	0	798	67	0	67	865	0	865	
	28 Days	793	0	793	117	0	117	910	0	910	
13	DLC 7 Days	509	0	509	135	0	135	644	0	644	
14	DLC FDD	895	0	895	112	0	112	1007	0	1007	
Cement											
1	Fineness	177	0	177	6	0	6	183	0	183	
2	Consistency	177	0	177	6	0	6	183	0	183	
3	Setting Time	177	0	177	6	0	6	183	0	183	
4	Soundness	157	0	157	6	0	6	163	0	163	
5	Compressive Strength										
	a) 3 Days	283	0	283	6	0	6	289	0	289	
	b) 7 Days	281	0	281	5	0	5	286	0	286	
	c) 28 Days	286	0	286	7	0	7	293	0	293	



WEATHER REPORT (Month of January-2021)

No.	Date	Temperature C		Humidity %		Rainfall (mm)	Climate
		Min. Temp. (°C)	Max. Temp. (°C)	Min.	Max.		
1	01-01-21	22.1	11.4	80.0	61.0	0.0	Clear
2	02-01-21	26.1	16.2	84.0	59.0	0.0	Cloudy/rain @ site
3	03-01-21	26.0	16.5	83.0	66.0	0.0	Cloudy
4	04-01-21	24.1	16.4	85.0	60.0	0.0	Cloudy
5	05-01-21	24.9	16.5	84.0	61.0	0.0	Clear
6	06-01-21	24.8	16.4	88.0	60.0	0.0	Cloudy
7	07-01-21	21.7	16.5	87.0	70.0	0.0	Cloudy
8	08-01-21	22.0	16.3	85.0	60.0	0.0	Cloudy
9	09-01-21	22.8	16.8	90.0	70.0	0.0	Cloudy
10	10-01-21	20.6	15.6	91.0	71.0	0.0	Cloudy
11	11-01-21	22.0	11.5	90.0	63.0	0.0	Clear
12	12-01-21	22.0	9.6	82.0	39.0	0.0	Clear
13	13-01-21	22.6	8.5	76.0	33.0	0.0	Clear
14	14-01-21	22.5	8.8	79.0	44.0	0.0	Clear
15	15-01-21	24.1	9.8	78.0	28.0	0.0	Clear
16	16-01-21	24.9	12.6	74.0	39.0	0.0	Clear
17	17-01-21	26.5	15.2	72.0	51.0	0.0	Clear
18	18-01-21	27.3	14.7	73.0	55.0	0.0	Clear
19	19-01-21	24.2	13.0	77.0	52.0	0.0	Clear
20	20-01-21	24.9	11.4	81.0	37.0	0.0	Clear
21	21-01-21	26.3	11.2	81.0	27.0	0.0	Clear
22	22-01-21	26.2	12.1	70.0	27.0	0.0	Clear
23	23-01-21	23.3	13.1	69.0	47.0	0.0	Clear
24	24-01-21	23.9	10.6	65.0	38.0	0.0	Clear

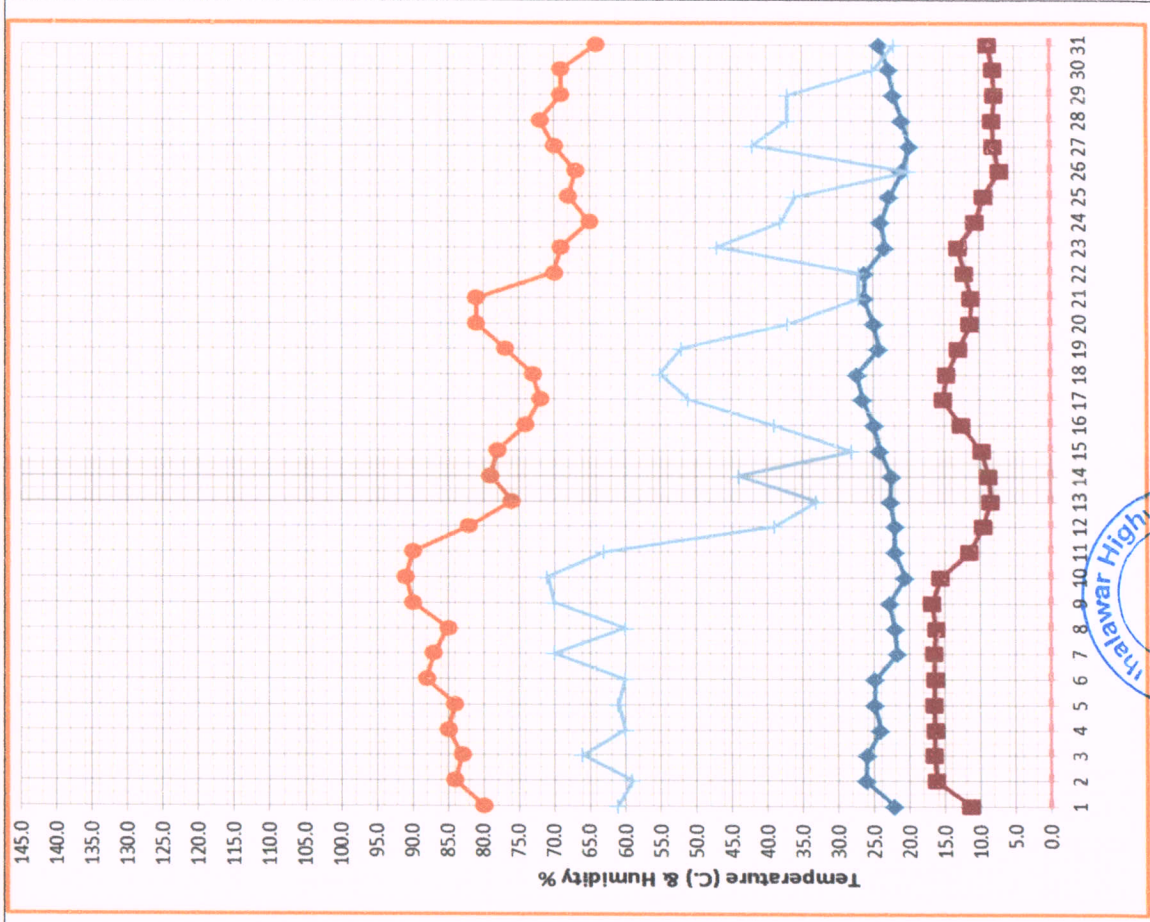


25	25-01-21	22.7	9.5	68.0	36.0	0.0	Clear
26	26-01-21	20.9	7.2	67.0	20.0	0.0	Clear
27	27-01-21	19.9	8.0	70.0	42.0	0.0	Clear
28	28-01-21	20.9	8.2	72.0	37.0	0.0	Clear
29	29-01-21	22.1	7.9	69.0	37.0	0.0	Clear
30	30-01-21	22.8	8.1	69.0	25.0	0.0	Clear
31	31-01-21	24.1	8.8	64.0	22.0	0.0	Clear



(Handwritten signature)

10. Status of Mix Design and Source Approval


Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
1	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	Submission of Mix Design	LASA/Concessionaire/D J/IE/2018/0003	21.08.2018
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-15(PCC Work) with flyash		
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-25(RCC Work) with flyash		
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-30(RCC Work) with flyash		
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-35(RCC Work) with flyash		
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-35(Pile Work with flyash		
2	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	Submission of Mix Design of Concrete from Ultratech&Mangalam Cement	LASA/Concessionaire/D J/IE/2018/0003	21.08.2018
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-35 RE Block (Ultratech&Mangalam cement)		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-35 with flyash RE Block (Ultratech&Mangalam cement)		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-15 PCC		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-25 RCC		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-30 RCC		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-35 RCC		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-35 Pile work		
3	PIL/CAMP/DJT/NHAI/2018-04/08	26.04.2018	Submission of Company profile & credential for the D.P. Wires	LASA/Concessionaire/D arah- Jhalawar/IE/2018/191	08.12.2018
4	PIL/CAMP/DJT/NHAI/2018-04/09	26.04.2018	Submission of Company profile & credential for the Shyam, Electrosteel and Premier Steel		
5	PDJHPL/NHAI/DJT/2018/019	12.03.2018	Submission of Company profile & credential for the Rashtriyaspat Nigam ltd (Vizag Steel),Nilkanth Steel Pvt.ltd, Steel authority of India limited (SAIL), Jindal steel & power limited ,Rashmi group ,Madhav Alloys Pvt.limited	LASA/Concessionaire/D J/IE/2018/17 and 58, 59 (10.09.2018)	30.08.2018
7	PIL/CAMP/DJP/N HAI/2018 -04 /063	21.06.2018	Submission of construction material for testing.		
8	PIL/CAMP/DJP/N HAI/2018 -04 /063	21.06.2018	Steel Dia 20mm JSW Steel (Fe-5.50D)		
10	PIL/CAMP/DJP/N HAI/2018 -04 /063	21.06.2018	Steel - Dia 12,25 & 32mm SAIL (Fe-500D)		
10	PDJHPL/NHAI/DJT/2018/013	26.02.2018	Submission of Company profile & credential for the Birla Corporation Limited ,Mangalam Cement Limited , Wonder cement Limited . Ultrtech cement Limited ,Vadraj cement . Shree cement Limited	LASA/Concessionaire/D J/IE/2018/14	28.08.2018
11	PIL/CAMP/DJT/NHAI/2018-04/01	26.04.2018	Submission of Company profile & credential for the BASF India Ltd.for Admixture,Grout and joint Sealant , Unirock Chemicals (Admixture) , Tikitar Ltd. For Joint Sealant	LASA/Concessionaire/D J/IE/2018/016	30.08.2018




Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
12	PDJHPL/NHAI/DJT/2018/020	22.03.2018	Submission of Company profile & credential for Admixture and curing compound ,Kunalconchempvt.ltd.,Grout and joint Sealant ,STPLimited&Chembond Chemicals Ltd.		
13	PIL/CAMP/DJP/N HAI/2018 -04 /063	21.06.2018	Admixture - PC 100R (KunallIndustries)		
14	PDJHPL/PIU/CLO-179/2018/095	04.07.2018	DLC Flyash		
15	PDJHPL/PIU/CLO-179/2018/095	04.07.2018	DLC without Flyash		
16	PIL/CAMP/DJP/N HAI/2018 -04 /063	21.06.2018	GSB (Julmi PIL Crusher)		
18	PIL/CAMP/DJT/NHAI/2018-04/06	26.04.2018	Submission of Company profile & credential for the IOCL (Bitumen) ,HPCL (Bitumen) ,ESSAR (Bituman) , GP global (Emulsions) , HINCOL (Emulsions) Total oil India pvt ltd. (Emulsions)	LASA/Concessionaire/D J/IE/2018/020 Bitumen& 19 for Emulsion	31.08.208
19	PIL/CAMP/DJT/NHAI/2018-04/02	26.04.2018	Submission of Company profile & credential for the SGG spun pipes	LASA/Cocessionaire/Darah- Jhalawar/IE/2018/050	07.09.2018
20	PIL/CAMP/DJT/NHAI/2018-04/03	26.04.2018	Submission of Company profile & credential for the TIKIDAN Danosa India	LASA/Concessionaire/Darah- Jhalawar/IE/2018/212	14.12.2018
21	PIL/CAMP/DJT/NHAI/2018-04/04	26.04.2018	Submission of Company profile & credential for the KANTAFLEX India Pvt.ltd. (Elastomeric & Pot bearing)	LASA/Concessionaire/Darah- Jhalawar/IE/2018/206	13.12.2018
22	PIL/CAMP/DJT/NHAI/2018-04/05	26.04.2018	Submission of Company profile & credential for the Dynamic Prestress (I) Pvt Ltd.	LASA/Concessionaire/Darah- Jhalawar/IE/2018/195	08.12.2018
23	PIL/CAMP/DJT/NHAI/2018-04/07	26.04.2018	Submission of Company profile & credential for the Amitek Infra (Thermoplastic Road Marking Paint)	LASA/Concessionaire/D J/IE/2018/018	30.08.2018
24	PDJHPL/NHAI/DJT/2018/021	22.03.2018	Submission of Company profile & credential for the Nakoda spun pipes		
25	PDJHPL/NHAI/DJT/2018/022	22.03.2018	Submission of Laboratory profile & credentials for the Star wire INDIA Pvt., Third party, Hind Heat		
26	PDJHPL/PIU/CLO-179/2018/047	21.06.2018	Submission of Gompny Profile &Gredential for source approval of Hercules Bridge Bearings & Bridge Expansion Joints	LASA/Concessionaire/Darah- Jhalawar/IE/2018/003	21.08.2018
27	PDJHPL/PIU/CLO-179/2018/096	04.07.2018	Submission of Company Profile &Gredential for Arihant Prefab	LASA/Concessionaire/Darah- Jhalawar/IE/2018/052	07.09.2018
28	PDJHPL/PIU/CLO-179/2018/100	05.07.2018	Submission of Gompny profile &Gredeniir for M.E. Testing Laboratory	LASA/Concessionaire/Darah- Jhalawar/IE/2018/178	04.12.2018
29	PDJHPL/PIU/CLO-179/2018/101	05.07.2018	Submission of Company Profile & Credential for MarutiBitumin Pvt. Ltd	LASA/Concessionaire/Darah- Jhalawar/IE/2018/054	07.09.2018
30	PDJHPL/PRJ/TEC/CLO-179/2018/022	02.06.2018	Submission of profite,Credentials& Basic design report on RE walls	LASA/Concessionaire/Darah- Jhalawar/IE/2018/055	07.09.2018
31	PDJHPL/PIU/D/2018/032	16.04.2018	Submission of Quality assurance Plan		
32	PDJHPL/PIU/CLO-179/2018/043	13.06.2018	Submission of Mix Design of Granular Sub-Base	LASA/Concessionaire/Darah- Jhalawar/IE/2018/155	28.11.2018
33	PDJHPL/PIU/CLO-179/2018/044	13.06.2018	Submission of Summary of OGL test results		
34	PDJHPL/PIU/CLO-179/2018/045	13.06.2018	Submission of Galibration Certificate of Batching Plant & Lab Equipments		
35	PDJHPL/PIU/CLO-179/2018/046	13.06.2018	Submission of Third party test reports of the material related to the project		




Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
36	PDJHPL/PIU/CLO-179/2018/056	18.06.2018	Submission of Petrographic Test Report of Coarse Aggregate		
37	PDJHPL/PIU/CLO-179/2018/108	06.07.2018	Submission of Borrow Area - 1,3,6,7,9,10,11,12,14,15,17,18,20,21,22,23,24,26,27,29,30,31,32,33,34 & 35		
38	PDJHPL/PIU/CLO-179/2018/110	07.07.2018	Submission of Company Profile & Credential for Earthcon Systems Pvt. Ltd	LASA/Concessionaire/Darah-Jhalawar/IE/2018/049	06.09.2018
39	PDJHPL/PIU/CLO-179/2018/111	07.07.2018	Submission of Construction Design (Geogrid Reinforced Soil Wall)	LASA/Concessionaire/Darah-Jhalawar/IE/2018/063	15.09.2018
40	PDJHPL/PIU/CLO-179/2018/122	10.07.2018	Testing for C & O Value of soil samples of Borrow area No. 1 & 22		
41	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	Submission of Mix-Design	LASA/Concessionaire/Darah-Jhalawar/IE/2018/003	21.08.2018
42	PDJHPL/PIU/CLO-179/2018/133	16.07.2018	Submission of Trial Patch Report of GSB & DLC		
43	PDJHPL/IE/ICO-181/2018/241	28.08.2018	Submission of Company Profile & Credential OF Maruti Rub Plast Pvt. Ltd.	LASA/Concessionaire/Darah-Jhalawar/IE/2018/088	15/10/2018
44	PDJHPL/IE/ICO-181/2018/242	28.08.2018	Submission of Company Profile & Credential Of Tar Products Pvt. Ltd.	LASA/Concessionaire/Darah-Jhalawar/IE/2018/053	07/09/2018
45	PDJHPL/NHAI/DJT/013/2018	28.08.2018	Submission of Company Profile & Credentials for Birla Corporation, Mangalam Cement, Wonder Cement, Ultratech Cement, Vadraj Cement & Shree Cement.	LASA/Concessionaire/Darah-Jhalawar/IE/2018/014	28/08/2018
46	PDJHPL/IE/ICO-181/2018/260	07.09.2018	Submission of Company Profile & Credential Of Sanfield (India) Ltd.	LASA/Concessionaire/Darah-Jhalawar/IE/2018/072	28/09/2018
47	PDJHPL/IE/ICO-181/2018/286	18.09.2018	Submission of Company Profile & Credential for RAMA TMT Bars	LASA/Concessionaire/Darah-Jhalawar/IE/2018/074	28/09/2018
48	PDJHPL/IE/ICO-181/2018/287	18.09.2018	Submission of Company Profile & Credential for SHYAM Steel	LASA/Concessionaire/Darah-Jhalawar/IE/2018/073	28/09/2018
49	PDJHPL/IE/ICO-181/2018/318	29.09.2018	Submission of Company Profile & Credential of Sanfield (India) Ltd.-reg	LASA/Concessionaire/Darah-Jhalawar/IE/2018/078	03.10.2018
50	PDJHPL/IE/ICO-181/2018/348	09.10.2018	Submission of Company Profile & Credentials of Katalinepaints.-reg	LASA/Concessionaire/Darah-Jhalawar/IE/2018/091	15/10/2018
51	PDJHPL/IE/ICO-181/2018/353	10.10.2018	Submission of Third party testing of RE wall concrete block in km. 23+600-reg	LASA/Concessionaire/Darah-Jhalawar/IE/2018/130	13.11.2018
52	PDJHPL/IE/ICO-181/2018/362	12.10.2018	Submission of Company Profile & Credentials of PNT designs Pvt. Ltd.	LASA/Concessionaire/Darah-Jhalawar/IE/2018/126	13.11.2018
53	PDJHPL/IE/ICO-181/2018/367	13.10.2018	Submission of GSB Mix design for approvals	LASA/Concessionaire/Darah-Jhalawar/IE/2018/111	29/10/2018
54	PDJHPL/IE/ICO-181/2018/381	18.10.2018	Submission of Filter media Mix-design-reg	LASA/Concessionaire/Darah-Jhalawar/IE/2018/217	13.11.2018
55	PDJHPL/IE/ICO-181/2018/408	26.10.2018	Submission of Company Profile and Credential of M/s Deevin Seismic Systems Pvt. Ltd. for Expansion Joints-reg	LASA/Concessionaire/Darah-Jhalawar/IE/2018/127	13.11.2018
56	PDJHPL/IE/ICO-181/2018/429	02/11/2018	Submission of DLC Mix Design Confirmatory Reports-reg	LASA/Concessionaire/Darah-Jhalawar/IE/2018/127	03.12.2018




Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
				Jhalawar/IE/2018/163	
57	PDJHPL/IE/ICO-181/2018/450	17/11/2018	Submission of Company profile & Credentials of M/s Deevin Seismic Systems Pvt. Ltd. for Expansion joints - reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/199	12.12.2018
58	PDJHPL/IE/ICO-181/2018/451	17/11/2018	Submission of third party test report of construction materials-reg		
59	PDJHPL/IE/ICO-181/2018/452	17/11/2018	Submission of Company profile & Credential of JK Lakshmi Cement Ltd-reg	LASA/Concessionaire/D arah -Jhalawar/IE/2018/148	26/11/2018
60	PDJHPL/IE/ICO-181/2018/453	17/11/2018	Submission of company Profile & Credentials of Supreme Bitumen India Pvt. Ltd.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/162	03.12.2018
61	PDJHPL/IE/ICO-181/2018/454	17/11/2018	Resubmission of Company Profile & Credentials of M/s Hind Heat Treatment & Testing House-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/158	30.11.2018
62	PDJHPL/IE/ICO-181/2018/455	17/11/2018	Submission of Company Profile & Credentials of M/s Yash Enterprises-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/177	04.12.2018
63	PDJHPL/IE/ICO-181/2018/460	20/11/2018	Submission of Company Profile & Credentials of M/s Electrotherm India Ltd. -	LASA/Concessionaire/D arah- Jhalawar/IE/2018/190	08.12.2018
64	PDJHPL/IE/ICO-181/2018/461	20/11/2018	Submission of Mix Design of WMM-reg	LASA/Concessionaire/D arah -Jhalawar/IE/2018/152	27/11/2018
66	PDJHPL/IE/ICO-181/2018/473	22/11/2018	Submission of Concrete Mix Design Done only with Wonder & Ultratech Cement-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/211	15.12.2018
67	PDJHPL/IE/ICO-181/2018/475	22/11/2018	Submission of Concrete Mix Design Using Fly ash with Wonder & Ultratech Cements-reg		
68	PDJHPL/IE/ICO-181/2018/479	23/11/2018	Submission of PQC M-40 Design Using Fly ash with Ultratech Cement-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/176	04.12.2018
69	PDJHPL/IE/ICO-181/2018/480	23/11/2018	Submission of Company Profile & Credentials of M/s KunalConchem Pvt. Ltd.-reg	LASA/Concessionaire/D arah -Jhalawar/IE/2018/147	26/11/2018
70	PDJHPL/IE/ICO-181/2018/510	30/11/2018	Submission of PQC M-40 Design with Ultratech Cement.		
71	PDJHPL/IE/ICO-181/2018/511	30/11/2018	Submission of Company Profile & Credentials of M/s. Normat India Pvt.Ltd	LASA/Concessionaire/D arah- Jhalawar/IE/2018/207	13/12/2018
72	PDJHPL/IE/ICO-181/2018/521	03/12/2018	Submission of Julmi Crusher Aggregate Test Reports-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/196	10/12/2018
73	PDJHPL/IE/ICO-181/2018/522	03/12/2018	Submission of Fine Aggregate Test Report of Kalisindh River-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/197	10/12/2018
74	PDJHPL/IC/ICO-181/2018/542	08/12/2018	Submission of company profile & credential of M/s HI-TECH Engineering Solutions - reg		
75	PDJHPL/IC/ICO-181/2018/599	21/12/2018	Submission of Test Report of Spun pipes for NP-4 pipe - reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/226	24/12/2018
76	PDJHPL/IC/ICO-181/2018/620	31/12/2018	Submission of Inspection Report of Elastomeric Bearing Testing (KANTAFLEX) - reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/247	04.01.2019
77	PDJHPL/IC/ICO-181/2018/626	02/01/2019	Submission of Chemical Composition Test Report of Steel.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/288	24/01/2019
78	PDJHPL/IC/ICO-181/2019/638	05/01/2019	Submission of PQC (M-40) Mix Design with Ultratech Cement.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/252	11/01/2019
79	PDJHPL/IC/ICO-181/2019/639	05/01/2019	Submission of PQC (M-40) Mix Design using Flyash with Ultratech Cement.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/250	10/01/2019
80	PDJHPL/IC/ICO-181/2019/643	07/01/2019	Submission of Company Profile and Credentials of Molecule Conchem Pvt.Ltd	LASA/Concessionaire/D arah- Jhalawar/IE/2018/273	21.01.2019




Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
81	PDJHPL/IC/ICO-181/2019/653	10/01/2019	Submission of Test Report of T.M.T Bars from Electrotherm (India) Ltd.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/297	04/02/2019
82	PDJHPL/IC/ICO-181/2019/665	15/01/2019	Submission of Third Party Test Report of Reinforcement Steel (Hind Heat Treatment)	LASA/Concessionaire/Darah-Jhalawar/IE/2019/292	28/01/2019
83	PDJHPL/IC/ICO-181/2019/666	15/01/2019	Review of Mix Design of PQC (M-40) with Ultratech Cement & Unirock Plasticizers.		
84	PDJHPL/IC/ICO-181/2019/672	16/01/2019	Review of Mix Design of PQC (M-40) with Ultratech Cement, Flyash & Unirock Plasticizers.		
85	PDJHPL/IC/ICO-181/2019/685	21/01/2019	Submission of Company Profile and Credentials of Choksey Chemicals Pvt. Ltd.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/289	28/01/2019
86	PDJHPL/IC/ICO-181/2019/686	21/01/2019	Submission of Company Profile and Credentials of J.K Cement Ltd.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/290	28/01/2019
87	PDJHPL/IC/ICO-181/2019/713	31/01/2019	Submission of Test Report of POT/PTFE Bearings for Flyover+Major Bridge 47+650 to 48+150 (Dynamic Prestress Pvt. Ltd).	LASA/Concessionaire/Darah-Jhalawar/IE/2019/304	06/02/2019
88	PDJHPL/IC/ICO-181/2019/732	06/02/2019	Submission of PQC Trial patch Report from Ch.28+400 to 28+147(LHS) - reg		
89	PDJHPL/IC/ICO-181/2019/753	12/02/2019	Submission of Company Profile & Credentials of Ooms Avenhorn Holding India Pvt. Ltd. & Ooms Polymer Modified Bitumen Pvt. Ltd.-reg	LASA/Concessionaire/Darah-Jhalawar/IE/2019/307	18/02/2019
90	PDJHPL/IC/ICO-181/2019/761	14/02/2019	Submission of Company Profile & Credential of Unirock Chemicals Pvt. Ltd.-reg	LASA/Concessionaire/Darah-Jhalawar/IE/2019/308	18/02/2019
91	PDJHPL/IC/ICO-181/2019/788	20/02/2019	Submission of Company Profile & Credential of MSP Group for procurement of Dowel Bars - reg		
92	PDJHPL/IC/ICO-181/2019/798	25/02/2019	Submission of Company Profile & Credetial of M/s Sika India - reg	LASA/NHAI/Darah-Jhalawar/IE/2019/350	16.03.2019
93	PDJHPL/IC/ICO-181/2019/804	26/02/2019	Submission of Company Profile & Credential of M/s STP Ltd - reg	LASA/NHAI/Darah-Jhalawar/IE/2019/351	16.03.2019
94	PDJHPL/IC/ICO-181/2019/812	28/02/2019	Submission of Company Profile & Credetial of MSP steel & Power Ltd - reg.		
95	PDJHPL/IC/ICO-181/2019/833	07/03/2019	Submission of Company Profile & Credetial of Chembond Chemicals - reg	LASA/Concessionaire/Darah-Jhalawar/IE/2019/352	16.03.2019
96	PDJHPL/IC/ICO-181/2019/962	23/04/2019	Submission of Company Profile & Credetial of Fortune Ltd -reg		
97	PDJHPL/IC/ICO-181/2019/967	25/04/2019	Submission of Company Profile & Credetial of Balajee Loha Ltd -reg		
98	PDJHPL/IC/ICO-181/2019/1018	09/05/2019	Submission of Company Profile & Credetial of Essar Steel -reg		
99	PDJHPL/IC/ICO-181/2019/1019	09/05/2019	Submission of Company Profile & Credetial of Bostik Pvt Ltd -reg	LASA/Concessionaire/Darah-Jhalawar/IE/2019/415	16/05/2019
100	PDJHPL/IC/ICO-181/2019/1031	11/05/2019	Submission of Methodology of Pile Load Test of Routine Pile @ 57+127 (MJB)		
101	PDJHPL/IC/ICO-181/2019/1048	16/05/2019	Submission of Methodology of Pile Load Test of Routine Pile @ 36+070 (MJB)	LASA/Concessionaire/Darah-Jhalawar/IE/2019/429	24/05/2019
102	PDJHPL/IC/ICO-181/2019/1074	25/05/2019	Submission of Plate Load Test Report Conducted at 36+070 (MJB) & 58+128 (Flyover).		
103	PDJHPL/IC/ICO-181/2019/1083	28/05/2019	Submission of Initial Load Test Report Conducted on Test Pile .		
104	PDJHPL/IC/ICO-181/2019/1088	30/05/2019	Submission of Company Profile & Credetial of Nuvoco Vistas Corp. Ltd -reg	LASA/Concessionaire/Darah-Jhalawar/IE/2019/583	27/09/2019



Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
105	PDJHPL/IC/ICO-181/2019/1098	03/06/2019	Submission of Kerb (M-20) with Ultratech Cement without Flyash.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/446	10/06/2019
106	PDJHPL/IC/ICO-181/2019/1099	03/06/2019	Submission of SPT Test Report for Ch.36+070 (MJB)		
107	PDJHPL/IC/ICO-181/2019/1100	03/06/2019	Submission of Bore Log Test Report @ 36+070 (MJB) & 58+128 (Flyover).		
108	PDJHPL/IC/ICO-181/2019/1189	30/06/2019	Submission of Company Profile & Credential of STECOL (Essar TMT Brand)		
109	PDJHPL/IC/ICO-181/2019/1369	07/09/2019	Submission of Company Profile & Credential of VADOL Corporation	LASA/Concessionaire/Darah-Jhalawar/IE/2019/587	28/09/2019
110	PDJHPL/IC/ICO-181/2019/1379	10/09/2019	Change in Company name Deevin Engineering Consulting group to DECG International.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/596	05/10/2019
110	PDJHPL/IC/ICO-181/2019/1402	18/09/2019	Submission of Company Profile & Credential of J Sons Engg Corporation	LASA/Concessionaire/Darah-Jhalawar/IE/2019/594	03/10/2019
111	PDJHPL/IC/ICO-181/2019/1437	30/09/2019	Submission of Company Profile & Credential of Shree Cement Limited	LASA/Concessionaire/Darah-Jhalawar/IE/2019/595	04/10/2019
112	PDJHPL/IC/ICO-181/2019/1564	21/11/2019	Submission of Inspection Report of Elastomeric Bearing Testing (KANTAFLEX India Pvt. Limited) for MJB 36+070	LASA/Concessionaire/Darah-Jhalawar/IE/2019/666	27/11/2019
113	PDJHPL/IC/ICO-181/2019/1574	23/11/2019	Submission of Company Profile & Credential of Electrosteel Steels Limited	LASA/Concessionaire/Darah-Jhalawar/IE/2019/671	29/11/2019
114	PDJHPL/IC/ICO-181/2019/1605	30/11/2019	Submission of company profile & credential of M/s Sika India Pvt. Ltd.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/699	12/12/2019
115	PDJHPL/IC/ICO-181/2019/1619	05/12/2019	Submission of Plate Load Test Report of BC (53+700).		
116	PDJHPL/IC/ICO-181/2019/1620	05/12/2019	Submission of Plate Load Test Report of VUP (Km 54+550).		
117	PDJHPL/IC/ICO-181/2019/1621	05/12/2019	Submission of Inspection Test Report of POT/ PTFE Bearing (Dynamic Prestress) of Elevated @ Km 47+830 & MJB @ Km 57+127.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/700	12/12/2019
118	PDJHPL/IC/ICO-181/2019/1654	14/12/2019	Submission of Company Profile and Credential of M/s BASF India Limited (for Admixture).	LASA/Concessionaire/Darah-Jhalawar/IE/2020/719	02/01/2020
119	PDJHPL/IC/ICO-181/2019/1665	17/12/2019	Submission of Factory Visit and TMT inspection Test Report of M/s Electrosteel Steels Limited for TMT Bars and Third Party Test Report.		
120	PDJHPL/IC/ICO-181/2019/1684	21/12/2019	Submission of Test Report of Strands of DP Wires.		
121	PDJHPL/IC/ICO-181/2019/1698	26/12/2019	Submission of Inspection Test Report of POT/ PTFE Bearing (Dynamic Prestress) of Flyover @ Km 46+957, Km 50+095, Km 58+128.	LASA/NHAI/Darah-Jhalawar/IE/2020/798	20/02/2020
122	PDJHPL/IC/ICO-181/2019/1700	26/12/2019	Submission of High Strain Dynamic Pile Load Test Report of MJB @ Km 36+070.		
123	PDJHPL/IC/ICO-181/2019/1743	08/01/2020	Submission of Mix Design of DBM with VG-40 Grade.		
124	PDJHPL/IC/ICO-181/2019/1745	08/01/2020	Submission of Concrete Mix design with Nuvoco Cement & Sika Admixture & Without Flyash.		
125	PDJHPL/IC/ICO-181/2019/1753	11/01/2020	Submission of Test Report of Core Sample of Retaining Wall Raft.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/754	22/01/2020
126	PIL/PRJ/TECH/ODO-189/2020/1755	11/01/2020	Submission of Company Profile & Credential of HMM Infra Ltd.		



Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
127	PDJHPL/IC/ICO-181/2020/1766	16/01/2020	Submission of Company Profile & Credential of GOEL TMT.		
128	PDJHPL/IC/ICO-181/2020/1770	17/01/2020	Submission of Test Report of Steel of MJB @ Ch 57+127, LVUP @ Ch 23+065.	LASA/NHAI/Darah-Jhalawar/IE/2020/766	30/01/2020
129	PDJHPL/IC/ICO-181/2020/1799	30/01/2020	Submission of Plate Load Test Report of ROB @ 44+158.		
130	PDJHPL/IC/ICO-181/2020/1810	30/01/2020	Submission of Environmental Monitoring Test Report for the year 2020.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/754	05/02/2020
131	PDJHPL/IC/ICO-181/2020/1842	07/02/2020	Submission of Company Profile & Credential of TATA Steel Ltd for Procurement of LRPC Strands		
132	PDJHPL/IC/ICO-181/2020/1886	19/02/2020	Submission of Independent Laboratory Test Reports of Geogrid of Strata Geosystems (India) Pvt. Ltd		
133	PDJHPL/IC/ICO-181/2020/2158	29/07/2020	Submission of Company Profile and Credential of J.K Prestressing Co. for Jack use in Girder prestressing work of MJB @ Km 57+127.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/963	07/08/2020
134	PDJHPL/IC/ICO-181/2020/2166	31/07/2020	Submission of Company Profile & Credential of BG Trade Infra for Procurement of Plastic for Bituminous Mixs.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/959	04/08/2020
135	PDJHPL/IC/ICO-181/2020/2231	25/08/2020	Submission of Company Profile & Credential of JSW Steel Ltd for TMT Steel.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1009	03/09/2020
136	PDJHPL/IC/ICO-181/2020/2260	07/09/2020	Submission of Test Report of Selected Soil / Reinforced soil proposed for RE Wall at Km 43+825, 44+150 & Km 45+875.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1041	25/09/2020
137	PDJHPL/IC/ICO-181/2020/2270	09/09/2020	Compressive Strength Test Reports of Core taken PQC @Km 28+680 (LHS).	LASA/NHAI/Darah-Jhalawar/IE/2020/1032	18/09/2020
138	PDJHPL/IC/ICO-181/2020/2290	16/09/2020	Submission of Company Profile & Credential of Shivam Concrete Tech. & Consultancy Ltd for NDY Testing & Rehabilitation Work.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1033	21/09/2020
139	PDJHPL/IC/ICO-181/2020/2324	28/09/2020	Submission of Test Report of Selected Soil / Reinforced soil proposed for RE Wall at Km 43+825, 44+150 & Km 45+875.		
140	PDJHPL/IC/ICO-181/2020/2325	28/09/2020	Submission of Test Reports from Independent Laboratory for Selected Soil of RE Wall Backfill Proposed with soil blended with Crusher run / GSB.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1056	05/10/2020
141	PDJHPL/IC/ICO-181/2020/2348	07/10/2020	Submission of Soil Samples Proposed for Reinforced Fill in RE Wall areas for Conducting Tests (Borrow area 136 at Shyampur Village - Jhalawar District)	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1065	13/10/2020
142	PDJHPL/IC/ICO-181/2020/2359	08/10/2020	Compliance on Review of Test Report for Selected Soil of RE Wall Back Fill Proposed Soil blended with Crusher run / GSB (Borrow Area No. 131).	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1063	13/10/2020
143	PDJHPL/IC/ICO-181/2020/2363	09/10/2020	Submission of Test Report of Selected Soil / Reinforced soil proposed for RE Wall Back fill (B.A No. 134).	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1064	13/10/2020
144	PDJHPL/IC/ICO-181/2020/2375	13/10/2020	Submission of Test Reports of Selected Soil / reinforced Soil proposed for RE Wall Backfill (B/A No. 136).	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1080	23/10/2020
145	PDJHPL/IC/ICO-181/2020/2381	15/10/2020	Submission of Test Report of Selected Soil / Reinforced Soil proposed for RE Wall Back fill (B.A No. 130).	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1088	28/10/2020
146	PDJHPL/IC/ICO-181/2020/2382	15/10/2020	Submission of Test Report of Selected Soil / Reinforced Soil proposed for RE Wall Back fill (B.A No. 131).	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1086	28/10/2020
147	PDJHPL/IC/ICO-181/2020/2385	17/10/2020	Submission of Compliance on Comments made by Independent	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1086	22/10/2020




Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
			Engineer for Source Approval of JSW Steel Ltd.	Jhalawar/IE/2020/1079	
148	PDJHPL/IC/ICO-181/2020/2386	17/10/2020	Submission of Test Reports (after screening & stocking) of selected Soil / Reinforced Soil Proposed for RE Wall Backfill (B/A No. 130) and compliance on comments by Independent Engineer.	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1088	28/10/2020
149	PDJHPL/IC/ICO-181/2020/2387	17/10/2020	Submission of Company Profile & Credentials of M/s Rajdeep Info Techno Pvt Ltd for supplying, providing, installing and commissioning of Traffic Management System & Advance Traffic Management System.	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1096	30/10/2020
150	PDJHPL/IC/ICO-181/2020/2391	19/10/2020	Submission of Test Report of Selected Soil / Reinforced Soil Proposed for RE Wall Backfill (B/A No. 138).	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1084	28/10/2020
151	PDJHPL/IC/ICO-181/2020/2404	24/10/2020	Submission of Job Mix Formula (JMF) for Bituminous Concrete with VG-40 Grade Bitumen & Plastic Waste.	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1100	02/11/2020
152	PDJHPL/IC/ICO-181/2020/2411	27/10/2020	Submission of Test report of Selected Soil/Reinforced Soil Proposed for RE Wall Backfill (B/A 141).	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1113	06/11/2020
153	PDJHPL/IC/ICO-181/2020/2413	28/10/2020	Submission of Test report of Selected Soil / Reinforced Soil Proposed for RE Wall Backfill (B/A No. 131).	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1086	28/10/2020
154	PDJHPL/IC/ICO-181/2020/2417	02/11/2020	Submission of Test report of Selected Soil / Reinforced Soil Proposed for RE Wall Backfill (B/A No. 141).		
155	PDJHPL/IC/ICO-181/2020/2465	07/12/2020	Submission of Test Report of Reinforcement Steel.	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1186	18/12/2020
156	PDJHPL/IC/ICO-181/2020/2472	12/12/2020	Submission of Routine Pile Load Test Report for MJB @ Km 36+070.	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1184	18/12/2020
157	PDJHPL/IC/ICO-181/2020/2482	12/12/2020	Submission of Company Profile and Credentials of M/s Nayara Energy Ltd (Earlier Known as: Essar Oil Ltd) for Bitumen VG-40 Grade	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1208	30/12/2020
158					
159	PDJHPL/IC/ICO-181/2021/2516	11/01/2021	Submission of Independent Laboratory Test Reports of Reinforcement Steel, Admixture & Water.	LASA/NHAI/Darah- Jhalawar/IE/2021/1236	15/01/2021
160	PDJHPL/IC/ICO-181/2021/2519	13/01/2021	Compressive Strength Test Reports of Core taken from PQC.		
161	PDJHPL/IC/ICO-181/2021/2529	23/01/2021	Submission of Company Profile & Credentials of M/s Reliance Industries Ltd. For Procurement of 'Reliance Recron 3s Fibers' to use in PQC Works.	LASA/NHAI/Darah- Jhalawar/IE/2021/1244	27/01/2021
162	PDJHPL/IC/ICO-181/2021/2533	25/01/2021	Submission of Compressive Strength Test Reports of Core Taken from PQC during Site Visit of Authority & Independent Engineer.	LASA/NHAI/Darah- Jhalawar/IE/2021/1247	27/01/2021
163	PDJHPL/IC/ICO-181/2021/2534	25/01/2021	Submission of Test Reports of Compressive Strength of RE Block Collected from Casting Yard of M/s Earthcon during Site Visit of Authority & Independent Engineer.	LASA/NHAI/Darah- Jhalawar/IE/2021/1246	27/01/2021
164	PDJHPL/IC/ICO-181/2021/2535	25/01/2021	Submission of Test Reports of Reinforcement Steel.	LASA/NHAI/Darah- Jhalawar/IE/2021/1249	28/01/2021




11. Status of submitted Drawings


S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
				Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
1	Pipe Culvert	09+925	09+919	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (075 D-26.06.18), (1029 D-11.05.19)			213 D-15.12.18, (499 D-23.07.19)		
2	Pipe Culvert	10+425	10+423	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (075 D-26.06.18), (1029 D-11.05.19)			213 D-15.12.18, (499 D-23.07.19)		
3	Pipe Culvert	10+595	10+592	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (075 D-26.06.18), (1029 D-11.05.19)			213 D-15.12.18, (499 D-23.07.19)		
4	Pipe Culvert	10+825	10+824	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (075 D-26.06.18), (1029 D-11.05.19)			213 D-15.12.18, (499 D-23.07.19)		
5	Pipe Culvert	11+030	11+031	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (075 D-26.06.18), (1029 D-11.05.19)			213 D-15.12.18, (499 D-23.07.19)		
6	Box Culvert	11+605	11+605	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (463 D-20.11.18), (060 D-23.10.18), (899 D-30.03.19)			094 D-15.10.18, (134 D-14.11.18), (515 D-31.07.19)		
7	Vehicular Underpass	12+125	12+125	Submitted	Submitted	Submitted	Not yet approved	Not yet approved	Approved
				018 D-12.03.18, (063 D-17.11.18), (188 D-08.08.19)			118 D-02.11.18, (123 D-10.11.18)		
8	Minor Bridge	12+400	12+380	Submitted	Submitted	Submitted	Approved	Approved	Approved
				138 D-18.07.18, (1210 D-11.07.19), (1321 D-22.08.19)			489 D-17.07.19, (503), (569 D-13.09.19)		
9	Light Vehicular Underpass	12+450	12+450	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (067 D-22.06.18), (1168 D-22.06.19)			092 D-15.10.18, (322 D-23.02.19)		
10	Box Culvert	13+400	13+400	Submitted	Submitted	Submitted	Not yet approved	Not yet approved	Not yet approved
				016 D-27.02.18, (463 D-20.11.18), (060 D-23.10.18)			094 D-15.10.18, (134 D-14.11.18)		
11	Box Culvert	13+980	13+980	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (463 D-20.11.18), (060 D-23.10.18)			094 D-15.10.18, (134 D-14.11.18), (481 D-11.07.19)		
12	Box Culvert	14+980	14+980	Submitted	Submitted	Submitted	Not yet approved	Not yet approved	Not yet approved
				016 D-27.02.18, (463 D-20.11.18), (060 D-23.10.18)			094 D-15.10.18, (134 D-14.11.18)		
13	VUP	15+725	15+725	Submitted	Submitted	Submitted	Not yet approved	Not yet approved	Approved
				018 D-12.03.18, (188 D-08.08.18)			123 D-10.11.18		
14	Minor	16+050	16+060	Submitted	Submitted	Submitted	Approved	Approved	Approved

Ra



S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
				Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
	Bridge			138 D-18.07.18, (850 D-15.03.19), (1422 D-25.09.19), (1289 D-08.08.19), (1290 D-08.08.19), (1486 D-21.10.19), (1534 D-09.11.19)			353 D-16.03.19, (394 D-26.04.19), (586 D-27.09.19), (627 D-01.11.19)		
15	Box Culvert	16+600	16+580	Submitted	Submitted	Submitted	Not yet approved	Not yet approved	Not Approved
				016 D-27.02.18, (463 D-20.11.18), (060 D-23.10.18)			094 D-15.10.18, (134 D-14.11.18)		
16	Pipe Culvert	17+320	17+320	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
17	Light Vehicular Underpass	17+353	17+353	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.2018, (67 D-22.06.18), 1168 (D-22.06.2019)			092 D-15.10.18, (348 D-14.03.19)		
18	Minor Bridge	17+950	17+890	Submitted	Submitted	Submitted	Approved	Approved	Approved
				037 D-07.06.18, (562 D-11.12.18)			394 D-26.04.19		
19	Pipe Culvert	18+210	18+206	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
20	Pipe Culvert	18+810	18+810	(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
21	Vehicular Underpass	19+965	19+930	Submitted	Submitted	Submitted	Not yet approved	Approved	Approved
				018 D-12.03.18, (188 D-08.08.18)			123 D-10.11.18, (747 D-09.01.20)		
22	Pipe Culvert	20+840	20+840	Submitted	Submitted	Submitted	Approved	Approved	Approved
				1377-D-10.09.2019			(1189 D-19.12.2020)		
23	Pipe Culvert	21+150	21+150	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
24	Light Vehicular Underpass	21+180	21+183	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (67 D-22.06.18), (1168 D-22.06.19)			092 D-15.10.18 (322 D-23.02.19)		
25	Pipe Culvert	21+700	21+647	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (075 D-26.06.18), (1029 D-11.05.19)			213 D-15.12.18, (499 D-23.07.19)		
26	Pipe Culvert	22286	22+277	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
27	Box Culvert	22+450	22+450	Submitted	Submitted	Submitted	Not Approved	Not Approved	Not Approved
				016 D-27.02.18, (463 D-20.11.18), (60 D-23.10.18)			094 D-15.10.18, (134 D-14.11.18)		
28	Pipe	22+850	22+850	Submitted	Submitted	Submitted	Approved	Approved	Approved




S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
				Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
	Culvert			016 D-27.02.18, (075 D-23.07.18), (1029 D-11.05.19), 1565 (D-21.11.19)			213 D-15.12.18, (506 D-26.07.19), (693 D-12.07.19), (698 D-12.12.19)		
29	Light Vehicular Underpass	23+065	23+065	Submitted	Submitted	Submitted	Approved	Approved	Approved
				16 D-27.02.18, (067 D-22.06.18), (1168 D-22.06.19)			092 D-15.10.18, (322 D-23.02.19)		
30	Pipe Culvert	23+670	23+666	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18 (75 D-23.07.18) (1029 D-11.05.19)			213 D-15.12.18, (499 D-23.07.19)		
30	Light Vehicular Underpass	23+695	23+687	Submitted	Submitted	Submitted	Approved	Approved	Approved
				16 D-27.02.18, (067 D-22.06.18), (1168 D-22.06.19)			092 D-15.10.18, (322 D-23.02.19)		
31	Pipe Culvert	23+950	23+950	(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
32	Light Vehicular Underpass	24+547	24+547	Submitted	Submitted	Submitted	Approved	Approved	Approved
				16 D-27.02.18, (067 D-22.06.18), (1168 D-22.06.19)			092 D-15.10.18, (322 D-23.02.19)		
33	Box Culvert	24+610	24+610	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (138 D-18.07.18), (388 D-20.10.18), (463 D-20.11.18)			093 D-15.10.18, (482 D-11.07.19) (717 D-28.12.19)		
34	Vehicular Underpass	25+100	25+100	Submitted	Submitted	Submitted	Not yet approved	Not yet approved	Approved
				018 D-12.03.18 (188 D-08.08.18)			123 D-10.11.18		
35	Box Culvert	25+800	25+800	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18 (463 D-20.11.18), (060 D-23.10.18)			094 D-15.10.18 (134 D-14.11.18) (481 D-11.07.19)		
36	Vehicular Underpass	27+025	27+029	Submitted	Submitted	Submitted	Not yet approved	Not yet approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			123 D-10.11.18		
37	Pipe Culvert	27+050	27+050	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
38	Pipe Culvert	27+600	27+600	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
39	Box Culvert	28+550	28+550	Submitted	Submitted	Submitted	Approved	Approved	Approved
				717 D-01.02.19, (1298 D-13.08.2019), (2470 D-07.12.2020)			(620 D-31.10.2019), (1189 D-19.12.2020)		
40	Box Culvert	29+000	29+000	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18 (463 D-20.11.18) (060 D-23.10.18)			094 D-15.10.18 (134 D-14.11.18) (481 D-11.07.19)		




S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
				Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
41	Minor Bridge	29+610	29+600	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18 (138 D-18.07.18) (487 D-26.11.18) (554 D-10.12.18) (006 D-18.01.19)			107 D-29.10.18 (188 D-08.12.18) (233 D-26.12.19)		
42	Box Culvert	29+900	29+900	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18 (138 D-18.07.18) (388 D-20.10.18) (463 D-20.11.18)			093 D-15.10.18, (104 D-26.10.18) (482 D-11.07.19) (714 D-28.12.19)		
43	Vehicular Underpass	30+075	30+078	Submitted	Submitted	Submitted	Not Approved	Not Approved	Approved
				041 D-12.06.18 (632 D-03.01.19), (1510 D-11.2.19), (1912 D-26.02.20), (1962 D-17.03.20)			479 D-09.07.19 (511 D-29.07.19) (645 D-15.11.19), (756 D-24.01.20), (818 D-05.03.2020), (839 D-13.04.20)		
44	Pipe Culvert	30+100	30+100	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
45	Pipe Culvert	31+245	31+245	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
46	Pipe Culvert	31+700	31+700	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
47	Pipe Culvert	32+130	32+150	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
48	Box Culvert	32+050	32+050	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18 (463 D-20.11.18) (060 D-23.10.18)			(094 D-15.10.18) (134 D-14.11.18) (481 D-11.07.19)		
49	Pipe Culvert	32+150	32+150	(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
50	Box Culvert	32+300	32+295	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18 (463 D-20.11.18) (060 D-23.10.18)			(094 D-15.10.18) (134 D-14.11.18) (481 D-11.07.19)		
51	Minor Bridge	33+000	33+000	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18 (037 D-06.07.18) (564 D-11.12.19), (1640 D-10.12.19)			505 (D-26.07.19) (512 D-30.07.19), (746 D-16.01.20)		
52	Pipe Culvert	33+100	33+100	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
53	Pipe Culvert	33+300	33+300	(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
54	RUB	33+585	33+585	Submitted	Submitted	Submitted	Approved by RLWY	Approved by RLWY	Approved by RLWY
				019 D-31.05.18 (828)			(1137 D-06.10.19)		
55	Minor Bridge	34+350	34+350	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (564 D-11.12.19), (1640 D-10.12.19), (1641 D-10.12.19)			(505 D-26.07.19), (512 D-30.07.19), (746 D-16.01.20)		




S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
				Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
56	Box Culvert	35+250	35+205	Submitted (093 D-04.07.2018),	Submitted (463 D-20.11.18),	Submitted	Approved	Approved	Approved (515 D-31.07.19)
57	Major Bridge	36+105	36+070	Submitted (034 D-19.04.18), (014 D-27.02.18), (037 D-07.06.18), (492 D-26.11.18), (014 D-18.03.19), (068 D-12.12.18), (1666&1705 D-27.12.19), (2227 D- 24.8.20), (2285 D-15.09.20)	Submitted	Submitted	Hold (Compliance on Geotechnical report is already submitted	Approved	Approved
58	Box Culvert	36+750	36+719	Submitted (093 D-04.07.2018),	Submitted (463 D-20.11.18),	Submitted	Not Approved	Not Approved	Not Approved
59	Pipe Culvert	37+040	37+040	Submitted 1377-D-10.09.2019	Submitted	Submitted	Approved	Approved	Approved (1189 D-19.12.2020)
60	Light Vehicular Underpass	37+050	37+053	Submitted (067 D-22.06.18), (004 D-10.01.19), (1168 D-22.06.19)	Submitted	Submitted	Approved	Approved	Approved (092 D-15.10.18), (219 D-21.12.19), (348 D-14.03.19)
61	Box Culvert	37+550	37+550	Submitted (037 D-07.06.18),	Submitted (463 D-20.11.18),	Submitted	Approved	Approved	Approved 481 D-11.07.19
62	Box Culvert	38+100	38+141	Submitted (093 D-04.07.18),	Submitted (463 D-20.11.18)	Submitted	Not Approved	Not Approved	Not Approved
63	Pipe Culvert	38+535	38+535	Submitted (1377-D-10.09.2019),	Submitted (1961-D- 16.03.2020)	Submitted	Approved	Approved	Approved (1189 D-19.12.2020)
64	Light Vehicular Underpass	38+545	38+547	Submitted (067 D-22.06.18),	Submitted (1168 D-22.06.19)	Submitted	Approved	Approved	Approved (092 D-15.10.18), (348 D-14.03.19)
65	Box Culvert	39+180	39+162	Submitted (037 D-07.06.18),	Submitted (463 D-20.11.18),	Submitted	Approved	Approved	Approved (481 D-11.07.19)
66	Pipe Culvert	39+570	39+625	Submitted (1377-D-10.09.2019),	Submitted (1961-D- 16.03.2020)	Submitted	Approved	Approved	Approved (1189 D-19.12.2020)
67	Pipe Culvert	40+200	40+200	Submitted (1377-D-10.09.2019),	Submitted (1961-D- 16.03.2020)	Submitted	Approved	Approved	Approved (1189 D-19.12.2020)
68	Pipe Culvert	40+600	40+600	Submitted (1377-D-10.09.2019),	Submitted (1961-D- 16.03.2020)	Submitted	Approved	Approved	Approved (1189 D-19.12.2020)



Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
			Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
Vehicular Underpass	41+095	41+102	Submitted	Submitted	Submitted	Not Approved	Not Approved	Approved
			(041 D-12.06.18), (632 D-03.01.19), (1498 D-24.10.19), (1571 D-22.11.19), (2097 D-06.07.20), (2125 D-16.07.20)			(479 D-09.07.20), (514 D-30.07.19), (517 D-31.07.19), (933 D-15.07.20), (949 D-27.07.20), (953 D-28.07.20),		
Light Vehicular Underpass	41+465	41+468	Submitted	Submitted	Submitted	Approved	Approved	Approved
			(067 D-22.06.18), (005 D-10.01.19), (1168 D-22.06.19)			(092 D-15.10.18), (220 D-21.12.19), (348 D-14.03.19)		
Pipe Culvert	41+478	41+481	Submitted	Submitted	Submitted	Approved	Approved	Approved
			(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
Pipe Culvert	41+950	41+917	Submitted	Submitted	Submitted	Approved	Approved	Approved
			(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
Pipe Culvert	42+252	42+252	Submitted	Submitted	Submitted	Approved	Approved	Approved
			(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
Light Vehicular Underpass	42+258	42+263	Submitted	Submitted	Submitted	Approved	Approved	Approved
			(067 D-22.06.18), (078 D-05.01.19), (1168 D-22.06.19)			(92 D-15.10.18), (348 D-14.03.19)		
Pipe Culvert	42+530	42+552	Submitted	Submitted	Submitted	Approved	Approved	Approved
			(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
Pipe Culvert	43+220	43+221	Submitted	Submitted	Submitted	Approved	Approved	Approved
			1377-D-10.09.2019			(1189 D-19.12.2020)		
Pipe Culvert	43+680	43+680	Submitted	Submitted	Submitted	Approved	Approved	Approved
			(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
Light Vehicular Underpass	43+825	43+670	Submitted	Submitted	Submitted	Not Approved	Not Approved	Not Approved
			(067 D-22.06.18), (377 D-17.10.18), (829 D-06.03.19)			(092 D-15.10.18), (335 D-05.03.19)		
Box Culvert	44+070	44+070	Submitted	Submitted	Submitted	Approved	Approved	Approved
			(1298 D-13.08.19)			(1130 D-12.11.2020)		
Rail Over Bridge	44+158	44+158	Submitted	Submitted	Submitted	P-1, P-2 is approved by RLWY & A1 & A-2 (BHS) is approved by IE	P-1, P-2 is approved by RLWY & A1 & A-2 (BHS) is approved by IE	P-1, P-2 is approved by RLWY & A1 & A-2 (BHS) is approved by IE
			(118 D-09.07.18), (550 D-10.12.18), (1355 D-04.09.19), (1397 D-17.09.19),			(7504 D-06.11.18), (572 D-17.09.19), (582 D-26.09.19), (669 D-27.11.19),		



S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
				Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
				(1570 D-22.11.19)			(797 D-20.02.20), (1038 D-25.09.20)		
81	Minor Bridge	44+900	44+910	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(146 D-23.07.18), (582 D-17.12.18), (608 D-26.12.18)			(225 D-24.12.18), (347 D-14.03.19), (394 D-26.04.19)		
82	Pipe Culvert	45+200	45+200	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(146 D-23.07.18), (075 D-26.06.18), (1029 D-11.05.19)			(499 D-23.07.19)		
83	Pipe Culvert	45+800	45+800	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(037 D-07.06.18), (075 D-26.06.18), (1029 D-11.05.19), (1565 D-21.11.19),			(213 D-15.12.18), (506 D-26.07.19), (693 D-07.12.19), (698 D-12.12.19)		
84	Light Vehicular Underpass	45+875	45+876	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(037 D-07.06.18), (067 D-22.06.18), (1168 D-22.06.19)			(092 D-15.10.18), (348 D-14.03.19)		
85	Pipe Culvert	45+875	45+925	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
86	Pipe Culvert	46+650	46+650	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
87	Flyover	46+957	46+900 to 47+000	Submitted	Submitted	Submitted	Not Approved	Not Approved	Not Approved
				(115 D-09.07.18), (431 D-03.11.18),			(328 D-28.02.19), (487 D-15.07.19)		
88	Elevated Highway	47+830	47+830	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(037 D-07.06.18), (003 D-09.01.19),			(284 D-23.01.19)		
89	Pipe Culvert	48+220	48+221	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(146 D-23.07.18), (075 D-26.06.18), (1029 D-11.05.19)			(213 D-15.12.18), (499 D-23.07.19)		
90	PUP	48+260	48+260	Submitted	Submitted	Submitted	Approved	Approved	Approved
				2181-D-06.08.2020			(1202 D-29.12.2020)		
91	Pipe Culvert	48+385	48+354	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(146 D-23.07.18), (075 D-26.06.18), (1029 D-11.05.19)			(213 D-15.12.18), (499 D-23.07.19)		
92	Pipe Culvert	48+645	48+654	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(146 D-23.07.18), (075 D-26.06.18), (1029 D-11.05.19)			(213 D-15.12.18), (499 D-23.07.19)		
93	Pipe Culvert	48+875	48+890	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(146 D-23.07.18), (075 D-26.06.18), (1029 D-11.05.19)			(213 D-15.12.18), (499 D-23.07.19)		
94	Vehicular Underpass	49+330	49+330	Submitted	Submitted	Submitted	Not Approved	Not Approved	Approved
				(041 D-12.06.19), (632 D-03.01.19), (1499 D-24.10.19), (1571 D-22.11.19),			(479 D-09.07.19), (514 D-30.07.19), (518 D-31.07.19), (639 D-11.11.19),		




S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
				Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
				(2097 D-06.07.20), (2125 D-16.07.20)			(715 D-28.12.19), (950 D-27.07.20), (953 D-28.07.20)		
95	Pipe Culvert	49+290	49+290	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
96	Minor Bridge	49+775	49+785	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(317 D-29.09.18)			(394 D-26.04.19)		
97	Flyover	50+095	50+099	Submitted	Submitted	Submitted	Not Approved	Not Approved	Not Approved
				(115 D-09.07.18), (431 D-03.11.18),			(329 D-28.02.19), (487 D-15.07.19)		
98	PUP	51+450	51+450	Submitted			Approved		
				2204-D-17.08.2020, (2255 D-05.09.2020), (2480 D-16.12.2020)			(1112 D-06.11.2020), (1203 D-29.12.2020)		
99	Pipe Culvert	51+750	51+750	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(037 D-07.06.18), (075 d-26.06.18), (1029 D-11.05.19), (1565 D-21.11.19)			(213 D-15.12.18), (506 D-26.07.19), (693 D-07.12.19), (698 D-12.12.19)		
100	Light Vehicular Underpass	51+762	51+774	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(067 D-22.06.18), (1168 D-22.06.19)			(092 D-15.10.18), (348 D-14.03.19)		
101	Pipe Culvert	52+630	52+690	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
102	Box Culvert	53+125	53+125	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(041 D-12.06.18), (463 D-20.11.18), (1533 D-09.11.19)			(482 D-11.07.19), (714 D-28.12.19)		
103	Box Culvert	53+700	53+700	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1211 D-11.07.19), (1349 D-03.09.19)			(493 D-19.07.19), (632 D-07.11.19)		
104	Box Culvert	53+900	53+900	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(041 D-12.06.18), (463 D-20.11.18), (1533 D-09.11.19)			(482 D-11.07.19), (714 D-28.12.19)		
105	Minor Bridge	54+075	54+072	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(041 D-12.06.18), (191 D-09.08.18), (830 D-06.03.19)			(336 D-05.03.19), (347 D-14.03.19), (394 D-26.04.19)		
106	Minor Bridge	54+125	54+040	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(146 D-23.07.18), (763 D-15.02.19), (816 D-01.03.19)			(314 D-21.02.19), (347 D-14.03.19), (394 D-26.04.19)		
107	Vehicular Underpass	54+500	54+605	Submitted	Submitted	Submitted	Not Approved	Not Approved	Approved
				(041 D-12.06.18), (632 D-03.01.19), (1357 D-04.09.19), (1398 D-17.09.19)			(565 D-11.09.19), (514 D-30.07.19), (571 D-17.09.19)		
108	Pipe Culvert	54+210	54+210	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		


S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
				Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
109	Pipe Culvert	55+125	54+143	Submitted (146 D-23.07.18), (075 D-26.06.18), (1029 D-11.05.19)	Submitted	Submitted	Approved	Approved	Approved
110	Box Culvert	55+820	55+830	Submitted (037 D-07.06.18), (463 D-20.11.18),	Submitted	Submitted	Approved	Approved	Approved
111	Major Bridge	57+127	57+127	Submitted	Submitted	Submitted	Hold (Compliance on Geotechnical report is already submitted)	Approved	Approved
				(072 D-25.06.18), (014 D-27.02.18), (358 D-11.10.18), (492 D-26.11.18), (578 D-15.12.18), (701 D-28.01.19), (820 D-02.03.19), (1356 D-04.09.19), (1434 D-28.09.19), (1465 D-11.10.19), (1611 D-03.12.19), (1672 D-18.12.19), (1719 D-31.12.19), (1951 D-11.03.20), (1559 D-19.11.19), (2227 D-24.08.20), (2285 D-15.09.20)			(203 D-12.12.18), (081 D-04.09.18), (293 D-28.01.19), (298&299 D-05.02.19), (316 D-23.02.19), (550 D-03.09.19), (573 D-17.09.19), (687&692 D-12.07.19), (670 D-29.11.19), (604&607 D-15.10.19), (370&372 D-03.04.19), (649 D-16.11.19), (826 D-17.03.20), (657 D-21.11.19), (1012 D-07.09.20)		
112	Flyover	58+125	58+125	Submitted (115 D-09.07.18), (431 D-03.11.18)	Submitted	Submitted	Approved	Approved	Approved
113	PUP	32+574	32+574	(2439 D- 24.11.2020), (2477 D-15.12.2020)			(1165 D- 15.12.2020), (1195 D-22.12.2020)		

S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site Condition	Concessionaire Submission (Letter No.)	Independent Engineer reply/review (Letter No.)
1	RE Wall Methodology (Selected Soil)			Submitted (Selected Soil) (1891 D-20.02.20), (1995 D-20.05.20), (2052 D-19.06.20),	Approved [for RE wall (Earthcon)] (860 D-14.05.20), (868 D-27.05.20), (923 D-07.07.20)
	RE Wall Methodology (Pondash)			Submitted (Pondash) (1653 D-13.12.2019), (1829 D-05.02.2020)	Approved [for RE wall (Earthcon)] (716 D-30.12.2019), (782 D-06.02.2020)
2	RE wall	12+125 & 12+450	12+125 & 12+450	Submitted (Pond Ash) (658 D-12.01.19/R0), (916 D-05.04.19), (1103 D-04.06.19)	Not yet Approved (367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill) (2337 D-01.10.2020), (2422 D-05.11.2020), (2466 D-07.12.2020), (2487 D-	Not yet Approved (1093 D-29.10.2020), 1118 (D-07.11.2020), (1205 D-29.12.2020)


S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site Condition	Concessionaire Submission (Letter No.) 23.12.2020)	Independent Engineer reply/review (Letter No.)
3	RE wall	15+725	15+725	Submitted (Pond Ash)	Not yet Approved
				(200 D-11.08.18/R0), (916 D-05.04.19), (1103 D-04.06.19)	(367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill)	Not yet Approved
				(851 D-15.03.19/R1)	
4	RE wall	17+353	17+353	Submitted (Pond Ash)	Not yet Approved
				(201 D-11.08.18/R0), (916 D-05.04.19), (1103 D-04.06.19)	(367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill)	Not yet Approved
				(851 D-15.03.19/R2), (1929 D-02.03.20)	
5	RE wall	19+965	19+930	Submitted (Pond Ash)	Not yet Approved
				(659 D-12.01.19/R0), (916 D-05.04.19), (1103 D-04.06.19)	(367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill)	Not yet Approved
				(851 D-15.03.19/R1), (2304 D-22.09.20/R2), (2492 D-26.12.2020)	1123 (D-11.11.2020), (1209 D-30.12.2020)
6	RE wall	21+180	21+183	Submitted (Pond Ash)	Not yet Approved
				(660 D-12.01.19/R0), (935 D-12.04.19/R1), (916 D-05.04.19), (1103 D-04.06.19)	(367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Not yet submitted (Reinforced fill)	Not yet Approved
7	RE wall	23+065	23+065	Submitted (Pond Ash)	Not yet Approved
				(661 D-12.01.19/R0), (971 D-26.04.19/R1)	(536 D-19.08.19)
				submitted (Reinforced fill)	Not yet Approved
				(2304 D-22.09.20/R2), (2492 D-26.12.2020)	1123 (D-11.11.2020), (1209 D-30.12.2020)
8	RE wall	23+695	23+687	Submitted (Pond Ash)	Not yet Approved
				(662 D-12.01.19/R0), (978 D-27.04.19/R1), (916 D-05.04.19), (1103 D-04.06.19)	(367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				submitted (Reinforced fill)	Not yet Approved
				(2304 D-22.09.20/R2), (2492 D-26.12.2020)	1123 (D-11.11.2020), (1209 D-30.12.2020)
9	RE wall	24+547 & 25+100	24+547 & 25+100	Submitted (Pond Ash)	Not yet Approved
				(202 D-11.08.18/R0), (916 D-05.04.19), (1103 D-04.06.19)	(367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill)	Not yet Approved
				(851 D-15.03.19/R1)	



S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site Condition	Concessionaire Submission (Letter No.)	Independent Engineer reply/review (Letter No.)
10	RE wall	27+025	27+029	Submitted (Pond Ash)	Not yet Approved
				(203 D-11.08.18/R0)	(367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill)	Not yet Approved
				(851 D-15.03.19/R1), (1929 D-02.03.20/R3)	
11	RE wall	30+075	30+078	Submitted (Pond Ash)	Not yet Approved
				(895 D-30.03.19/R0), ((367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill)	Not yet Approved
				(1929 D-02.03.20/R1)	
12	RE wall	37+050	37+053	Submitted (Pond Ash)	Not yet Approved
				(204 D-11.08.18/R0), (851 D-15.03.19/R1)	(367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill)	Not yet Approved
				(1929 D-02.03.20/R4)	
13	RE wall	38+545	38+547	Submitted (Pond Ash)	Not yet Approved
				(205 D-11.08.18/R0), (851 D-15.03.19/R1)	(367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill)	Not yet Approved
				(1929 D-02.03.20/R4)	
14	RE wall	41+095 & 41+465	41+102 & 41+468	Submitted (Pond Ash)	Approved
				(719 D-01.02.19/P1), (2086 D-02.07.20)	(243 D-01.01.19), (334 D-01.03.19), (367 D-02.04.19), (991 D-26.08.20)
				Submitted (Selected Soil)	
				(536 D-07.12.18/P0), (078 D-05.01.19)	
15	RE wall	42+258	42+263	Submitted (Pond Ash)	Approved
				(720 D-01.02.19/P1), (2086 D-02.07.20)	(243 D-01.01.19), (334 D-01.03.19), (367 D-02.04.19)
				Submitted (Selected Soil)	
				(537 D-07.12.18/P0), (078 D-05.01.19)	
				Submitted (A1-Pondash & A2-selected soil)	Not yet Approved
				(2284 D-15.09.20/P3), (2305 D-22.09.20)	(1026 D-16.09.20), (1128 D-12.11.2020)
16	RE wall	44+158	44+158	Submitted (Pond Ash)	Not yet Approved
				(1164 D-21.05.19/P0), (1603 D-30.11.19/P0)	(684 D-04.12.19), (925 D-08.07.20), (946 D-20.07.20),




S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site Condition	Concessionaire Submission (Letter No.)	Independent Engineer reply/review (Letter No.)
				Submitted (Reinforced fill)	(1021 D-11.09.20), (1140 D-18.11.2020)
17	RE wall	45+875	45+876	Submitted (Pond Ash)	Approved
				(1000 D-03.05.19/P1), (1606 D-30.11.19/P2)	(422 D-23.05.19), (688 D-05.12.19)
				Submitted (Reinforced fill)	Not yet Approved
				(2275 D-10.09.20/P3)	(1085 D-28.10.2020)
18	RE wall	49+330	49+330	Submitted (Pond Ash)	Approved
				(760 D-14.02.19/P1)	(243 D-01.01.19), (334 D-01.03.19), (367 D-02.04.19)
				Submitted (Reinforced fill)	
				(534 D-07.12.18/P0), (603 D-24.12.18/P0)	
19	RE wall	50+095	50+099	Submitted (Pond Ash)	Approved
				(759 D-14.02.19/P1), (1590 D-27.11.19/P2)	(243 D-01.01.19), (331 D-28.02.19), (334 D-01.03.19), (367 D-02.04.19)
				Submitted (Reinforced fill)	
				(535 D-07.12.18/P0), (602 D-24.12.18/P0)	
20	RE wall	51+762	51+774	Submitted (Pond Ash)	Approved
				(1001 D-03.05.19/P1)	(416 D-21.05.19)
				(Reinforced fill)	Not yet approved
				(2490 D-26.12.2020)	(1216 D-05.01.2021)
21	RE wall	54+500	54+605	Submitted (Pond Ash)	Not yet approved
				(2524 D-20.01.2021)	(1248 D-27.01.2021)
22	RE wall	58+125	58+125		
				Submitted (Reinforced fill)	Not yet approved
				(2478 D-15.12.2020)	(1192 D-21.12.2020)



Bearing Drawings Status

S.No	Chainage	Name of Structure	Type of Bearing	Submission Letter No	Approved vide Letter No	Remarks
1	12+125	VUP	Elastomeric	Letter No. 571 dated 13.12.2018	Letter No. 525 dated 06.08.2019	
2	15+725	VUP	Elastomeric	Letter No. 571 dated 13.12.2018	Letter No. 525 dated 06.08.2019	
3	19+965	VUP	Elastomeric	Letter No. 571 dated 13.12.2018	Letter No. 525 dated 06.08.2019	
4	25+095	VUP	Elastomeric	Letter No. 571 dated 13.12.2018	Letter No. 525 dated 06.08.2019	
5	27+029	VUP	Elastomeric	Letter No. 571 dated 13.12.2018	Letter No. 525 dated 06.08.2019	
6	30+078	VUP	Elastomeric	Letter No. 1511 dated 02.11.2019	Letter No. 650 dated 16.11.2019	
7	41+102	VUP	Elastomeric	Letter No. 1511 dated 02.11.2019	Letter No. 650 dated 16.11.2019	
8	49+330	VUP	Elastomeric	Letter No. 1511 dated 02.11.2019	Letter No. 650 dated 16.11.2019	
9	30+078	VUP	Pin & Guided	Letter No. 1953 dated 11.03.2020	Letter No. 810 dated 02.03.2020	IE observation vide letter no.810 with Marked correction and it complied by Concessionaire vide letter no. 1953
10	36+070	MJB	Elastomeric	Letter No. 1391 dated 16.09.2019	Letter No. 575 dated 18.09.2019	
11	41+102	VUP	Pin & Guided	Letter No. 1953 dated 11.03.2020	Letter No. 810 dated 02.03.2020	IE observation vide letter no.810 with Marked correction and it complied by Concessionaire vide letter no. 1953
12	44+158	ROB	POT / PTFE	Letter No. 1942 dated 06.03.2020	Letter No. 1038 dated 24.09.2020	
13	46+957	Flyover	POT / PTFE	Letter No. 705 dated 28.01.2019	Letter No. 651 dated 16.11.2019	
14	47+830	Elevated Highway	POT / PTFE	Letter No. 972 dated 26.04.2019	Not yet Approved	
15	49+330	VUP	Pin & Guided	Letter No. 1953 dated 11.03.2020	Letter No. 810 dated 02.03.2020	IE observation vide lettr no.810 with Marked correction and it complied by Concessionaire vide letter no. 1953
16	50+095	Flyover	POT / PTFE	Letter No. 705 dated 28.01.2019	Letter No. 651 dated 16.11.2019	




Bearing Drawings Status

S.No	Chainage	Name of Structure	Type of Bearing	Submission Letter No	Approved vide Letter No	Remarks
17	54+550	VUP	Elastomeric	Letter No. 1357 04.09.2019	Letter No. 565 dated 11.09.2019	
18	57+127	MJB	Free, Pin & Metallic Guided	Letter No. 1465 dated 11.10.2019	Letter No. 649 dated 16.11.2019	
19	58+128	Flyover	POT / PTFE	Letter No. 705 dated 28.01.2019	Letter No. 651 dated 16.11.2019	


DJT – Plan & Profile and Miscellaneous Drawing Status

S.No	Types of Drawing	Availability of Drawings	Submission Status	Approval of Drawings
1	Plan & Profile (MCW)	Available	Submitted by letter no. 079 (28.06.2018) & 106 (06.07.2018)	Approved by IE Letter No.285 (23.01.2019)
2	Plan & Profile (Service Road)	Available	Submitted by letter no. 079 (28.06.2018) & 896 (30.03.2019)	Approved by IE Letter No.966 (11.08.2019)
3	Street Lightning (Electrical plan)	Available	Submitted vide letter no. 2453 D-28.11.2020	Approved by IE Letter No.1197 (23.12.2020)
4	Truck Lay-byes	Available	Submitted by (letter no 990 D-01.05.2019)	Approved by (IE Letter No.1007)
5	Bus bay	Available	Bus Bay Submitted vide (letter no. 1723 01.01.2020)	Bus Bay Approved by IE Letter no. 784 (08.02.2020)
	Bus Shelters	Available	Bus Shelter vide letter no. 2233(26.08.2020)	Not yet approved (IE replied vide letter no. 1013 D-07.09.20), (1143 D-20.11.20)
6	Rest Area	Available	Submitted vide letter no 989 (01.05.2019)	Not yet Approved (IE replied vide letter no. 724 D- 04.01.20)
7	Toll Plaza Drawings	Available	Toll Plaza submitted vide letter no. 316 (29.09.2018) & 1370 (07.09.2019)	Approved (IE letter no. 098 D-17.10.2018) & 738 (11.01.2020)
8	Toll Plaza Canopy	Available	Submitted vide Letter no. 1969 (20.03.2020), 2145 (24.07.2020)	Approved (IE letter no. 1045 D-28.09.20)
9	Toll Plaza & Admin Building	Available	Toll Plaza submitted vide letter no. 316 (29.09.2018) & Admin Building submitted vide letter no. 2152 (27.07.2020)	Approved (IE letter no. 1142 D-11.11.20)
10	Traffic Aid Posts	Available	Admin Building submitted vide letter no. 2152 (27.07.2020), 2388 (D- 17.10.20)	Not yet Approved (IE replied vide letter no. 1015 D-08.09.20), 1115 (D- 06.11.2020)
11	Medical Aid Posts	Available	Admin Building submitted vide letter no. 2152 (27.07.2020), 2388 (D- 17.10.20)	Not yet Approved (IE replied vide letter no. 1015 D-08.09.20), 1115 (D- 06.11.2020)
12	Vehicle Rescue Posts	Available	Admin Building submitted vide letter no. 2152	Not yet Approved (IE replied vide letter no. 1015




DJT – Plan & Profile and Miscellaneous Drawing Status

S.No	Types of Drawing	Availability of Drawings	Submission Status	Approval of Drawings
			(27.07.2020), 2388 (D-17.10.20)	D-08.09.20), 1115 (D-06.11.2020)
13	Landscaping and Tree Plantation	Available	Tree Plantation Submitted vide letter no. 1457 (09.10.2019).	Approved by IE Letter No. 626 (01.11.2019)
14	Rain Water Harvesting	Available	Submitted vide letter no. 2104 (08.07.2020)	Approved by IE letter no. 937 (18.07.2020)
15	Median Chute Drain	Available	Submitted vide letter no. 1231 (18.07.2019)	Approved by IE letter no. 936 (17.07.2020)
16	Friction Slab with Crash Barrier	Available	Submitted vide letter no. 1671 (18.12.2019)	Approved by IE letter no. 723 (04.01.2020)
17	Drainage Spout	Available	Submitted vide letter no. 2184 (07.08.2020)	Approved by IE letter no. 979 (19.08.2020) & 981 (20.08.2020)
18	RCC Railing / Parapet Wall	Available	Submitted vide letter no. 549 (10.12.2018)	Approved by IE letter no. 755 (23.01.2020)
19	Crash Barrier & Approach Slab	Available	Submitted vide letter no. 549 (10.12.2018)	Approved by IE letter no. 653 (20.11.2019)
20	Chute Drain & Stone Pitching	Available	Submitted vide letter no. 549 (10.12.2018)	Not yet Approved
21	Wearing Coat	Available	Submitted vide letter no. 549 (10.12.2018)	Not yet Approved
22	Kerb	Available	Submitted vide letter no. 549 (10.12.2018)	Not yet Approved
23	Junction Drawing (Plan)	Available	Submitted vide letter no. 1618 (05.12.2019), (2450 D-28.11.2020)	Approved (Found in order with marked observation IE letter No. 710 D-23.12.2019 & 1180 D-12.12.2020).
24	Signage Plan	Available	Submitted vide letter no. 1699 (26.12.2019)	Approved by IE letter no. 1156 (D- 26.11.2020), (1210 D-31.12.2020)
25	Median Opening	Available	Submitted vide letter no. 1713 (30.12.2019)	Approved by IE letter no. 951 (27.07.2020)
26	L-shaped Retaining wall (4.5m to 5.5m)	Available	Submitted vide letter no. (2426 D-07.11.2020), (2452 D-28.11.20)	Approved by IE letter no. 1171 (08.12.2020)
27	Retaining wall (2m to 10m)	Available	Submitted vide letter no. (1487 D-21.10.2019), (2446 D-28.11.20)	Approved by IE letter no. 1169 (08.12.2020)
28	Crash Barrier details over Retaining wall	Available	Submitted vide letter no. (2397 D-21.10.2020), (2445 D-28.11.20)	Approved by IE letter no. 1170 (08.12.2020)
29	Gantry & Signage Foundation	Available	Submitted vide letter no. 2517 D- 13.01.2021	Approved by IE letter no.1241 (21.01.2021)
31	Electric Work Plan	Available	Submitted vide letter no. 2495 D- 30.12.2020	Approved by IE letter no.1234 (14.01.2021)
32	Stair Case of ROB	Available	Submitted vide letter no. 2479 D- 17.12.2020	Approved by IE letter no.1211 (14.01.2021)




12. Mobilization of Manpower


Name of the Employee	Designation	Department
P.Gangadhar	General Manager	Technical
Milind Pande	Project Incharge	Technical
Atul Kumar Mishra	Sr. Project Manager	Technical
Shubhash Kumar	Sr.Manager	Mechanical
Praveen Kahar	Manager	Liasion
Balram Singh Shekhawat	Manager	Liasion
Bhagwan Jha	Manager	Purchase
Subhash Singh	Dy. Project Manager	Technical (Highway)
Shiv Kumar	Dy. Project Manager	Technical (Highway)
Ranjay Kumar Anju	Dy. Project Manager	Planning & Billing
Ramesh Chandra Barad	Dy. Manager (HR & Admin)	HR & Admin
Ritesh Verma	Dy. Manager (HR & Admin)	HR & Admin
Mahesh Pandey	Dy. Project Manager	Highway
SajjanLal Sharma	Dy. Project Manager	Structure
Sanjay Gaur	Dy. Project Manager	QA/QC
Rajesh Rawal	Dy. Project Manager	QA/QC
Bal Krishna Rath	Dy. Project Manager	Structure
Kuldeep Singh	Sr.Surveyor	Survey
Ravi Kishore Pandey	Sr.Accountant	Finance & Accounts
Rajan Upadhyay	Dy. Project Manager	Health & Safety
HR & ADMIN DEPARTMENT		
Dy. Manager	01 No	HR & Admin
Sr. Executive	02 Nos	HR & Admin
Officer (S & V)	01 Nos	HR & Admin
Executive	02 Nos	HR & Admin
Jr.Executive	02 Nos	HR & Admin
Office Boy	04 Nos	HR & Admin
PLANNING & BILLING DEPARTMENT		
Sr.Engineer	03 Nos	Planning & Billing
Engineer	03 Nos	Planning & Billing
Asst. Engineer	01 Nos	Planning & Billing
QA/QC DEPARTMENT		
Lab Asst.	01 Nos	QA/QC
Sr.Lab Technician	02 Nos	QA/QC
Lab Technician	12 Nos	QA/QC
Engineer	01 No	QA/QC
Jr.Engineer	06 Nos	QA/QC
HIGHWAY DEPARTMENT		
Sr. Engineer	01 Nos	Highway
Engineer	05 Nos	Highway
Asst. Engineer	10 Nos	Highway



Jr.Engineer	06 Nos	Highway
Engineer Trainee	01 No	Highjway
Sr. Supervisor	03 Nos	Highway
Supervisor	19 Nos	Highway
STRUCTURE DEPARTMENT		
Sr. Engineer	03 Nos	Structure
Engineer	07 Nos	Structure
Asst. Engineer	07 Nos	Structure
Jr.Engineer	08 Nos	Structure
Sr.Supervisor	02 Nos	Structure
Supervisor	07 Nos	Structure
SURVEY DEPARTMENT		
Sr. Surveyor	01 Nos	Survey
Surveyor	10 Nos	Survey
Jr.Surveyor	04 Nos	Survey
STORE DEPARTMENT		
Jr. Executive	25 Nos	Store
Executive	04 Nos	Store
Asst. Executive	01 No	Store
WEIGH BRIDGE		
Jr.Executive	13 Nos	Weigh Bridge
PURCHASE DEPARTMENT		
Dy.Manager	01 Nos	Purchase
Sr.Executive	01 Nos	Purchase
Executive	01 Nos	Purchase
HEALTH & SAFETY DEPARTMENT		
Dy. Manager	01 Nos	Health & Safety
Sr.Executive	01 Nos	Health & Safety
Asst Executive	01 Nos	Health & Safety
Executive	01 Nos	Health & Safety
Safety officer	04 Nos	Health & Safety
Supervisor	02 Nos	Health & Safety
IT DEPARTMENT		
Sr.Executive	02 Nos	IT
Executive	01 Nos	IT
MECHANICAL DEPARTMENT		
Sr.Supervisor	01 Nos	Mechanical
Sr. Engineer	05 Nos	Mechanical
Supervisor	13 Nos	Mechanical
Engineer	01 Nos	Mechanical
Executive	01 Nos	Mechanical
Asst. Mechanic	03 Nos	Mechanical
Fitter	01 Nos	Mechanical
Tyre Fitter	04 Nos	Mechanical
Jr.Engineer	05 Nos	Mechanical
Jr.Executive	03 Nos	Mechanical




Supervisor	13 Nos	Mechanical
Driver	182 Nos	Mechanical
Operator / Helper/ Mechanic	198 Nos	Mechanical
S & V		
Asst Manager	01 No	S & V
Sr.Officer	03 Nos	S & V
Officer	04 Nos	S & V



13. Mobilization of Resources (Plant and Machineries)

S.No	Name of Machinery	TOTAL	Remarks
1	Excavator	38	
2	Hywa/Tipper	178	
3	Soil Compactor	18	
4	Dozer	2	
5	Water Tanker	25	
6	Diesel Dispenser	6	
7	Grader	18	
8	Loader	10	
9	Back Hoe	6	
10	Transit Mixer	17	
11	Crusher	4	
12	Concrete Batching Plant	5	
13	Weigh Bridge	7	
14	WMM Plant	1	
15	Hydra Crane	8	
16	Hot Mix Plant	1	
17	Concrete Pump	3	
18	Sand Classifier	2	
19	Tractor	13	
20	Tower Light	9	
21	DG Set	17	
22	Light Vehicle	40	
23	Trailer	4	
24	JCB	12	
25	Boom Placer	2	
26	Tandem Roller	5	
27	Baby Roller	4	
28	Mobile Service Van	3	
29	DLC Paver	3	
30	Automatic PQC Paver	1	
31	Kerb Paver	2	
32	Chilling Plant	1	
33	Bus	2	
34	Fork Lift	3	
35	Block Casting Machine	1	
36	Ambulance Van	1	
37	Tempo	2	
	Total	474	



14. Site Progress Photo



Km. 30+350

Median Earthwork is in
progress

BHS



Km. 30+400

Selected Soil Compaction is
in Progress

LHS





21+020 to 21+170

Emb.6th Layer finishing Work



BHS



25+112 to 25+165

RE Wall Pondash Layer rolling

RHS



Km 15+444 to Km
15+550

RE wall median portion SG top in
progress


RHS



Km. 17+353

Cooping Beam in
Progress

W2





45+680 to
45+869

Subgrade Top Testing in RE
Wall

BHS



51+780 to
51+855

Block Erection is in Progress

LHS



45+880 to 46+220	GSB Top Work in Progress	RHS
---------------------	--------------------------	-----



15+400 to 15+700	Earthwork Rolling Work in Progress	LHS
------------------	------------------------------------	-----





53+530 to 53+600

Embankment 6th layer in Progress

RHS



50+135 to
50+300

Pond ash Bed Rolling

LHS





53+905 to 54+035

Emb Rolling Progress

BHS



56+740 to 56+780

GSB Top Progress

RHS








44+265 to 44+344	Geo Grid Laying and Covering	LHS
------------------	------------------------------	-----



51+491 to 51+662	A-1 Side Selected Soil Rolling	LHS
------------------	--------------------------------	-----



Rolling Edge of selected soil wall- 3
at CH 30+300

Km 30+300	Rolling of Selected Soil Wall-3	-----
-----------	---------------------------------	-------



48+090 to 48+150	MCW Earthwork in Progress	BHS
------------------	---------------------------	-----



25+430 to
25+500

Subgrade Top Layer


RHS



23+694 to
23+950

Pond Ash Rolling W-4

RHS





56+400


PQC Laying



25+600

DLC Laying

RHS





12+550

DLC Laying



25+100

Kerb Laying

RHS



44+600 to
44+750

RE wall selected soil bed rolling
work in progress A2 side

LHS



41+300

DBM Laying





MJB @ Km
36+070

Girder launching is in progress



41+300

Drain Raft Casting






VUP @ Km
49+330

Girder launching is in progress



RUB @ Km
33+585

Excavation for thrust bed is
in progress





MJB @ Km
36+070

Pouring start (P6- P7)slab

RHS



BC @ Km
53+700

Raft Steel Reinforcement
Check by IE Representative



MJB @ Km
36+070

Pouring start (P5- P6)slab

LHS



BC @ Km
53+700


P-10 Pile cap concrete done

RHS



S- CURVE OF FINANCIAL PROGRESS AS PER SUBMITTED PROGRAMME

MONTH	Dev. Period	Jun-18	Jul-18	Aug-18	Sep-18	Oct-18	Nov-18	Dec-18	Jan-19	Feb-19	Mar-19	Apr-19	May-19	Jun-19	Jul-19	Aug-19	Sep-19	Oct-19	Nov-19	Dec-19	Jan-20	Feb-20	Mar-20	Apr-20	May-20	Jun-20	Jul-20	Aug-20	Sep-20	Oct-20	Nov-20	Dec-20	Jan-21	Feb-21	Mar-21	Apr-21	May-21	Jun-21	Jul-21	Aug-21	Sep-21	
PLANNED (MONTHLY)	22.60	25.56	17.37	22.79	14.34	18.41	24.74	29.81	30.39	24.30	29.31	17.05	29.71	36.10	25.60	19.42	14.98	19.52	37.01	39.72	35.29	39.27	17.50	1.92	0.01	6.48	6.80	4.92	7.37	32.49	33.63	35.84	45.65	60.64	63.42	61.84	61.58	56.64	25.79	13.16	14.69	
PLANNED (CUMULATIVE)	22.60	48.16	65.54	88.33	102.67	121.09	145.82	175.63	206.02	230.32	259.62	276.67	306.39	342.48	368.09	387.50	402.48	422.00	459.01	498.72	534.01	573.28	590.79	592.70	592.71	599.19	605.99	610.90	618.28	650.77	684.39	720.23	785.88	826.51	889.93	951.77	1,013.35	1,070.00	1,095.79	1,108.95	1,123.64	
Achieved (MONTHLY)	20.08	22.77	15.55	20.27	12.81	16.39	22.12	26.49	27.01	21.79	26.11	15.15	26.41	32.07	24.23	18.03	14.07	18.05	34.58	34.03	61.64	41.36	35.65	-	1.35	8.36	16.15	25.24	20.26	26.55	-	39.85	33.496									
Achieved (CUMULATIVE)	20.08	42.85	58.39	78.66	91.47	107.86	129.98	156.47	183.48	205.27	231.38	246.53	272.94	305.01	329.24	347.27	361.34	379.39	413.97	448.00	509.64	551.00	586.65	586.65	588.00	596.36	612.51	637.75	658.01	684.56	684.56	724.41	757.906									

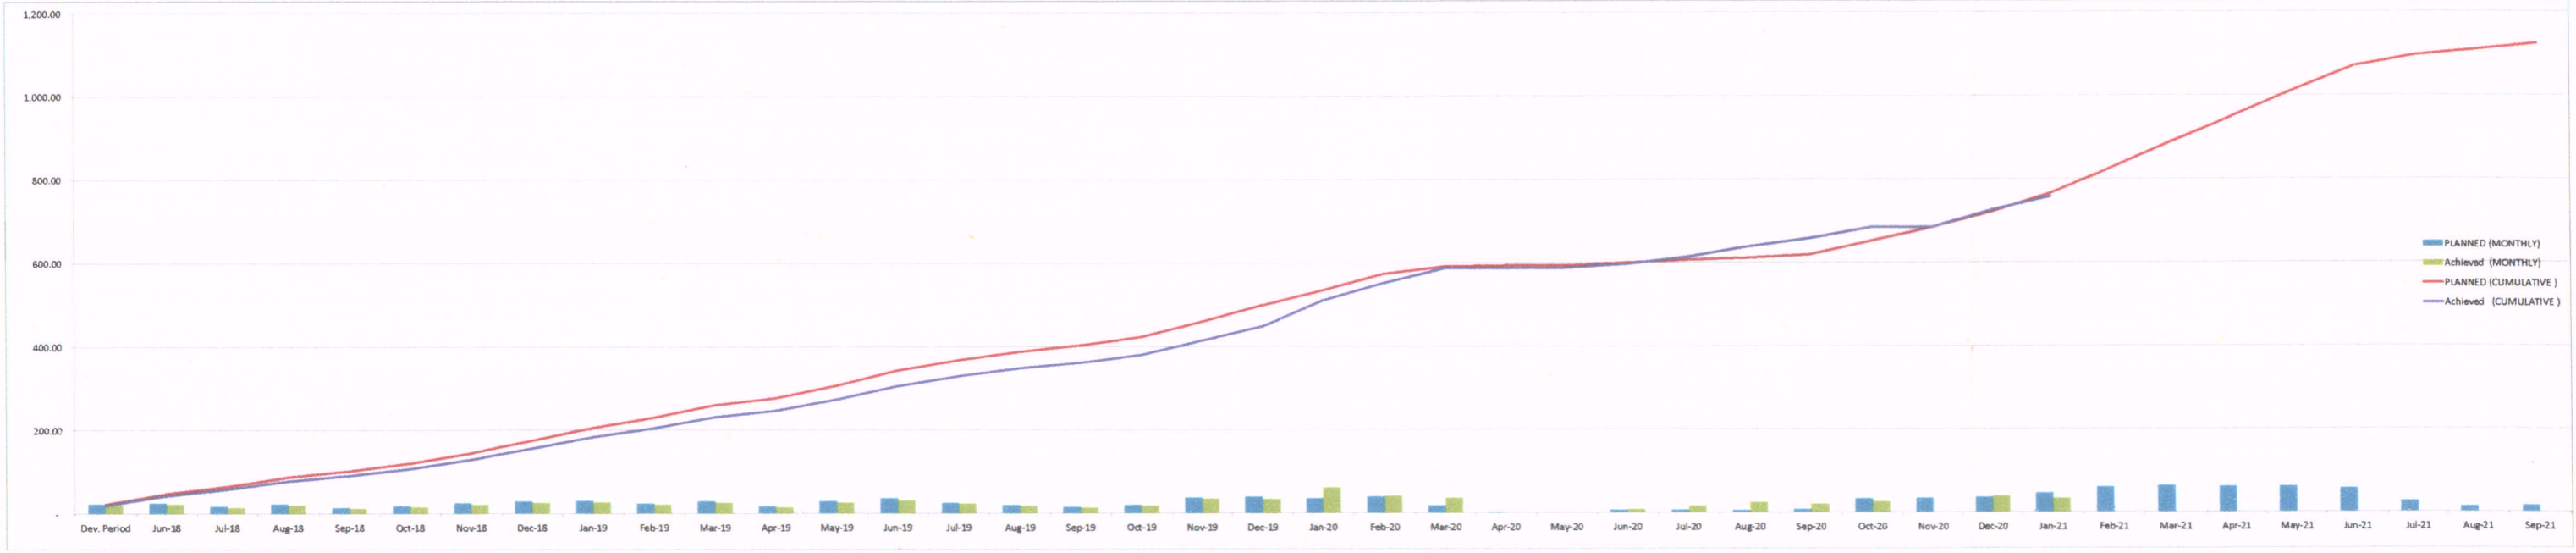

Ravi
 Patel
 Patel Daxah-Jhalawar Highway Pvt. Ltd.


Strip Chart
Darah-Jhalawar-Teendhar section

Index	C & G	EMB	SG	GSB	DLC	PQC
	Length 46.100Km	Length 36.20Km	Length 34.80Km	Length 32.400Km	Length 28.270Km	Length 26.580Km

PQC	LHS	
DLC		
GSB		
SG		
EMB		
C&G		
Chainage		9800 9900 10000 10100 10200 10300 10400 10500 10600 10700 10800 10900 11000 11100 11200 11300 11400 11500 11600 11700 11800 11900 12000 12100 12200 12300 12400 12500 12600 12700 12800 12900 13000 13100 13200 13300 13400 13500 13600 13700 13800 13900 14000 14100 14200 14300 14400 14500
C&G	RHS	
EMB		
SG		
GSB		
DLC		
PQC		


PQC	LHS	
DLC		
GSB		
SG		
EMB		
C&G		
Chainage		14500 14600 14700 14800 14900 15000 15100 15200 15300 15400 15500 15600 15700 15800 15900 16000 16100 16200 16300 16400 16500 16600 16700 16800 16900 17000 17100 17200 17300 17400 17500 17600 17700 17800 17900 18000 18100 18200 18300 18400 18500 18600 18700 18800 18900 19000 19100 19200
C&G	RHS	
EMB		
SG		
GSB		
DLC		
PQC		

PQC	LHS	
DLC		
GSB		
SG		
EMB		
C&G		
Chainage		19200 19300 19400 19500 19600 19700 19800 19900 20000 20100 20200 20300 20400 20500 20600 20700 20800 20900 21000 21100 21200 21300 21400 21500 21600 21700 21800 21900 22000 22100 22200 22300 22400 22500 22600 22700 22800 22900 23000 23100 23200 23300 23400 23500 23600 23700 23800 23900
C&G	RHS	
EMB		
SG		
GSB		
DLC		
PQC		




Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Pa

BOX CULVERT 11+605

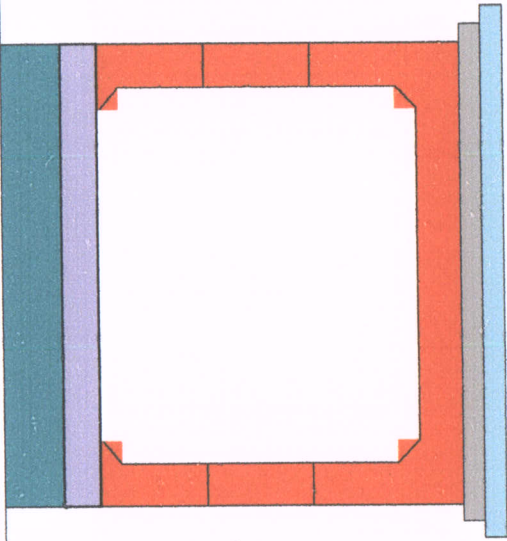


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation

BOX CULVERT 13+400

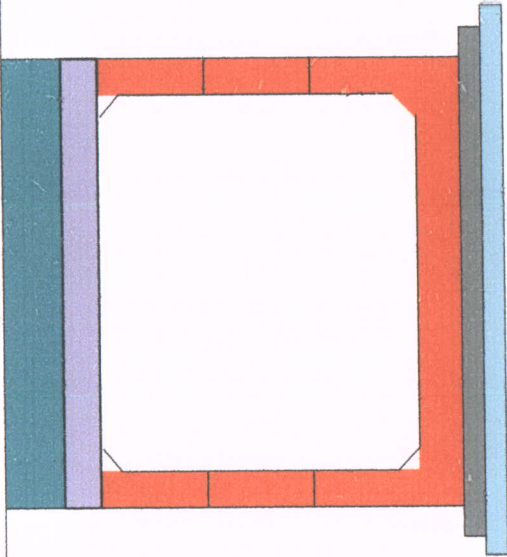


BOX CULVERT 14+980

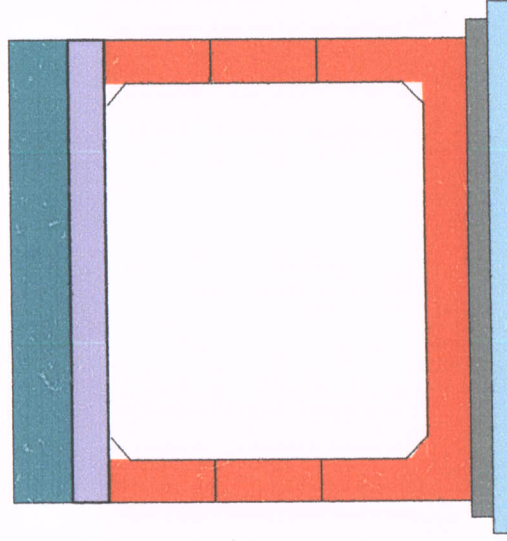


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation


BOX CULVERT 13+980

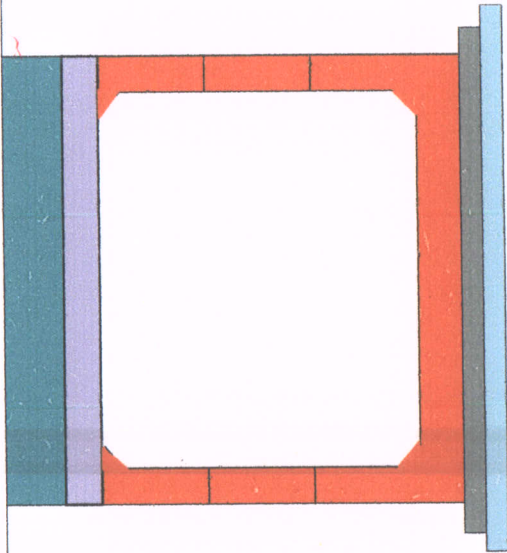

BOX CULVERT 22+450

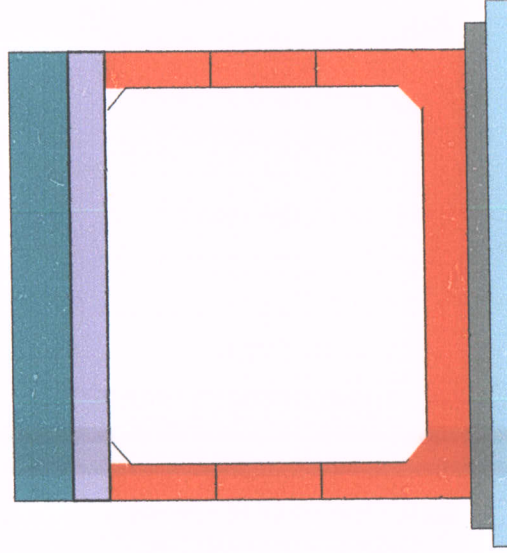


BOX CULVERT 16+600

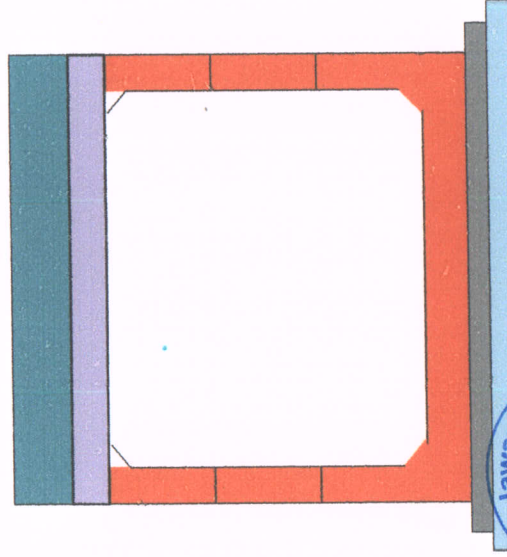

[Handwritten signature]


Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Pa

BOX CULVERT 24+610

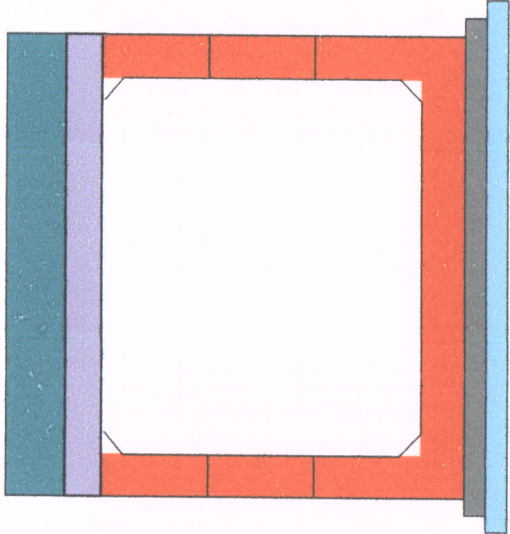


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation

BOX CULVERT 25+800

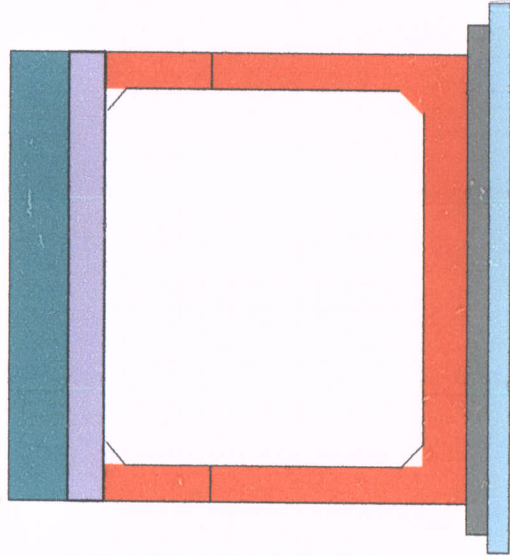


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation

BOX CULVERT 29+000

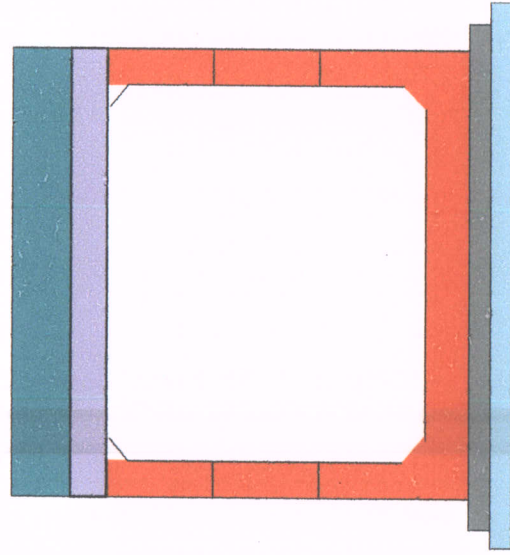


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation

BOX CULVERT 29+900

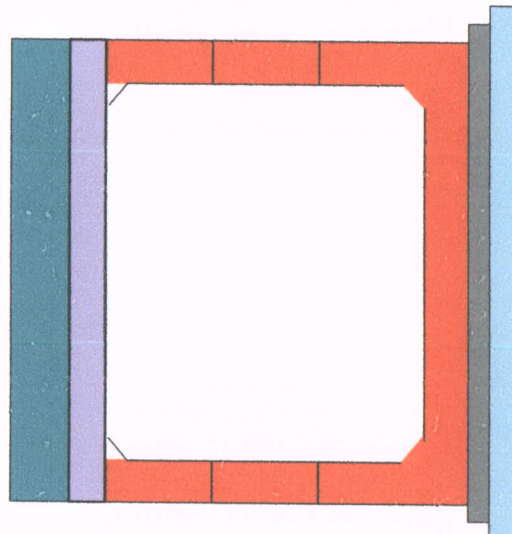


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation

BOX CULVERT 32+050

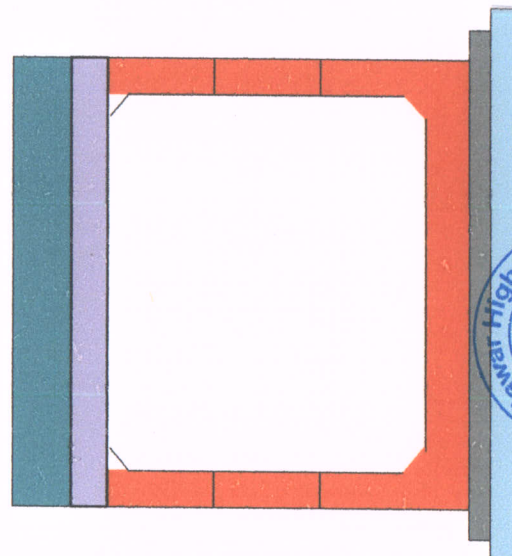





CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation

BOX CULVERT 32+300



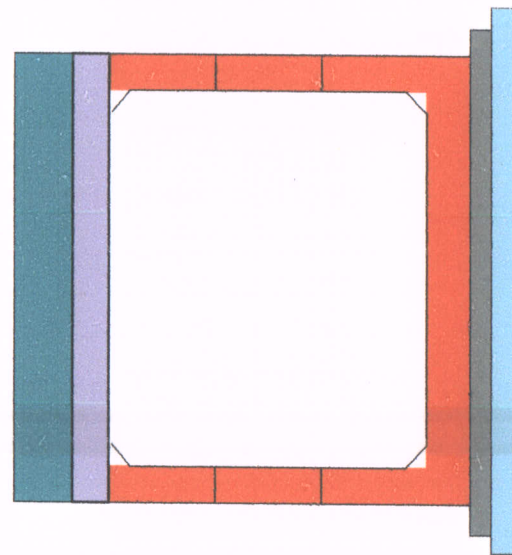


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation



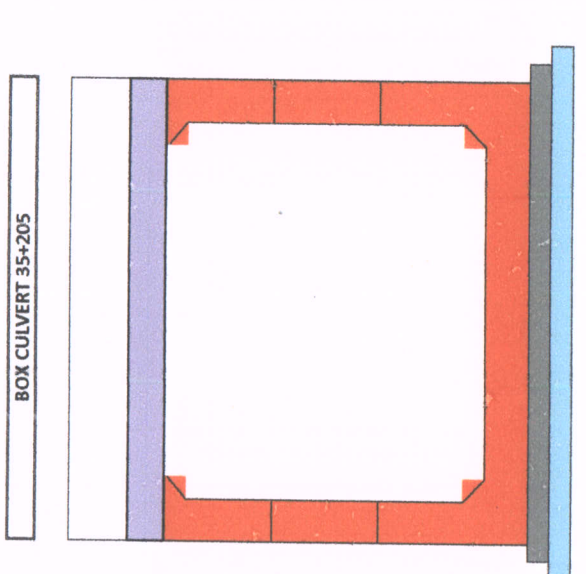
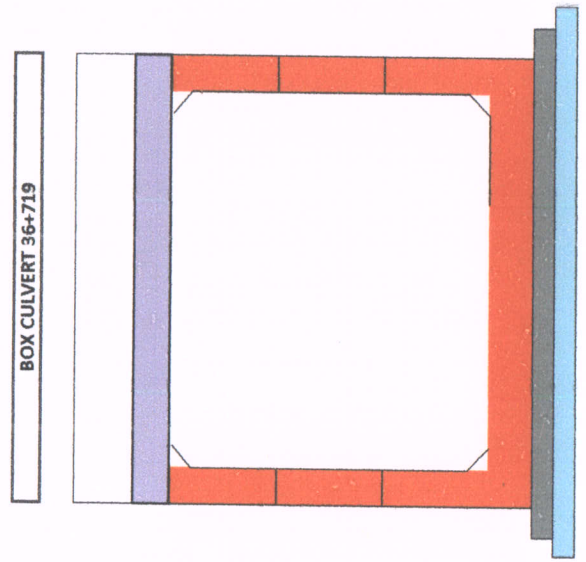
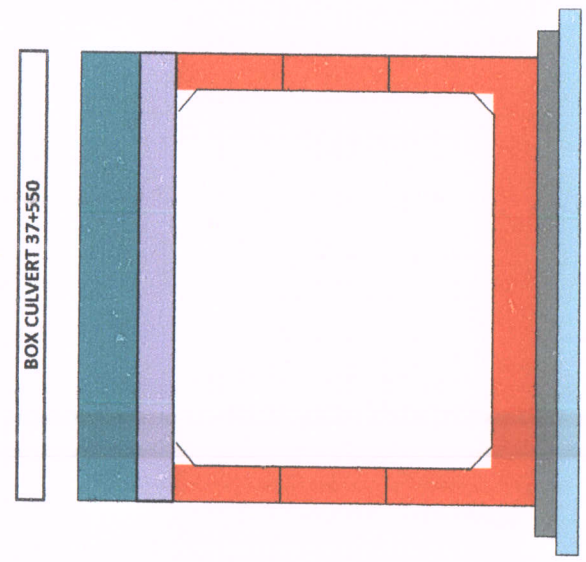


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation


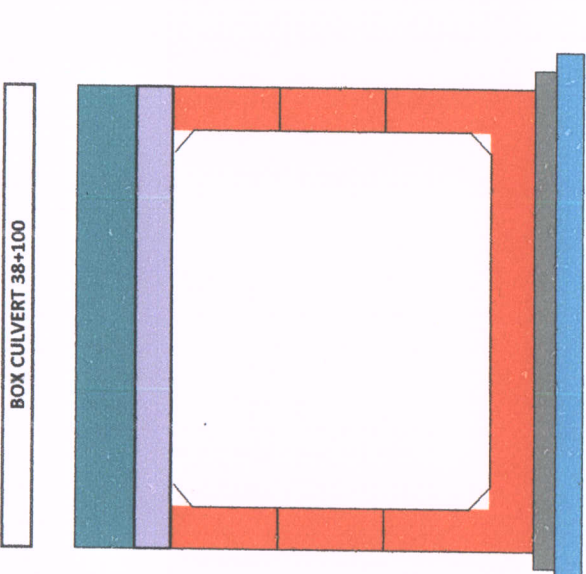
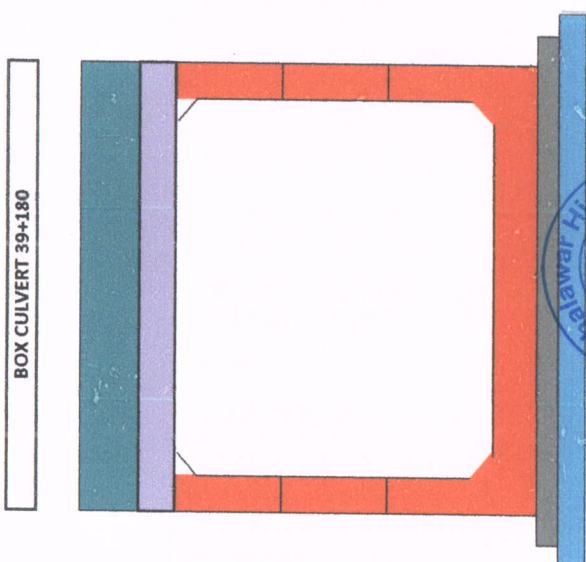
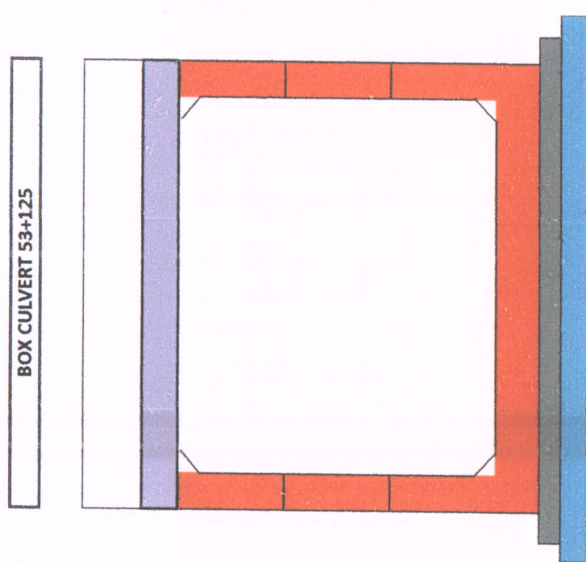


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation



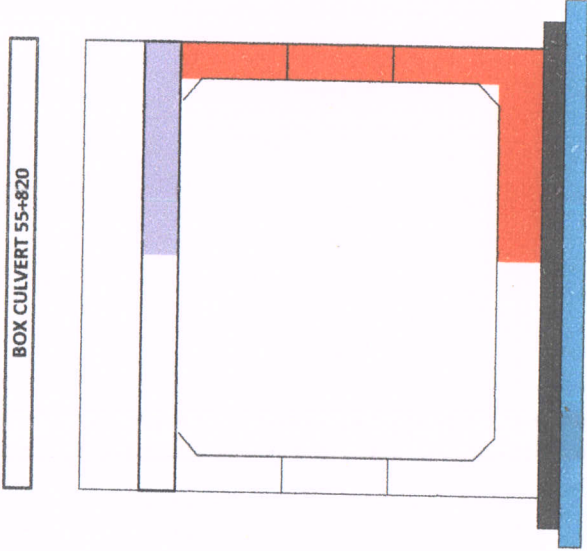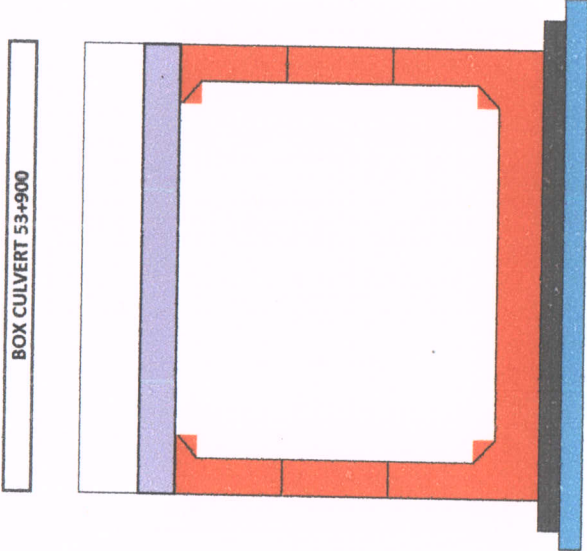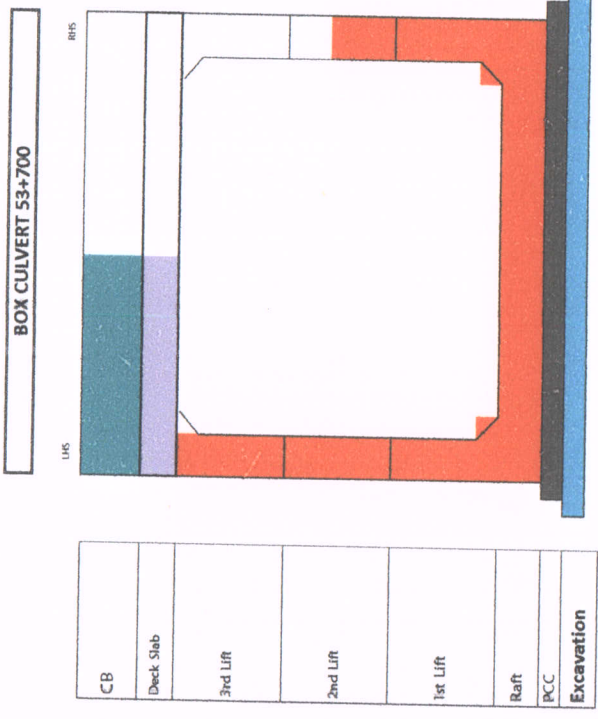




Additional / SR

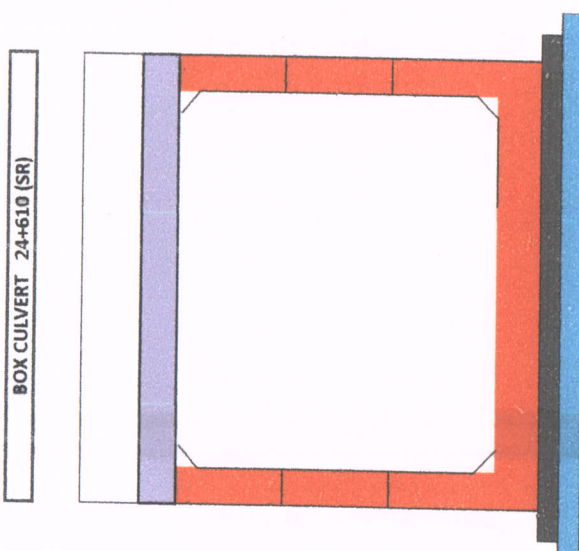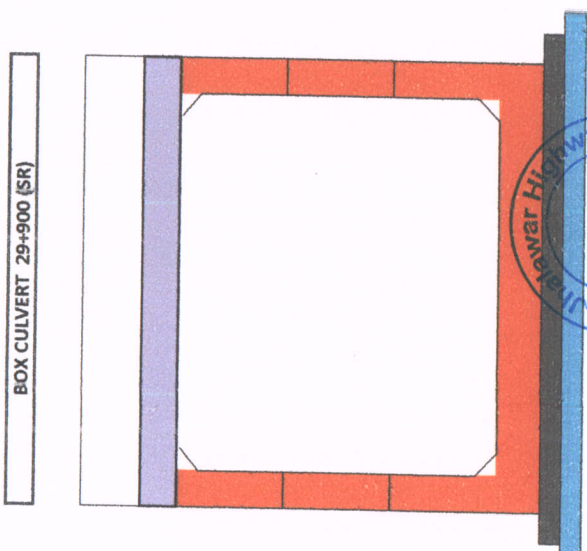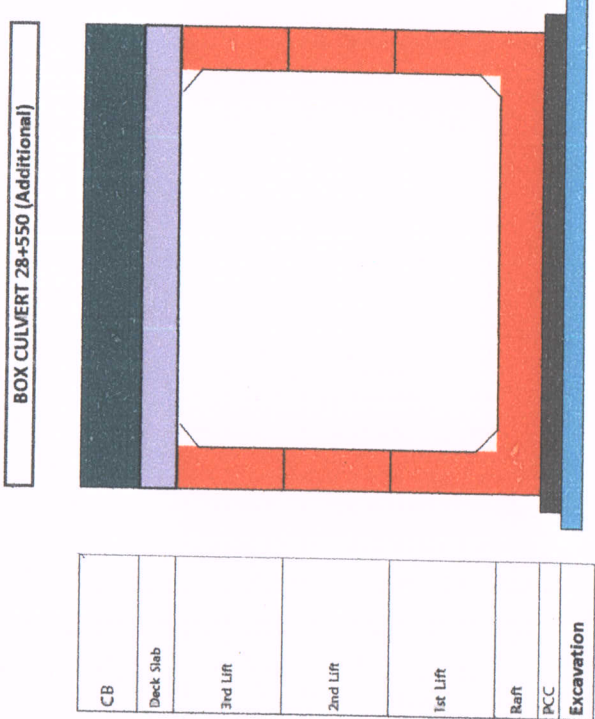

(Handwritten signature)


Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Pa

CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation

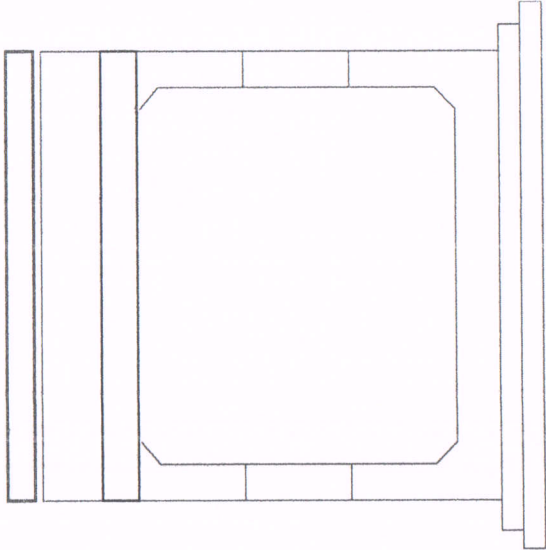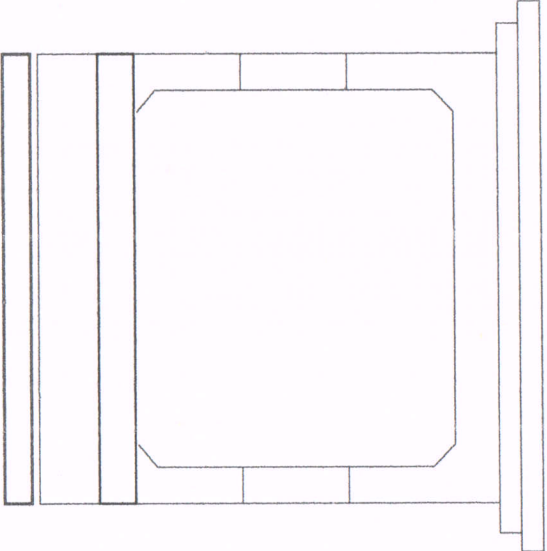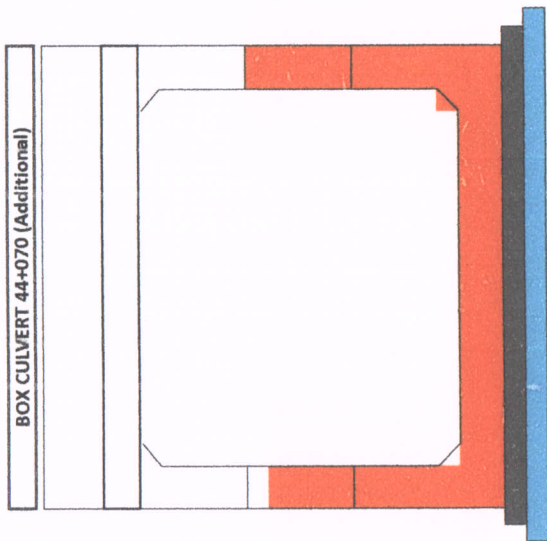


(Handwritten signature)

MINOR BRIDGE AT KM. 12+380 RHS

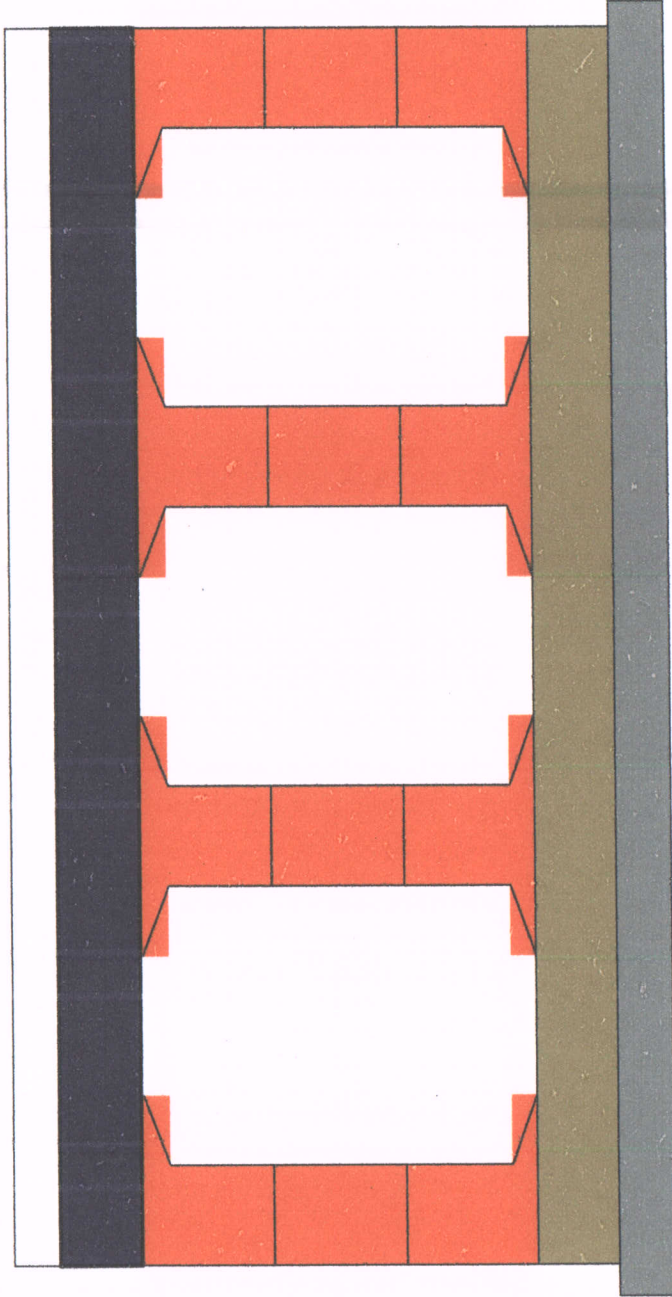


CB					
	3rd Lift				
		2nd Lift			
			1st Lift		
				Raft	
					PCC

MINOR BRIDGE AT KM. 12+380 LHS

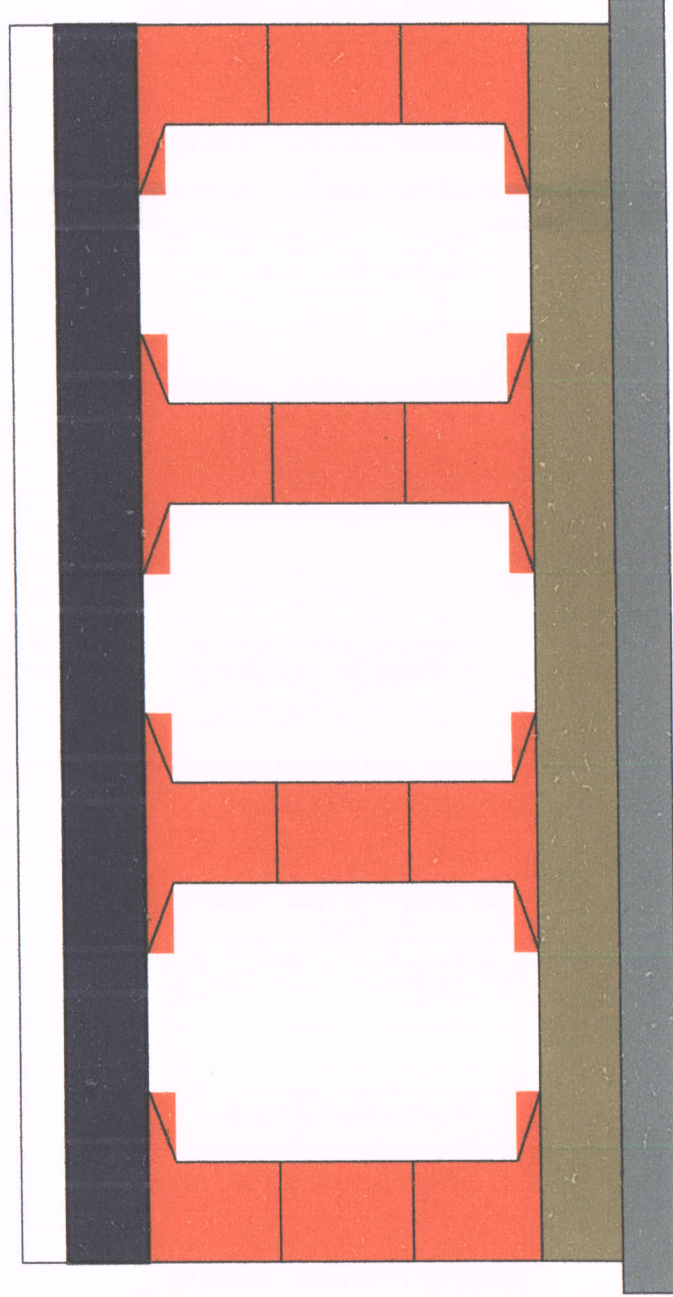


CB					
	3rd Lift				
		2nd Lift			
			1st Lift		
				Raft	
					PCC




[Handwritten signature]

MINOR BRIDGE AT KM. 12+380 RHS Service Road

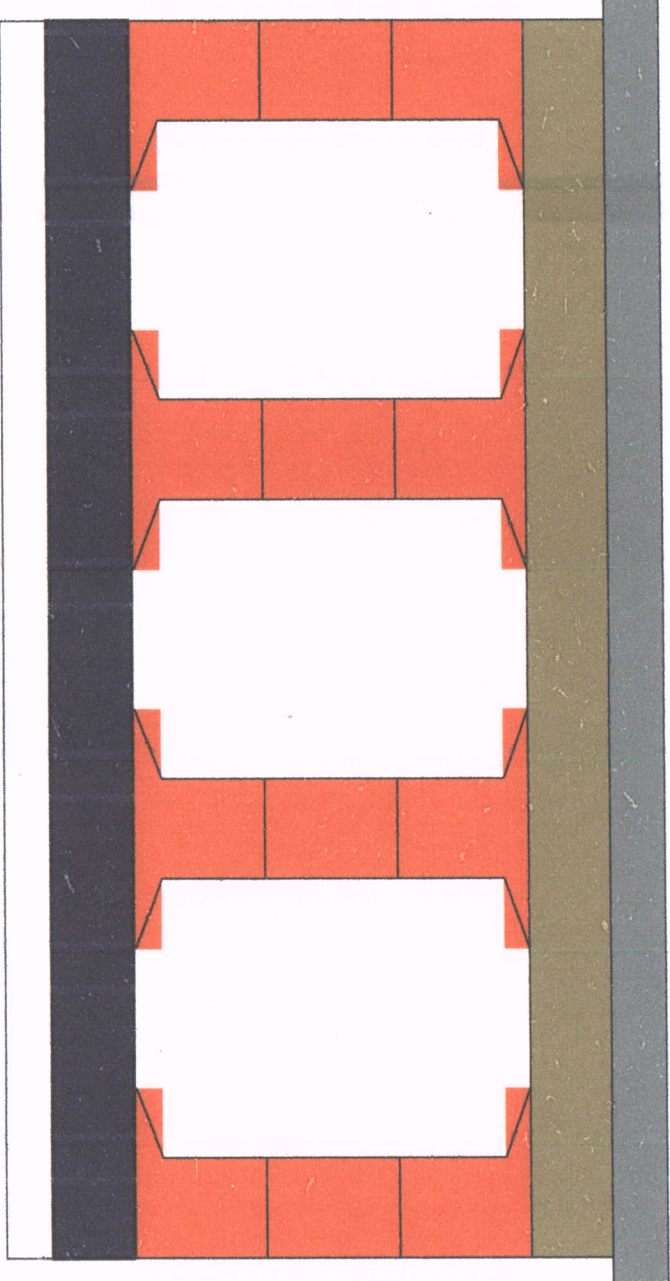

CB					
	3rd Lift				
		2nd Lift			
			1st Lift		
				Raft	
					PCC


MINOR BRIDGE AT KM. 12+380 LHS Service Road

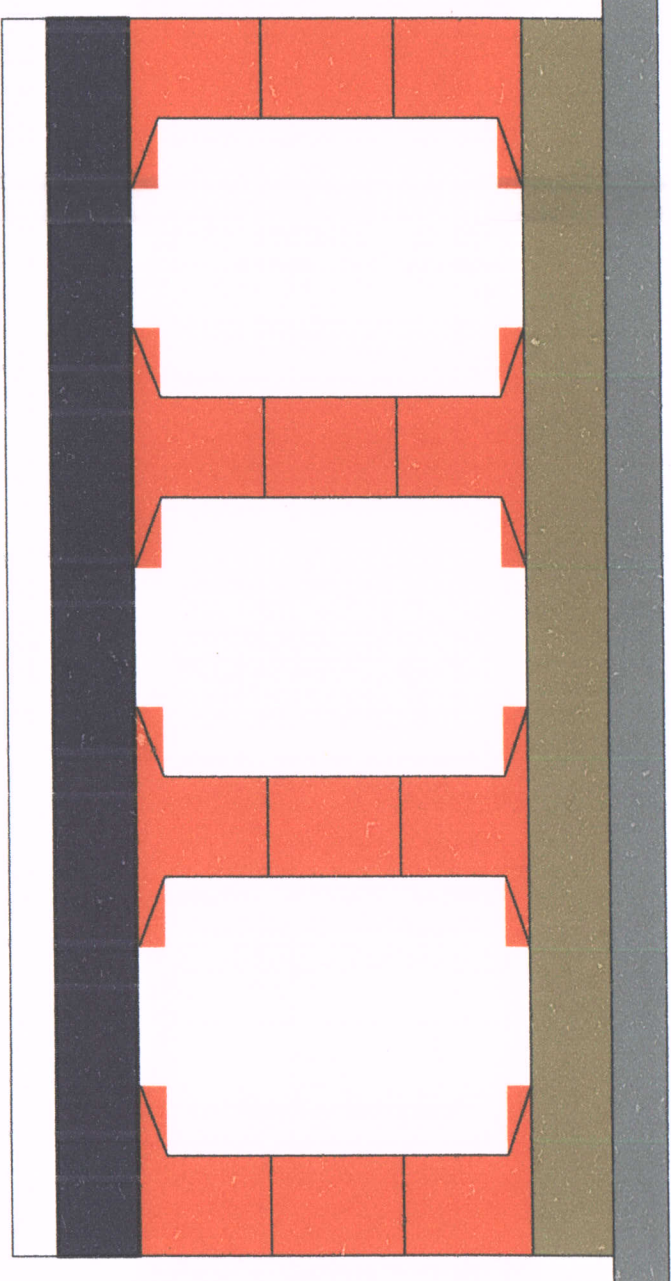

CB					
	3rd Lift				
		2nd Lift			
			1st Lift		
				Raft	
					PCC


(Handwritten signature)
 PATEL
 Darah-Jhavar Highway Pvt. Ltd. ★

MINOR BRIDGE AT KM. 16+060 (Service Road) RHS

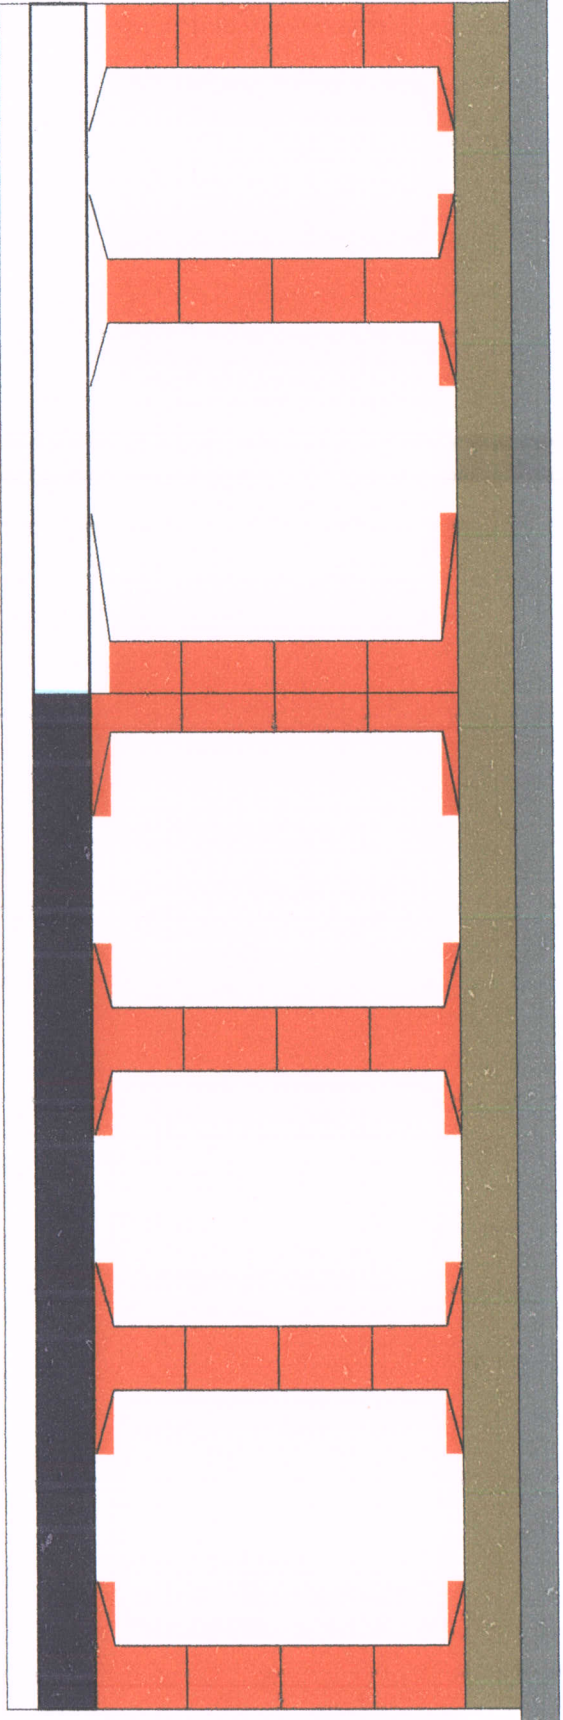


CB							
	4th Lift						
	3rd Lift						
	2nd Lift						
	1st Lift						
	Raft						
	PCC						

MINOR BRIDGE AT KM. 16+060 (Service Road) LHS

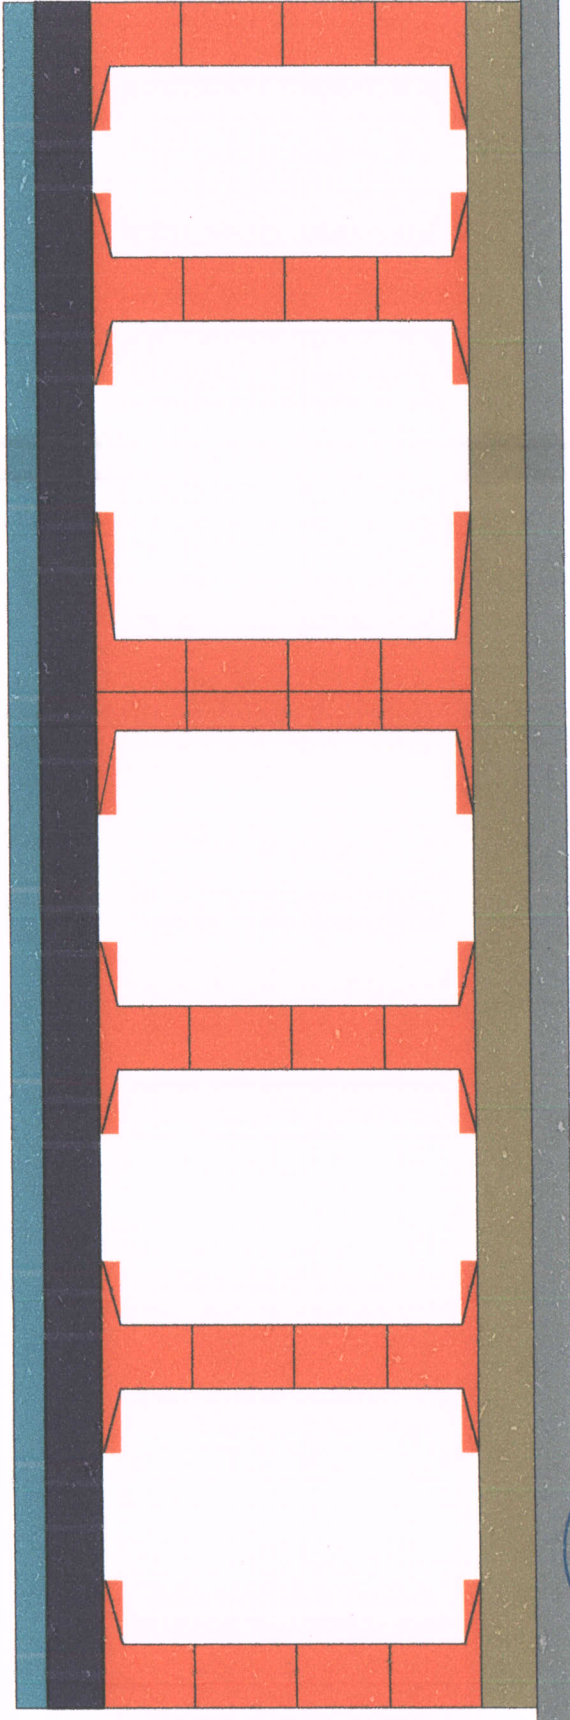


CB							
	4th Lift						
	3rd Lift						
	2nd Lift						
	1st Lift						
	Raft						
	PCC						



Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project (Length 48.880 Km.) - Package II


MINOR BRIDGE AT KM. 16+060 (Main Carriage Way) RHS

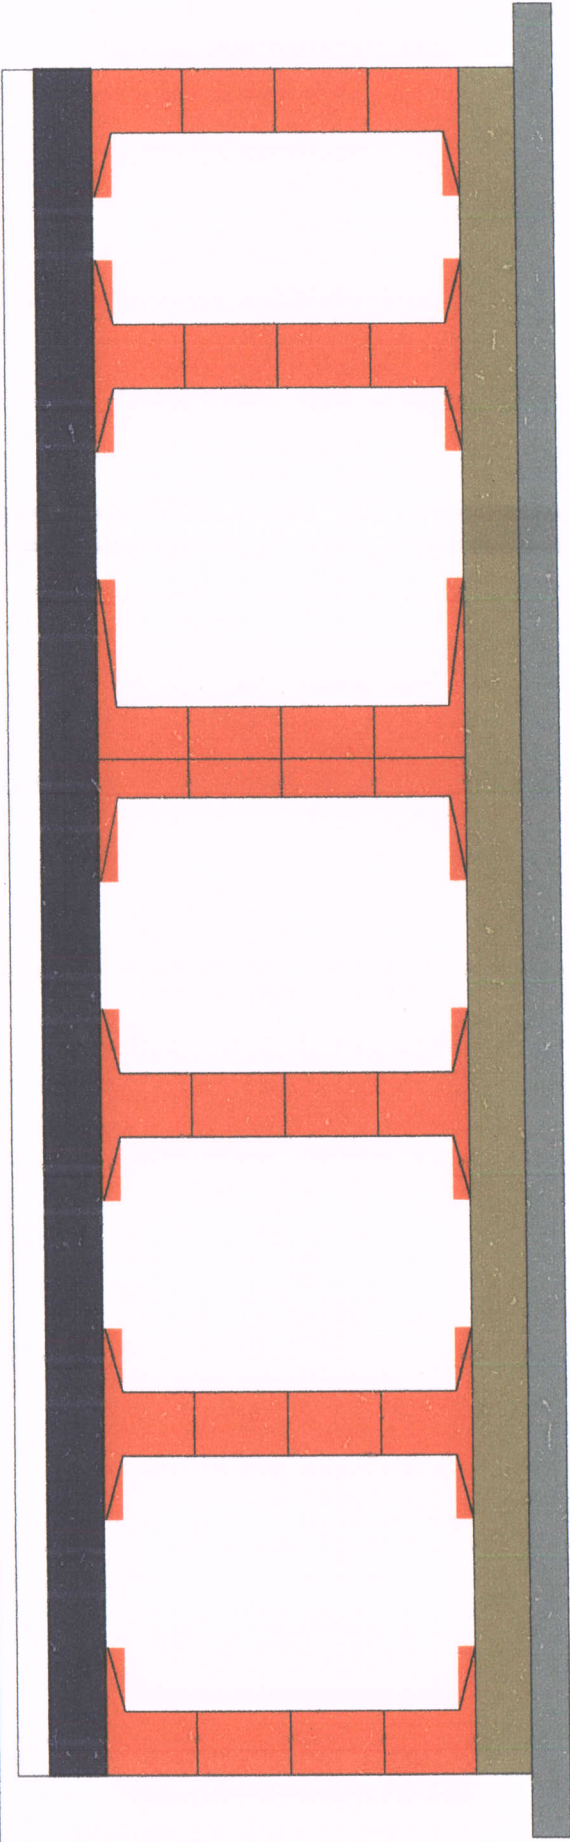

CB						
4th Lift						
3rd Lift						
2nd Lift						
1st Lift						
Raft						
PCC						

Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project (Length 48.880 Km.) - Package II

MINOR BRIDGE AT KM. 16+060 (Main Carriage Way) LHS

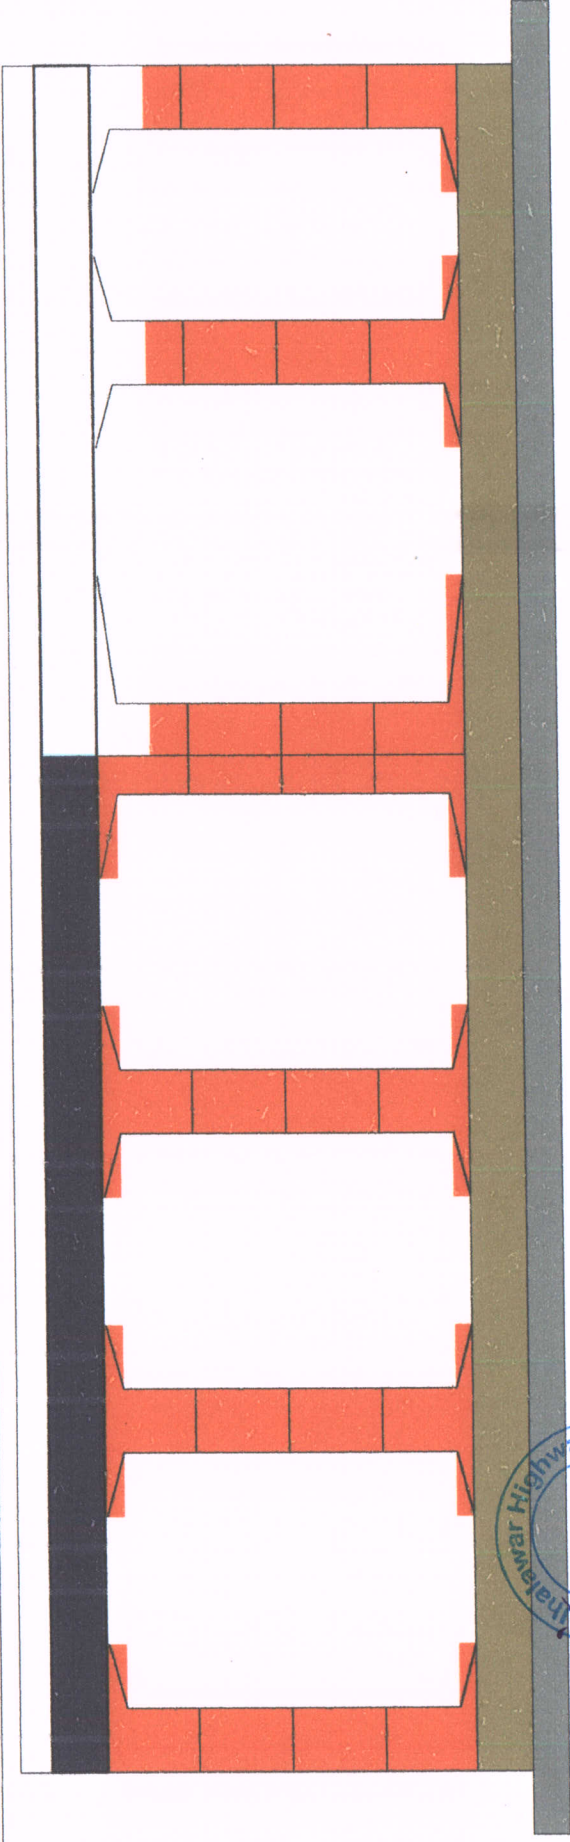


CB						
4th Lift						
3rd Lift						
2nd Lift						
1st Lift						
Raft						
PCC						




(Handwritten signature)

MINOR BRIDGE AT KM. 17+880 RHS

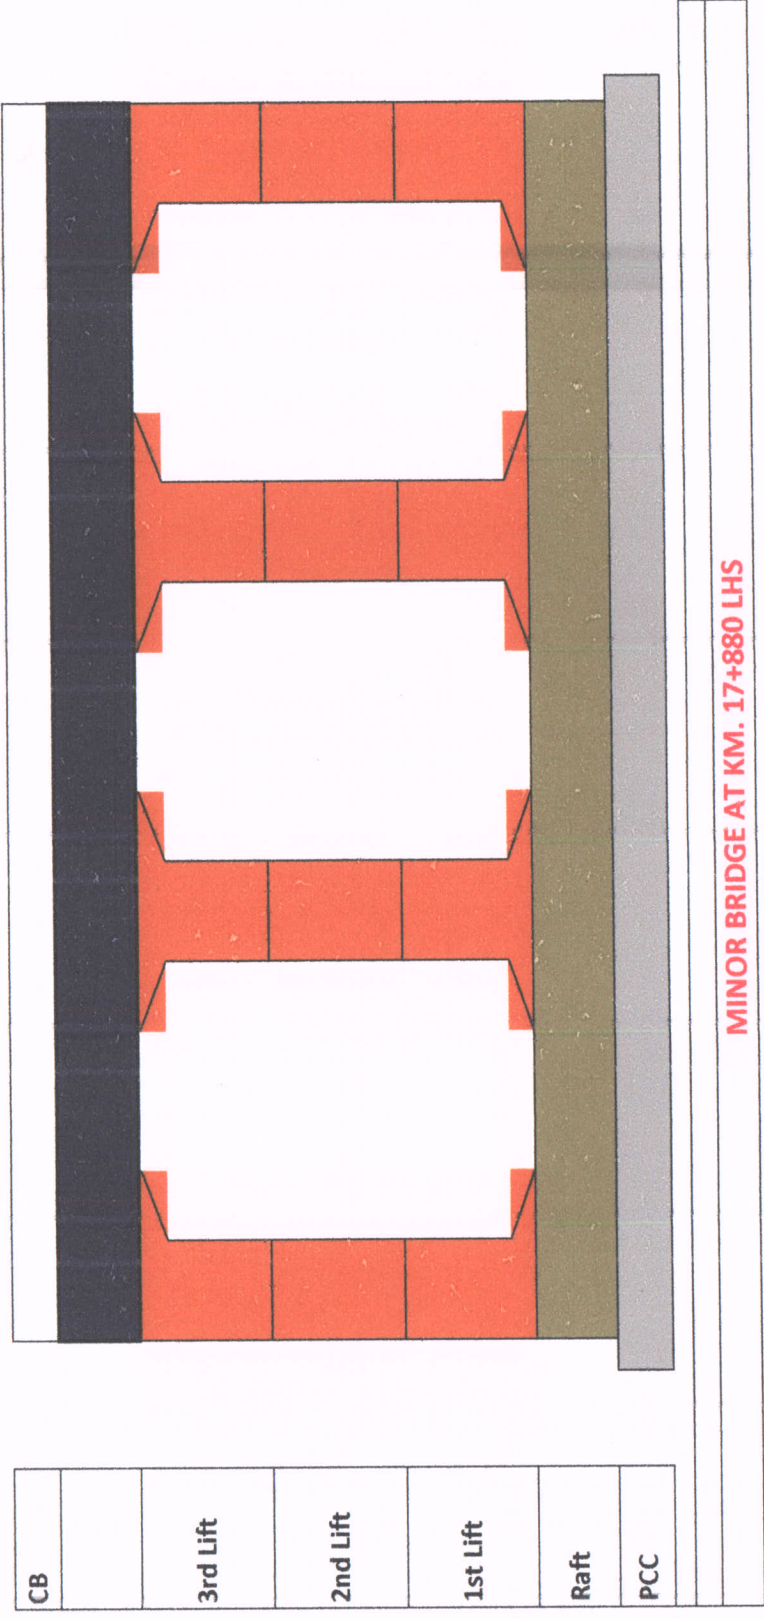

CB						
	3rd Lift					
		2nd Lift				
			1st Lift			
				Raft		
					PCC	


MINOR BRIDGE AT KM. 17+880 LHS

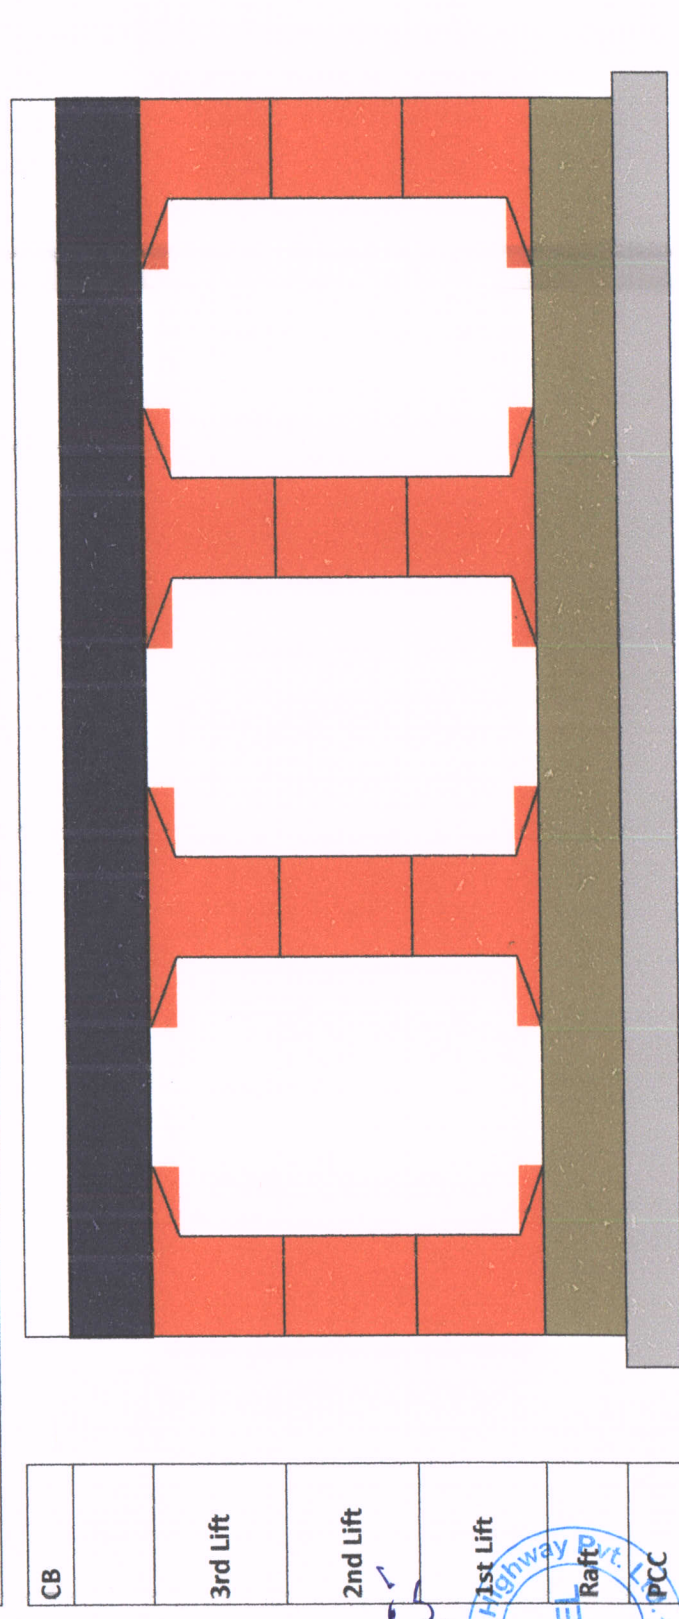

CB						
	3rd Lift					
		2nd Lift				
			1st Lift			
				Raft		
					PCC	


Patel Darah-Pratap Highway Pvt. Ltd.

MINOR BRIDGE AT KM. 29+600 RHS

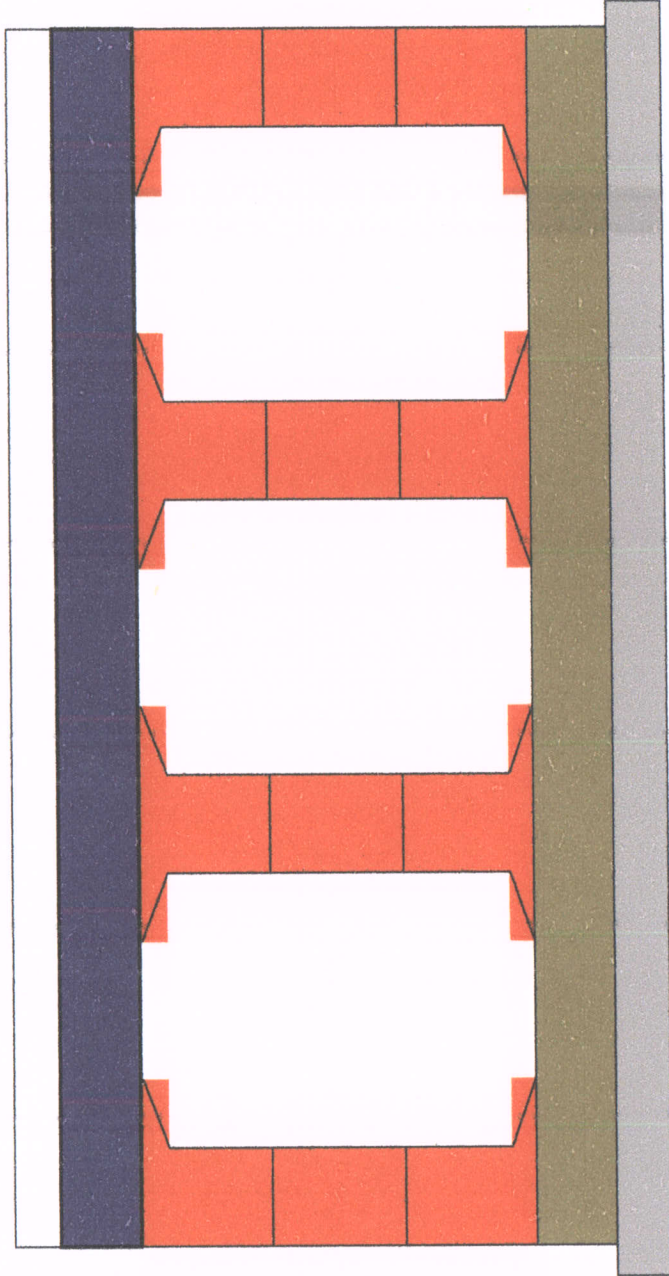

CB					
	3rd Lift				
		2nd Lift			
			1st Lift		
				Raft	
					PCC


MINOR BRIDGE AT KM. 29+600 LHS

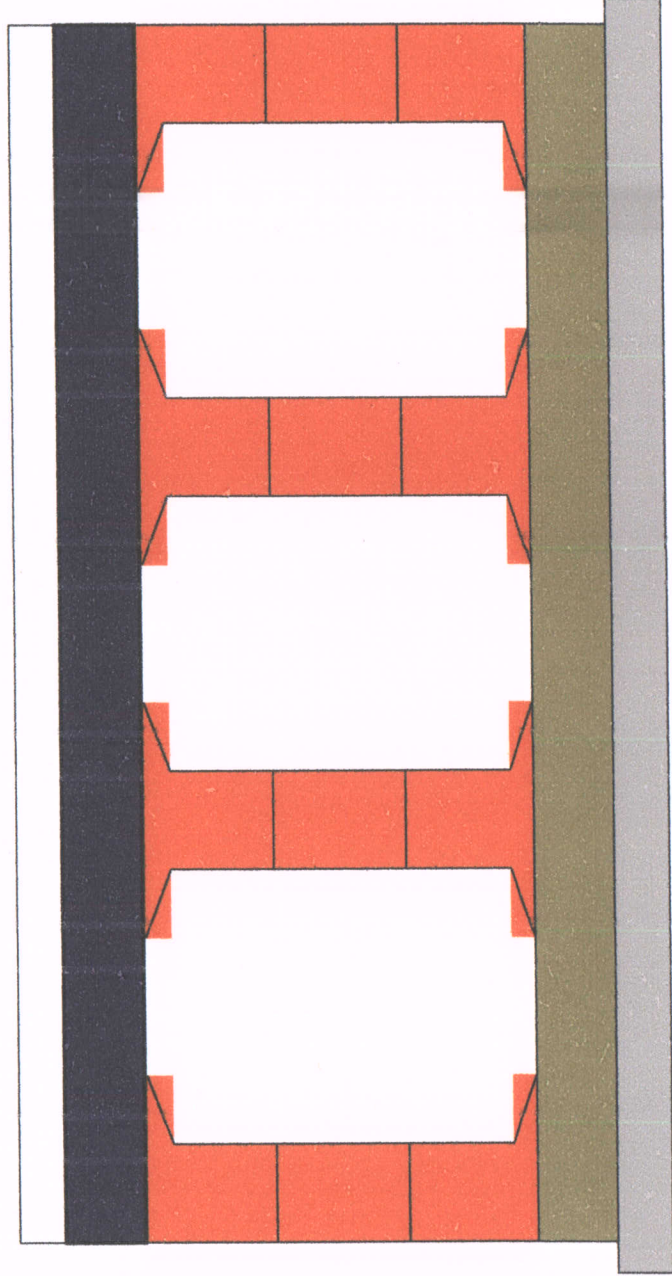

CB					
	3rd Lift				
		2nd Lift			
			1st Lift		
				Raft	
					PCC




MINOR BRIDGE AT KM. 33+000 RHS

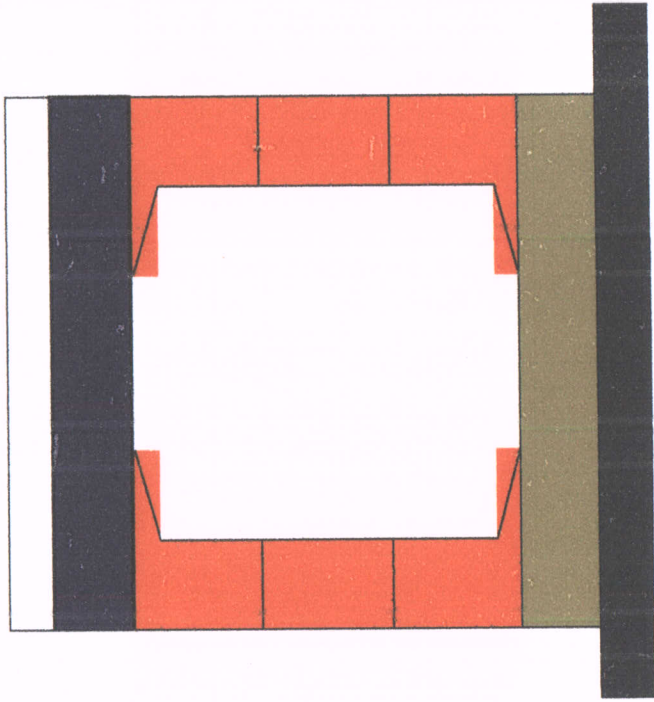

CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC

MINOR BRIDGE AT KM. 33+000 LHS

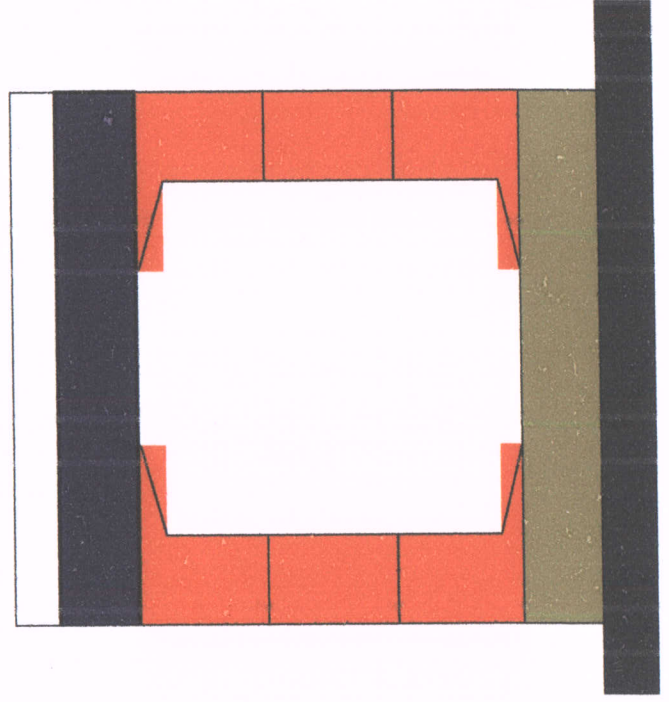


CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC




Handwritten signature and initials in blue ink.

MINOR BRIDGE AT KM. 34+360 RHS

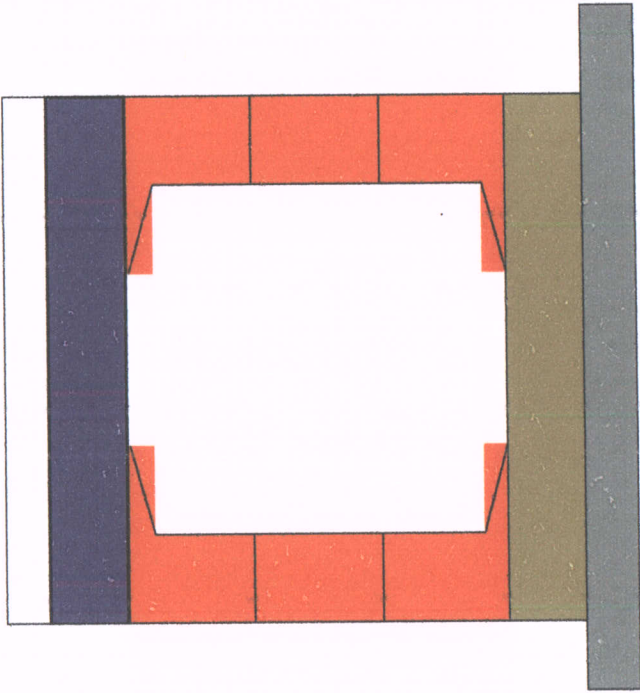

CB						
	3rd Lift					
		2nd Lift				
			1st Lift			
				Raft		
					PCC	

MINOR BRIDGE AT KM. 34+360 LHS

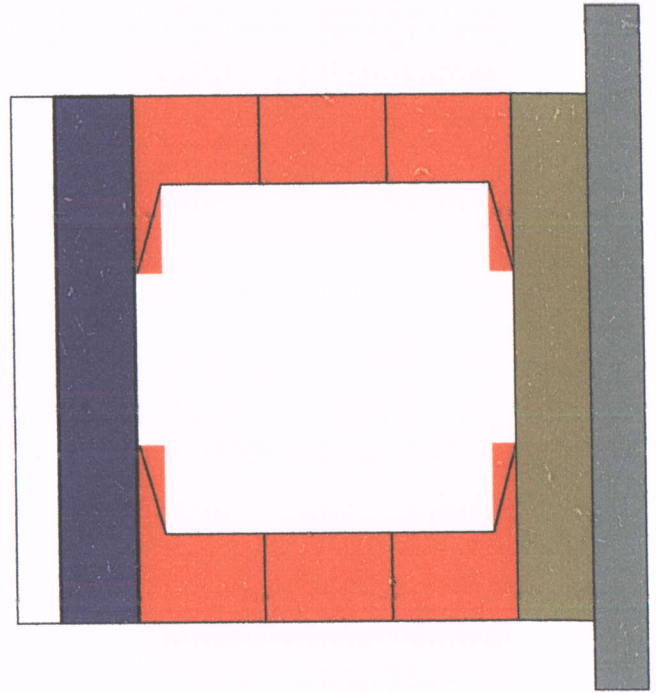


CB						
	3rd Lift					
		2nd Lift				
			1st Lift			
				Raft		
					PCC	




[Handwritten signature]

MINOR BRIDGE AT KM. 44+900 RHS

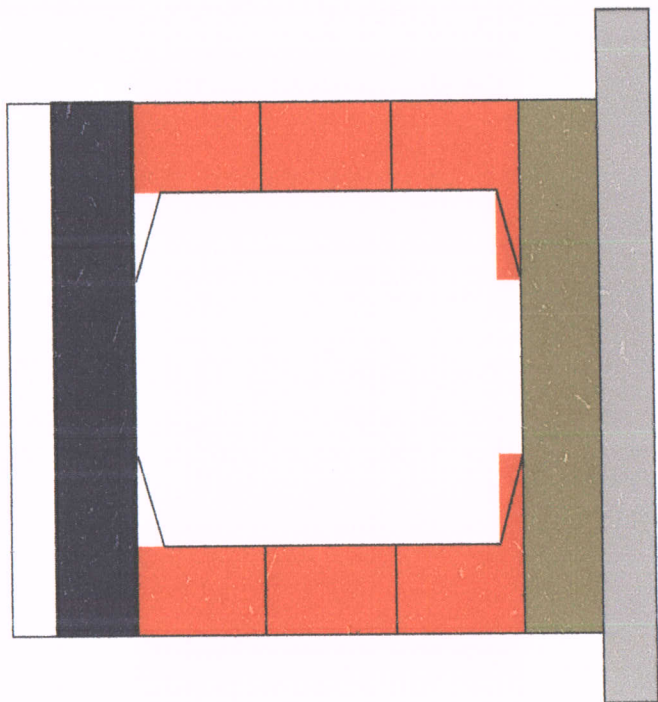


CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC

MINOR BRIDGE AT KM. 44+900 LHS

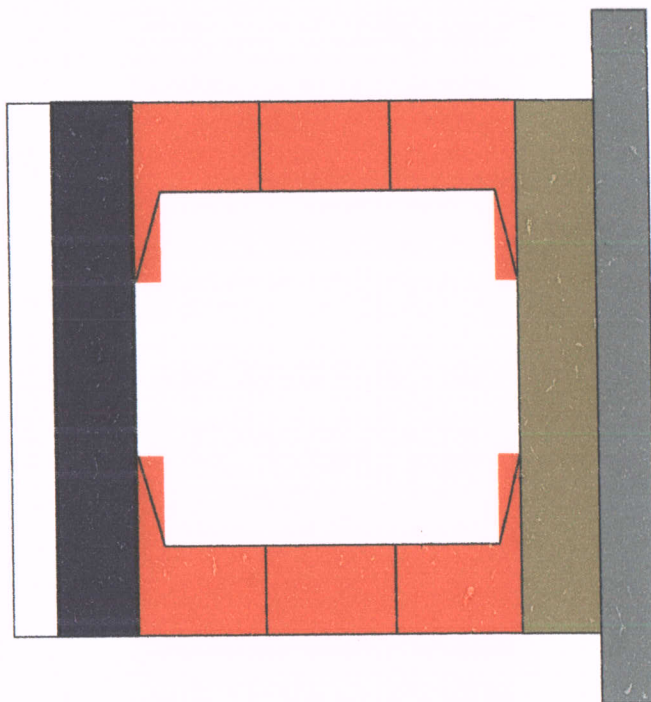


CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC



Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project (Length 48.880 Km.) -Package II


MINOR BRIDGE AT KM. 49+785 (Main Carriage Way) RHS

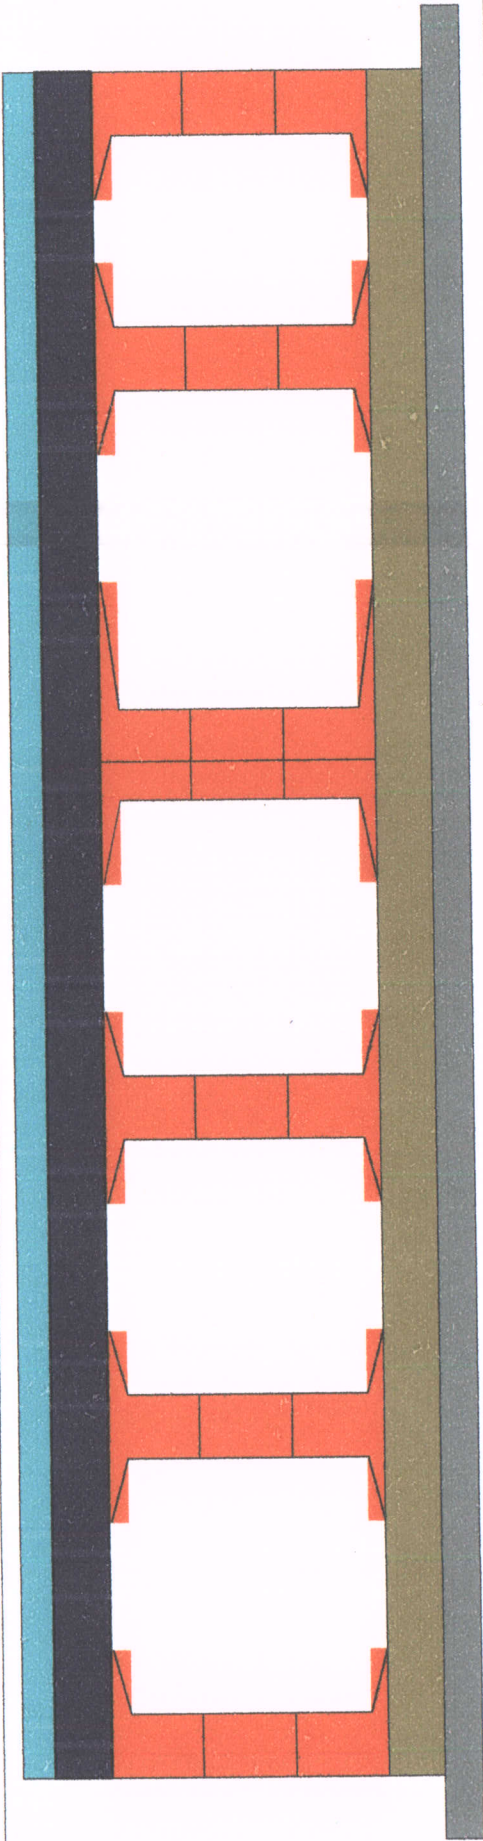

CB						
3rd Lift						
2nd Lift						
1st Lift						
Raft						
PCC						

Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project (Length 48.880 Km.) -Package II

MINOR BRIDGE AT KM. 49+785 (Main Carriage Way) LHS

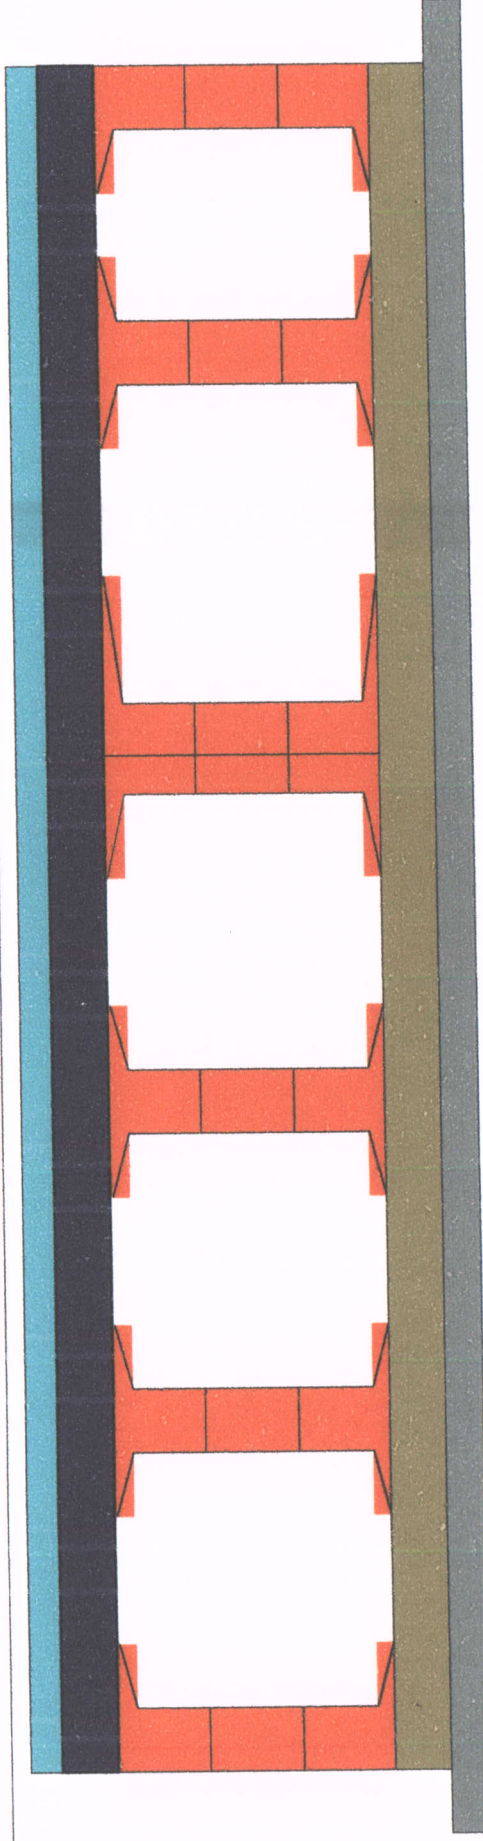


CB						
3rd Lift						
2nd Lift						
1st Lift						
Raft						
PCC						




Handwritten signature in blue ink.

MINOR BRIDGE AT KM. 49+785 (Service Road) RHS

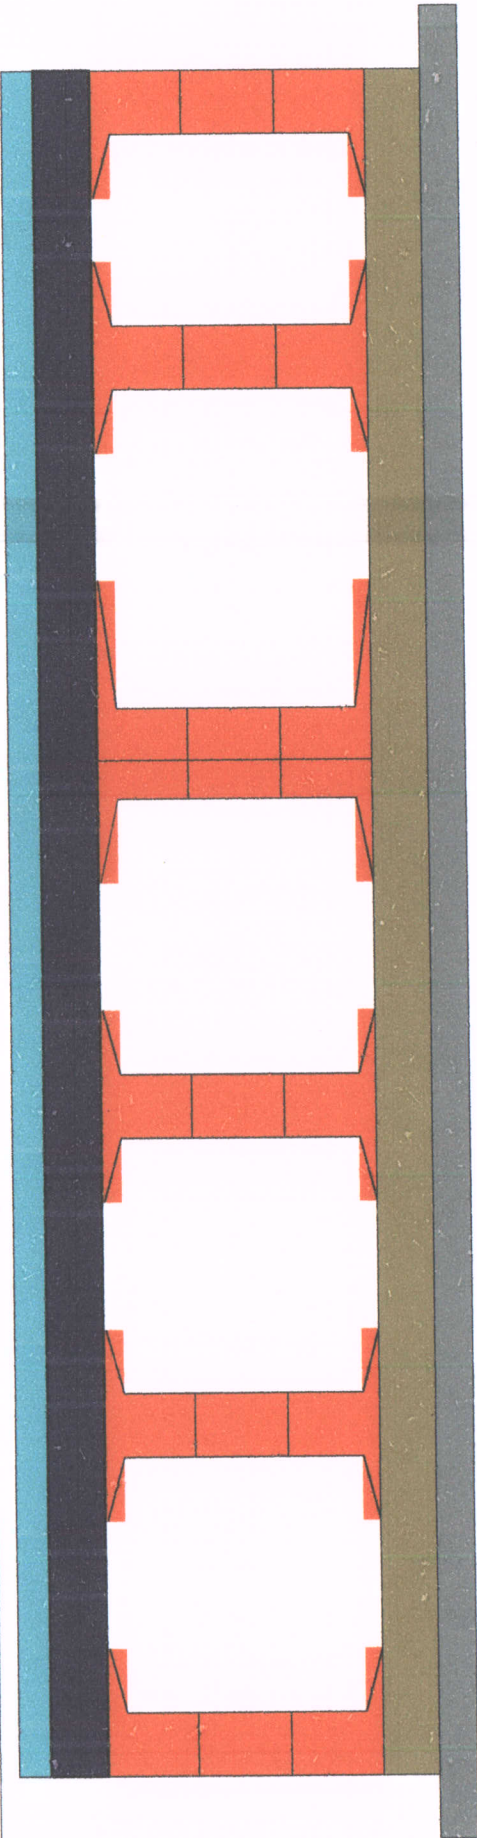

CB					
	3rd Lift				
		2nd Lift			
			1st Lift		
				Raft	
					PCC


MINOR BRIDGE AT KM. 49+785 (Service Road) LHS

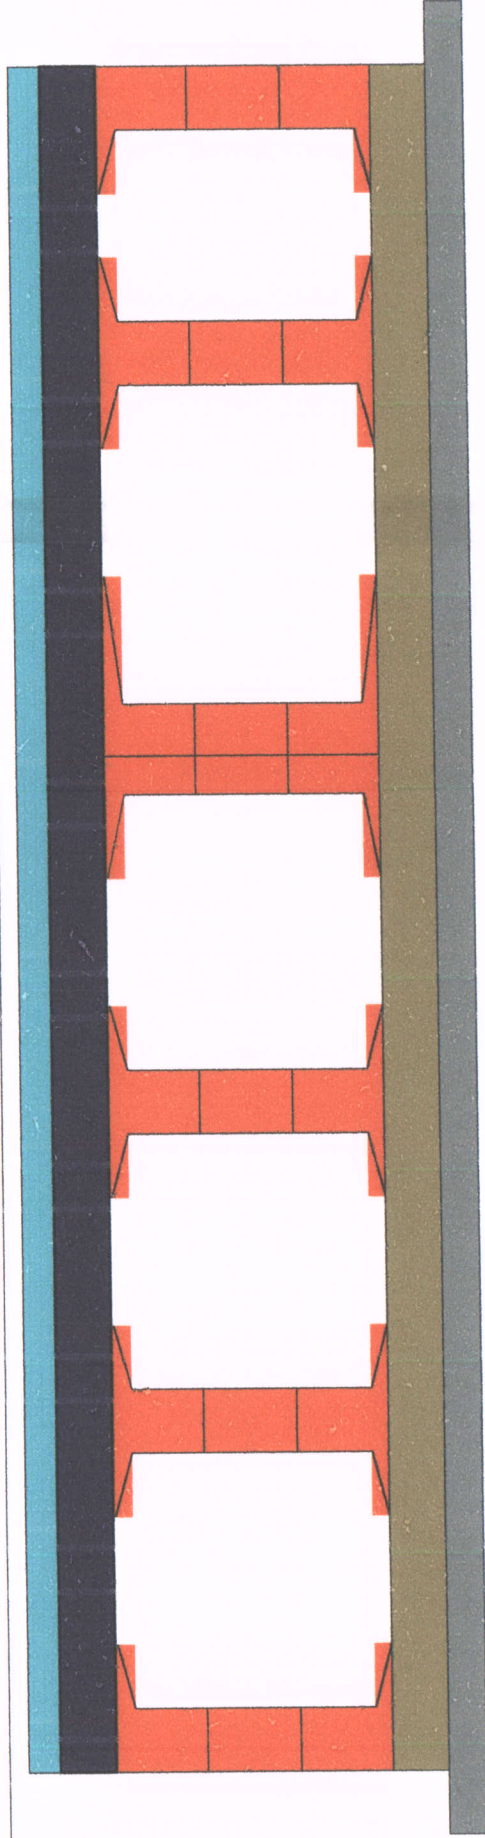

CB					
	3rd Lift				
		2nd Lift			
			1st Lift		
				Raft	
					PCC




MINOR BRIDGE AT KM. 54+040 RHS

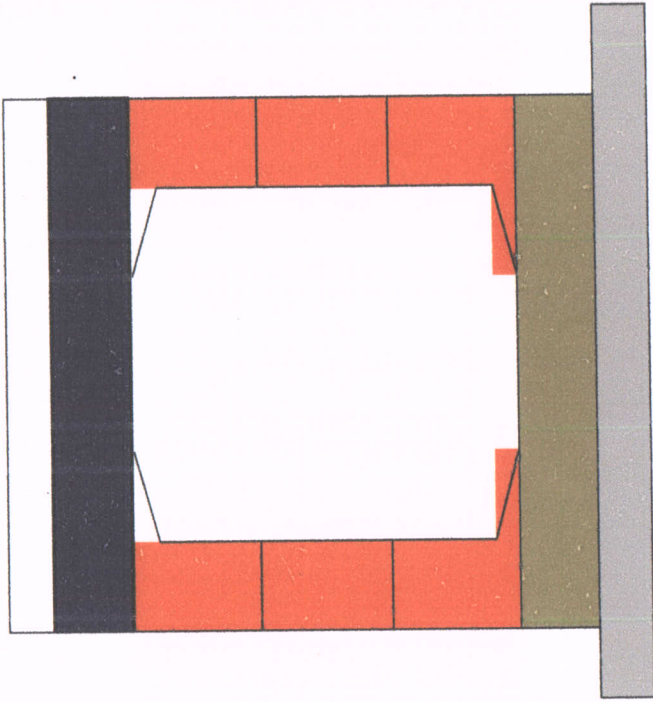



CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC

MINOR BRIDGE AT KM. 54+040 LHS

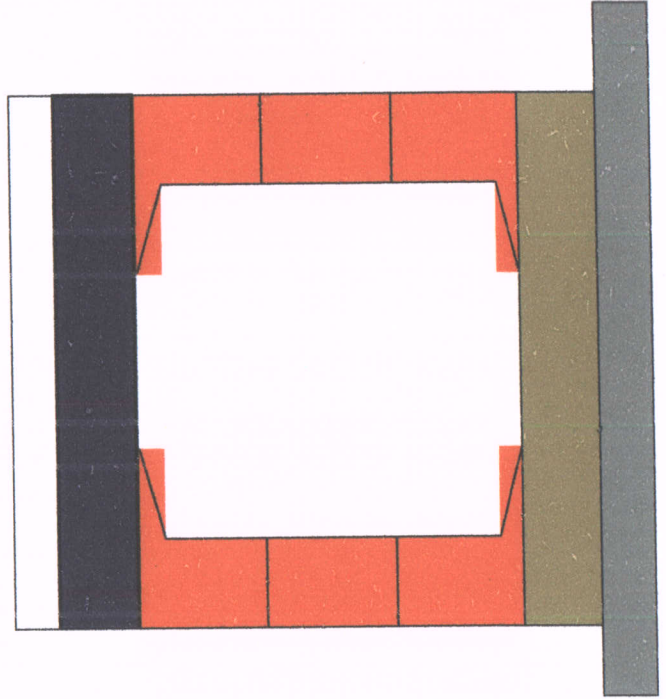


CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC



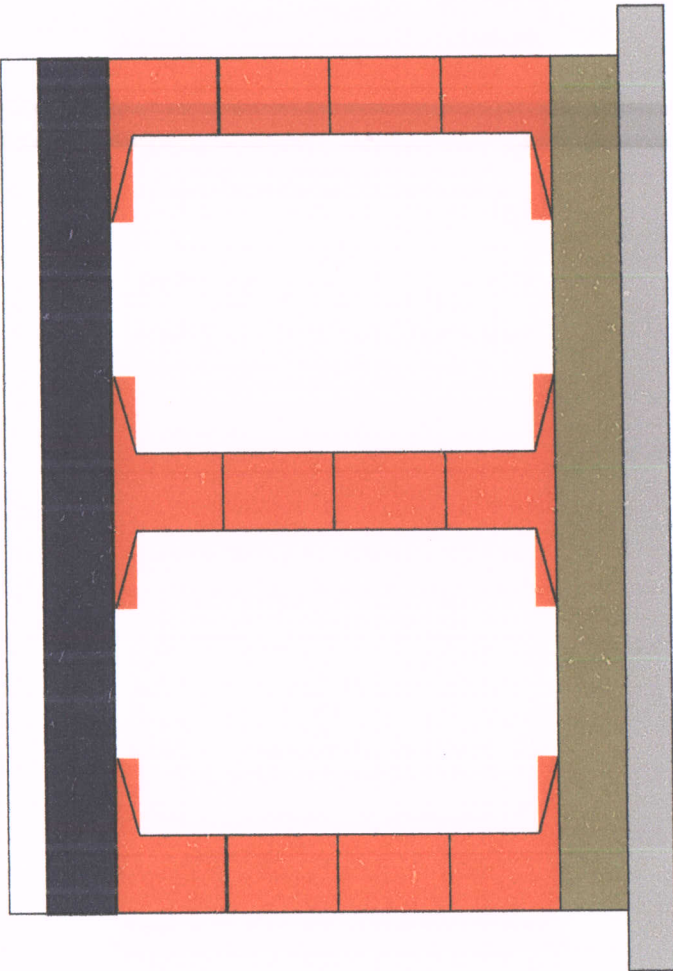





CB
Slab
4th Lift
3rd Lift
2nd Lift
1st Lift
Raft
PCC

MINOR BRIDGE AT KM. 54+070 LHS



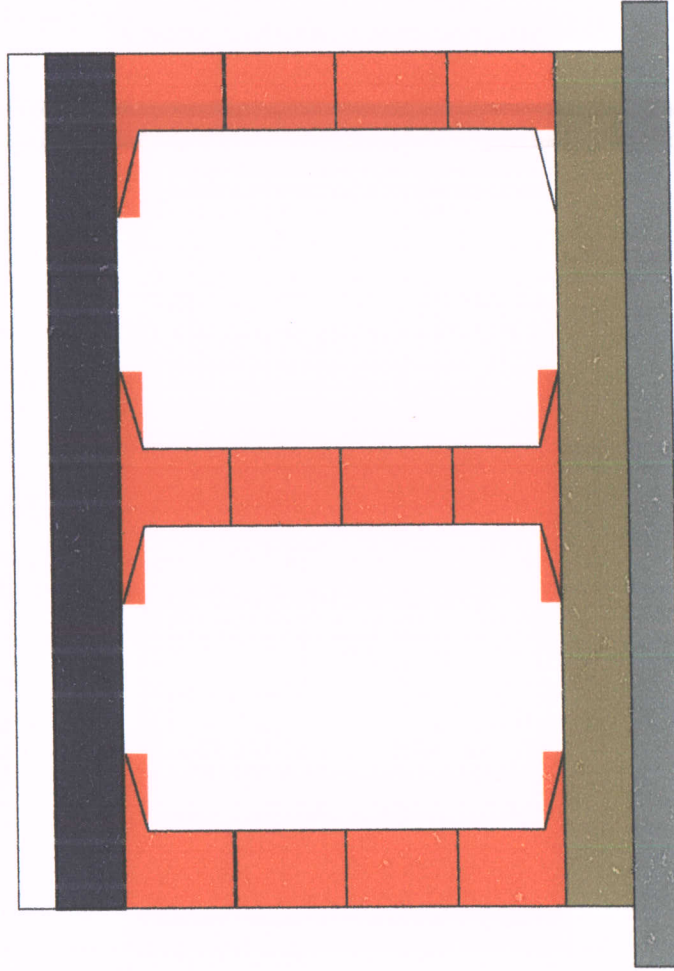


CB
Slab
4th Lift
3rd Lift
2nd Lift
1st Lift
Raft
PCC






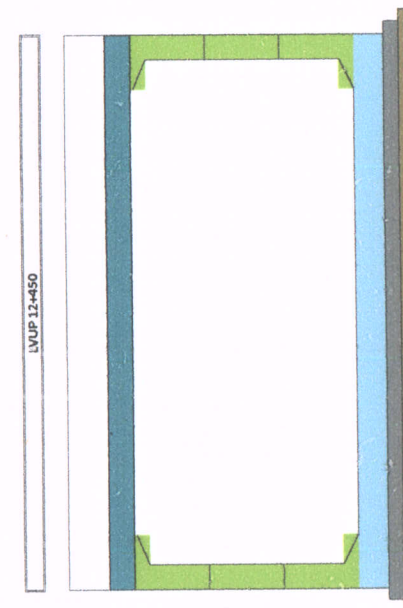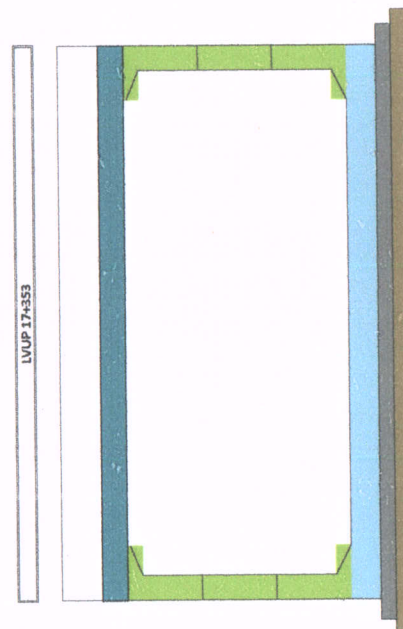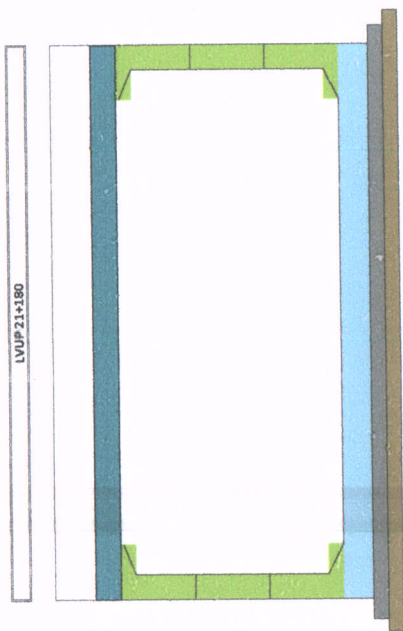

CB
Deck Slab
U/R
U/R
U/R
Raft
PCC
Excavation
Chainage


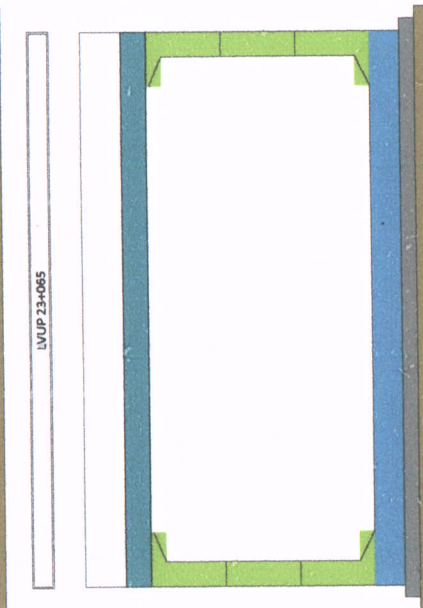
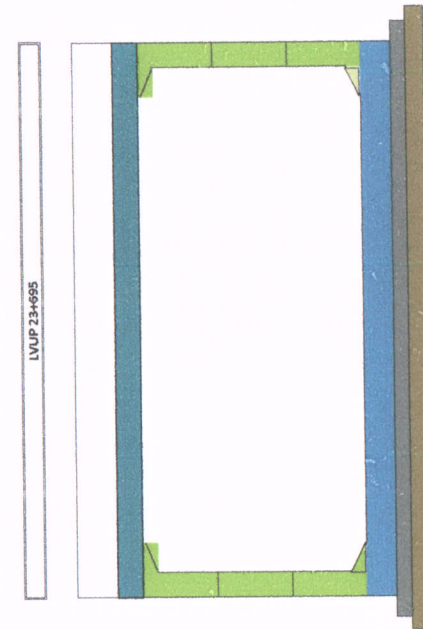
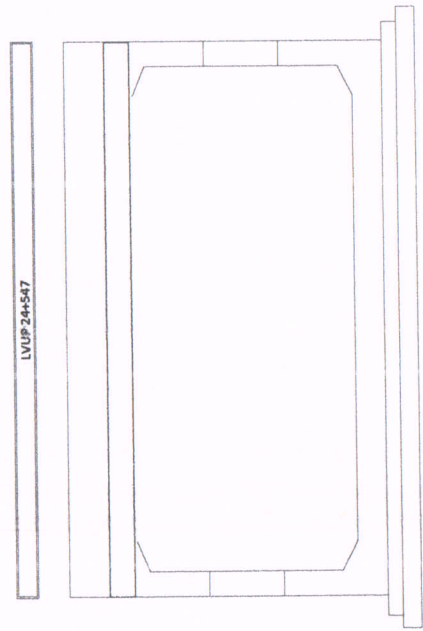


CB
Deck Slab
U/R
U/R
U/R
Raft
PCC
Excavation

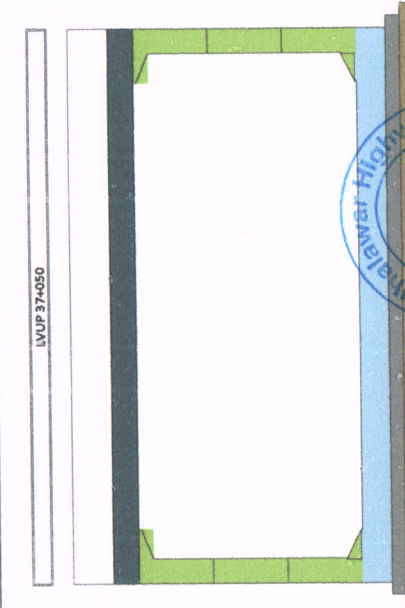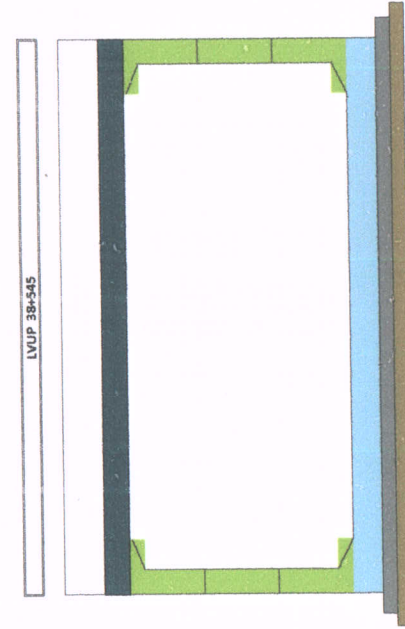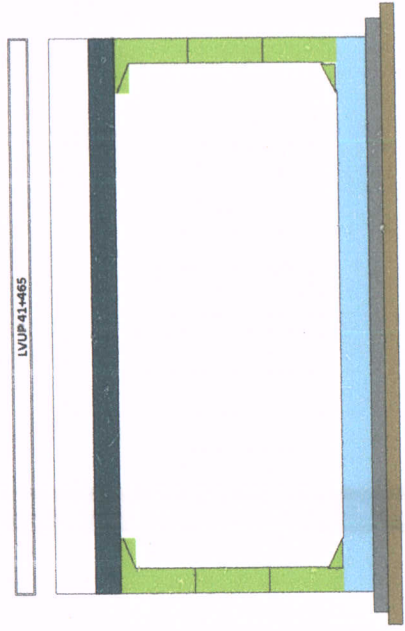

CB
Deck Slab
U/R
U/R
U/R
Raft
PCC
Excavation


Patel Dahan-Jhalawar Highway Pvt. Ltd. ★
 PATEL
 (Signature)

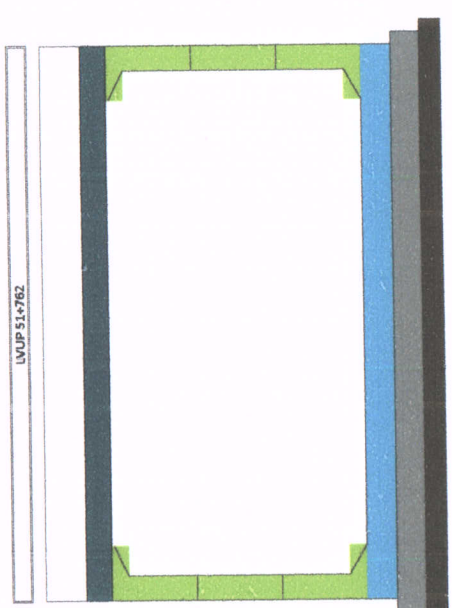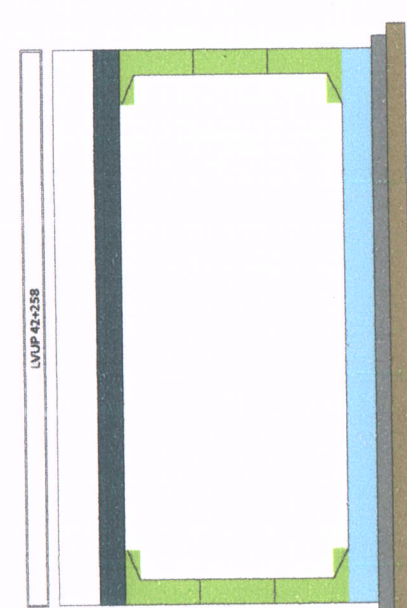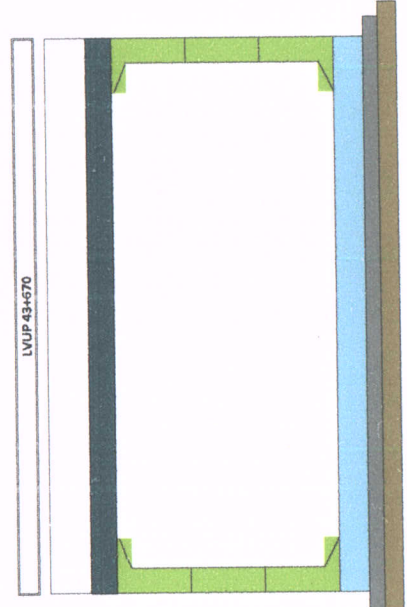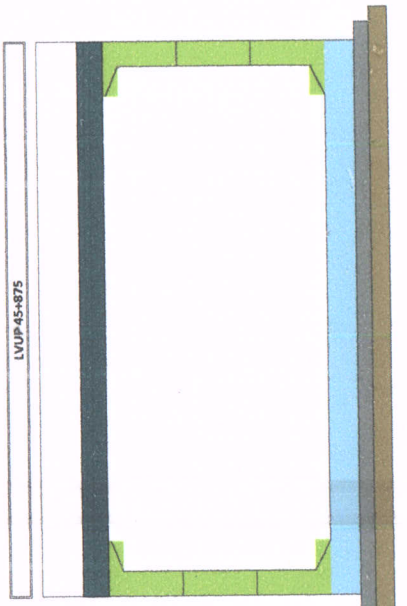

Chainage
CB
Deck Slab
UP
UP
UP
Barf
PCC
Excavation

CB
Deck Slab
UP
UP
UP
Barf
PCC
Excavation



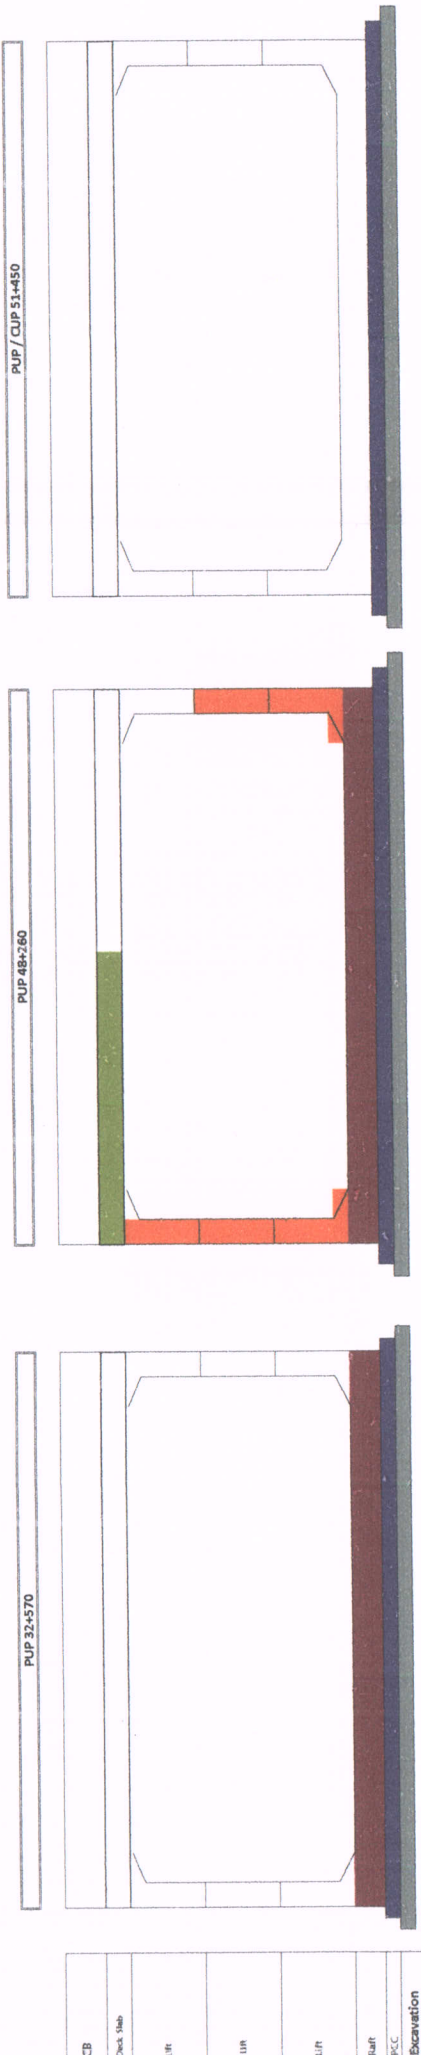


CB
Deck Slab
L/H
L/H
L/H
Surf
PCC
Excavation




Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II.

VEHICULAR UNDERPASS AT 12+125 A1/A2RHS

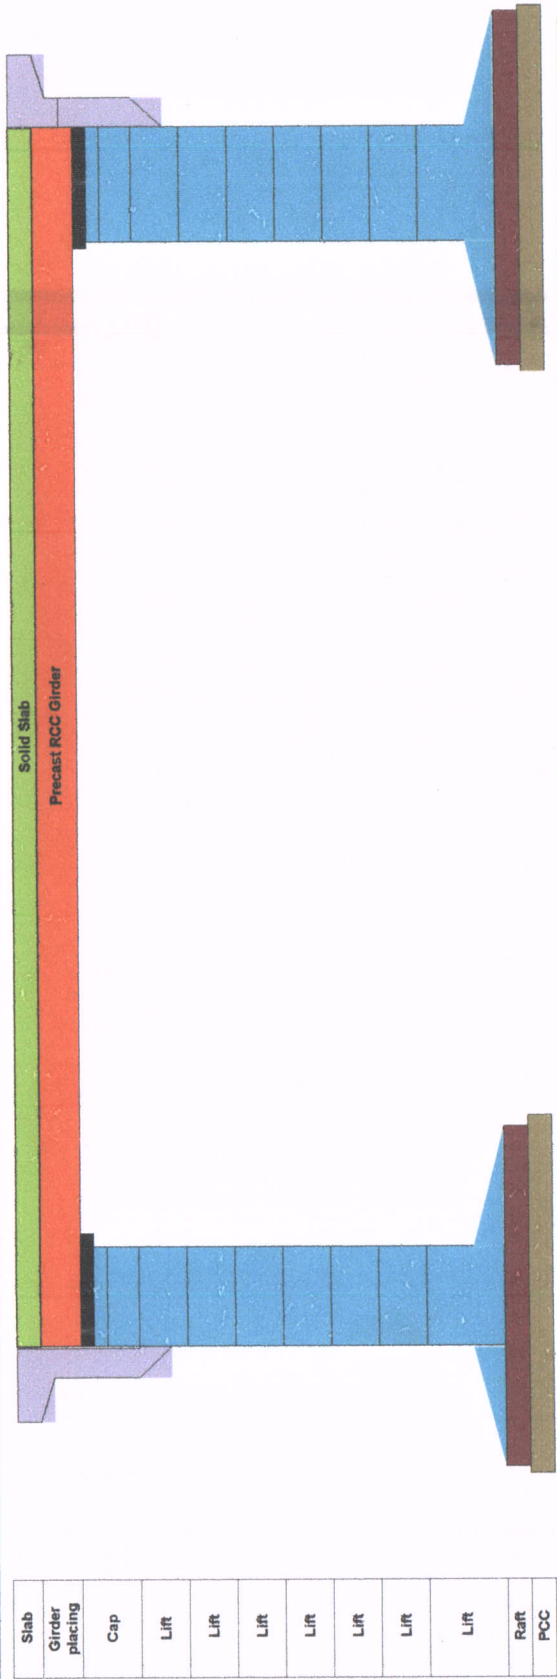


Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
POC

VEHICULAR UNDERPASS AT 12+125A1/A2 LHS

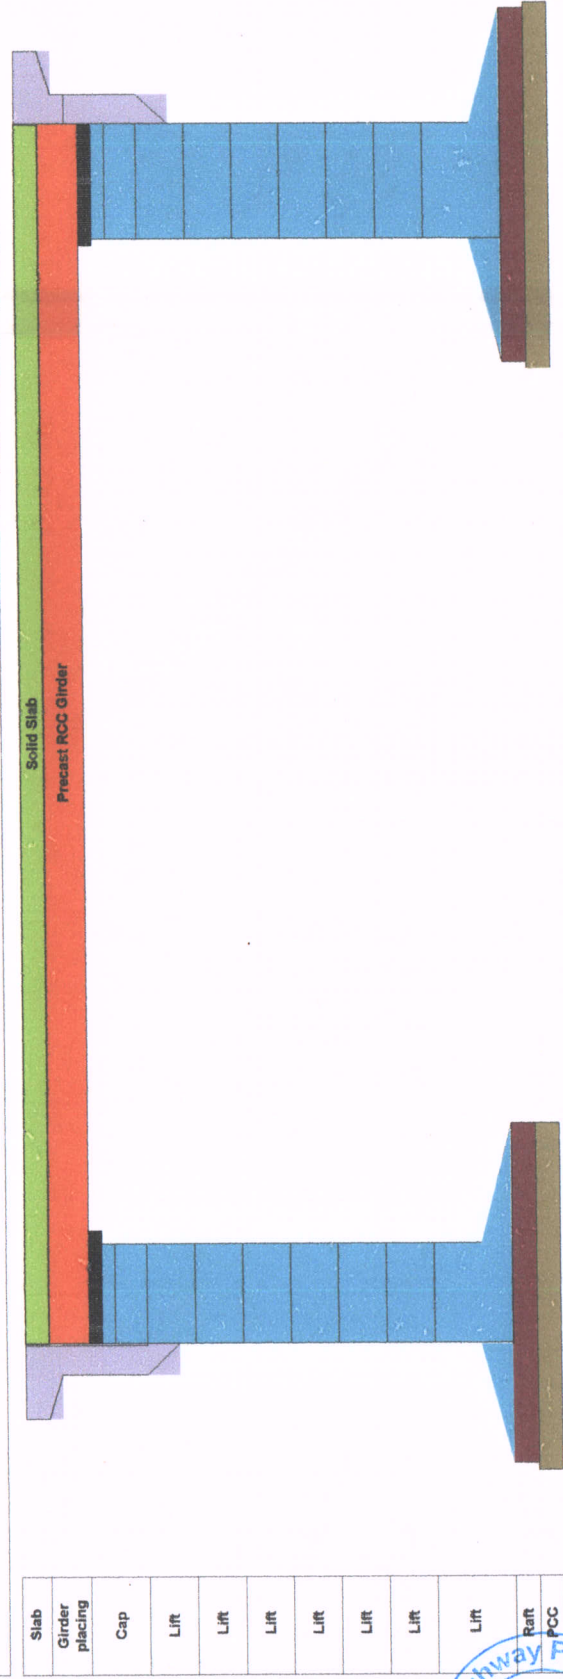


Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
POC




Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darrah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDIP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

VEHICULAR UNDERPASS AT 15+725 A1/A2 RHS

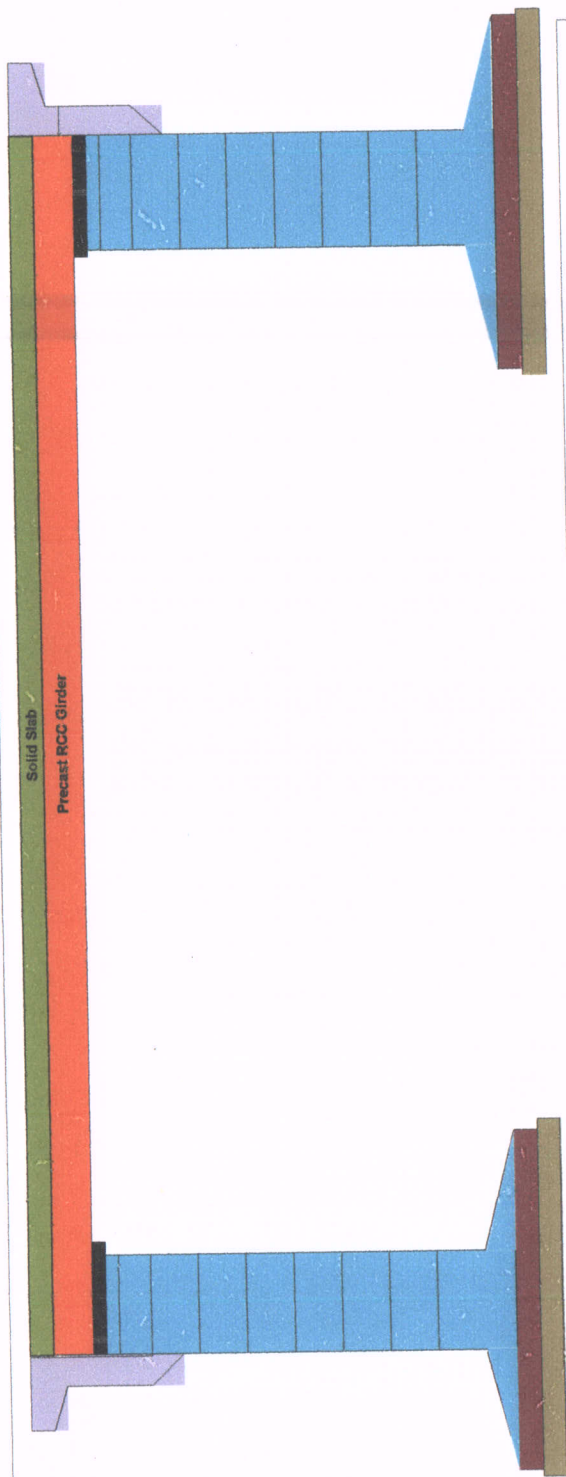

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

VEHICULAR UNDERPASS AT 15+725 A1/A2 LHS

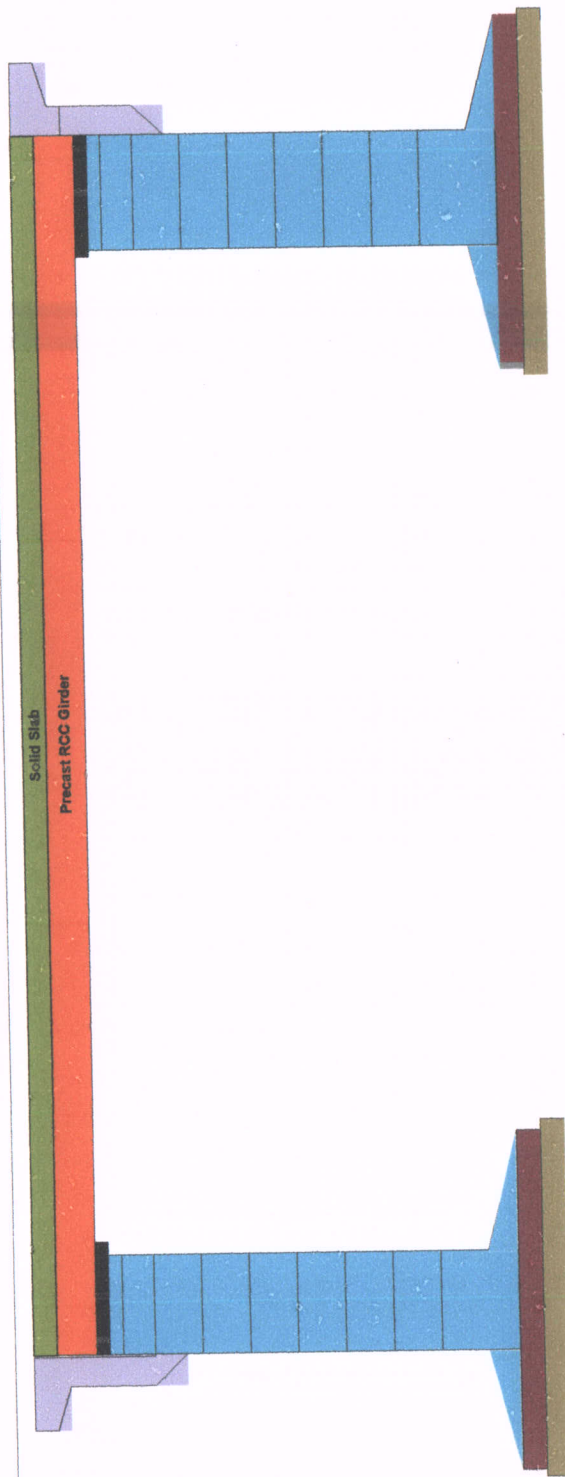


Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

(Handwritten signature)
 Patel Darrah Jhalawar Highway
PATEL
 Patel Darrah Jhalawar Highway


Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km. 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

VEHICULAR UNDERPASS AT 19+965 A1/ A2 LHS

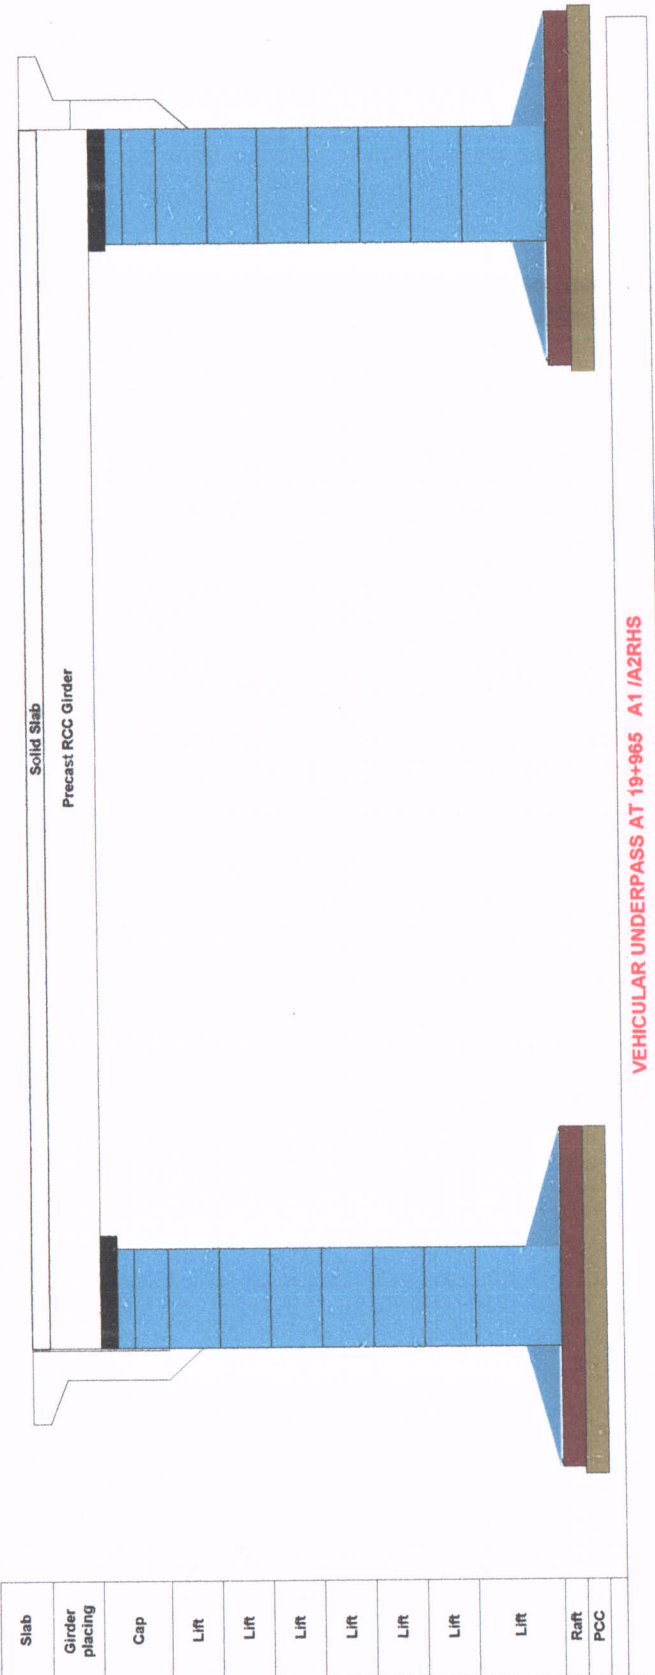

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

VEHICULAR UNDERPASS AT 19+965 A1 /A2RHS

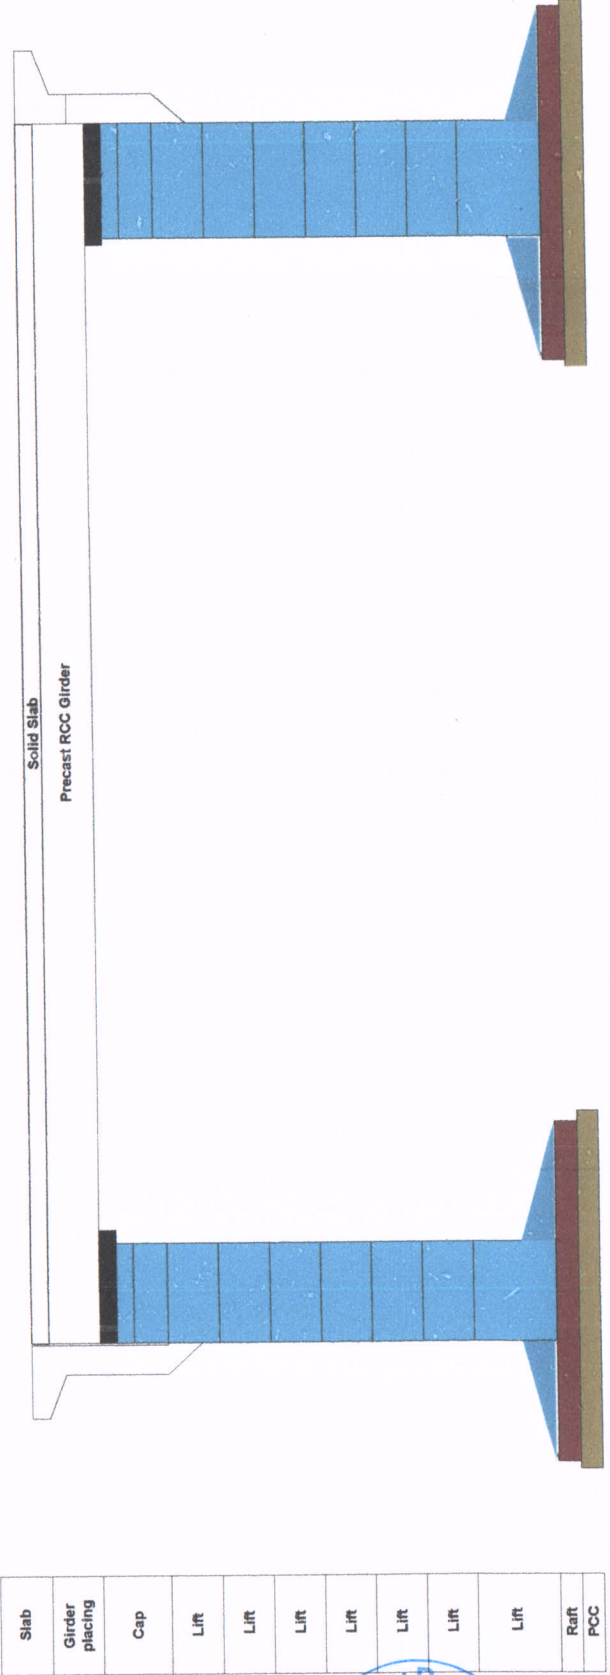


Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

(Handwritten signature)


 Patel Darah-Jhalawar Highway Pvt. Ltd. * PATEL


Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

VEHICULAR UNDERPASS AT 25+100 A1/A2 RHS

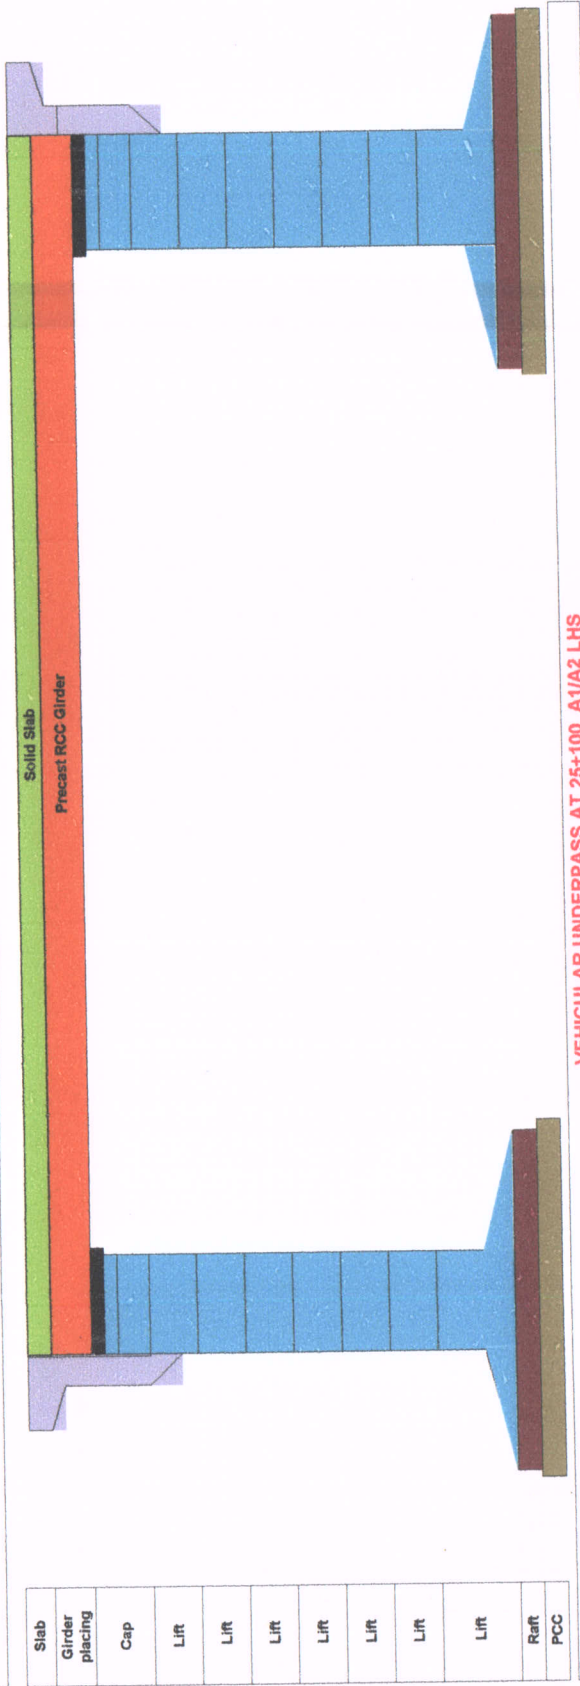

VEHICULAR UNDERPASS AT 25+100 A1/A2 LHS

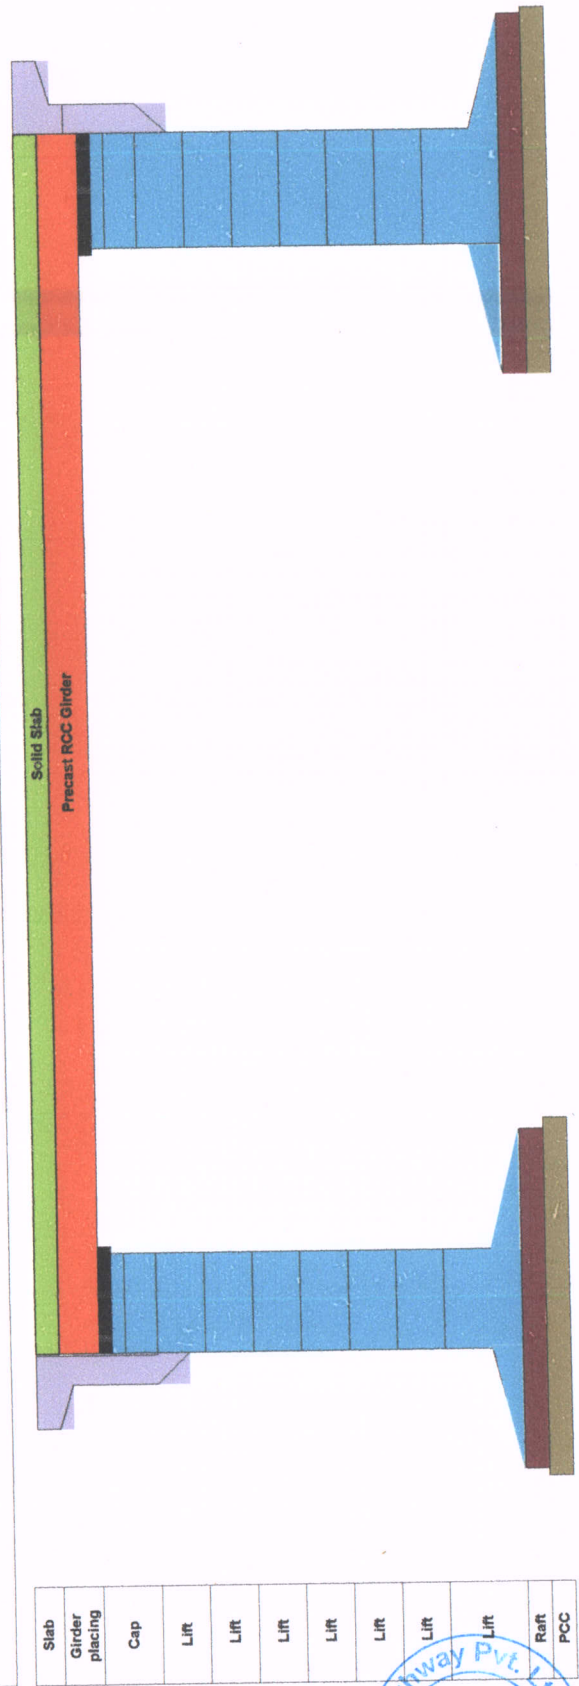

(Handwritten signature)

 Patel Darah-Jhalawar Highway Pvt. Ltd. ★
 PATEL

Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darrah-Jhalawat-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

VEHICULAR UNDERPASS AT 27+029 A1/A2 RHS



Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

VEHICULAR UNDERPASS AT 27+029 A1/A2 LHS



Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

[Handwritten signature]

 Patel Darrah-Jhalawat Highway Pvt. Ltd. * PATEL


Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darrah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

VEHICULAR UNDERPASS AT 30+075 A1/ A2 LHS



Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

VEHICULAR UNDERPASS AT 30+075 A1/A2RHS

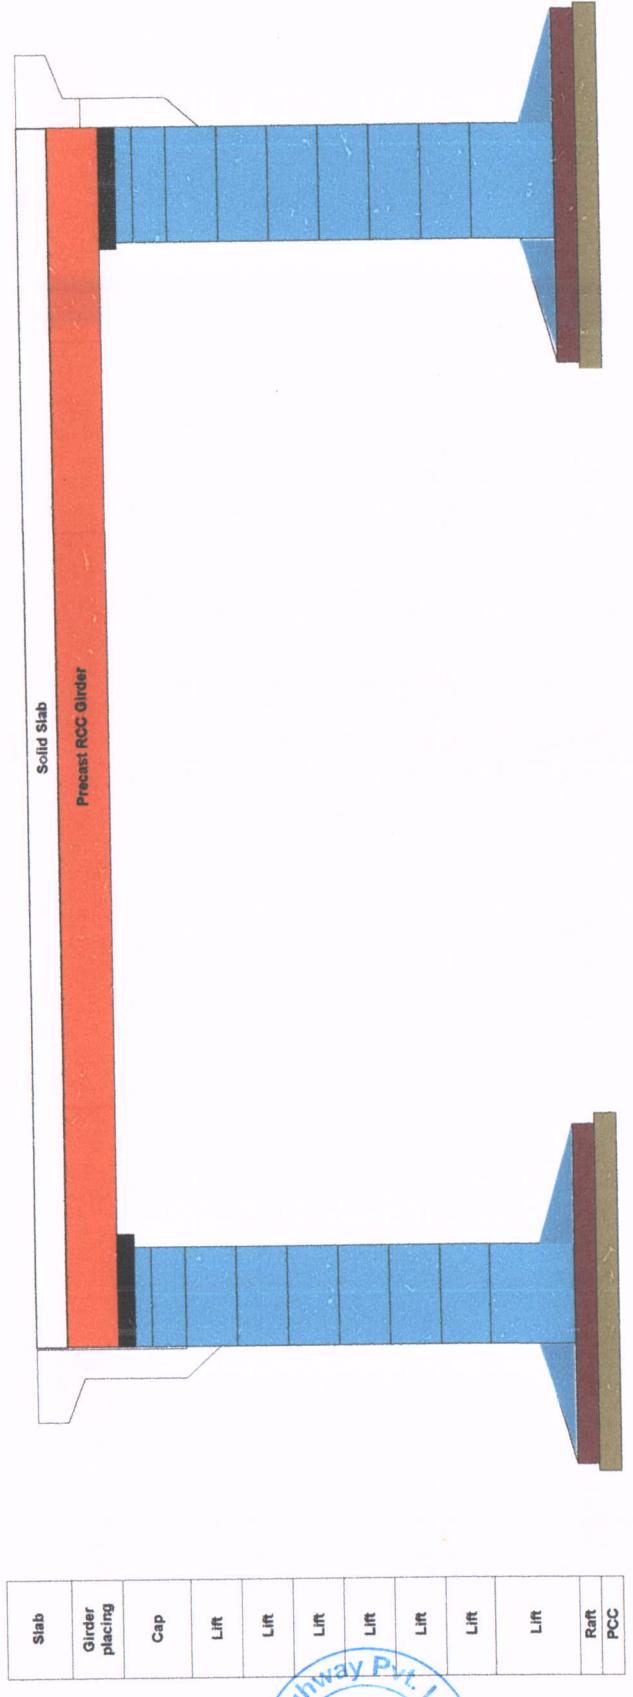


Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

25

 Patel Darrah-Jhalawar Highway Pvt. Ltd. * PATEL

Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDIP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

VEHICULAR UNDERPASS AT 41+095 A1/ A2 LHS

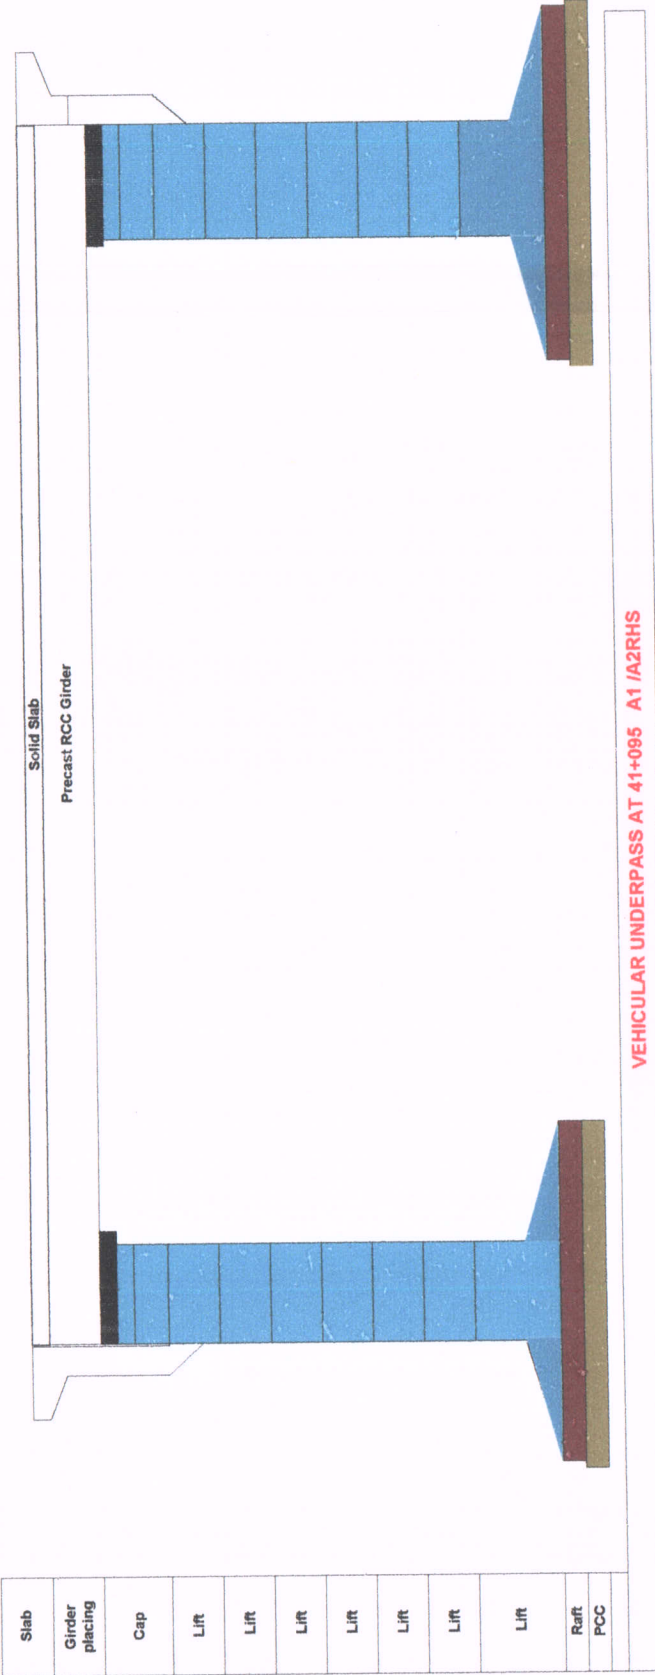

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

VEHICULAR UNDERPASS AT 41+095 A1 /A2RHS




Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

(Handwritten signature)

 Page-703

Project:- Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project (Length 48.880 Km.) -Package II

VEHICULAR UNDERPASS AT 49+330A1/ A2 LHS

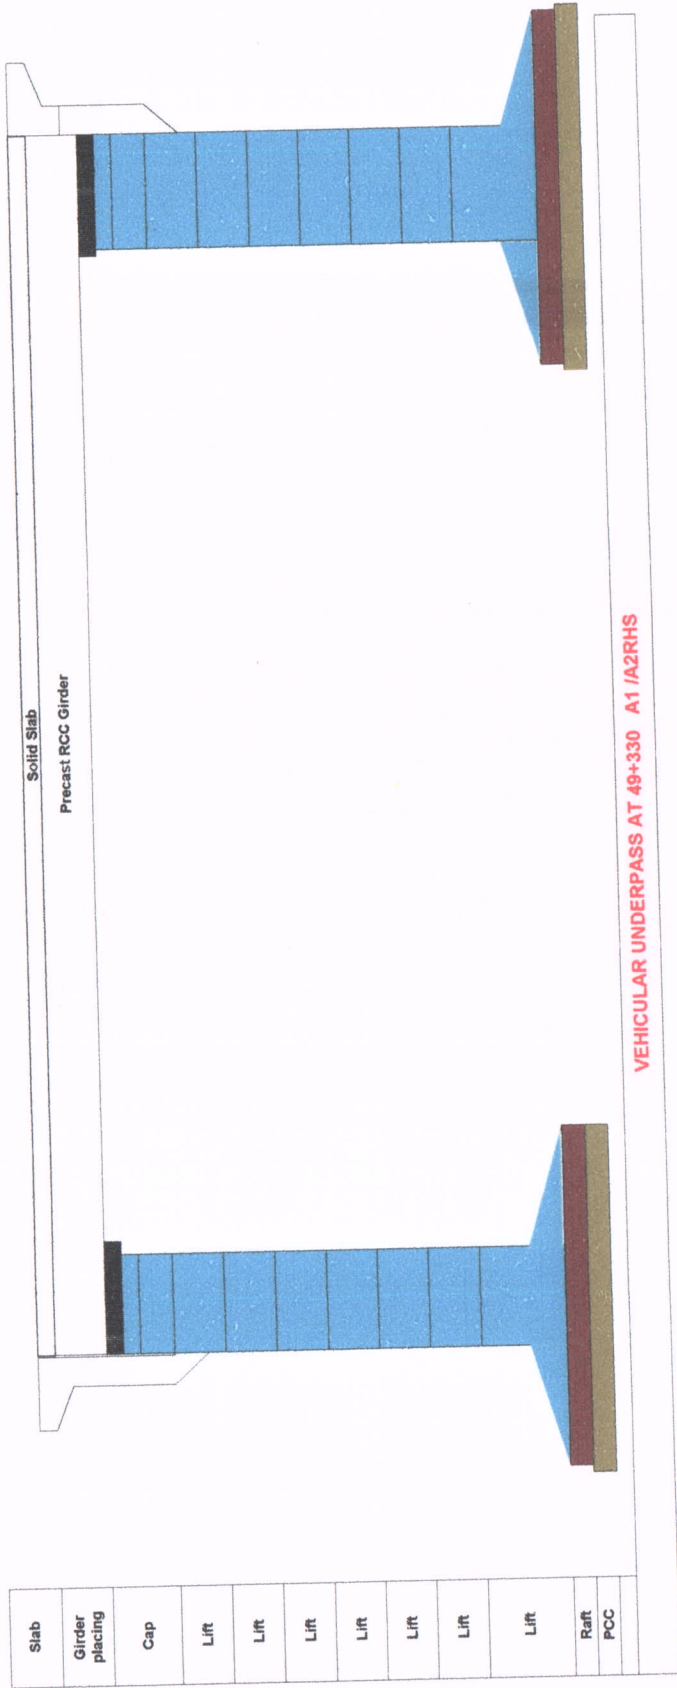

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

VEHICULAR UNDERPASS AT 49+330 A1 /A2RHS



Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

Handwritten signature and a circular stamp. The stamp contains the text 'PATEL' and 'Patel Darah-Jhalawar Highway Pvt. Ltd.' around the perimeter.


Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.)-Package II

VEHICULAR UNDERPASS AT 54+550 A1/ A2 LHS




Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

VEHICULAR UNDERPASS AT 54+550 A1/A2RHS


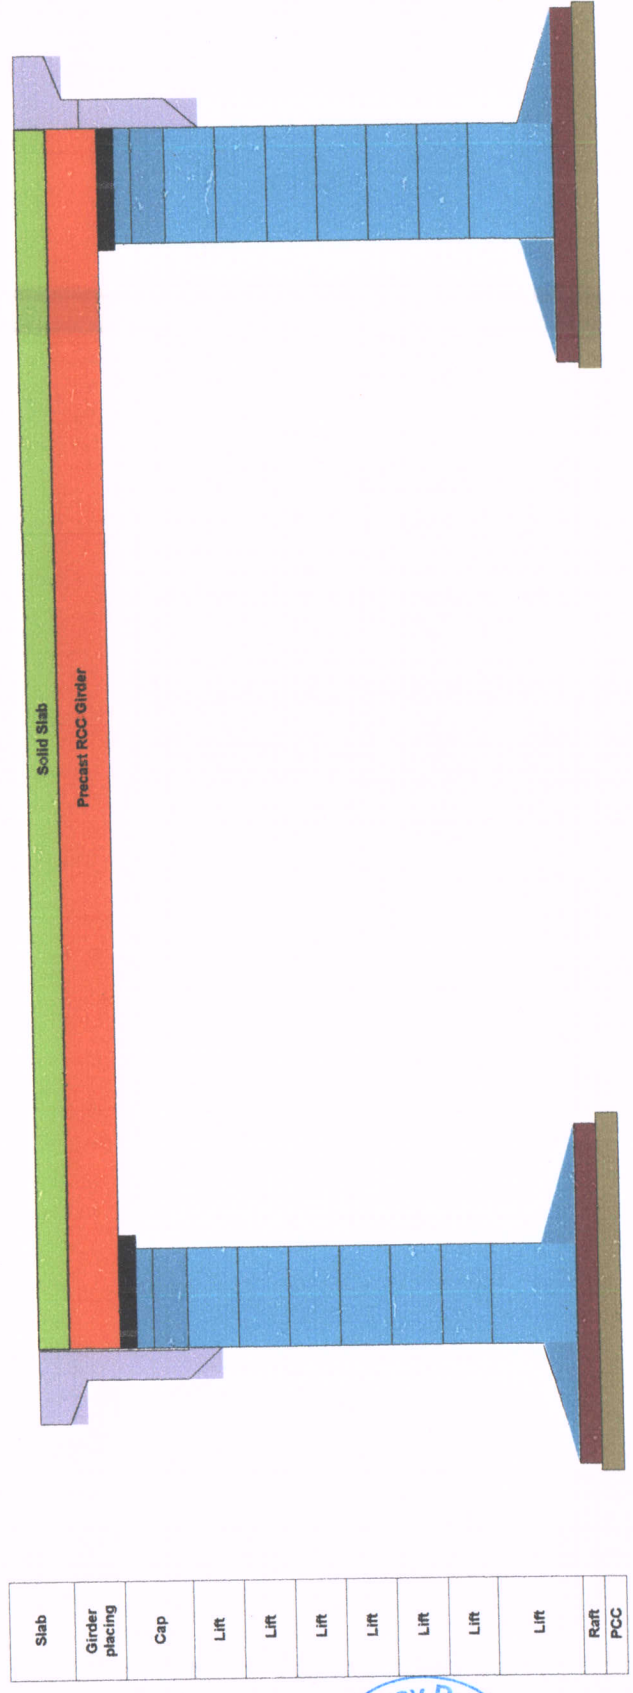


Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

Handwritten signature




Project:-Construction of 4-lane Road (Lawar-Teendhar section) in the State

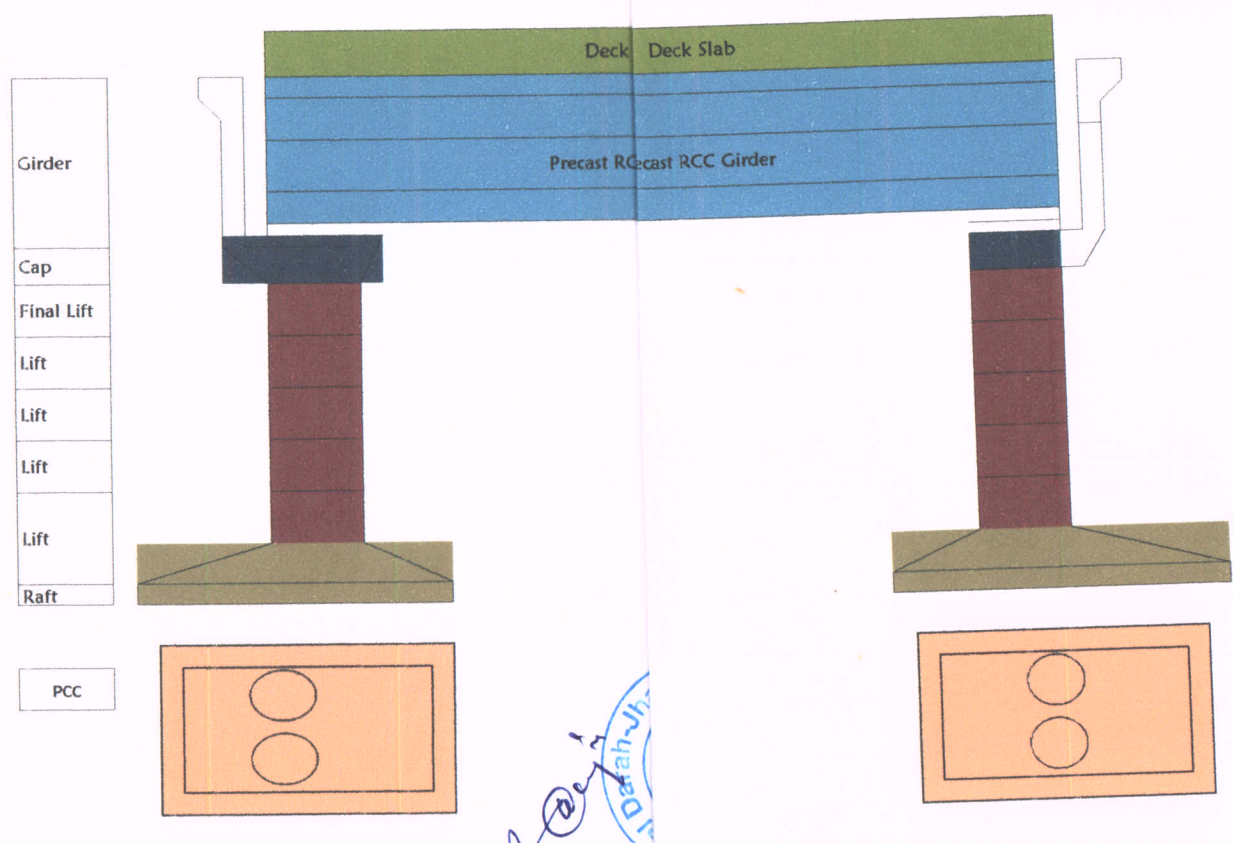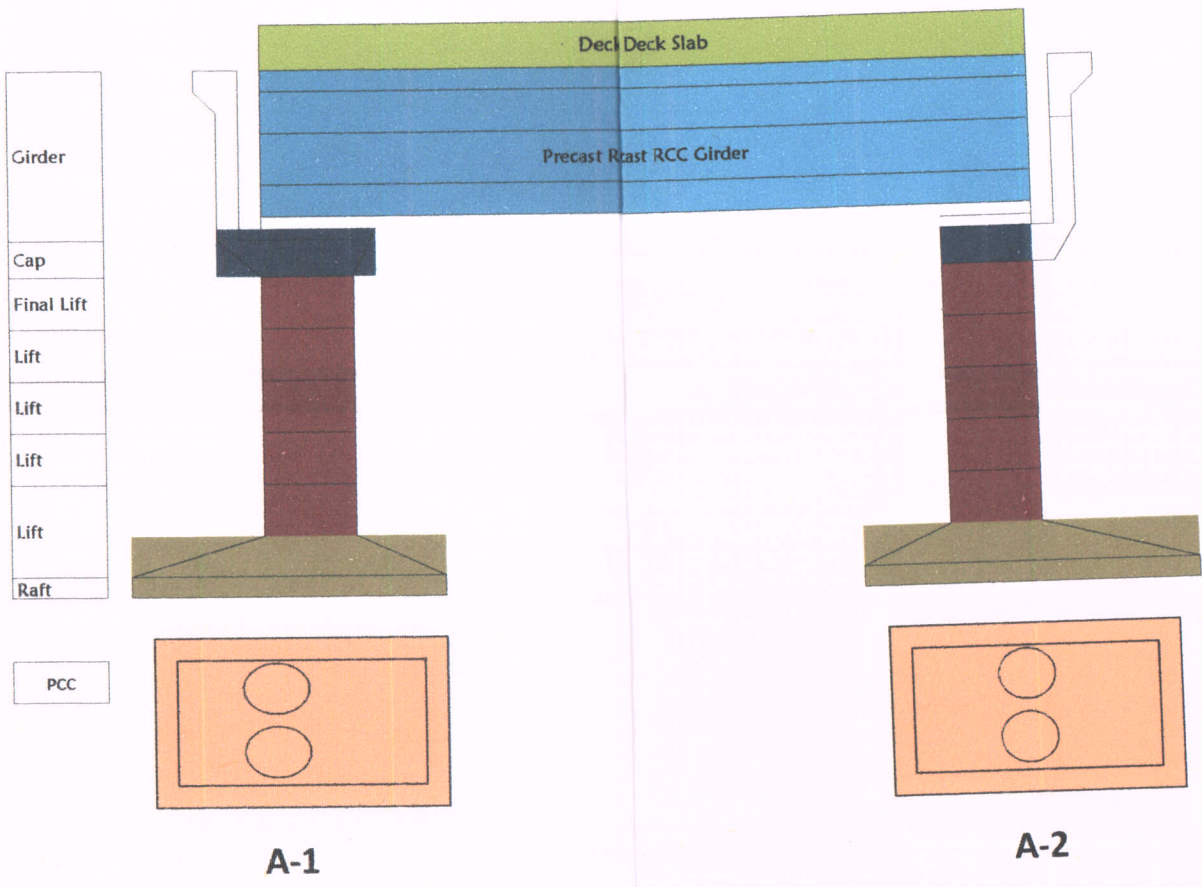


[Handwritten signature and official stamp]


FLYOVER (50+095)RHS

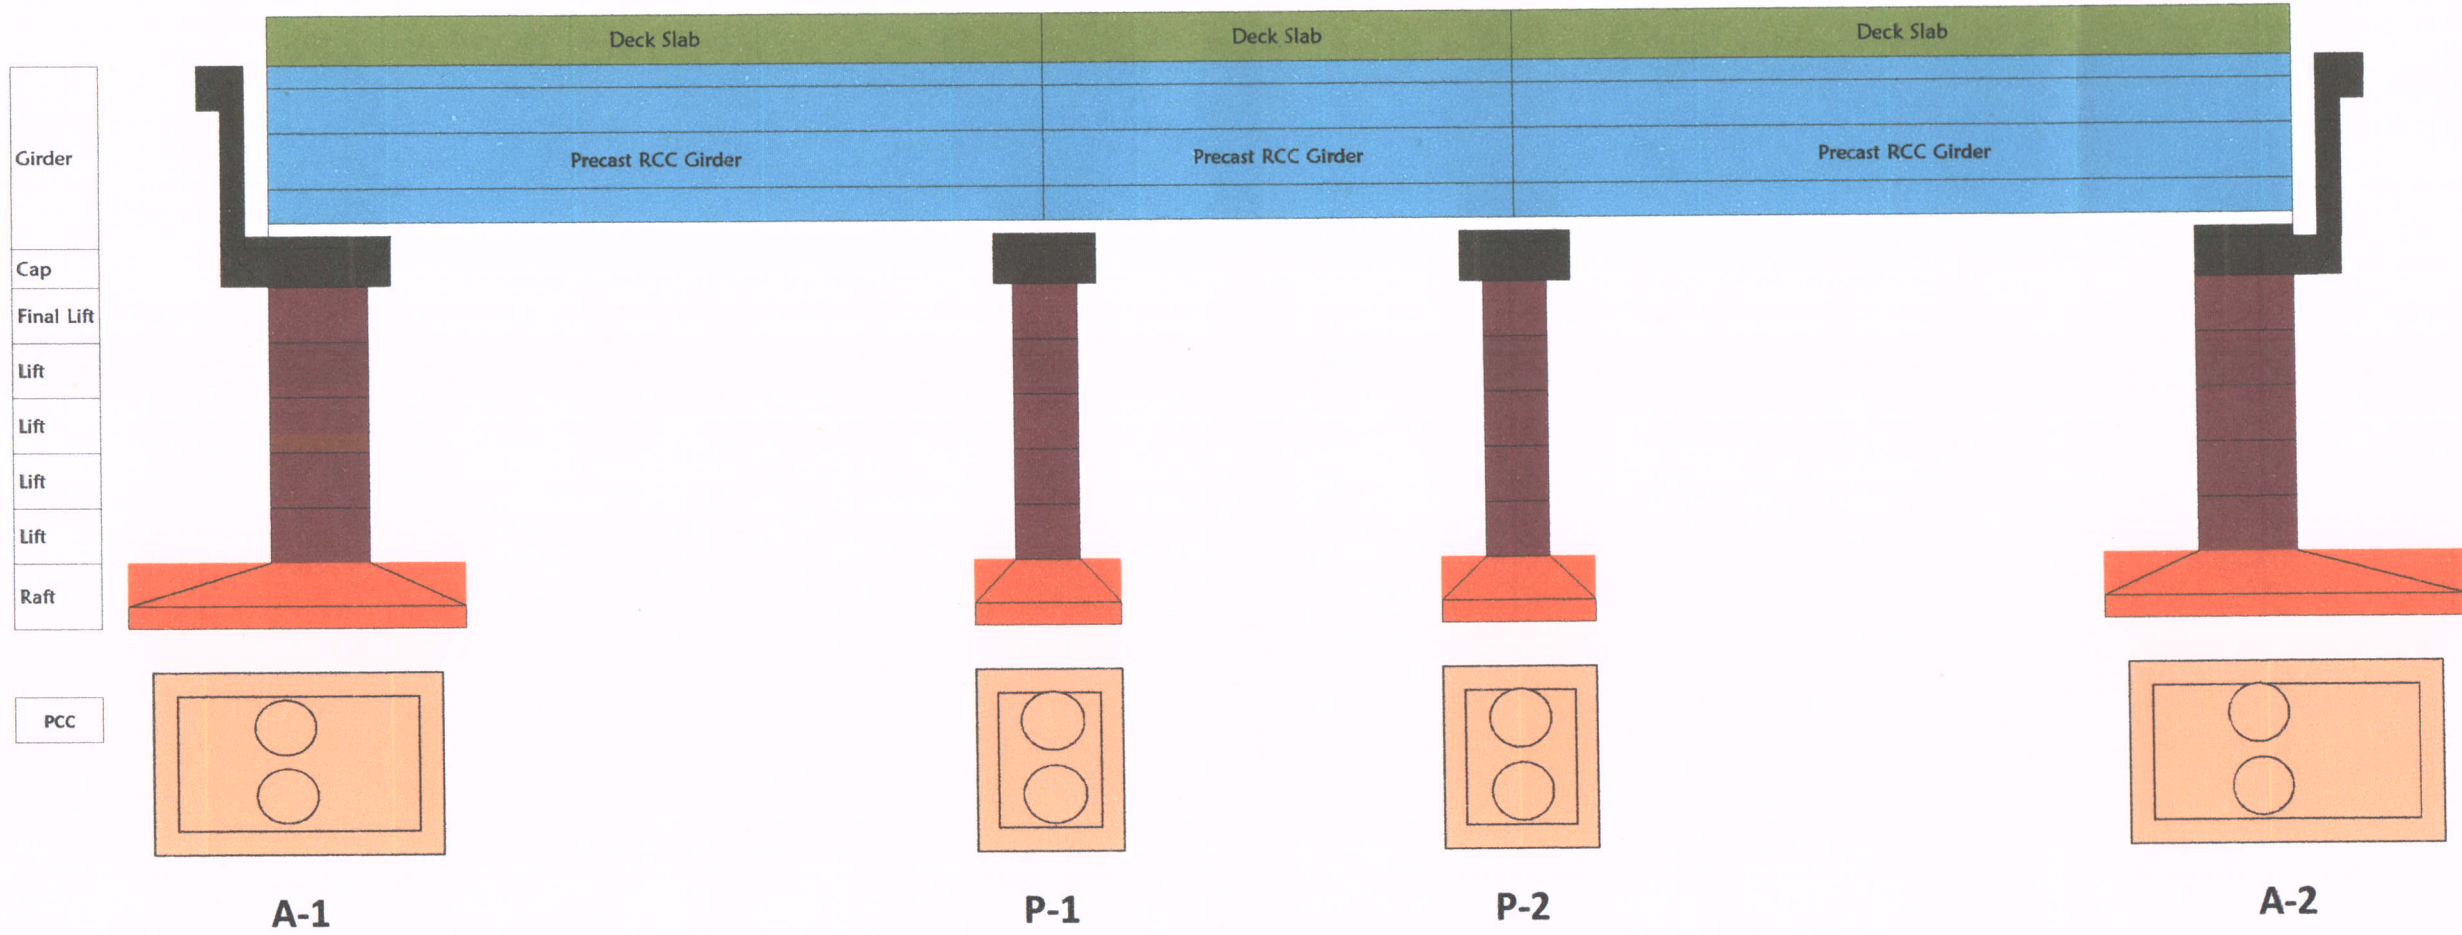


FLYOVER (50+095)LHS

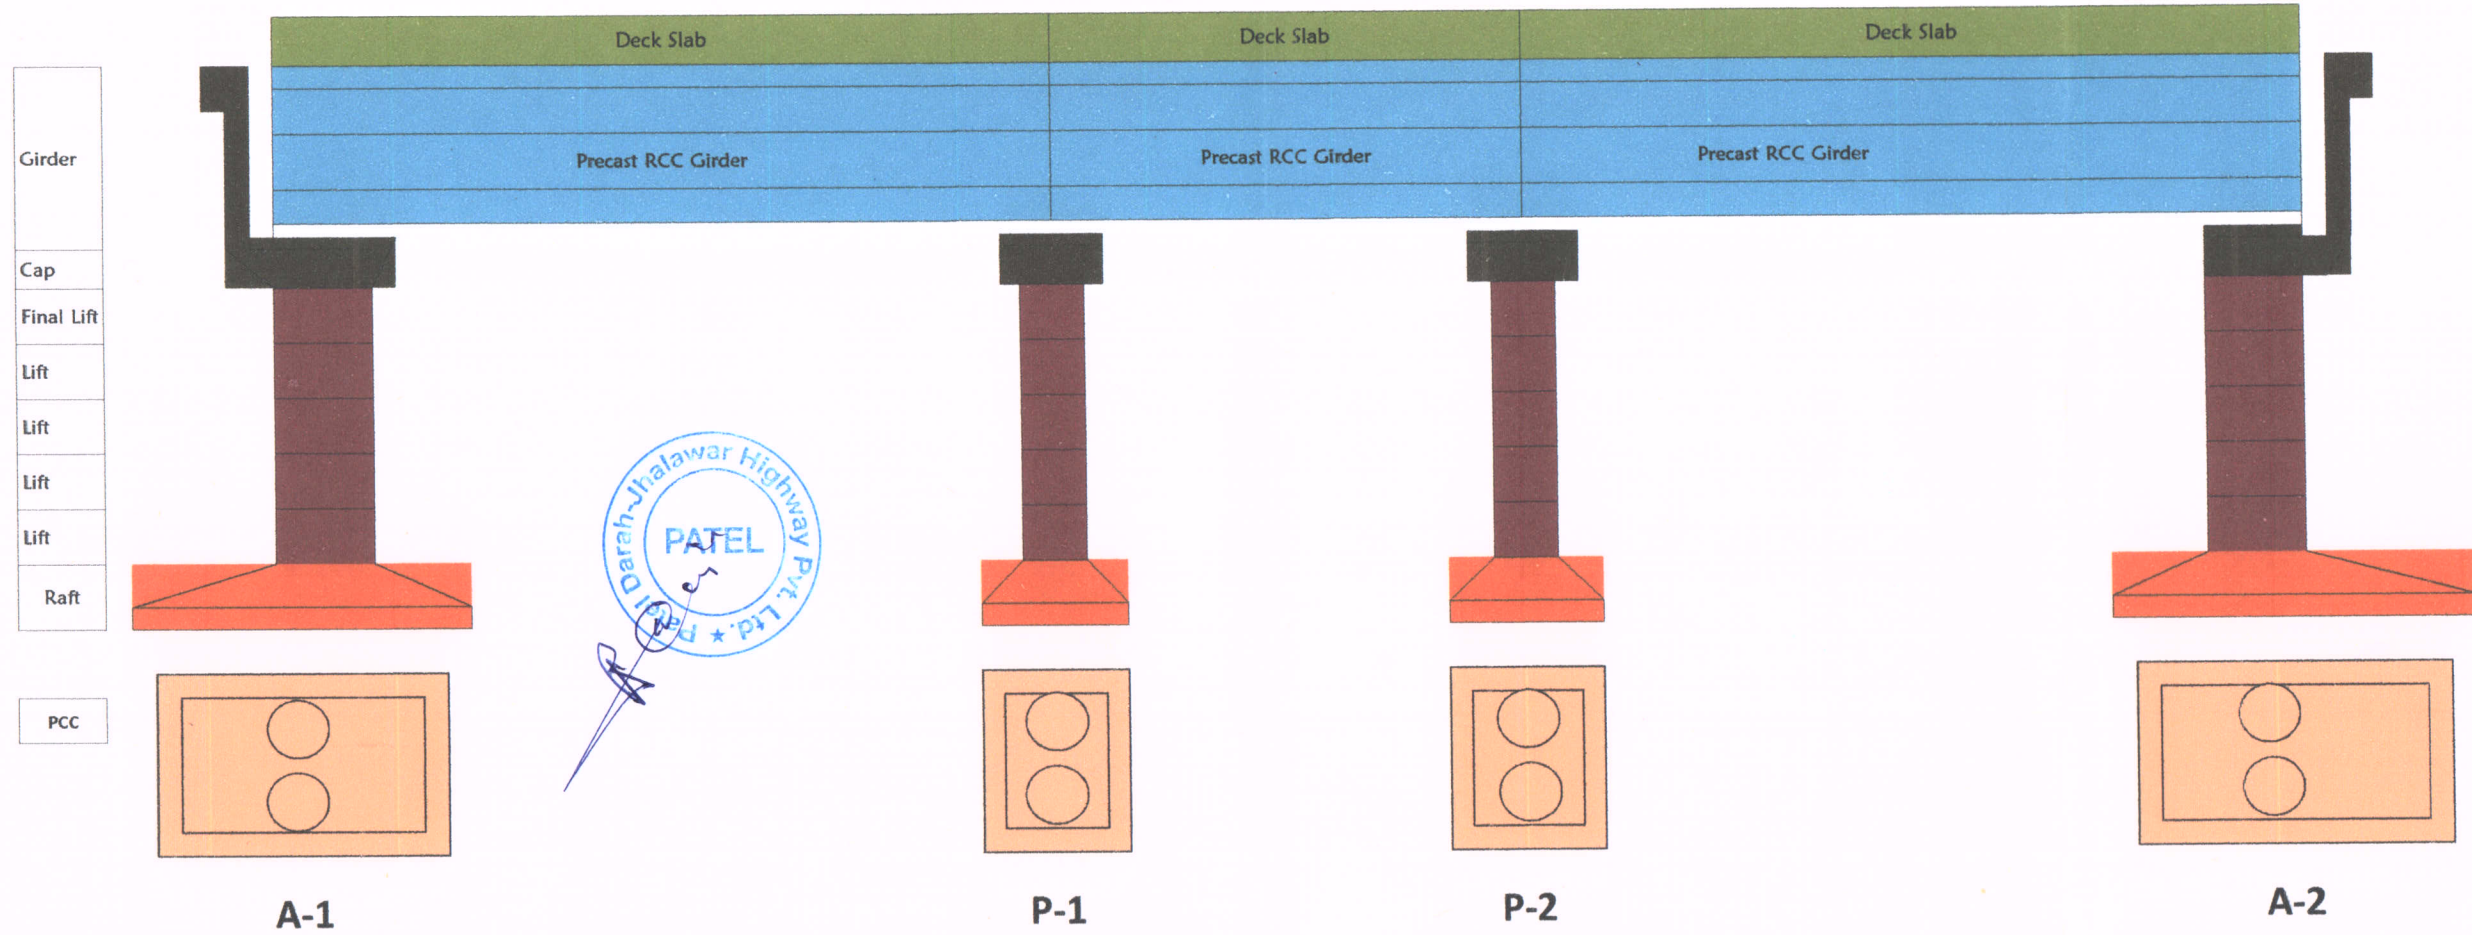

FLYOVER (58+128)RHS

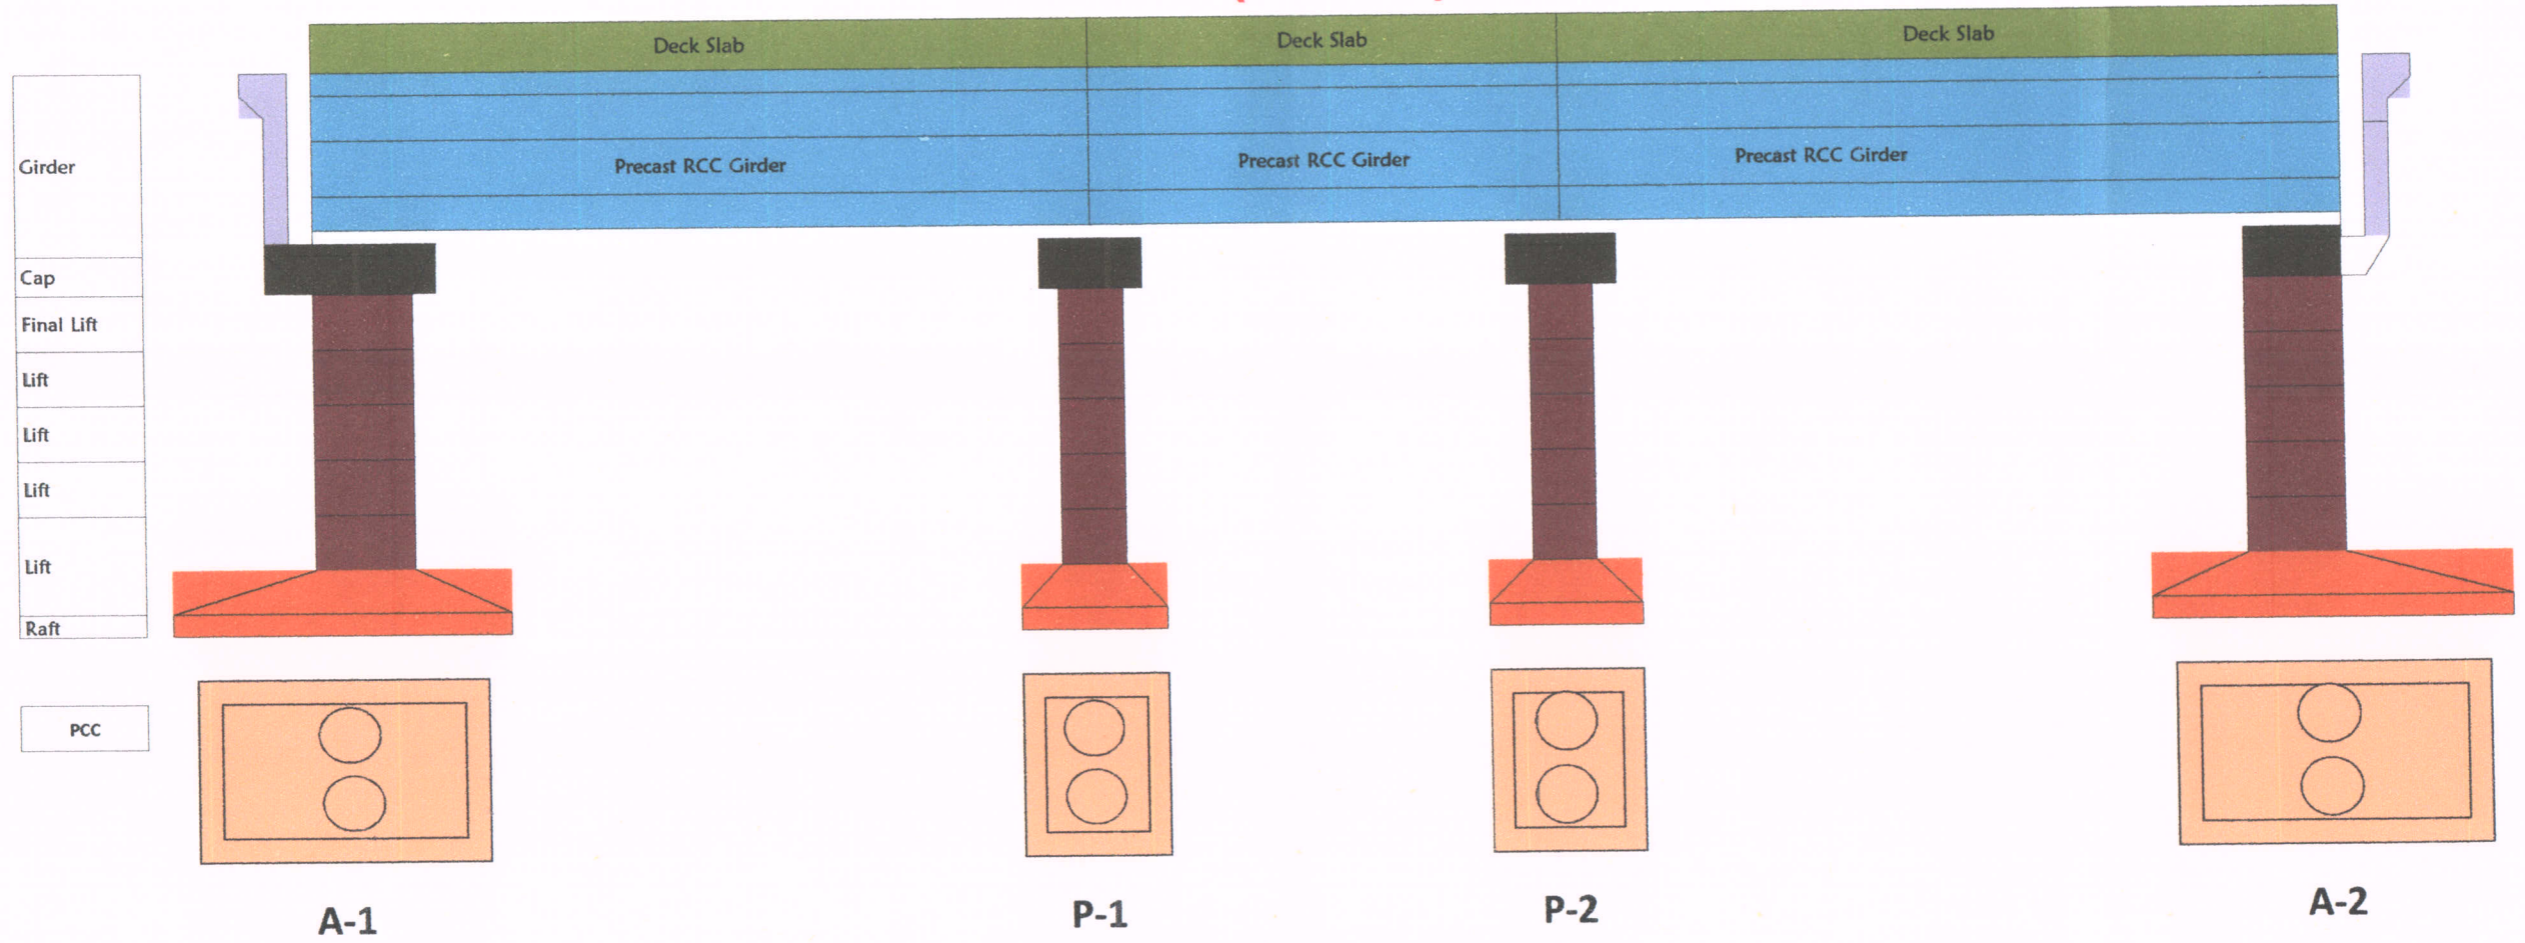


FLYOVER (58+128)LHS

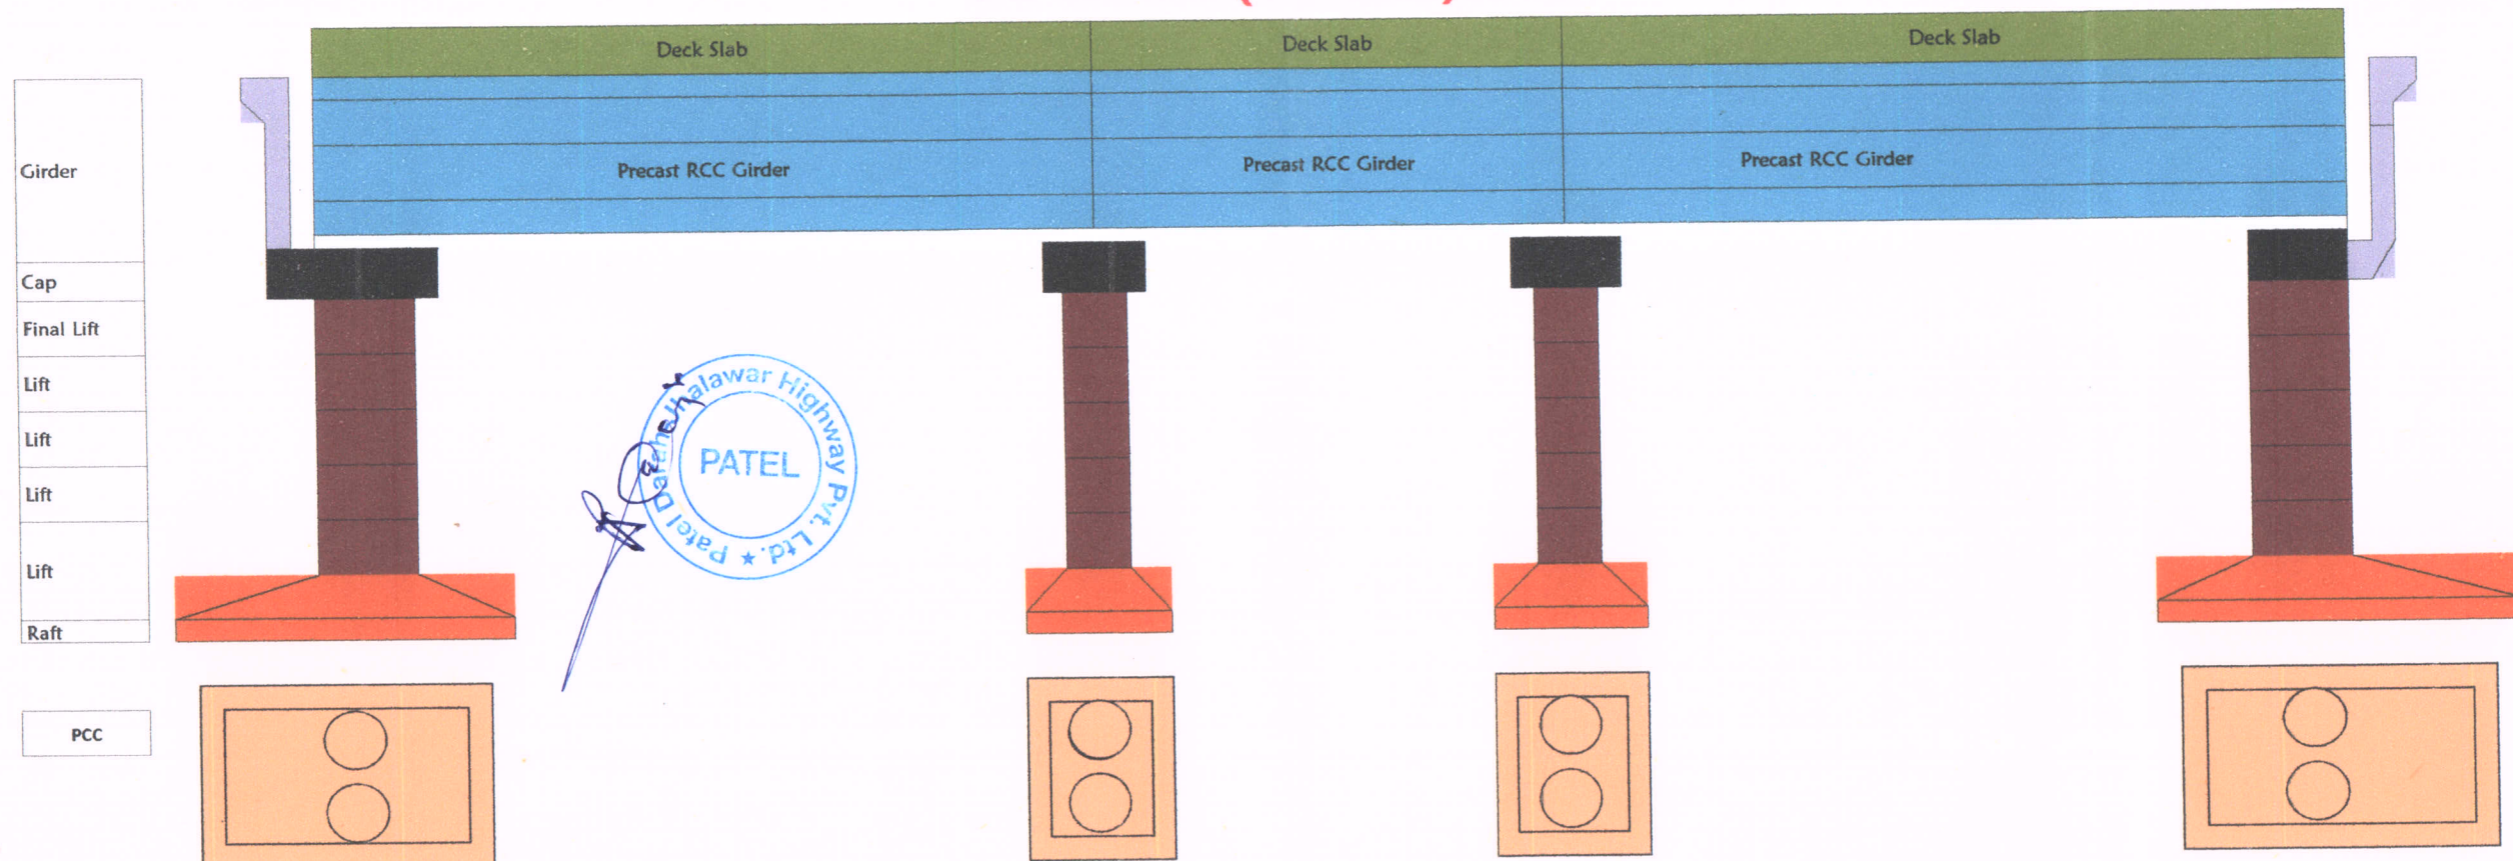


Patel Design & Engineering Pvt. Ltd.

MAJOR BRIDGE AT 36+070 (AHU RIVER) LHS

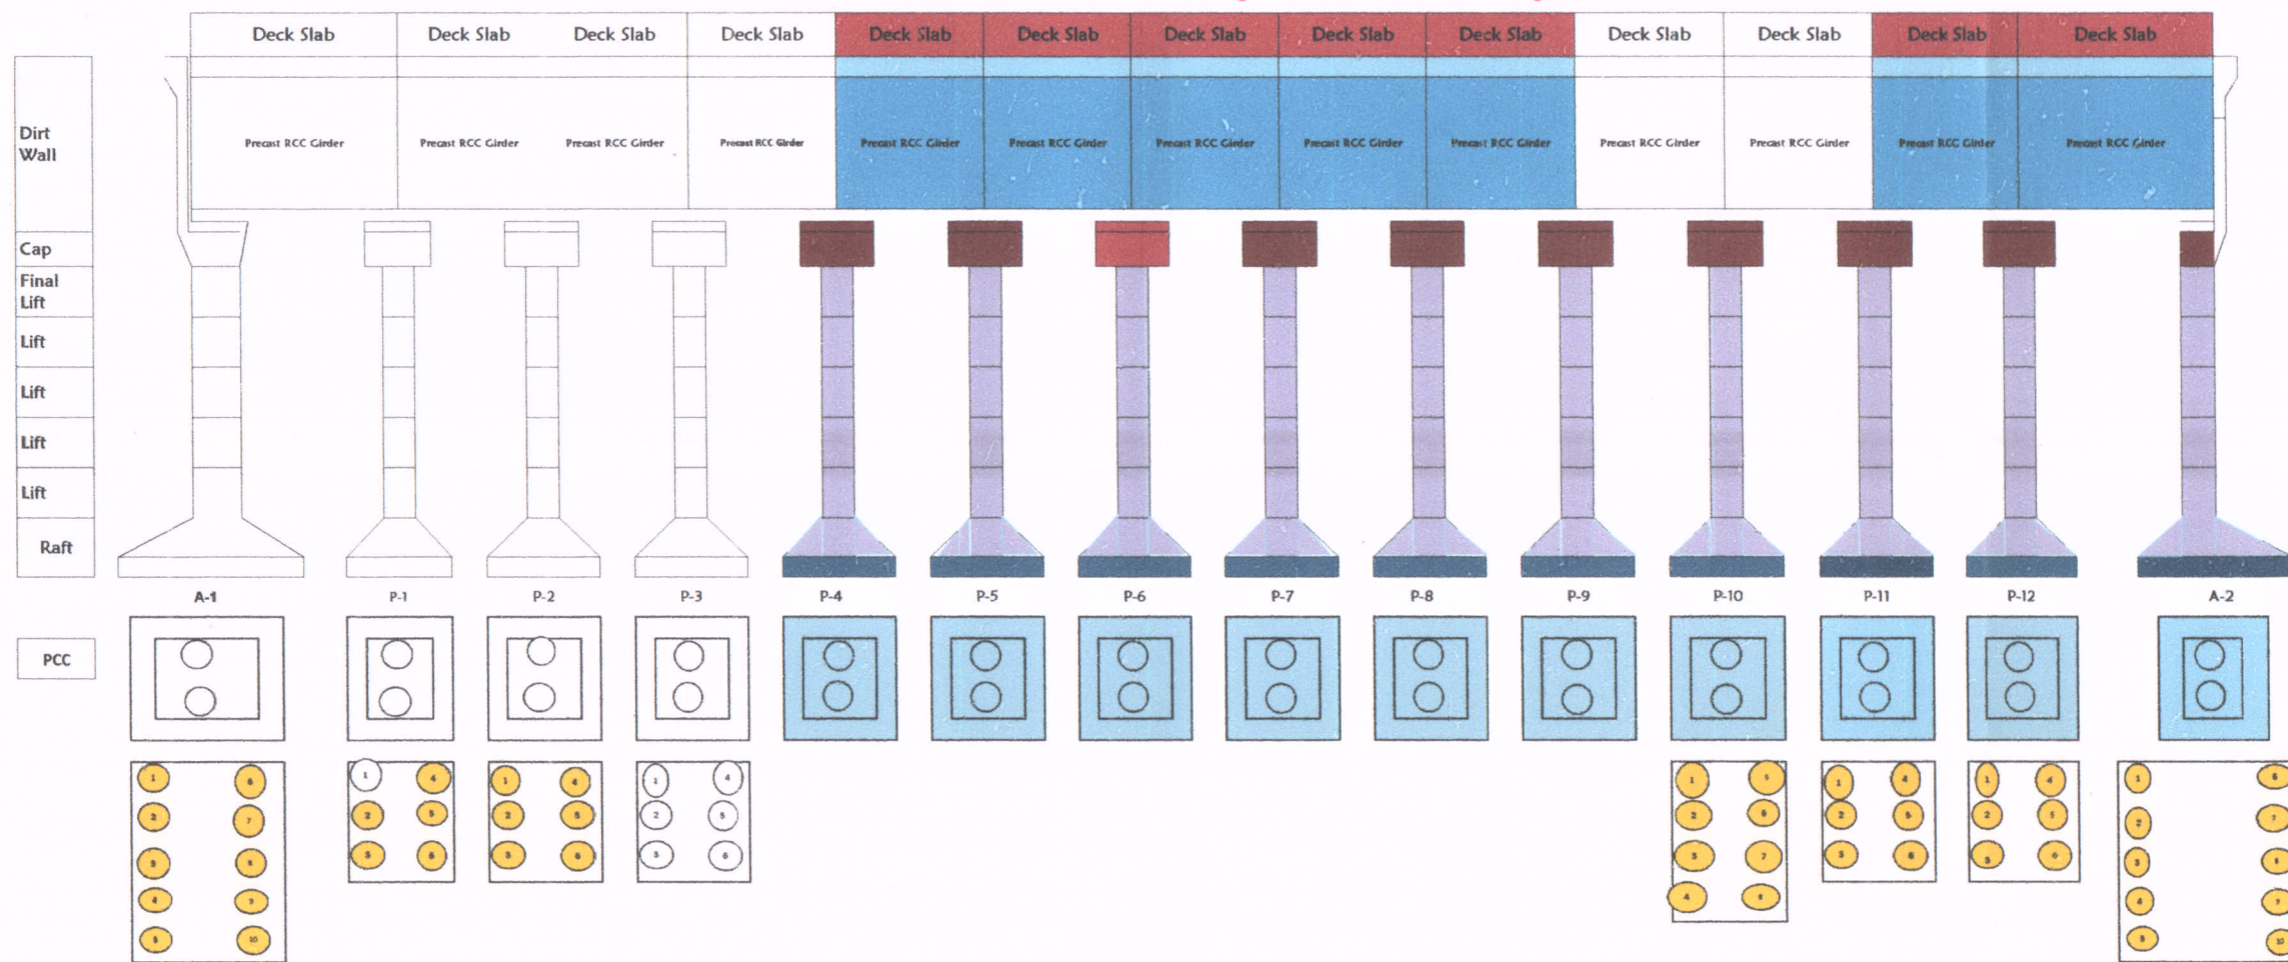


MAJOR BRIDGE AT 36+070 (AHU RIVER) RHS

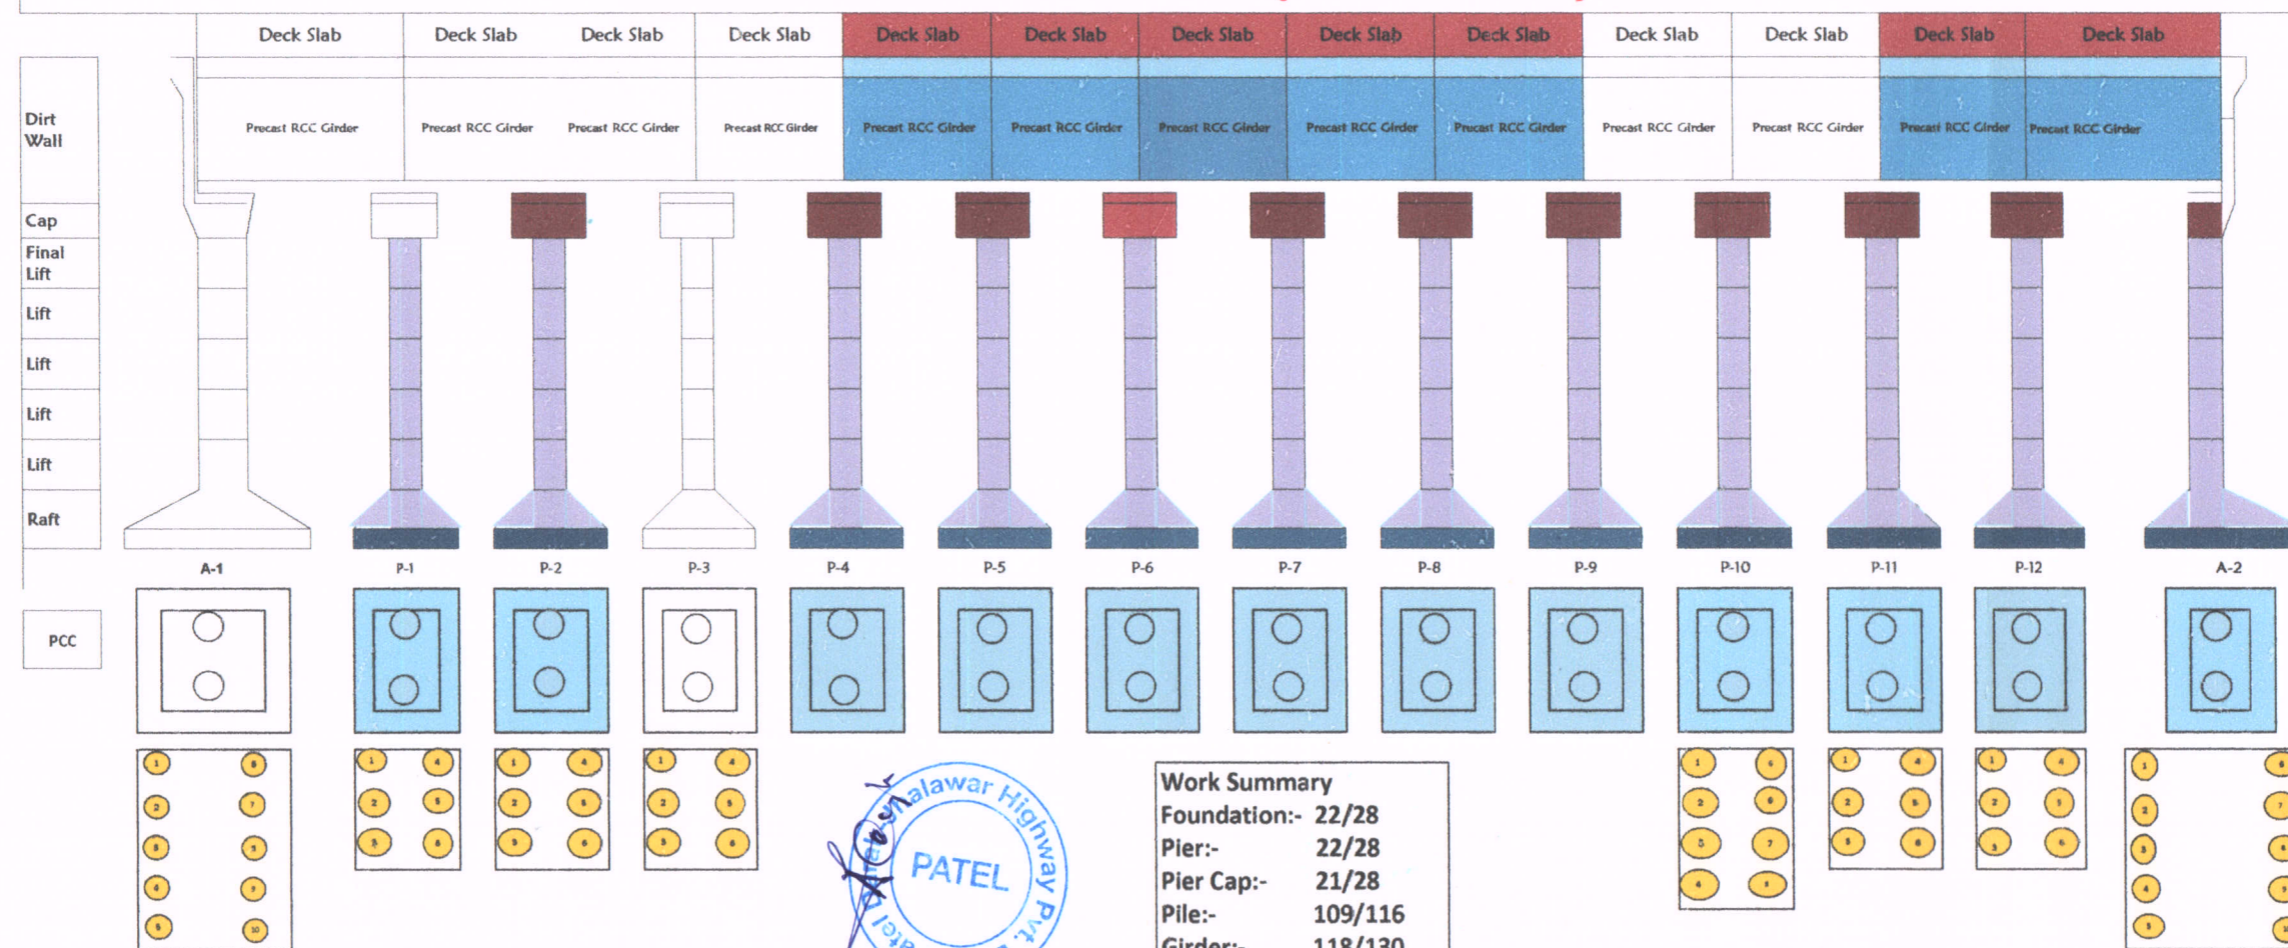

Work Summary	
Foundation:-	22/28
Pier:-	22/28
Pier Cap:-	21/28
Pile:-	109/116
Girder:-	118/130
Slab:-	14/26

MAJOR BRIDGE AT 57+127

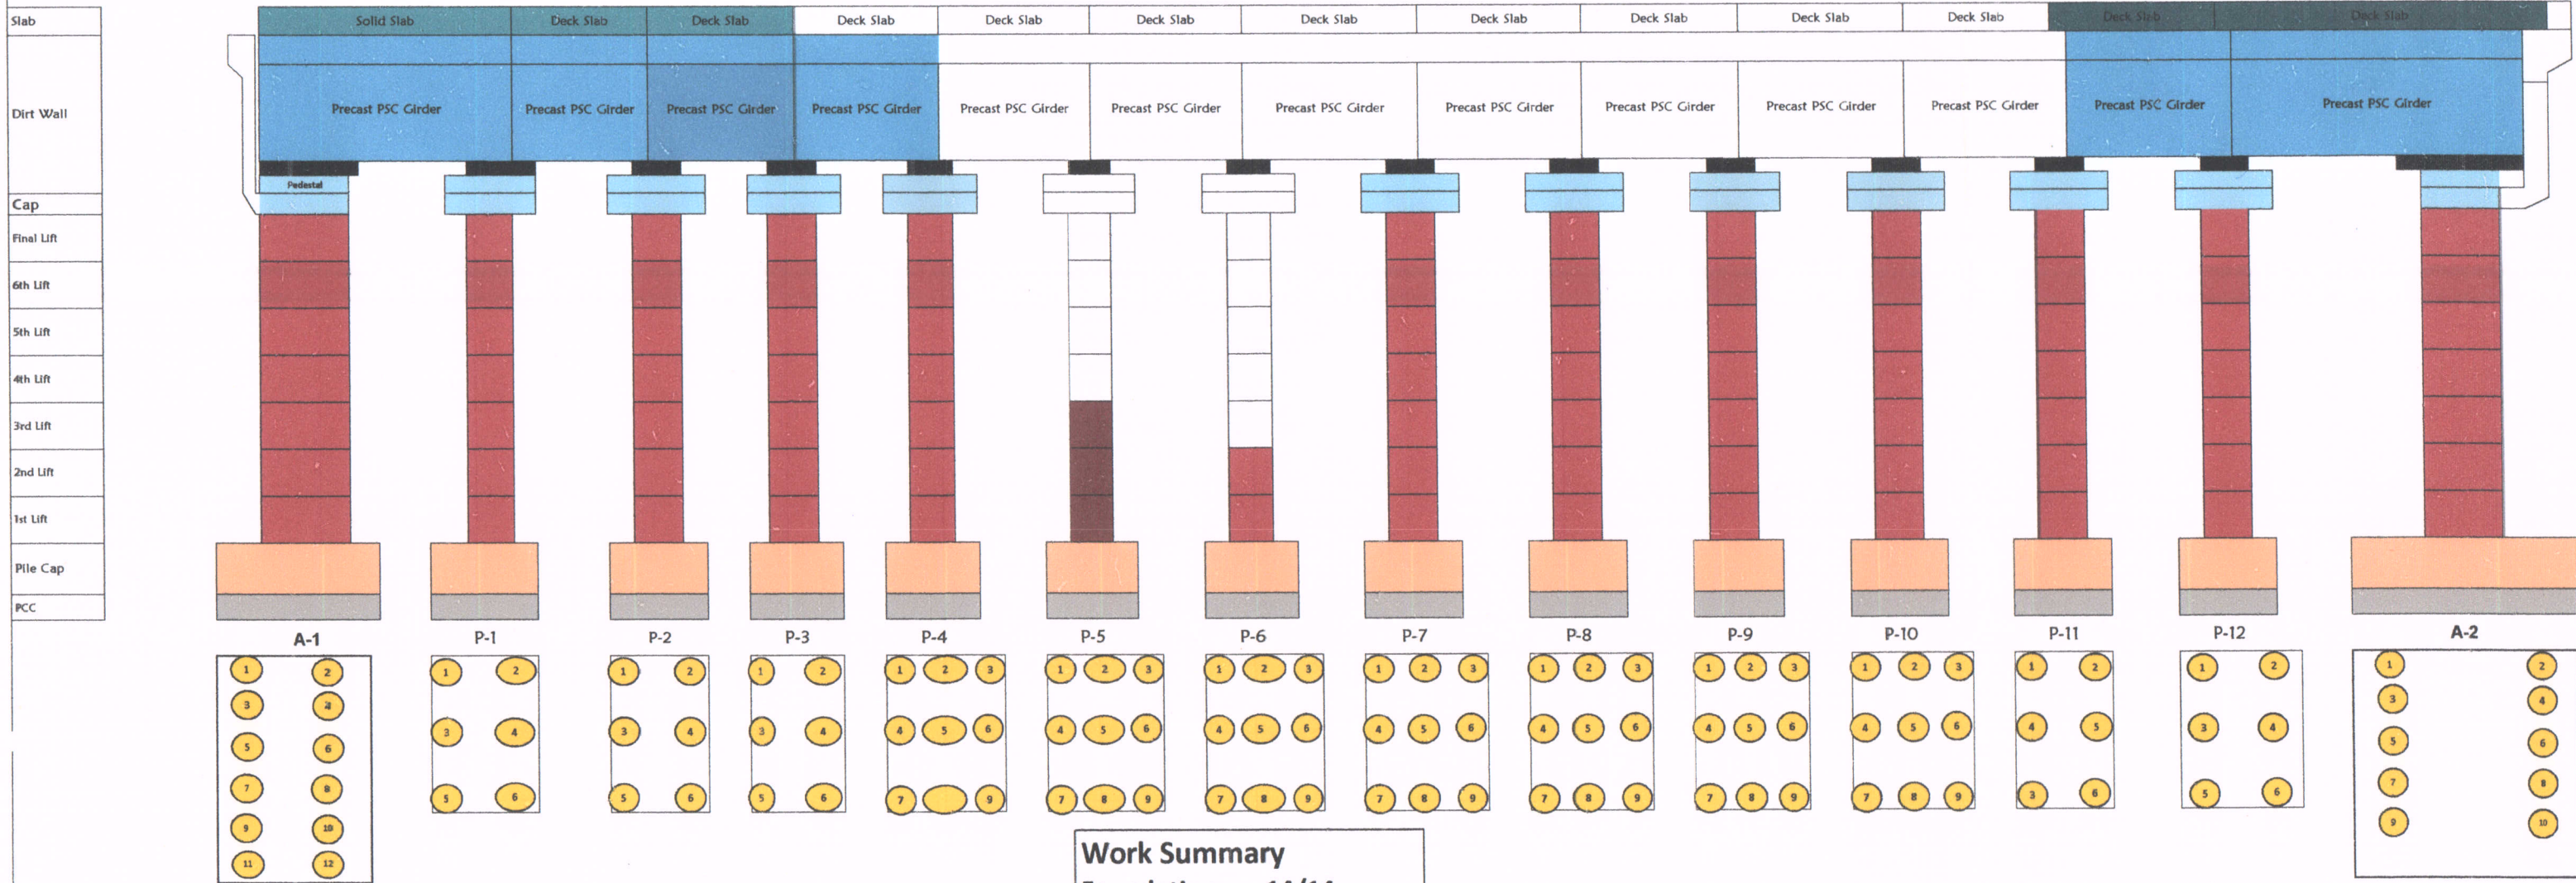

Work Summary	
Foundation:-	14/14
Pile:-	115/115
Pile Cap:-	14/14
Pier:-	12/14
Pier Cap:-	12/14
Girer Casting:-	65/65

(Handwritten signature)

PATEL
Patel Darah-Jhalawar Highway Pvt. Ltd.

Patel Daraj-Jhalawar Highway Private Limited

Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II


RUB CH. 33+585 (RHS).




RUB CH. 33+585



RUB CH. 33+585 (LHS).

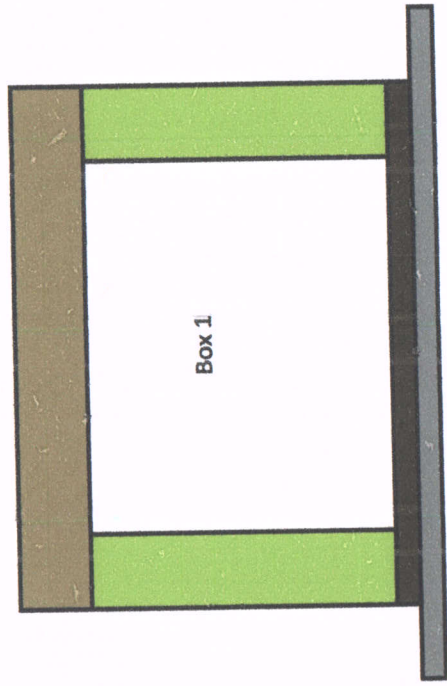


RUB CH. 33+585




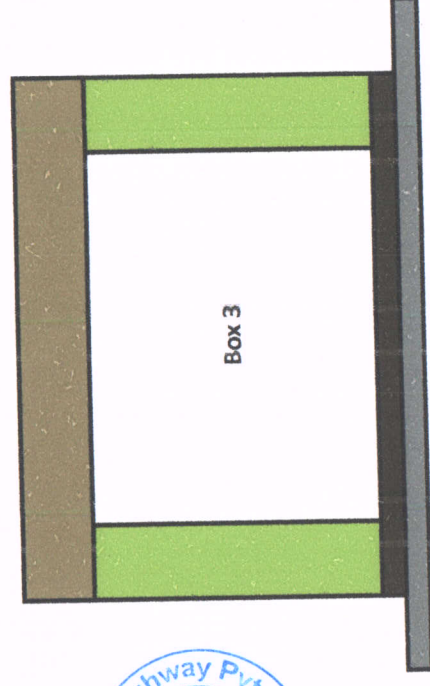


Patel Daraj-Jhalawar Highway Private Limited

Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Daraj-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

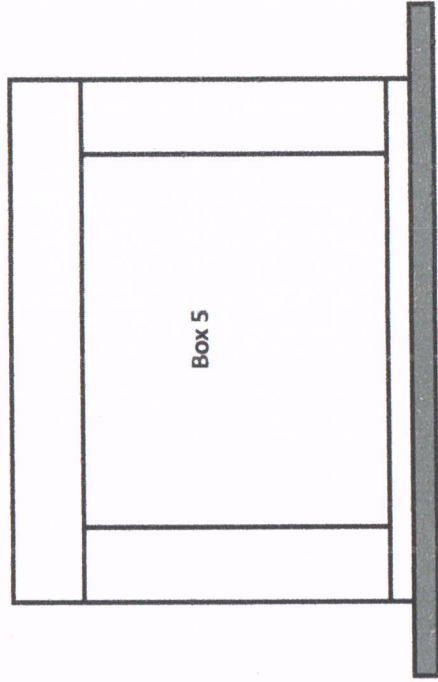


Signature

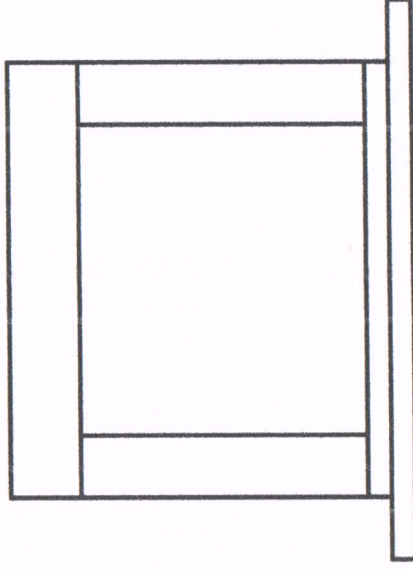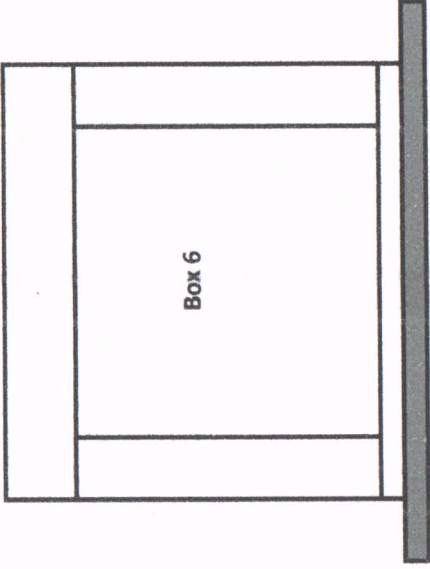




Patel Daraj-Jhalawar Highway Private Limited

Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) - Package II



ROB at 44+158

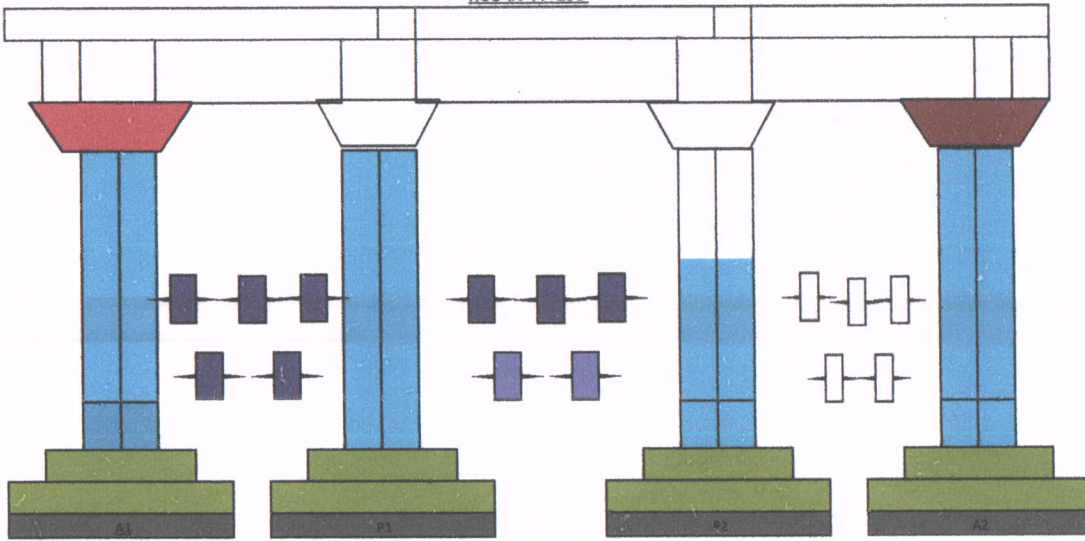


LHS

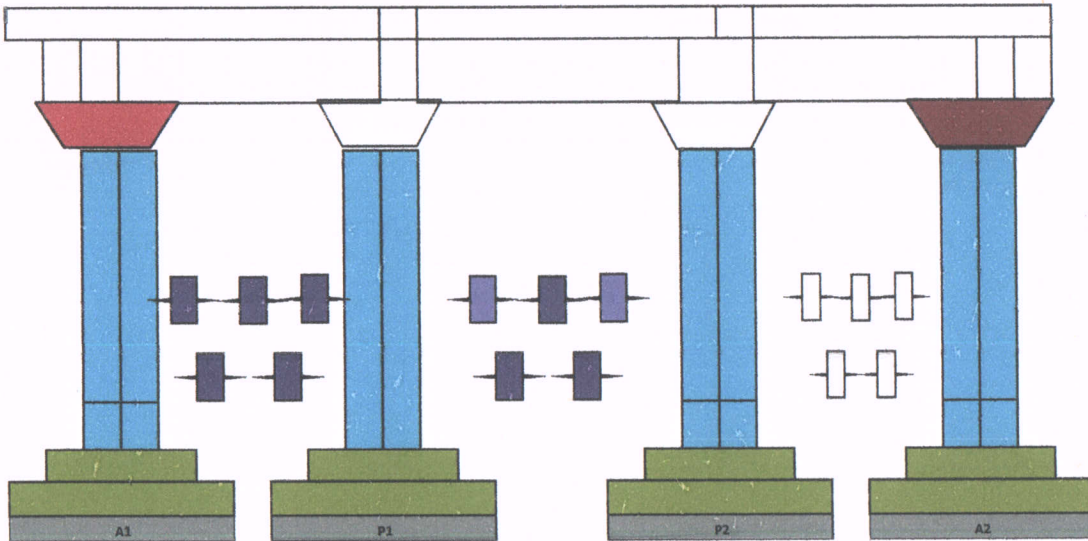

RHS




Work Summary	
Foundation:-	8/8
Pier:-	7/8
Pier Cap:-	4/8
Pile:-	32/32
Slab:-	0/6




[Handwritten signature]

Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II



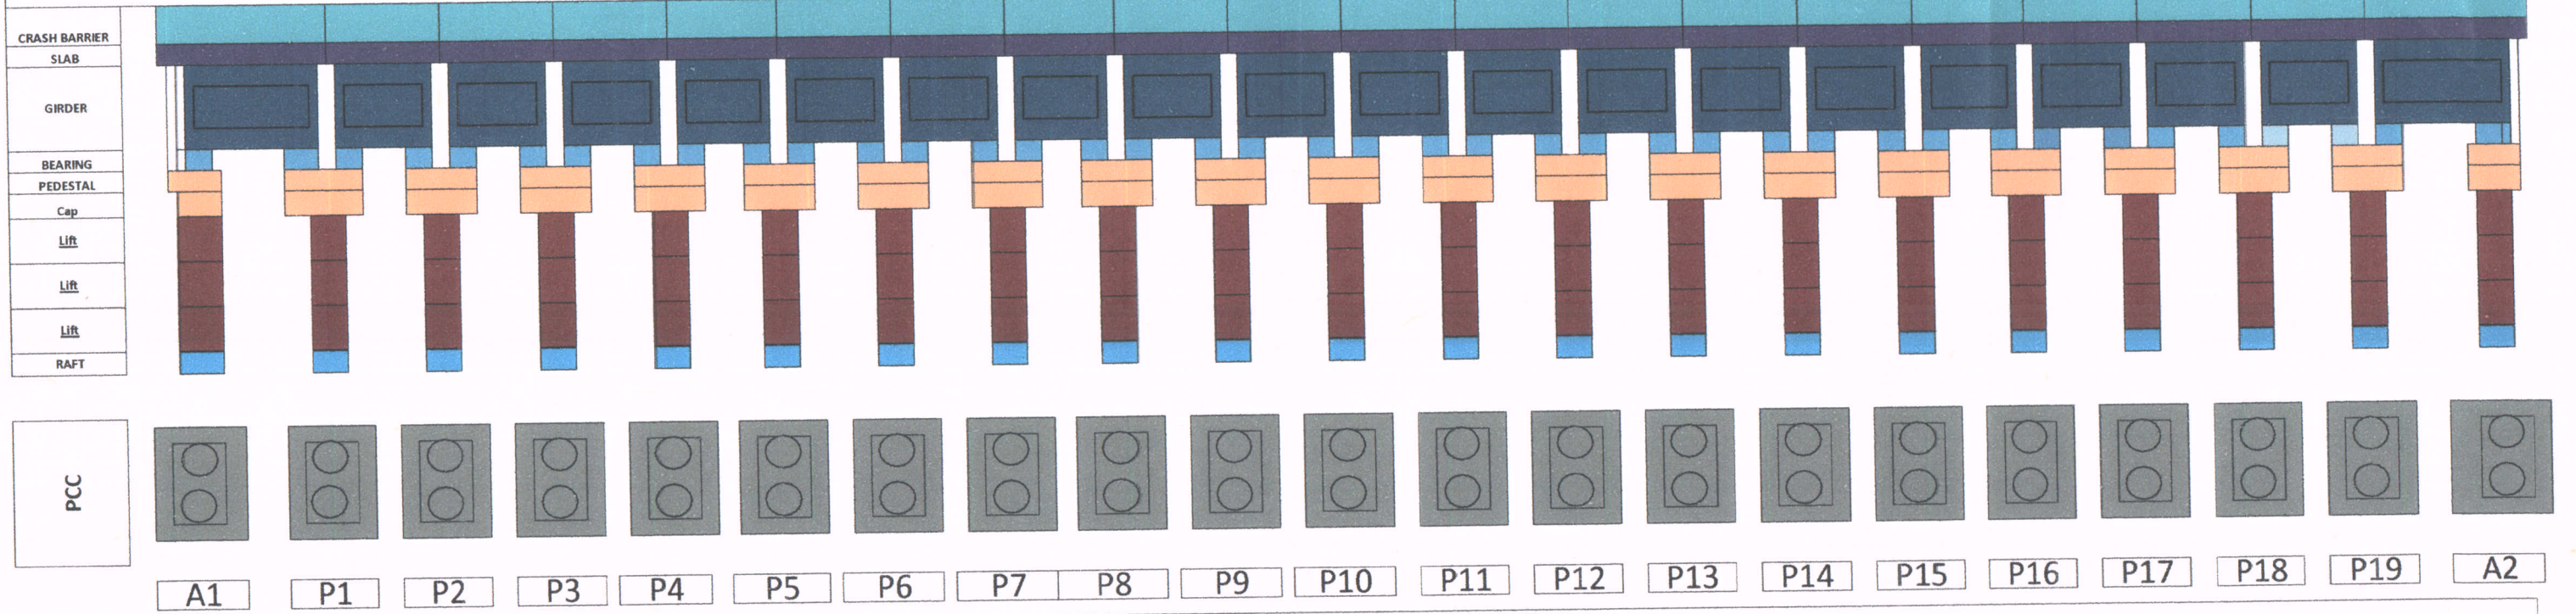

FLY OVER + MAJOR BRIDGE(ELEVATED STRUCTURE- 47+450 TO 48+150)LHS

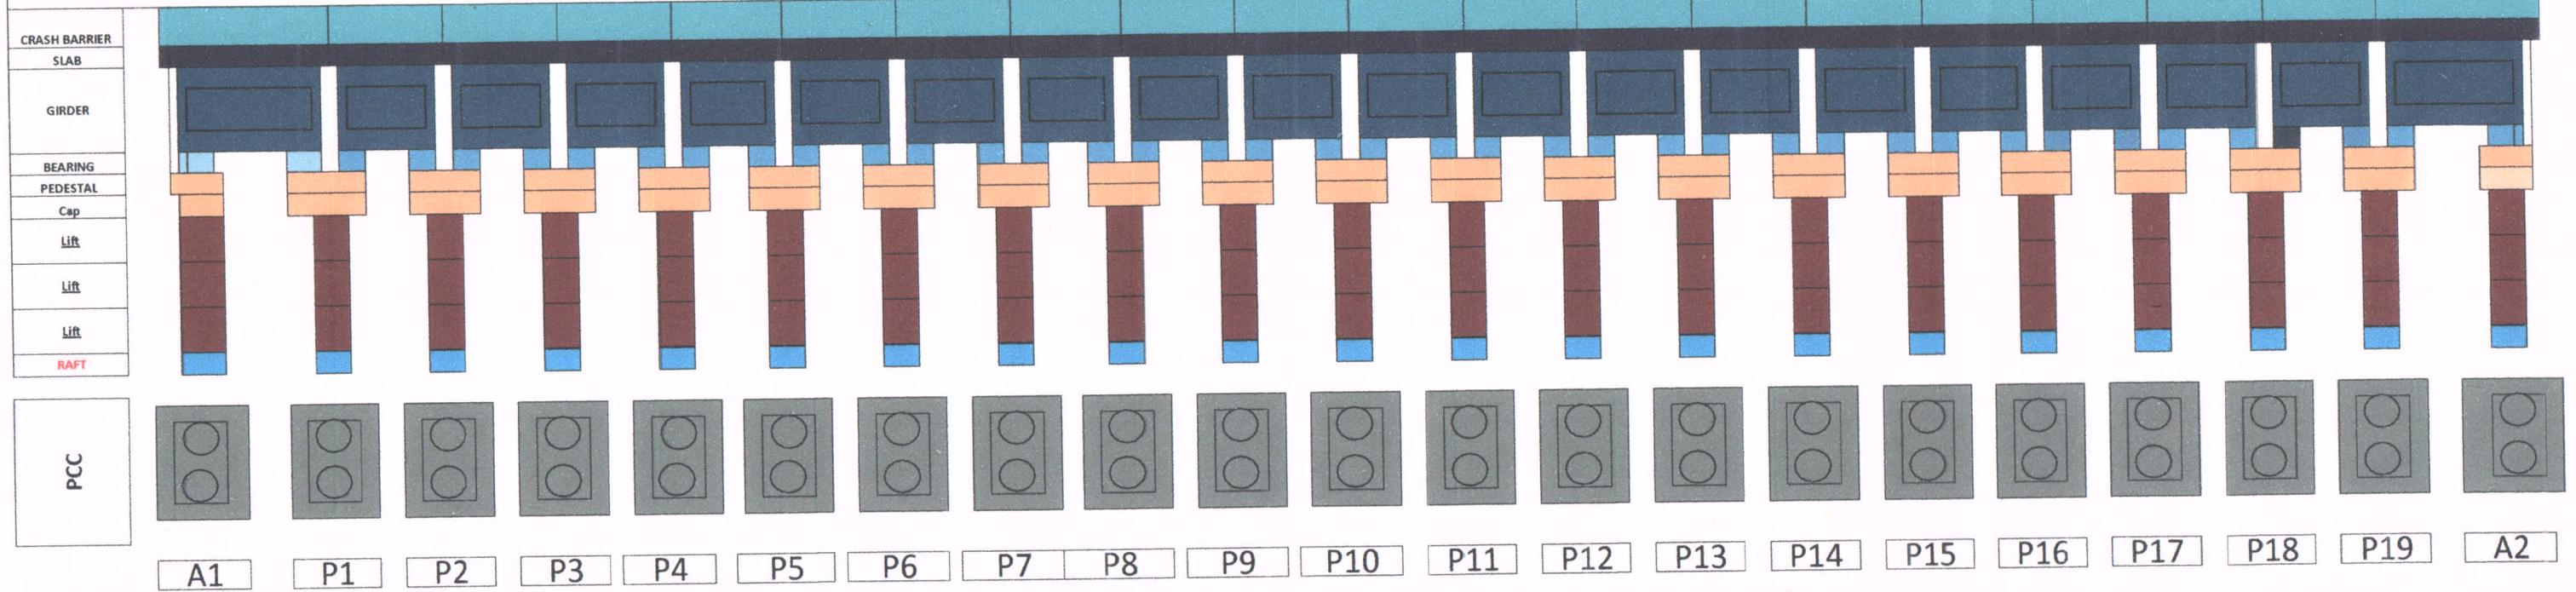







FLY OVER + MAJOR BRIDGE(ELEVATED STRUCTURE- 47+450 TO 48+150) RHS



Work Summary
 Foundation:- 42/42
 Pier:- 42/42
 Pier Cap:- 42/42
 Girders:- 200/200
 Girder Launch:- 200/200

Sr. No.	Chainage No.		Lane	Obstruction Length (m)	Type of Hindrance	Photo	Remark's
	From	To					
1	10+890	11+000	RHS		Compansation problem		Dispute in DM court. PQC is completed but ROW affcted.
2	11+100	11+700	LHS		Boundry wall, House		Stay order by civil court. PQC is completed but shifting of Utility affected. To be taken up.
3	11+330	11+350	RHS		Mango Tree		Award approval pending from NHAI.
4	20+680	20+690	RHS	10	Fruit tree		Award approval pending
5	26+150	26+200	RHS	50	Mango & lemon Tree		Nandsingh S/o Madhavsingh Award under process between LAO & NHAI
6	32+500	36+000	BHS		DLC issue		Some Villagers are unsatisfied for fruit & non-fruit tree award done by NHAI.



Sr. No.	Chainage No.		Lane	Obstruction Length (m)	Type of Hindrance	Photo	Remark's
	From	To					
7	34+610	34+630	BHS	20	Fruit Trees		Award approval pending
8	34+870	34+890	BHS	20	Fruit Trees		Award approval pending
9	35+290	35+300	BHS	10	Fruit tree		Award approval pending
10	35+460	35+470	BHS	10	Fruit & Non Fruit Trees		Award approval pending
11	35+580	35+590	BHS	10	Fruit Trees		Award approval pending
12	35+900	35+940	BHS	40	Land		Stay order by civil court (Ahu river bridge approach)
	Total			170			

