


सड़क परिवहन और राजमार्ग मंत्रालय
MINISTRY OF ROAD TRANSPORT & HIGHWAYS
भारत सरकार Government of India

National Highways Authority of India
(Ministry of Road Transport & Highways)

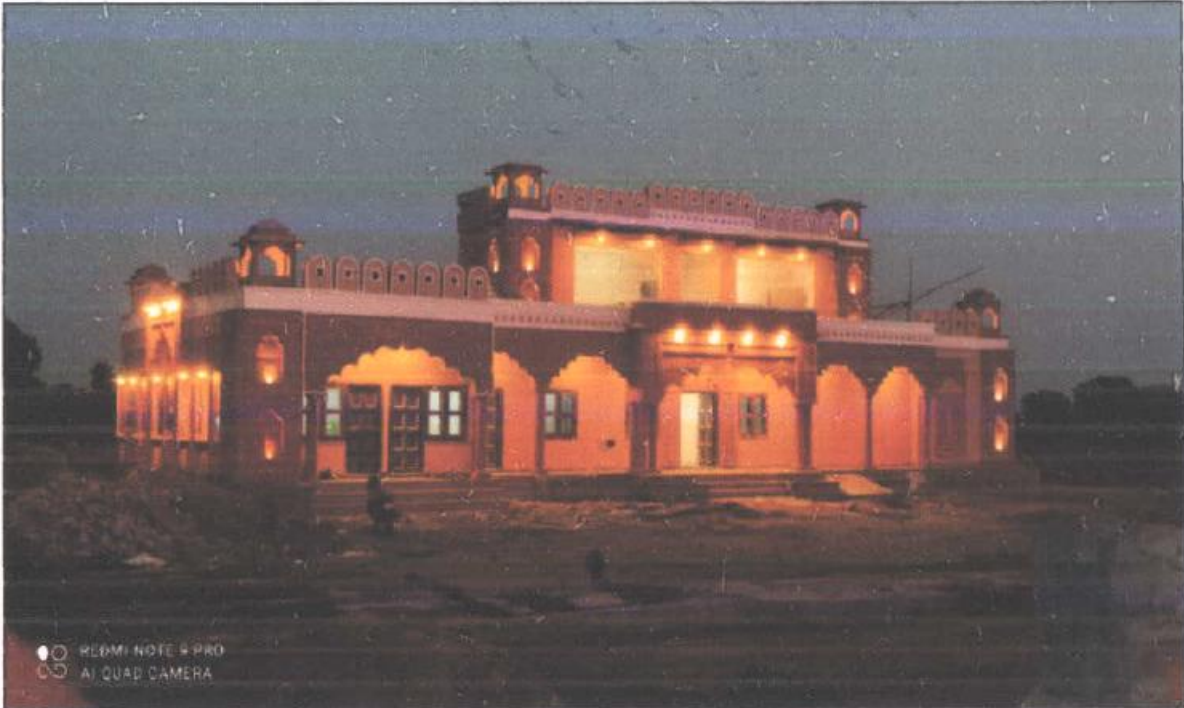

PATEL DARAH-JHALAWAR HIGHWAY PRIVATE LIMITED

CONSTRUCTION OF 4-LANE ROAD ON NH-12 (NEW NH-52) FROM Km. 299.000 TO Km. 346.540 (DESIGN CHAINAGE 9.860 TO 58.740) (DARAH – JHALAWAR – TEENDHAR) IN THE STATE OF RAJASTHAN UNDER NHDP PHASE-III ON HYBRID ANNUITY PROJECT.

INDEPENDENT ENGINEER

LEA ASSOCIATES SOUTH ASIA PVT. LTD

MONTHLY PROGRESS REPORT

For The Month of March - 2022

INDEX

S.No	Description of Item	Page No
1	Executive Summary	4
1.1	Project Synopsis	5-6
1.2	Map of Project	7
1.3	Key Plan of Project	8
2	Project Summary	9
2.1	Project Overview	10
2.1.1	Structures Detail	10
2.1.2	Project Milestones	11
3	Project Progress	12-14
4	Utility Shifting Progress	15-16
5	Tree Cutting Status	17
6	Status of Condition Precedent	18
7	Status of Railway Approval	19
8	Issues of Concern	20-21
9	LAB MPR	22-27
10	Status of Mix Design & Source Approval	28-37
11	Status of Submitted Drawings	37-45
11.1	RE Wall Drawings Status	45-48

Amstos

11.2	Bearing Drawings Status	48-49
11.3	Plan & Profile and Miscellaneous Drawings	50-53
12	Mobilization of Manpower	54-55
13	Mobilization of Resources	56
14	Site Progress Photographs	57-69
15	S-Curve	70
16	Highway Stripchart	71-74
17	Structures Pictorial	75-113
18	Hindrance Details	114

Handwritten signature

1. Executive Summary

The old National Highway 12 runs through two big states Rajasthan and Madhya Pradesh. The total length of the old NH- 12 was 897/00 Km. The length of Old NH 12 was 408/700 Km in the state of Rajasthan. Recently MORTH has amended the number and length of the National highways. The old NH 12 in the state of Rajasthan has become the part of the New National highway 52. The New NH 52 starting from its junction with NH-7 near Sangrur in the state of Punjab connecting Narwana, Hisar in the state of Haryana, Fatehpur, Jaipur, Tonk, Kota, Aklera in the state of Rajasthan, Rajgarh, Biora, Dewas, Indore, Sendhwa in the state of Madhya Pradesh, Dhule, Aurangabad, bed, Osmanabad, Solapur in the state of Maharashtra, Bijapur, Hubli and terminating at its junction with NH-66 near Ankola in the state of Karnataka.

The Project stretch Darah-Teendhar is connected to Jaipur at one end and it is connected to Bhopal at the other end. The project highway is very important highway as it connects the Capital of Rajasthan states and National capital of country through Jaipur- Delhi Highway.

The project highway is very important highway as it connects to two state Rajasthan and Madhya Pradesh. The Darah-Jhalawar-Teendhar section of National Highway has moderate traffic density. In addition to this there are few sections where alignment needs geometric improvements to maintain riding quality of highway and safe movement of vehicles. Apart from this the present alignment of NH is passing through various congested towns and villages. All of the above factors are demanding the existing 2-lane highway to be developed as 4-lane divided carriageway with bypass provisions in congested towns/ villages.

The Project Highway traverses through two districts viz. Kota and Jhalawar in Rajasthan State. The project study corridor starts at the end of ROB approach near to Darah at km 289+500 and passes through five major towns Darah, Sarvada, Dabadeh, Suket and Jhalawar, and it ends at Teendhar, Existing km 346.540 Km. Existing road width is 2 lane standard. The Existing ROW varies from 15 m to 30 m. The entire project length is under the administrative control of PIU Kota.



Project Synopsis

ional Highways Authority of India plans to undertake the Construction of 4-lane Road on NH- (New NH-52) from Km 299.000 to 346.540 (Design Chainage From 9.860 to 58.740) (Darah-lawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity de (Length 48.880 Km.) – Package II.

National Highways Authority of India (NHAI) is undertaking the up-gradation of NH-12 from sting two lane road to four lane divided carriageway in state of Rajasthan.

project involves up gradation of 48.88 Km from two-lane to the four-lane divided carriageway. ncludes the construction of bridges, intersections, service roads, culverts and related astructure, and the installation of signaling systems and signboards. The project will be eloped under National Highways Development Project (NHDP) Phase-III on Hybrid Annuity de.


Existing and Proposed alignment

SR. NO.	Existing Chainage (Km)		Length	Design Chainage (Km)		Design Length (Km)	Name of Revenue Village
	To	From		To	From		
1	299.000	299.340	0.340	9.860	10.200	0.340	KAMALPURA
2	299.340	299.740	0.400	10.200	10.600	0.400	KAMALPURA
3	299.740	300.140	0.400	10.600	11.000	0.400	KAMALPURA
4	300.140	300.440	0.300	11.000	11.300	0.300	KAMALPURA
5	300.440	300.778	0.338	11.300	11.638	0.338	KOOKARA KHURD
6	300.778	301.255	0.477	11.638	12.115	0.477	MANPURA
7	Dabadeh&Sahrawada Bypass			12.115	12.300	0.185	MANPURA
8				12.300	13.028	0.728	ZALIMPURA
9				13.028	14.200	1.172	SAHRAWADA
10				14.200	15.661	1.461	TELYA KHERI
11				15.661	17.242	1.581	ASKALI
12				17.242	19.273	2.031	HIRIYA KHERI
13				19.273	19.788	0.515	KHEEMACH
14	308.203	308.515	0.312	19.788	20.100	0.312	KHEEMACH
15	308.515	308.715	0.200	20.100	20.300	0.200	KHEEMACH
16	308.715	308.915	0.200	20.300	20.500	0.200	ATRALIYA
17	308.915	309.079	0.164	20.500	20.664	0.164	ATRALIYA
18	Atraliya Realignment			20.664	21.682	1.018	ATRALIYA
19	310.007	310.125		21.682	21.800	0.118	ATRALIYA
20	310.125	310.325		21.800	22.000	0.200	ATRALIYA
21	310.325	310.444		22.000	22.119	0.119	GORDHANPURA
22	Atraliya Realignment			22.119	22.464	0.345	GORDHANPURA & PAMA KHERI
23	310.789	311.125		22.464	22.800	0.336	PAMA KHERI


SR. NO.	Existing Chainage (Km)		Length	Design Chainage (Km)		Design Length (Km)	Name of Revenue Village
24	311.125	311.494		22.800	23.169	0.369	PAMA KHERI
25	311.494	311.625		23.169	23.300	0.131	PAMA KHERI
26	311.625	311.776		23.300	23.451	0.151	PAMA KHERI
27	311.776	312.025		23.451	23.700	0.249	PAMA KHERI
28	312.025	312.725		23.700	24.400	0.700	DEENGASI
29	312.725	312.925		24.400	24.600	0.200	DEENGASI
30	312.925	313.025		24.600	24.700	0.100	DEENGASI
31	313.025	313.125		24.700	24.800	0.100	DEENGASI
32	313.125	313.370		24.800	25.045	0.245	DEENGASI
33	313.370	313.535		25.045	25.210	0.165	DEENGASI
34				25.210	25.254	0.044	DEENGASI
35				25.254	26.124	0.870	UMMEDPURA
36				26.124	27.000	0.876	RAMPURIYA
37				27.000	27.358	0.358	SUKET
38				27.358	27.854	0.496	BEER MANDI
39				27.854	28.000	0.146	SUKET
40				28.000	29.571	1.571	ARANYA KHURD
41				29.571	31.212	1.641	SURERA
42				31.212	33.617	2.405	BANSYA HERI
43				33.617	35.565	1.948	ARANYA KALAN
44	Suket,			35.565	36.100	0.535	KALMANDI
45	Jhalawar&Jhalrapatan Bypass			36.100	38.000	1.900	HARISH PURA
46				38.000	38.537	0.537	RALAYTI
47				38.537	40.343	1.806	RALAYTA
48				40.343	41.784	1.441	JHALRAPATAN
49				41.784	44.224	2.440	MADHOPUR
50				44.224	49.800	5.576	HARIPURA
51				49.800	51.434	1.634	HARIPURA,
52				51.434	52.516	1.082	BANJARI &
53				52.516	54.200	1.684	BHANWARSA
54				54.200	54.565	0.365	BHANWARSA
55	342.895	343.673		54.565	55.343	0.778	BHANWARSA
56	343.673	347.127		55.343	58.740	3.397	BHANWARSA & ROOPAREL



1.2 Project Map

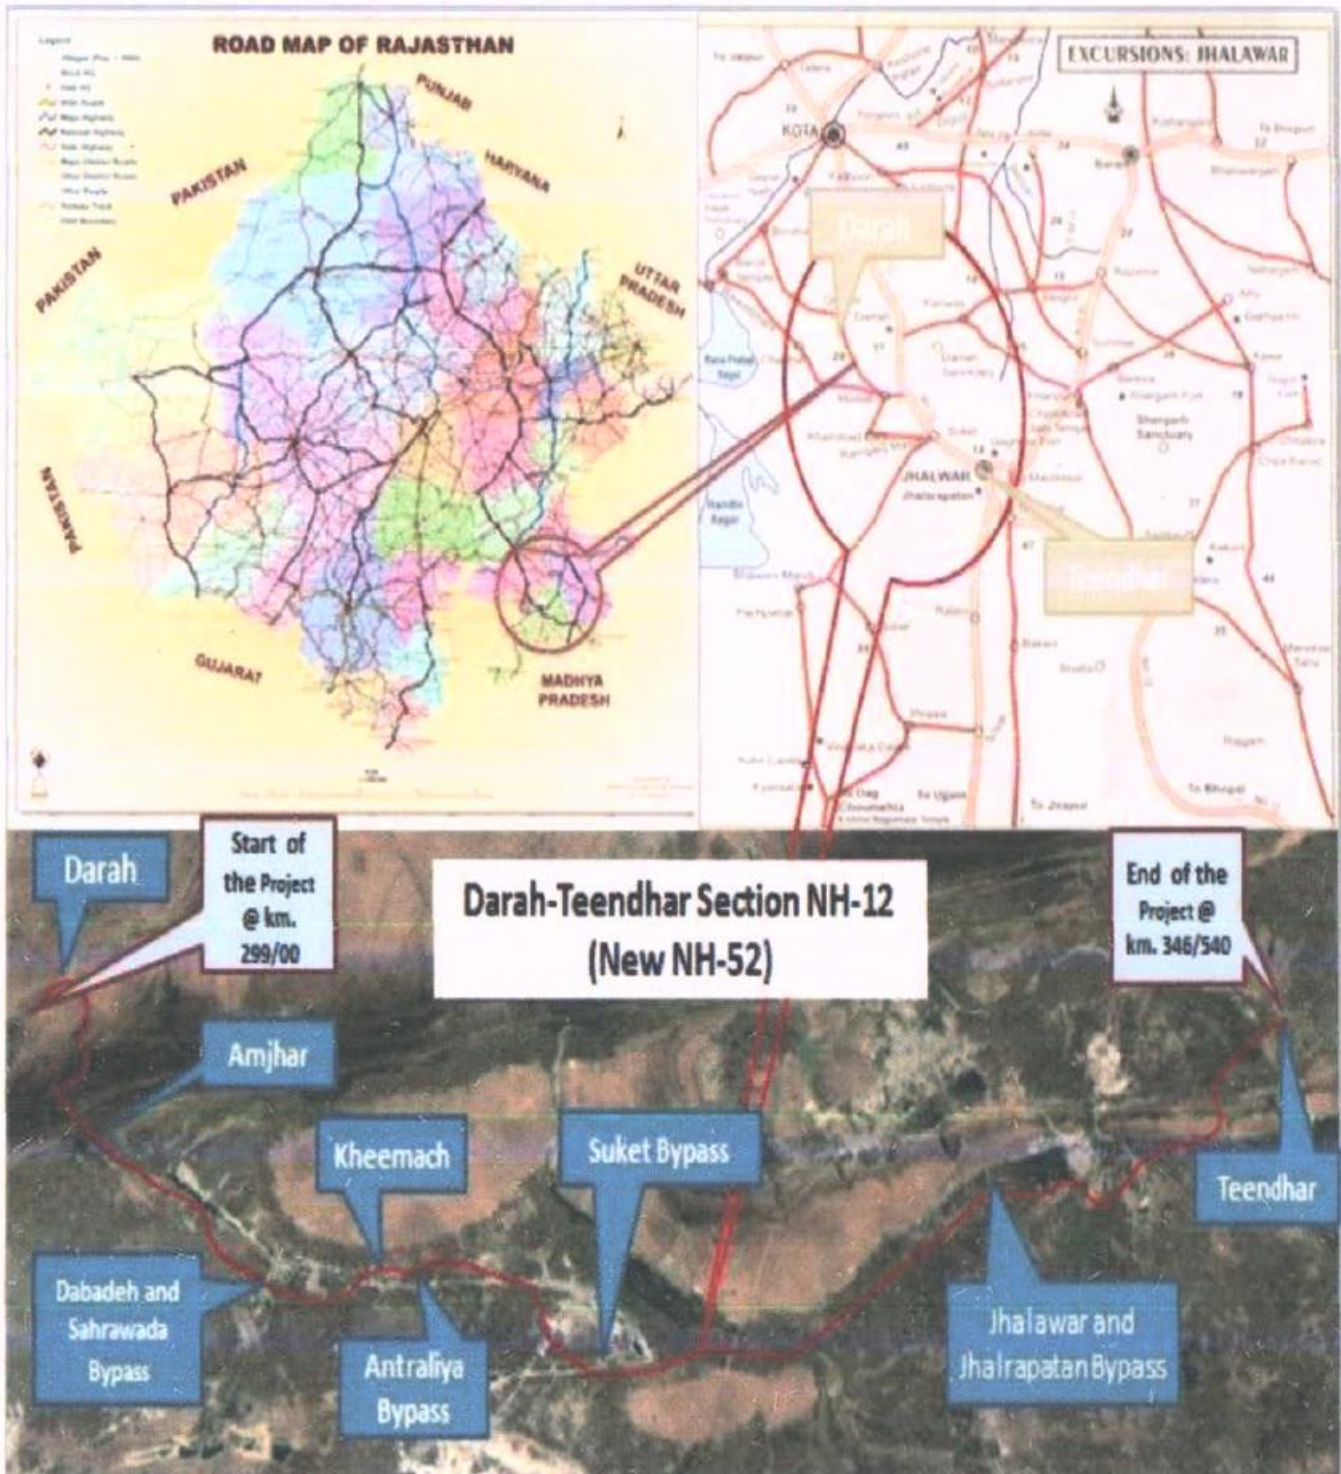

KEY PLAN OF THE PROJECT

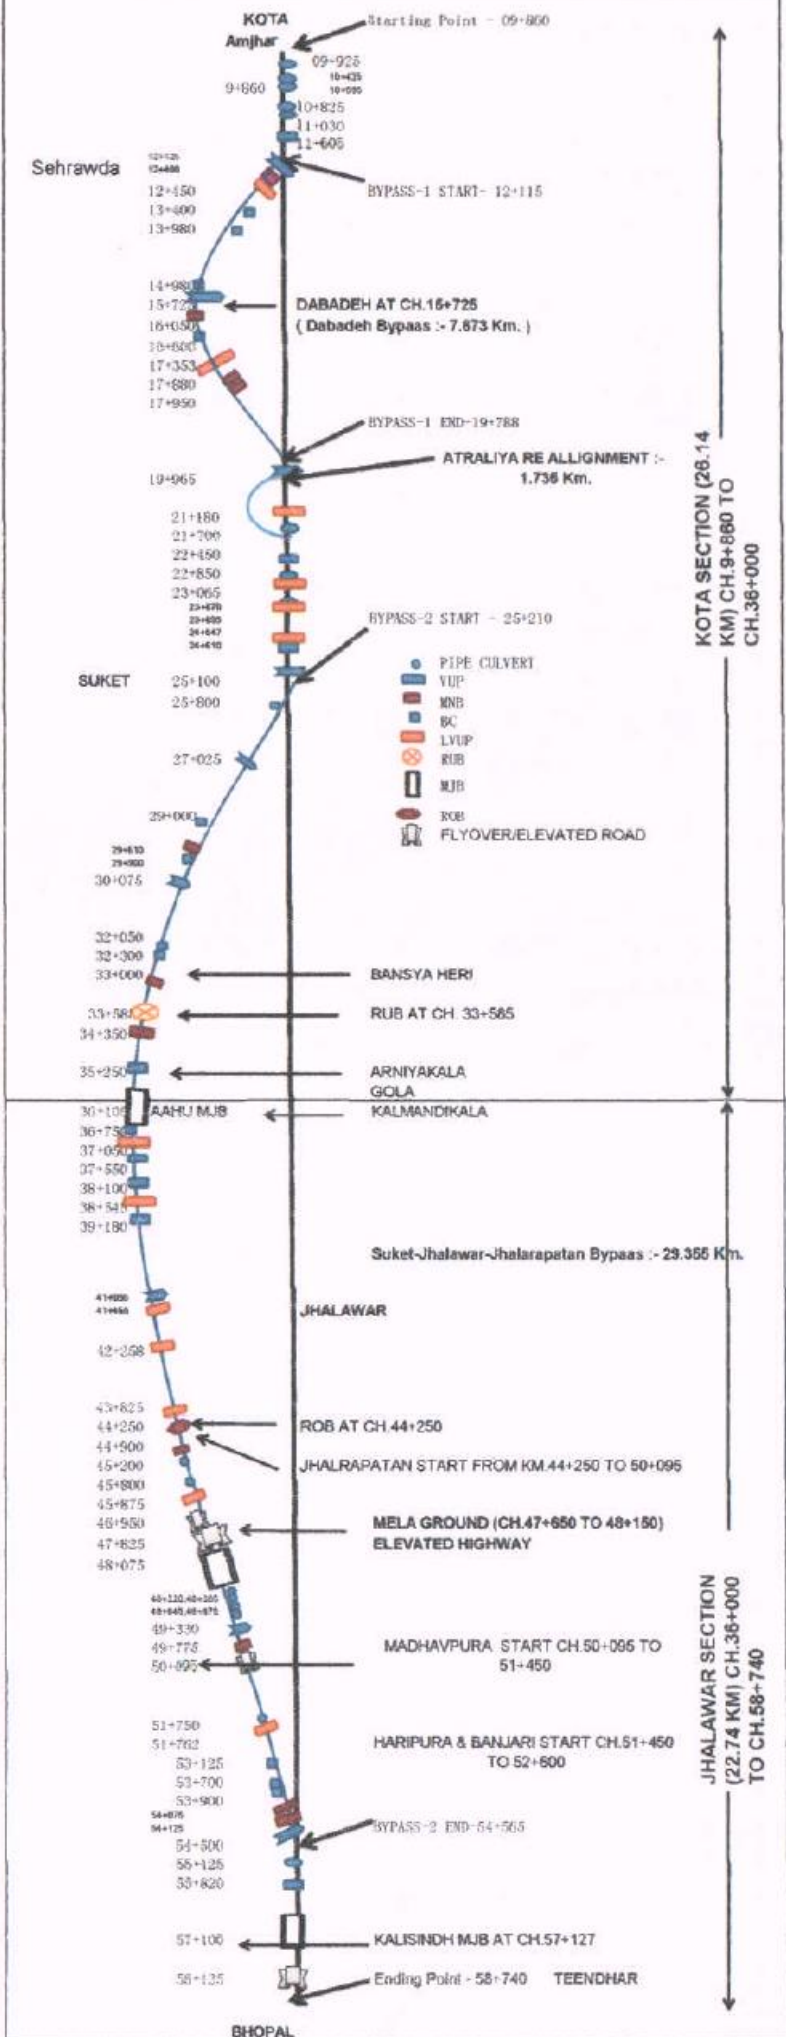

2. PROJECT SUMMARY

Project	Construction of 4-lane Road on NH-12 New NH-52 from Km 299.000 to 346.540 Design Chainage From 9.860 to 58.740 Darah-Jhalawar-TeendharSection in the State of Rajasthan under NHDP Phase-III Length 48.880 km Package II on Hybrid Annuity Mode.
Owner/Client	National Highways Authority of India
Concessionaire	Patel Darah - Jhalawar Highway Pvt. Ltd.
Independent Engineer	LEA ASSOCIATE SOUTH ASIA PVT. LTD
Project Length (In Km)	48.88 Km
Total Project Cost as per CA	1123.63 Cr.
Concession Period	15 Years
Construction Period	910 Days from the Appointed Date.
Contractual Completion Date	19 th November 2020.
Extended Completion Date	31.05.2022 (As per Settlement Agreement Dated 17.11.2021)
Date of Signing of Concession Agreement	16 th November 2017
Appointed Date	24 th May 2018 (Letter ref. No. NHAI /19030/Dara-Teen/Raj/2016/1/120723 dated 09 th July 2018.



2.1 Project Overview

2.1.1 Structures

S. No.	Feature	Description
1	Major Bridge	02 Nos. – (13 x 25mtr) & (13 x 31.6mtr_3-Lane)
2	Elevated Flyover cum MJB	01 Nos. – (20 x 25mtr)
3	Flyovers/ Interchange	03 Nos. (1 Nos. – 4x25mtr.) (2 Nos. – 3 x 24mtr.)
4	ROB/ RUB	1/1 = 2 No.
5	Minor bridges	As per CA -11 Nos. (01 No. deleted as per site condition)
6	Vehicular underpass	09 Nos. – (1x24mtr)
7	Light Vehicular Underpasses	13 Nos.
8	Culverts (HP/BC/PUP) as per CA & Additional	37 Nos. (16 Nos. Pipe & 21 Nos. Box)+Additional (31 Nos Pipe, 2 nos Box and 03 Nos PUP) Total- 47 Nos Pipe and 23 nos Box Culvert
9	RE Wall	14.454 Km
10	Toll Plaza	1 No (16 Lanes)
11	Truck Lay Bys	1 (Both side)
12	Bus Shelter	5 Nos. (Both side)
13	Rest Area	1 No.


Anurag
(Deputy Mising)

2.1.2 Project Milestones

Project Milestone	Condition	Time Line	Date	Financial Progress
I	Commenced construction of Project and achieved 20% of Physical Progress	290 th Day from Appointed date	10 th March 2019	224.73 Cr.
II	Commenced construction of Project and achieved 35% of Physical Progress	430 th Day from Appointed date	28 th July 2019	393.27 Cr.
III	Commenced construction of all Project Facilities and achieved 75% of Physical Progress	690 th Day from Appointed date	13 th April 2020	842.72 Cr.
IV	Completion Of the Project	910 th Day from Appointed date	19 th Nov 2020 (extended up to 31.05.2022)	1123.63 Cr.

Payment Milestones

Project Milestone	Condition	Status
I	Commenced construction of Project and achieved 10% of Physical Progress	Achieved on 20 th Dec 2018
II	Commenced construction of Project and achieved 30% of Physical Progress	Achieved on 31 st August 2019
III	Commenced construction of all Project Facilities and achieved 50% of Physical Progress	Achieved on 21 st August 2020
IV	Commenced construction of all Project Facilities and achieved 75% of Physical Progress	Achieved on 31 st May 2021
V	Commenced construction of all Project Facilities and achieved 90% of Physical Progress	Achieved on 31 st January 2022



3. Progress Status

Progress Status as per submitted Programme

Sr. no.	Item	Unit	Scope of work as per schedule -B	Planned upto March-2022	Progress Achieved upto Feb-2022	This Month Progress	Cumulative in progress & Completed upto March-2022	Target for the month of April-2022	Remarks
Highway Progress (Km.)									
1	C & G	Km	45.819	45.819	45.819	0.000	45.819	0.000	
2	Embankment Top	Km	45.819	45.819	45.700	0.119	45.819	0.000	
3	Subgrade	Km	45.819	45.819	45.620	0.199	45.819	0.000	
4	G.S.B	Km	45.819	45.819	45.620	0.000	45.620	0.199	
5	D.L.C	Km	45.819	45.819	44.500	0.820	45.320	0.499	
6	P.Q.C	Km	45.819	45.419	44.500	0.820	45.320	0.499	
Structure Progress: (No.s)									
1	HPC	No	16+31=47	47	47		47		completed
2	BC	No	21+2=23	23	23		23		completed
3	PUP Slab	No	8	8	8		8		completed
4	MNB Slab	No	22	20	20		20		completed
5	MJB Slab	No	39	39	39		39		completed
6	VUP Slab	No	18	18	18		18		completed
7	LVUP Slab	No	26	26	26		26		completed
8	Elevated Slab	No	40	40	40		40		completed
9	ROB Slab	No	6	6	6		6		completed
10	RUB Slab	No	10	8	9	0	9		1
11	Flyover Slab	No	20	20	20		20		completed

1. Physical Progress Planned up to March -2022:- **99.82 %**

(As per Revised program Submitted on 17.08.2021)

2. Physical Progress achieved up to March -2022:- **95.58 %**

3. Physical progress achieved in Month of March - 2022:- **02.66 %**



Summary of Progress (March 2022)

Highway Progress:

Sr. No.	Item	Unit	Scope of work	Completed / Work in progress	Balance work
1	C & G	Km	45.819	45.819	0.000
2	Embankment Top	Km	45.819	45.819	0.000
3	Sub- Grade	Km	45.819	45.819	0.000
4	GSB	Km	45.819	45.620	0.199
5	DLC (MC)	Km	45.819	45.320	0.499
6	PQC (MC)	Km	45.819	45.320	0.499
7	Embankment(SR)	Km	28.380	28.380	0.000
8	Sub- Grade(SR)	Km	28.380	28.380	0.000
9	GSB(SR)	Km	28.380	28.380	0.000
10	WMM (SR)	Km	28.380	28.380	0.000
11	DBM (SR)	Km	28.380	28.100	0.280
12	BC (SR)	Km	28.380	16.000	12.380

Structure Progress Status:-

Sl. No.	Structure Details:-	Unit	Scope	Completed	Work in progress	Balance	Remarks
1	Major Bridge	Nos	2	2	0	0	completed
2	Elevated Road	Nos	1	1	0	0	completed
3	Minor Bridge	Nos	11	10	0	0	completed (1 No. deleted)
4	Box Culvert	Nos	23	23	0	0	2 Nos. (Additional)
5	Pipe Culvert	Nos	47	47	0	0	31 No. (Additional)
7	PUP/CUP	Nos	04	04	0	0	(04 No. Additional)
8	Vehicular Underpass	Nos	9	9	0	0	completed
9	Light Vehicular Underpass	Nos	13	13	0	0	completed
10	Flyover	Nos	3	3	0	0	completed
11	ROB	Nos	1	1	0	0	completed
12	RUB	Nos	1	0	1	0	Work in progress
13	Drain	Km	28.38	28.38	0.88	0	

1. Physical progress Achieved upto March 2022- 95.58 %

2. Financial Progress Achieved upto March 2022- 96.01 % (1078.797 Crs)

3. Financial Progress Planned upto March 2022- 99.70 %
(Financial S- Curve attached at the end)



(Deepak Mishra)

4. Utility Shifting Progress

1. Permission for cutting of trees on Government land and forestland received. Cutting of trees in progress. Ref. no 1594 dated 03 / 05 / 2018 (Jhalawar) &1837-44 dated 22/05/2018(Kota).
2. Electrical Utilities estimate approved in both district Kota &Jhalawar vide letter 41010 & 41011 1/2016- Kota / US – Electric- Kota and Jhalawar / Package-2/7077 dated 24th August 2018. Works for shifting of electrical utilities are completed.
3. Water Pipelines Estimate is approved vide letter no. _41024 / 1 / 2016- Kota/ US - PHED- Kota / Pkg-II/ 6998 dated 16-08 2018 and 41025 / _1 / 2016- Kota / US /6997 dated 16-08-2018 Shifting works are completed.
4. Estimate of HT Lines is approved. Material received at site for execution. Survey done with department for finalizing locations of new tower. Foundation works has been completed. And Tower erection works are in progress.

Details of numbers and length are as below: -

<u>Utility Shifting</u>							
Sr. No.	Particulars	Total	Progress till last month	Current month	Cumulative Progress till March-22	Balance to be completed	Remarks
1	Electric Poles						
	Kota Section	600	600	-	600	0	
	Jhalawar Section	141	141	-	141	0	
	Total	741	741	-	741	0	completed
2	Structures (Nos.)						
	Kota Section	403	403	-	403	0	
	Jhalawar Section	159	159	-	159	0	
	Total	562	562	-	562	0	completed
3	Religious Strs (Nos.)						

Utility Shifting

Sr. No.	Particulars	Total	Progress till last month	Current month	Cumulative Progress till March-22	Balance to be completed	Remarks
	Kota Section	13	11	-	11	2	02 Nos. constructions in progress at Ch. No. 09+860 RHS, 11+300 LHS.
	Jhalawar Section	2	2	-	2	0	
	Total	15	13	-	13	2	

4 Water Utilities (km)

	Kota Section	9.875	9.875	-	9.875	0	
	Jhalawar Section	11.125	11.125	-	11.125	0	
	Total	21	21.00	-	21.00	0	completed

5 High Tension Line

Sr. No.	Chainage No.	Foundation		Tower Erection		String	
		LHS	RHS	LHS	RHS	LHS	RHS
1	23+100	Completed	Completed	Completed	Completed	Completed	Completed
2	27+085	Completed	Completed	Completed	Completed	Work in Progress	Work in Progress
3	30+800	Completed	Completed	Completed	Completed	Completed	Completed
4	41+875	Completed	Completed	To be taken up	To be taken up	To be taken up	To be taken up
5	42+075	Completed	Completed	To be taken up	To be taken up	To be taken up	To be taken up
6	57+075	Completed	Completed	Completed	Completed	Completed	Completed
7	33+710	Profile & Estimate approved (Sanction / Approval as per Authority awaited).					
8	42+950	Profile & Estimate approved (Sanction / Approval as per Authority awaited).					



5 Tree Cutting Status:-

Status of Tree Cutting:

Sr. No.	District	Category		Total Nos.	Status of Cutting permission	Cumulative No. of Cutting upto this month	Balance	Approval Letter No.	Remark
1	Kota	Govt Trees	All	465	Yes	439	26	Revenue-III/2018/1837-44 dated 22.05.2018	Balance only in kukdakhurd from Km. 11+200 to 11+690 LHS.
		Pvt. Trees	Fruit Bearing	2882	Not required	2882	0	No.41002/2016 - kota/L.A/Ramganjmandi/pkg-2/6243 dated 17.04.2018	completed
			Non fruit Bearing	1560	Not required	1560	0		
2	Jhalawar	Govt Trees	All	972	Yes	972	0	Revenue/18/1594 dated 03.05.2018 & 1861 dated 25.05.2018	completed
		Pvt. Trees	Fruit Bearing	1836	Not required	1836	0	No.41003/2016 - kota/L.A/Jhalawar/pkg-2/6242 dated 17.04.2018	completed
			Non fruit Bearing	702	Not required	702	0		
		Forest		104	Yes	104	0	F-14()2017/Jhalawar Road/FCA/1998 dated 19.04.2018	completed
		Total Trees		8521		8495	26		99.69%

Note:-

- 1) Total No. of trees increased from 7727 to 8521 Nos. because of (a) 429 trees along existing alignment added in Jhalawar District (b) 365 Nos (85 fruits+ 280 nonfruits) trees added in Kota District

6. Status of Conditions precedent

a	Provided Performance Security to the Authority	Released on 26.08.2019
b	Executed and procured execution of Escrow Agreement	Submitted. Vide this office letter No. PDJHPL / NHAI / FC / 039 .2018 Dt. 21-05-2018.
c	Executed and procured execution of Substitution Agreement	Submitted. Vide this office letter No. PDJHPL / NHAI / FC / 039 .2018 Dt. 21-05-2018.
d	Procure all Applicable Permits as per Schedule -E	Obtained
e	Executed Financing Agreements and delivered 3 copies duly attested by Director of the Concessionaire	Submitted. Vide this office letter No. PDJHPL / NHAI / FC / 039 .2018 Dt. 21-05-2018
f	Delivered to Authority 3 true copies of Financial Package and Financial Model duly attested by Director of the Concessionaire	Submitted. Vide this office letter No. PDJHPL / NHAI / FC / 039 .2018 Dt. 21-05-2018.
g	Delivered to Authority from Selected Bidder its respective confirmation in original of the correctness of their representations and warranties set forth in Sub Clause (k), (l) and (m) of Clause 7.1 of CA	Submitted
h	Environment Clearance	Done
i	Forest Land Clearance	Stage –II Clearance obtained
j	Wild Life Clearance	NA



7. Status of Railway Approvals

Proposal Description	Status	Length Impacted	Current Stage	Issues/ Comments
Rail ROB (Ch.44+158)	GAD of ROB Approved	-	Detailed design and drawing Approved by Railways.	Steel Girder Launching & slab casting on Railway span (P1-P2) is Completed. Girder launching on Non-railway span P2-A2 LHS & RHS completed. Railway Portion P1-P2 Slab completed, Non-railway span P2-A2 LHS & RHS slab completed.
RUB (Ch.33+585)	GAD of RUB Approved	-	Detailed design and drawing Approved by Railways. Work permission received on date 02.12.2019	Soil Nailing works in railway embankment portion completed and extension of thrust bed to the required length has been completed. Accordingly leading Box Works with cutting edge are completed. Assemble of RH Girder & Fixing of Rails over the girder are completed. Further Box pushing work is Completed in LHS (50.00 Meter). In RHS Side Approximate 5.00 Meter completed.



8. ISSUES OF CONCERN: -

1. EHV Lines :

- 1.1) Approval of estimates for 06 Nos. EHV lines shifting/raising accorded by NHAI / Concerned Authorities. Further Profile & Estimates of balance 02 Nos. EHV lines are approved by Concerned Authorities vide letter No. 1411 dated 29.10.2021 & 1433 dated 01.11.2021.
 - 1.2) 06 Nos. of EHV lines foundations completed.
 - 1.3) Raising / shifting of 02 Nos. EHV lines at Km. 23+150, & Km. 57+075 completed at site.
 - 1.4) Further works at Km. 30+800, Km. 27+085 are in progress.
 - 1.5) Foundations for Monopole work at Km. 27+085 completed and material inspection completed by concerned authorities & material received at site.
2. The Works of Major Bridge (Ahu river bridge) at A-1 side i.e A-1, P-1, P-2, P-3 in the village boundary of Gola are affected and works are not progressed because of land Acquisition Issues from 20.10.2020 to 07.02.2021. The issue has been discussed with the land owner by concessionaire in the interest of the project and convinced him to give his consent to start the work by paying compensation from concessionaire on 01st February 2021. Issue at present resolved and work commenced from 07th feb 2021.

3. Extension of Time:


- Independent Engineer has recommended the EOT to Authority vide letter no. 1264 dated 08-02-2021 the revision of date of completion 07-09-2021.
- Project Director, NHAI, PIU has recommended Extension of Time (EOT) up to 26.08.2021 and communicated to Regional officer, RO, Jaipur (Rajasthan) for further process & approval.
- RO has sent communication for certain clarification & justification on EOT issue vide letter No. 2856 dated 24.03.2021.
- Concessionaire has submitted all documents with justification to Independent Engineer along with work program.
- Independent Engineer has **approved the work plan** (with Extension of Time (EOT) up to 26.08.2021) subject to approval of EOT from competent Authority vide letter No. 1364 dated 08.04.2021.
- Further PD, PIU, NHAI, Kota send his recommendation to RO office for further process vide letter No. 3048 dated 27.04.2021.
- RO has sent his recommendation to HO, NHAI, New Delhi for further approval vide letter No. 0234 dated 04.05.2021.
- **Extended date post COVID 180 days approved, further EOT of 101 days under review at HO, NHAI, New Delhi).**

- Further to the above, concessionaire intimated the impact of 2nd wave of Covid-19 to Independent Engineer / Authority vide various letter No. 009 Dt. 23.03.2021, 011 Dt. 07.04.2021 & 013 Dt. 23.04.2021.
 - Meeting at HQ, NHAI had been conveyed on 09.07.2021 and discussions made regarding EOT issues.
 - Communication sent to NHAI, HQ for our willingness/consent for the process of resolution / conclusion through the mechanism of Conciliation Committee of Independent Experts for our pending matter of Extension of Time vide letter No. 042 dated 16.07.2021.
 - As per the Meeting of CCIE held on 26th Oct, 2021 all modalities for settlement agreement are concluded.
 - **Accordingly settlement Agreement has been executed between NHAI & concessionaire on dated 17.11.2021.**
 - **As per the Settlement Agreement,**
 - **Provisional certificate (PCOD) to be issued by Authority to concessionaire on completion of 42.88 Km. length of highway in all respects.**
 - **Concessionaire to complete the total 48.88 Km. length of the project Highway except one side of RUB (i.e, RHS of RUB) by 28.02.2022.**
 - **The complete scope of work including remaining one side of RUB (RHS) will be completed by 31.05.2022 and accordingly Extension of Time will be granted by the Authority to concessionaire up to 31.05.2022.**
4. As per condition of Settlement Agreement Concessionaire communicated Independent Engineer regarding request for provisional completion of project for length of 42.88 Km & to conduct necessary tests as per Schedule- I of Concession Agreement.
 5. **COS-1:** Competent Authority approved Financial Proposal of COS-1 vide letter No. 3435 dated 29th June 2021 amounting to Rs. 17.01 Crs. Concessionaire executed works under Change of Scope & submitted IPC-01 amounting to Rs. 11.33 Crs. vide letter No. 2886 dated 13th Oct. 2021. Payment released to concessionaire as per provisions.
 6. **COS-2:** As per the discussion at site during site visit of CGM (T)-Raj, NHAI, HQ, New Delhi, Concessionaire has submitted the Change of Scope (COS No. 02) vide letter No. 2785 dated 27.08.2021. The Independent Engineer recommended proposal of COS-2 to NHAI vide letter No. 1651 dated 26.10.2021 for In-principle Approval of Competent Authority.
 7. The details of hindrances is attached as **Annexure-I.**



Lab Test Conducted Report for the month of March – 2022

Sr. No.	Name of Test	Number of Tests Conducted									Remarks
		Up To Previous Month			This Month			Total upto Date			
		Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test	
OGL & Cutting soil											
1	Free Swell Index	329	0	329	0	0	0	329	0	329	
2	Grain Size Analysis	329	0	329	0	0	0	329	0	329	
3	Plasticity Index	329	0	329	0	0	0	329	0	329	
4	Max. Dry Density	329	0	329	0	0	0	329	0	329	
5	CBR	11	0	11	0	0	0	11	0	11	
6	Density of Comp.Layer	6921	143	7064	0	0	0	6921	143	7064	
7	Moisture Cont.	0	0	0	0	0	0	0	0	0	
Borrow Area (Embankment & Subgrade)											
1	Free Swell Index	2960	130	3090	0	0	0	2960	130	3090	
2	Grain Size Analysis	2980	130	3110	0	0	0	2980	130	3110	
3	Plasticity Index	2992	122	3114	0	0	0	2992	122	3114	
4	Max. Dry Density	3029	122	3151	0	0	0	3029	122	3151	
5	CBR	685	32	717	0	0	0	685	32	717	
Earthwork Field test											
1	Density of Comp.Layer (Emb.)	203258	882	204140	523	0	523	203781	882	204663	
2	Density of Comp.Layer (Sub grade & Earthen shoulder)	23046	181	23227	1062	0	1062	24108	181	24289	
GSB											
1	Sieve Analysis	1163	0	1163	32	0	32	1195	0	1195	
2	Plasticity Index	1160	0	1160	32	0	32	1192	0	1192	
3	Max. Dry Density	4	0	4	0	0	0	4	0	4	
4	CBR	2	0	2	0	0	0	2	0	2	
5	Water Absorption	2	0	2	0	0	0	2	0	2	
6	AIV	3	0	3	0	0	0	3	0	3	
7	Density of Comp.Layer	3443	35	3478	129	0	129	3572	35	3607	



WMM											
1	Sieve Analysis	426	0	426	23	0	23	449	0	449	
2	Plasticity Index	426	0	426	23	0	23	449	0	449	
3	Aggregate Impact Value	342	0	342	22	0	22	364	0	364	
4	Combined F.I & E.I.	355	0	355	22	0	22	377	0	377	
5	Max. Dry Density	30	0	30	0	0	0	30	0	30	
6	Density of Comp.Layer	1830	0	1830	138	0	138	1968	0	1968	
7	Water Absorption	0	0	0	0	0	0	0	0	0	
8	Soundness Test	0	0	0	0	0	0	0	0	0	

DBM											
1	Aggregate Impact Value	158	0	158	9	0	9	167	0	167	
2	Flakiness & Elongation	149	0	149	9	0	9	158	0	158	
3	Mix Grading	169	0	169	9	0	9	178	0	178	
4	Individual Grading	18	0	18	0	0	0	18	0	18	
5	Stability of Mix	603	0	603	54	0	54	657	0	657	
6	Binder Content & Grading Mix	222	0	222	9	0	9	231	0	231	
7	Density of Compacted layer	482	0	482	52	0	52	534	0	534	
8	Gmm Test	207	0	207	9	0	9	216	0	216	

BC											
1	Aggregate Impact Value	89	0	89	26	0	26	115	0	115	
2	Flakiness & Elongation	89	0	89	26	0	26	115	0	115	
3	Mix Grading	89	0	89	26	0	26	115	0	115	
4	Individual Grading	0	0	0	0	0	0	0	0	0	
5	Stability of Mix	549	0	549	156	0	156	705	0	705	
6	Binder Content & Grading Mix	105	0	105	26	0	26	131	0	131	
7	Density of Compacted layer	166	0	166	166	0	166	332	0	332	
8	Gmm Test	105	0	105	26	0	26	131	0	131	

Bitumen											
1	Softening Point	132	0	132	6	0	6	138	0	138	
2	Ductility	0	0	0	0	0	0	0	0	0	
3	Penetration	132	0	132	6	0	6	138	0	138	
4	Viscosity	136	0	136	6	0	6	142	0	142	

(Deepak Mishra)

Prime Coat											
1	Quality Of Binder (Viscosity)	8	0	8	0	0	0	8	0	8	
2	Rate of Spray of Binder	610	0	610	72	0	72	682	0	682	

Tack Coat											
1	Quality Of Binder	9	0	9	0	0	0	9	0	9	
2	Rate of Spray of Binder	911	0	911	234	0	234	1145	0	1145	

PHYSICAL PROPERTIES OF AGGREGATE FOR CONCRETE											
1	Sieve Analysis of CA	2364	0	2364	27	0	27	2391	0	2391	
2	Sieve Analysis of FA	2281	0	2281	27	0	27	2308	0	2308	
3	Sieve Analysis of DLC	497	0	497	0	0	0	497	0	497	
4	Sieve Analysis of PQC	721	0	721	10	0	10	731	0	731	
5	Aggregate Impact Value	3158	0	3158	37	0	37	3195	0	3195	
6	Flakiness Index	3158	0	3158	37	0	37	3195	0	3195	
7	Silt Content	309	0	309	0	0	0	309	0	309	
8	Specific Gravity & W A	17	0	17	0	0	0	17	0	17	

Concrete Mix Design (cube sets)											
1	M15	7 Days	43	0	43	0	0	0	43	0	43
		28 Days	71	0	71	0	0	0	71	0	71
2	M20 Kerb	7 Days	19	0	19	0	0	0	19	0	19
		28 Days	26	0	26	0	0	0	26	0	26
	M20	7 Days	12	0	12	0	0	0	12	0	12
		28 Days	18	0	18	0	0	0	18	0	18
3	M25	7 Days	70	0	70	0	0	0	70	0	70
		28 Days	111	0	111	0	0	0	111	0	111
4	M30	7 Days	71	0	71	0	0	0	71	0	71
		28 Days	15	0	15	0	0	0	15	0	15
5	M35	7 Days	149	0	149	0	0	0	149	0	149
		28 Days	265	0	265	0	0	0	265	0	265
6	M35 Pile	7 Days	72	0	72	0	0	0	72	0	72
		28 Days	142	0	142	0	0	0	142	0	142
7	M35 RE block	7 Days	45	0	45	0	0	0	45	0	45
		28 Days	144	0	144	0	0	0	144	0	144

Handwritten signature

8	M40 7 Days	78	0	78	0	0	0	78	0	78
	28 Days	118	0	118	0	0	0	118	0	118
9	M45 7 Days	62	0	62	0	0	0	62	0	62
	28 Days	116	0	116	0	0	0	116	0	116
10	M50 7 Days	7	0	7	0	0	0	7	0	7
	28 Days	26	0	26	0	0	0	26	0	26
11	M40 PQC 7 Days	227	0	227	0	0	0	227	0	227
	28 Days	295	18	313	0	0	0	295	18	313
12	M40 PQC Fl. Strength 7 Days	165	0	165	0	0	0	165	0	165
	28 Days	164	18	182	0	0	0	164	18	182
13	DLC 7 Days	101	0	101	0	0	0	101	0	101
14	Grouting	6	0	6	0	0	0	6	0	6

Field Concrete (cube sets)

1	M15 7 Days	3966	0	3966	50	0	50	4016	0	4016
	28 Days	6308	0	6308	166	0	166	6474	0	6474
2	M20 Kerb 7 Days	1047	0	1047	32	0	32	1079	0	1079
	28 Days	1792	0	1792	150	0	150	1942	0	1942
3	M25 7 Days	4418	0	4418	10	0	10	4428	0	4428
	28 Days	6175	0	6175	30	0	30	6205	0	6205
4	M30 7 Days	872	0	872	2	0	2	874	0	874
	28 Days	1945	0	1945	3	0	3	1948	0	1948
5	M35 7 Days	4875	0	4875	35	0	35	4910	0	4910
	28 Days	11692	0	11692	82	0	82	11774	0	11774
6	M35 Pile 7 Days	220	0	220	0	0	0	220	0	220
	28 Days	392	0	392	0	0	0	392	0	392
7	M35 RE block 7 Days	940	0	940	0	0	0	940	0	940
	28 Days	2847	0	2847	0	0	0	2847	0	2847
8	M40 7 Days	2010	0	2010	42	0	42	2052	0	2052
	28 Days	4028	0	4028	210	0	210	4238	0	4238
9	M45 7 Days	272	0	272	1	0	1	273	0	273
	28 Days	1079	0	1079	9	0	9	1088	0	1088

10	M50 7 Days	22	0	22	0	0	0	22	0	22	
	28 Days	49	0	49	4	0	4	53	0	53	
11	M40 PQC 7 Days	2817	0	2817	39	0	39	2856	0	2856	
	28 Days	3030	0	3030	123	0	123	3153	0	3153	
12	M40 PQC Flexural Strength 7 Days	2698	0	2698	39	0	39	2737	0	2737	
	28 Days	2911	0	2911	123	0	123	3034	0	3034	
13	DLC 7 Days	1873	0	1873	30	0	30	1903	0	1903	
14	DLC FDD	2011	0	2011	24	0	24	2035	0	2035	

Cement

1	Fineness	258	0	258	6	0	6	264	0	264	
2	Consistency	258	0	258	6	0	6	264	0	264	
3	Setting Time	258	0	258	6	0	6	264	0	264	
4	Soundness	258	0	258	6	0	6	264	0	264	
5	Compressive Strength										
	a) 3 Days	363	0	363	6	0	6	369	0	369	
	b) 7 Days	360	0	360	6	0	6	366	0	366	
	c) 28 Days	366	0	366	8	0	8	374	0	374	


Signature

WEATHER REPORT (Month of March-2022)

Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project (Length 48.880 Km.) -Package II

WEATHER REPORT (Month of March-2022)

Sl. No.	Date	Temperature C		Humidity %		Rainfall (mm)	Climate
		Max. Temp. (°C)	Min. Temp. (°C)	Max	Min		
1	01-03-22	23.8	12.2	61.0	18.0	0.0	Clear
2	02-03-22	24.7	13.5	59.0	25.0	0.0	Clear
3	03-03-22	25.2	14.0	60.0	31.0	0.0	Clear
4	04-03-22	24.8	13.8	61.0	31.0	0.0	Clear
5	05-03-22	25.1	13.3	58.0	25.0	0.0	Clear
6	06-03-22	25.8	13.9	59.0	22.0	0.0	Clear
7	07-03-22	26.6	16.1	59.0	25.0	0.0	Clear
8	08-03-22	27.0	17.7	56.0	34.0	0.0	Clear
9	09-03-22	26.8	15.5	61.0	34.0	0.0	Clear
10	10-03-22	26.3	15.9	62.0	34.0	0.0	Clear
11	11-03-22	27.1	16.2	61.0	26.0	0.0	Clear
12	12-03-22	28.1	16.9	59.0	21.0	0.0	Clear
13	13-03-22	28.9	17.0	59.0	22.0	0.0	Clear
14	14-03-22	30.8	18.2	54.0	17.0	0.0	Clear
15	15-03-22	31.4	17.5	50.0	17.0	0.0	Clear
16	16-03-22	31.9	16.7	55.0	16.0	0.0	Clear
17	17-03-22	32.2	18.1	54.0	17.0	0.0	Clear
18	18-03-22	32.5	18.6	52.0	16.0	0.0	Clear
19	19-03-22	32.8	18.9	74.0	12.0	0.0	Clear
20	20-03-22	34.2	19.1	60.0	13.0	0.0	Clear
21	21-03-22	36.1	22.0	50.0	14.0	0.0	Clear
22	22-03-22	35.5	23.2	67.0	18.0	0.0	Clear
23	23-03-22	35.5	23.9	46.0	18.0	0.0	Clear
24	24-03-22	31.5	21.3	45.0	26.0	0.0	Clear
25	25-03-22	35.2	22.0	5.0	16.0	0.0	Clear
26	26-03-22	36.4	21.1	44.0	15.0	0.0	Clear
27	27-03-22	36.9	22.1	43.0	12.0	0.0	Clear
28	28-03-22	37.6	22.3	42.0	14.0	0.0	Clear
29	29-03-22	38.6	23.1	40.0	10.0	0.0	Clear
30	30-03-22	38.1	23.4	40.0	10.0	0.0	Clear
31	31-03-22	38.0	23.5	42.0	12.0	0.0	Clear

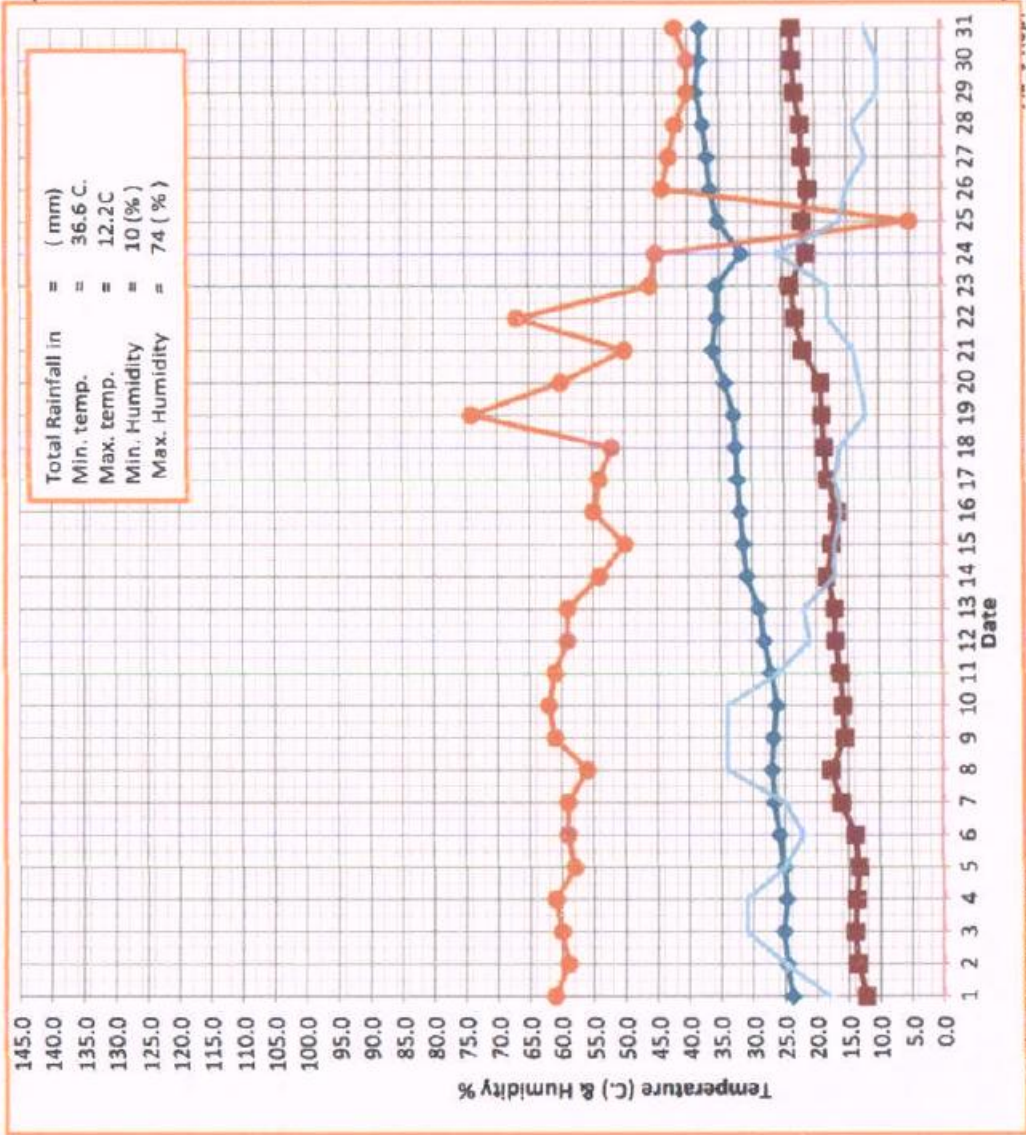

10. Status of Mix Design and Source Approval

Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
1	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	Submission of Mix Design	LASA/Concessionaire/D J/IE/2018/0003	21.08.2018
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-15(PCC Work) with flyash		
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-25(RCC Work) with flyash		
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-30(RCC Work) with flyash		
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-35(RCC Work) with flyash		
	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	M-35(Pile Work with flyash		
2	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	Submission of Mix Design of Concrete from Ultratech&Mangalam Cement	LASA/Concessionaire/D J/IE/2018/0003	21.08.2018
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-35 RE Block (Ultratech&Mangalam cement)		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-35 with flyash RE Block (Ultratech&Mangalam cement)		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-15 PCC		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-25 RCC		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-30 RCC		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-35 RCC		
	PDJHPL/PIU/CLO-179/2018/047	13.06.2018	M-35 Pile work		
3	PIL/CAMP/DJT/NHAI/2018-04/08	26.04.2018	Submission of Company profile & credential for the D.P. Wires	LASA/Concessionaire/D arah- Jhalawar/IE/2018/191	08.12.2018
4	PIL/CAMP/DJT/NHAI/2018-04/09	26.04.2018	Submission of Company profile & credential for the Shyam, Electrosteel and Premier Steel		
5	PDJHPL/NHAI/DJT/2018/019	12.03.2018	Submission of Company profile & credential for the Rashtriyalspat Nigam Ltd (Vizag Steel),Nilkanth Steel Pvt.ltd ,Steel authority of India limited (SAIL) ,Jindal steel & power limited ,Rashmi group ,Madhav Alloys Pvt.limited	LASA/Concessionaire/D J/IE/2018/17 and 58, 59 (10.09.2018)	30.08.2018
7	PIL/CAMP/DJP/N HAI/2018 -04 / 063	21.06.2018	Submission of construction material for testing.		
8	PIL/CAMP/DJP/N HAI/2018 -04 / 063	21.06.2018	Steel Dia 20mm JSW Steel (Fe-5.50D)		
10	PIL/CAMP/DJP/N HAI/2018 -04 / 063	21.06.2018	Steel - Dia 12,25 & 32mm SAIL (Fe-500D)		
10	PDJHPL/NHAI/DJT/2018/013	26.02.2018	Submission of Company profile & credential for the Birla Corporation Limited ,Mangalam Cement Limited , Wonder cement Limited , Ultrtech cement Limited ,Vadraj cement . Shree cement Limited	LASA/Concessionaire/D J/IE/2018/14	28.08.2018
11	PIL/CAMP/DJT/NHAI/2018-04/01	26.04.2018	Submission of Company profile & credential for the BASF India Ltd.for Admixture,Grout and joint Sealant , Unirock Chemicals (Admixture) , Tikitar Ltd. For Joint Sealant	LASA/Concessionaire/D J/IE/2018/016	30.08.2018

Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
12	PDJHPL/NHAI/DJT/2018/020	22.03.2018	Submission of Company profile & credential for Admixture and curing compound ,Kunalconchempvt.ltd.,Grout and joint Sealant ,STPLimited&Chembond Chemicals Ltd.		
13	PIL/CAMP/DJP/N HAI/2018 -04 /063	21.06.2018	Admixture - PC 100R (KunalIndustries)		
14	PDJHPL/PIU/CLO-179/2018/095	04.07.2018	DLC Flyash		
15	PDJHPL/PIU/CLO-179/2018/095	04.07.2018	DLC without Flyash		
16	PIL/CAMP/DJP/N HAI/2018 -04 /063	21.06.2018	GSB (Julmi PIL Crusher)		
18	PIL/CAMP/DJT/NHAI/2018-04/06	26.04.2018	Submission of Company profile & credential for the IOCL (Bitumen) ,HPCL (Bitumen) ,ESSAR (Bitumen) , GP global (Emulsions) , HINCOL (Emulsions) Total oil India pvt ltd. (Emulsions)	LASA/Concessionaire/D J/IE/2018/020 Bitumen& 19 for Emulsion	31.08.2018
19	PIL/CAMP/DJT/NHAI/2018-04/02	26.04.2018	Submission of Company profile & credential for the SGG spun pipes	LASA/Cocessionaire/Darah- Jhalawar/IE/2018/050	07.09.2018
20	PIL/CAMP/DJT/NHAI/2018-04/03	26.04.2018	Submission of Company profile & credential for the TIKIDAN Danosa India	LASA/Concessionaire/Darah- Jhalawar/IE/2018/212	14.12.2018
21	PIL/CAMP/DJT/NHAI/2018-04/04	26.04.2018	Submission of Company profile & credential for the KANTAFLEX India Pvt.ltd. (Elastomeric & Pot bearing)	LASA/Concessionaire/Darah- Jhalawar/IE/2018/206	13.12.2018
22	PIL/CAMP/DJT/NHAI/2018-04/05	26.04.2018	Submission of Company profile & credential for the Dynamic Prestress (I) Pvt Ltd.	LASA/Concessionaire/Darah- Jhalawar/IE/2018/195	08.12.2018
23	PIL/CAMP/DJT/NHAI/2018-04/07	26.04.2018	Submission of Company profile & credential for the Amitek Infra (Thermoplastic Road Marking Paint)	LASA/Concessionaire/D J/IE/2018/018	30.08.2018
24	PDJHPL/NHAI/DJT/2018/021	22.03.2018	Submission of Company profile & credential for the Nakoda spun pipes		
25	PDJHPL/NHAI/DJT/2018/022	22.03.2018	Submission of Laboratory profile & credentials for the Star wire INDIA Pvt., Third party, Hind Heat		
26	PDJHPL/PIU/CLO-179/2018/047	21.06.2018	Submission of Gompany Profile &Gredential for source approval of Hercules Bridge Bearings & Bridge Expansion Joints	LASA/Concessionaire/Darah- Jhalawar/IE/2018/003	21.08.2018
27	PDJHPL/PIU/CLO-179/2018/096	04.07.2018	Submission of Company Profile &Gredential for Arihant Prefab	LASA/Concessionaire/Darah- Jhalawar/IE/2018/052	07.09.2018
28	PDJHPL/PIU/CLO-179/2018/100	05.07.2018	Submission of Gompany profile &Gredeniir for M.E. Testing Laboratory	LASA/Concessionaire/Darah- Jhalawar/IE/2018/178	04.12.2018
29	PDJHPL/PIU/CLO-179/2018/101	05.07.2018	Submission of Company Profile & Credential for MarutiBitumin Pvt. Ltd	LASA/Concessionaire/Darah- Jhalawar/IE/2018/054	07.09.2018
30	PDJHPL/PRJ/TEC/CLO-179/2018/ 022	02.06.2018	Submission of profite,Credentials& Basic design report on RE walls	LASA/Concessionaire/Darah- Jhalawar/IE/2018/055	07.09.2018
31	PDJHPL/PIU/D/2018/032	16.04.2018	Submission of Quality assurance Plan		
32	PDJHPL/PIU/CLO-179/2018/043	13.06.2018	Submission of Mix Design of Granular Sub-Base	LASA/Concessionaire/Darah- Jhalawar/IE/2018/155	28.11.2018
33	PDJHPL/PIU/CLO-179/2018/044	13.06.2018	Submission of Summary of OGL test results		
34	PDJHPL/PIU/CLO-179/2018/045	13.06.2018	Submission of Galibration Certificate of Batching Plant & Lab Equipments		
35	PDJHPL/PIU/CLO-179/2018/046	13.06.2018	Submission of Third party test reports of the material related to the project		

Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
36	PDJHPL/PIU/CLO-179/2018/056	18.06.2018	Submission of Petrographic Test Report of Coarse Aggregate		
37	PDJHPL/PIU/CLO-179/2018/108	06.07.2018	Submission of Borrow Area - 1,3,6,7,9,10,11,12,14,15,17,18,20,21,22, 23,24,26,27,29,30,31,32,33,34 & 35		
38	PDJHPL/PIU/CLO-179/2018/110	07.07.2018	Submission of Company Profile & Credential for Earthcon Systems Pvt. Ltd	LASA/Concessionaire/D arah- Jhalawar/IE/2018/049	06.09.2018
39	PDJHPL/PIU/CLO-179/2018/111	07.07.2018	Submission of Construction Design (Geogrid Reinforced Soil Wall)	LASA/Concessionaire/D arah- Jhalawar/IE/2018/063	15.09.2018
40	PDJHPL/PIU/CLO-179/2018/122	10.07.2018	Testing for C & O Value of soil samples of Borrow area No. 1 & 22		
41	PDJHPL/PIU/CLO-179/2018/129	13.07.2018	Submission of Mix-Design	LASA/Concessionaire/D arah- Jhalawar/IE/2018/003	21.08.2018
42	PDJHPL/PIU/CLO-179/2018/133	16.07.2018	Submission of Trial Patch Report of GSB & DLC		
43	PDJHPL/IE/ICO-181/2018/241	28.08.2018	Submission of Company Profile & Credential OF Maruti Rub Plast Pvt. Ltd.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/088	15/10/2018
44	PDJHPL/IE/ICO-181/2018/242	28.08.2018	Submission of Company Profile & Credential Of Tar Products Pvt. Ltd.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/053	07/09/2018
45	PDJHPL/NHAI/DJT/013/2018	28.08.2018	Submission of Company Profile & Credentials for Birla Corporation, Mangalam Cement, Wonder Cement, Ultratech Cement, Vardraj Cement & Shree Cement.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/014	28/08/2018
46	PDJHPL/IE/ICO-181/2018/260	07.09.2018	Submission of Company Profile & Credential Of Sanfield (India) Ltd.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/072	28/09/2018
47	PDJHPL/IE/ICO-181/2018/286	18.09.2018	Submission of Company Profile & Credential for RAMA TMT Bars	LASA/Concessionaire/D arah- Jhalawar/IE/2018/074	28/09/2018
48	PDJHPL/IE/ICO-181/2018/287	18.09.2018	Submission of Company Profile & Credential for SHYAM Steel	LASA/Concessionaire/D arah- Jhalawar/IE/2018/073	28/09/2018
49	PDJHPL/IE/ICO-181/2018/318	29.09.2018	Submission of Company Profile & Credential of Sanfield (India) Ltd.-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/078	03.10.2018
50	PDJHPL/IE/ICO-181/2018/348	09.10.2018	Submission of Company Profile & Credentials of Katalinepaints.-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/091	15/10/2018
51	PDJHPL/IE/ICO-181/2018/353	10.10.2018	Submission of Third party testing of RE wall concrete block in km. 23+600-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/130	13.11.2018
52	PDJHPL/IE/ICO-181/2018/362	12.10.2018	Submission of Company Profile & Credentials of PNT designs Pvt. Ltd.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/126	13.11.2018
53	PDJHPL/IE/ICO-181/2018/367	13.10.2018	Submission of GSB Mix design for approvals	LASA/Concessionaire/D arah- Jhalawar/IE/2018/111	29/10/2018
54	PDJHPL/IE/ICO-181/2018/381	18.10.2018	Submission of Filter media Mix-design -reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/217	13.11.2018
55	PDJHPL/IE/ICO-181/2018/408	26.10.2018	Submission of Company Profile and Credential of M/s Deevin Seismic Systems Pvt. Ltd. for Expansion Joints-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/127	13.11.2018
56	PDJHPL/IE/ICO-181/2018/429	02/11/2018	Submission of DLC Mix Design Confirmatory Reports-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/163	03.12.2018

Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
57	PDJHPL/IE/ICO-181/2018/450	17/11/2018	Submission of Company profile & Credentials of M/s Deevin Seismic Systems Pvt. Ltd. for Expansion joints - reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/199	12.12.2018
58	PDJHPL/IE/ICO-181/2018/451	17/11/2018	Submission of third party test report of construction materials-reg		
59	PDJHPL/IE/ICO-181/2018/452	17/11/2018	Submission of Company profile & Credential of JK Lakshmi Cement Ltd-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/148	26/11/2018
60	PDJHPL/IE/ICO-181/2018/453	17/11/2018	Submission of company Profile & Credentials of Supreme Bitumen India Pvt. Ltd.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/162	03.12.2018
61	PDJHPL/IE/ICO-181/2018/454	17/11/2018	Resubmission of Company Profile & Credentials of M/s Hind Heat Treatment & Testing House-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/158	30.11.2018
62	PDJHPL/IE/ICO-181/2018/455	17/11/2018	Submission of Company Profile & Credentials of M/s Yash Enterprises-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/177	04.12.2018
63	PDJHPL/IE/ICO-181/2018/460	20/11/2018	Submission of Company Profile & Credentials of M/s Electrotherm India Ltd. -	LASA/Concessionaire/D arah- Jhalawar/IE/2018/190	08.12.2018
64	PDJHPL/IE/ICO-181/2018/461	20/11/2018	Submission of Mix Design of WMM-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/152	27/11/2018
66	PDJHPL/IE/ICO-181/2018/473	22/11/2018	Submission of Concrete Mix Design Done only with Wonder & Ultratech Cement-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/211	15.12.2018
67	PDJHPL/IE/ICO-181/2018/475	22/11/2018	Submission of Concrete Mix Design Using Fly ash with Wonder & Ultratech Cements-reg		
68	PDJHPL/IE/ICO-181/2018/479	23/11/2018	Submission of PQC M-40 Design Using Fly ash with Ultratech Cement-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/176	04.12.2018
69	PDJHPL/IE/ICO-181/2018/480	23/11/2018	Submission of Company Profile & Credentials of M/s KunalConchem Pvt. Ltd.-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/147	26/11/2018
70	PDJHPL/IE/ICO-181/2018/510	30/11/2018	Submission of PQC M-40 Design with Ultratech Cement.		
71	PDJHPL/IE/ICO-181/2018/511	30/11/2018	Submission of Company Profile & Credentials of M/s. Normat India Pvt.Ltd	LASA/Concessionaire/D arah- Jhalawar/IE/2018/207	13/12/2018
72	PDJHPL/IE/ICO-181/2018/521	03/12/2018	Submission of Julmi Crusher Aggregate Test Reports-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/196	10/12/2018
73	PDJHPL/IE/ICO-181/2018/522	03/12/2018	Submission of Fine Aggregate Test Report of Kalisindh River-reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/197	10/12/2018
74	PDJHPL/IC/ICO-181/2018/542	08/12/2018	Submission of company profile & credential of M/s HI-TECH Engineering Solutions - reg		
75	PDJHPL/IC/ICO-181/2018/599	21/12/2018	Submission of Test Report of Spun pipes for NP-4 pipe - reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/226	24/12/2018
76	PDJHPL/IC/ICO-181/2018/620	31/12/2018	Submission of Inspection Report of Elastomeric Bearing Testing (KANTAFLEX) - reg	LASA/Concessionaire/D arah- Jhalawar/IE/2018/247	04.01.2019
77	PDJHPL/IC/ICO-181/2018/626	02/01/2019	Submission of Chemical Composition Test Report of Steel.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/288	24/01/2019
78	PDJHPL/IC/ICO-181/2019/638	05/01/2019	Submission of PQC (M-40) Mix Design with Ultratech Cement.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/252	11/01/2019
79	PDJHPL/IC/ICO-181/2019/639	05/01/2019	Submission of PQC (M-40) Mix Design using Flyash with Ultratech Cement.	LASA/Concessionaire/D arah- Jhalawar/IE/2018/250	10/01/2019
80	PDJHPL/IC/ICO-181/2019/643	07/01/2019	Submission of Company Profile and Credentials of Molecule Conchem Pvt.Ltd	LASA/Concessionaire/D arah- Jhalawar/IE/2018/273	21.01.2019
81	PDJHPL/IC/ICO-181/2019/653	10/01/2019	Submission of Test Report of T.M.T Bars from Electrotherm (India) Ltd.	LASA/Concessionaire/D arah-	04/02/2019

Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
				Jhalawar/IE/2019/297	
82	PDJHPL/IC/ICO-181/2019/665	15/01/2019	Submission of Third Party Test Report of Reinforcement Steel (Hind Heat Treatment)	LASA/Concessionaire/Darah- Jhalawar/IE/2019/292	28/01/2019
83	PDJHPL/IC/ICO-181/2019/666	15/01/2019	Review of Mix Design of PQC (M-40) with Ultratech Cement & Unirock Plasticizers.		
84	PDJHPL/IC/ICO-181/2019/672	16/01/2019	Review of Mix Design of PQC (M-40) with Ultratech Cement, Flyash & Unirock Plasticizers.		
85	PDJHPL/IC/ICO-181/2019/685	21/01/2019	Submission of Company Profile and Credentials of Choksey Chemicals Pvt. Ltd.	LASA/Concessionaire/Darah- Jhalawar/IE/2019/289	28/01/2019
86	PDJHPL/IC/ICO-181/2019/686	21/01/2019	Submission of Company Profile and Credentials of J.K Cement Ltd.	LASA/Concessionaire/Darah- Jhalawar/IE/2019/290	28/01/2019
87	PDJHPL/IC/ICO-181/2019/713	31/01/2019	Submission of Test Report of POT/PTFE Bearings for Flyover+Major Bridge 47+650 to 48+150 (Dynamic Prestress Pvt. Ltd).	LASA/Concessionaire/Darah- Jhalawar/IE/2019/304	06/02/2019
88	PDJHPL/IC/ICO-181/2019/732	06/02/2019	Submission of PQC Trial patch Report from Ch.28+400 to 28+147(LHS) - reg		
89	PDJHPL/IC/ICO-181/2019/753	12/02/2019	Submission of Company Profile & Credentials of Ooms Aycnorn Holding India Pvt. Ltd. & Ooms Polymer Modified Bitumen Pvt. Ltd. -reg	LASA/Concessionaire/Darah- Jhalawar/IE/2019/307	18/02/2019
90	PDJHPL/IC/ICO-181/2019/761	14/02/2019	Submission of Company Profile & Credential of Unirock Chemicals Pvt. Ltd. -reg	LASA/Concessionaire/Darah- Jhalawar/IE/2019/308	18/02/2019
91	PDJHPL/IC/ICO-181/2019/788	20/02/2019	Submission of Company Profile & Credential of MSP Group for procurement of Dowel Bars - reg		
92	PDJHPL/IC/ICO-181/2019/798	25/02/2019	Submission of Company Profile & Credetial of M/s Sika India - reg	LASA/NHAI/Darah- Jhalawar/IE/2019/350	16.03.2019
93	PDJHPL/IC/ICO-181/2019/804	26/02/2019	Submission of Company Profile & Credential of M/s STP Ltd - reg	LASA/NHAI/Darah- Jhalawar/IE/2019/351	16.03.2019
94	PDJHPL/IC/ICO-181/2019/812	28/02/2019	Submission of Company Profile & Credetial of MSP steel & Power Ltd - reg.		
95	PDJHPL/IC/ICO-181/2019/833	07/03/2019	Submission of Company Profile & Credetial of Chembond Chemicals - reg	LASA/Concessionaire/Darah- Jhalawar/IE/2019/352	16.03.2019
96	PDJHPL/IC/ICO-181/2019/962	23/04/2019	Submission of Company Profile & Credetial of Fortune Ltd -reg		
97	PDJHPL/IC/ICO-181/2019/967	25/04/2019	Submission of Company Profile & Credetial of Balajee Loha Ltd -reg		
98	PDJHPL/IC/ICO-181/2019/1018	09/05/2019	Submission of Company Profile & Credetial of Essar Steel -reg		
99	PDJHPL/IC/ICO-181/2019/1019	09/05/2019	Submission of Company Profile & Credetial of Bostik Pvt Ltd -reg	LASA/Concessionaire/Darah- Jhalawar/IE/2019/415	16/05/2019
100	PDJHPL/IC/ICO-181/2019/1031	11/05/2019	Submission of Methodology of Pile Load Test of Routine Pile @ 57+127 (MJB)		
101	PDJHPL/IC/ICO-181/2019/1048	16/05/2019	Submission of Methodology of Pile Load Test of Routine Pile @ 36+070 (MJB)	LASA/Concessionaire/Darah- Jhalawar/IE/2019/429	24/05/2019
102	PDJHPL/IC/ICO-181/2019/1074	25/05/2019	Submissio of Plate Load Test Report Conducted at 36+070 (MJB) & 58+128 (Flyover).		
103	PDJHPL/IC/ICO-181/2019/1083	28/05/2019	Submission of Initial Load Test Report Conducted on Test Pile.		
104	PDJHPL/IC/ICO-181/2019/1088	30/05/2019	Submission of Company Profile & Credetial of Nuvoco Vistas Corp. Ltd -reg	LASA/Concessionaire/Darah- Jhalawar/IE/2019/583	27/09/2019

(Deepak Mishra)

Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
105	PDJHPL/IC/ICO-181/2019/1098	03/06/2019	Submission of Kerb (M-20) with Ultratech Cement without Flyash.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/446	10/06/2019
106	PDJHPL/IC/ICO-181/2019/1099	03/06/2019	Submission of SPT Test Report for Ch.36+070 (MJB)		
107	PDJHPL/IC/ICO-181/2019/1100	03/06/2019	Submission of Bore Log Test Report @ 36+070 (MJB) & 58+128 (Flyover).		
108	PDJHPL/IC/ICO-181/2019/1189	30/06/2019	Submission of Company Profile & Credential of STECOL (Essar TMT Brand)		
109	PDJHPL/IC/ICO-181/2019/1369	07/09/2019	Submission of Company Profile & Credential of VADOL Corporation	LASA/Concessionaire/Darah-Jhalawar/IE/2019/587	28/09/2019
110	PDJHPL/IC/ICO-181/2019/1379	10/09/2019	Change in Company name Deevin Engineering Consulting group to DECG International.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/596	05/10/2019
110	PDJHPL/IC/ICO-181/2019/1402	18/09/2019	Submission of Company Profile & Credential of J Sons Engg Corporation	LASA/Concessionaire/Darah-Jhalawar/IE/2019/594	03/10/2019
111	PDJHPL/IC/ICO-181/2019/1437	30/09/2019	Submission of Company Profile & Credential of Shree Cement Limited	LASA/Concessionaire/Darah-Jhalawar/IE/2019/595	04/10/2019
112	PDJHPL/IC/ICO-181/2019/1564	21/11/2019	Submission of Inspection Report of Elastomeric Bearing Testing (KANTAFLEX India Pvt. Limited) for MJB 36+070	LASA/Concessionaire/Darah-Jhalawar/IE/2019/666	27/11/2019
113	PDJHPL/IC/ICO-181/2019/1574	23/11/2019	Submission of Company Profile & Credential of Electrosteel Steels Limited	LASA/Concessionaire/Darah-Jhalawar/IE/2019/671	29/11/2019
114	PDJHPL/IC/ICO-181/2019/1605	30/11/2019	Submission of company profile & credential of M/s Sika India Pvt. Ltd.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/699	12/12/2019
115	PDJHPL/IC/ICO-181/2019/1619	05/12/2019	Submission of Plate Load Test Report of BC (53+700).		
116	PDJHPL/IC/ICO-181/2019/1620	05/12/2019	Submission of Plate Load Test Report of VUP (Km 54+550).		
117	PDJHPL/IC/ICO-181/2019/1621	05/12/2019	Submission of Inspection Test Report of POT/ PTFE Bearing (Dynamic Prestress) of Elevated @ Km 47+830 & MJB @ Km 57+127.	LASA/Concessionaire/Darah-Jhalawar/IE/2019/700	12/12/2019
118	PDJHPL/IC/ICO-181/2019/1654	14/12/2019	Submission of Company Profile and Credential of M/s BASF India Limited (for Admixture).	LASA/Concessionaire/Darah-Jhalawar/IE/2020/719	02/01/2020
119	PDJHPL/IC/ICO-181/2019/1665	17/12/2019	Submission of Factory Visit and TMT inspection Test Report of M/s Electrosteel Steels Limited for TMT Bars and Third Party Test Report.		
120	PDJHPL/IC/ICO-181/2019/1684	21/12/2019	Submission of Test Report of Strands of DP Wires.		
121	PDJHPL/IC/ICO-181/2019/1698	26/12/2019	Submission of Inspection Test Report of POT/ PTFE Bearing (Dynamic Prestress) of Flyover @ Km 46+957, Km 50+095, Km 58+128.	LASA/NHAI/Darah-Jhalawar/IE/2020/798	20/02/2020
122	PDJHPL/IC/ICO-181/2019/1700	26/12/2019	Submission of High Strain Dynamic Pile Load Test Report of MJB @ Km 36+070.		
123	PDJHPL/IC/ICO-181/2019/1743	08/01/2020	Submission of Mix Design of DBM with VG-40 Grade.		
124	PDJHPL/IC/ICO-181/2019/1745	08/01/2020	Submission of Concrete Mix design with Nuvoco Cement & Sika Admixture & Without Flyash.		
125	PDJHPL/IC/ICO-181/2019/1753	11/01/2020	Submission of Test Report of Core Sample of Retaining Wall Raft.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/754	22/01/2020
126	PIL/PRJ/TECH/ODO-189/2020/1755	11/01/2020	Submission of Company Profile & Credential of HMM Infra Ltd.		

Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
127	PDJHPL/IC/ICO-181/2020/1766	16/01/2020	Submission of Company Profile & Credential of GOEL TMT.		
128	PDJHPL/IC/ICO-181/2020/1770	17/01/2020	Submission of Test Report of Steel of MJB @ Ch 57+127, LVUP @ Ch 23+065.	LASA/NHAI/Darah-Jhalawar/IE/2020/766	30/01/2020
129	PDJHPL/IC/ICO-181/2020/1799	30/01/2020	Submission of Plate Load Test Report of ROB @ 44+158.		
130	PDJHPL/IC/ICO-181/2020/1810	30/01/2020	Submission of Environmental Monitoring Test Report for the year 2020.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/754	05/02/2020
131	PDJHPL/IC/ICO-181/2020/1842	07/02/2020	Submission of Company Profile & Credential of TATA Steel Ltd for Procurement of LRPC Strands		
132	PDJHPL/IC/ICO-181/2020/1886	19/02/2020	Submission of Independent Laboratory Test Reports of Geogrid of Strata Geosystems (India) Pvt. Ltd		
133	PDJHPL/IC/ICO-181/2020/2158	29/07/2020	Submission of Company Profile and Credential of J.K Prestressing Co. for Jack use in Girder prestressing work of MJB @ Km 57+127.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/963	07/08/2020
134	PDJHPL/IC/ICO-181/2020/2166	31/07/2020	Submission of Company Profile & Credential of BG Trade Infra for Procurement of Plastic for Bituminous Mix.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/959	04/08/2020
135	PDJHPL/IC/ICO-181/2020/2231	25/08/2020	Submission of Company Profile & Credential of JSW Steel Ltd for TMT Steel.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1009	03/09/2020
136	PDJHPL/IC/ICO-181/2020/2260	07/09/2020	Submission of Test Report of Selected Soil / Reinforced soil proposed for RE Wall at Km 43+825, 44+150 & Km 45+875.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1041	25/09/2020
137	PDJHPL/IC/ICO-181/2020/2270	09/09/2020	Compressive Strength Test Reports of Core taken PQC @Km 28+680 (LHS).	LASA/NHAI/Darah-Jhalawar/IE/2020/1032	18/09/2020
138	PDJHPL/IC/ICO-181/2020/2290	16/09/2020	Submission of Company Profile & Credential of Shivam Concrete Tech. & Consultancy Ltd for NDY Testing & Rehabilitation Work.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1033	21/09/2020
139	PDJHPL/IC/ICO-181/2020/2324	28/09/2020	Submission of Test Report of Selected Soil / Reinforced soil proposed for RE Wall at Km 43+825, 44+150 & Km 45+875.		
140	PDJHPL/IC/ICO-181/2020/2325	28/09/2020	Submission of Test Reports from Independent Laboratory for Selected Soil of RE Wall Backfill Proposed with soil blended with Crusher run / GSB.	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1056	05/10/2020
141	PDJHPL/IC/ICO-181/2020/2348	07/10/2020	Submission of Soil Samples Proposed for Reinforced Fill in RE Wall areas for Conducting Tests (Borrow area 136 at Shyampur Village - Jhalawar District)	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1065	13/10/2020
142	PDJHPL/IC/ICO-181/2020/2359	08/10/2020	Compliance on Review of Test Report for Selected Soil of RE Wall Back Fill Proposed Soil blended with Crusher run / GSB (Borrow Area No. 131).	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1063	13/10/2020
143	PDJHPL/IC/ICO-181/2020/2363	09/10/2020	Submission of Test Report of Selected Soil / Reinforced soil proposed for RE Wall Back fill (B.A No. 134).	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1064	13/10/2020
144	PDJHPL/IC/ICO-181/2020/2375	13/10/2020	Submission of Test Reports of Selected Soil / reinforced Soil proposed for RE Wall Backfill (B/A No. 136).	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1080	23/10/2020
145	PDJHPL/IC/ICO-181/2020/2381	15/10/2020	Submission of Test Report of Selected Soil / Reinforced Soil proposed for RE Wall Back fill (B.A No. 130).	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1088	28/10/2020
146	PDJHPL/IC/ICO-181/2020/2382	15/10/2020	Submission of Test Report of Selected Soil / Reinforced Soil proposed for RE Wall Back fill (B.A No. 131).	LASA/Concessionaire/Darah-Jhalawar/IE/2020/1086	28/10/2020
147	PDJHPL/IC/ICO-181/2020/2385	17/10/2020	Submission of Compliance on Comments made by Independent	LASA/Concessionaire/Darah-	22/10/2020

Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
		Engineer for Source Approval of JSW Steel Ltd.	Jhalawar/IE/2020/1079	
PDJHPL/IC/ICO-181/2020/2386	17/10/2020	Submission of Test Reports (after screening & stocking) of selected Soil / Reinforced Soil Proposed for RE Wall Backfill (B/A No. 130) and compliance on comments by Independent Engineer.	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1088	28/10/2020
PDJHPL/IC/ICO-181/2020/2387	17/10/2020	Submission of Company Profile & Credentials of M/s Rajdeep Info Techno Pvt Ltd for supplying, providing, installing and commissioning of Traffic Management System & Advance Traffic Management System.	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1096	30/10/2020
PDJHPL/IC/ICO-181/2020/2391	19/10/2020	Submission of Test Report of Selected Soil / Reinforced Soil Proposed for RE Wall Backfill (B/A No. 138)	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1084	28/10/2020
PDJHPL/IC/ICO-181/2020/2404	24/10/2020	Submission of Job Mix Formula (JMF) for Bituminous Concrete with VG-40 Grade Bitumen & Plastic Waste.	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1100	02/11/2020
PDJHPL/IC/ICO-181/2020/2411	27/10/2020	Submission of Test report of Selected Soil/Reinforced Soil Proposed for RE Wall Backfill (B/A 141).	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1113	06/11/2020
PDJHPL/IC/ICO-181/2020/2413	28/10/2020	Submission of Test report of Selected Soil / Reinforced Soil Proposed for RE Wall Backfill (B/A No. 131).	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1086	28/10/2020
PDJHPL/IC/ICO-181/2020/2417	02/11/2020	Submission of Test report of Selected Soil / Reinforced Soil Proposed for RE Wall Backfill (B/A No. 141).		
PDJHPL/IC/ICO-181/2020/2465	07/12/2020	Submission of Test Report of Reinforcement Steel.	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1186	18/12/2020
PDJHPL/IC/ICO-181/2020/2472	12/12/2020	Submission of Routine Pile Load Test Report for MJB @ Km 36+070.	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1184	18/12/2020
PDJHPL/IC/ICO-181/2020/2482	12/12/2020	Submission of Company Profile and Credentials of M/s Nayara Energy Ltd (Earlier Known as: Essar Oil Ltd) for Bitumen VG-40 Grade	LASA/Concessionaire/Darah- Jhalawar/IE/2020/1208	30/12/2020
PDJHPL/IC/ICO-181/2021/2516	11/01/2021	Submission of Independent Laboratory Test Reports of Reinforcement Steel, Admixture & Water.	LASA/NHAI/Darah- Jhalawar/IE/2021/1236	15/01/2021
PDJHPL/IC/ICO-181/2021/2519	13/01/2021	Compressive Strength Test Reports of Core taken from PQC.		
PDJHPL/IC/ICO-181/2021/2529	23/01/2021	Submission of Company Profile & Credentials of M/s Reliance Industries Ltd. For Procurement of 'Reliance Recron 3s Fibers' to use in PQC Works.	LASA/NHAI/Darah- Jhalawar/IE/2021/1244	27/01/2021
PDJHPL/IC/ICO-181/2021/2533	25/01/2021	Submission of Compressive Strength Test Reports of Core Taken from PQC during Site Visit of Authority & Independent Engineer.	LASA/NHAI/Darah- Jhalawar/IE/2021/1247	27/01/2021
PDJHPL/IC/ICO-181/2021/2534	25/01/2021	Submission of Test Reports of Compressive Strength of RE Block Collected from Casting Yard of M/s Earthcon during Site Visit of Authority & Independent Engineer.	LASA/NHAI/Darah- Jhalawar/IE/2021/1246	27/01/2021
PDJHPL/IC/ICO-181/2021/2535	25/01/2021	Submission of Test Reports of Reinforcement Steel.	LASA/NHAI/Darah- Jhalawar/IE/2021/1249	28/01/2021
PDJHPL/IC/ICO-181/2021/2546	06/02/2021	Submission of Mix Design of Concrete with Nuvoco Cement & Flyash.	LASA/Concessionaire/Darah- Jhalawar/IE/2021/1273	16/02/2021
PDJHPL/IC/ICO-181/2021/2553	13/02/2021	Submission of Company Profile & Credential of M/s Bajaj Reinforcements LLP for Procurement of 'Fibre' to use in PQC Mix.	LASA/Concessionaire/Darah- Jhalawar/IE/2021/1306	05/03/2021
PDJHPL/IC/ICO-181/2021/2558	17/02/2021	Submission of Company Profile & Credentials of M/s Solucio Infra Solutions Pvt. Ltd for Procurement of 'Retroreflective Traffic Sign Sheeting	LASA/Concessionaire/Darah- Jhalawar/IE/2021/1286	22/02/2021

Sr. no.	Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
			and road safety Furniture Products'		
167	PDJHPL/IC/ICO-181/2021/2559	17/02/2021	Approval of Mix Design of Concrete with Nuvoco Cement & Flyash.		
168	PDJHPL/IC/ICO-181/2021/2572	25/02/2021	Submission of Company Profile & Credential of M/s Logicmo Systems Private Limited for the Work of 'Toll Collection & Management Systems'.	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1313	10/03/2021
169	PDJHPL/IC/ICO-181/2021/2573	25/02/2021	Submission of Optical Fibre Cable (OFC) work methodology & strip map for equipment location (M/s Logicmo Systems Pvt Ltd, Pune, Maharashtra).	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1314	10/03/2021
170	PDJHPL/IC/ICO-181/2021/2578	03/03/2021	Submission of Test Reports of Reinforcement Steel.	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1299	05/03/2021
171	PDJHPL/IC/ICO-181/2021/2579	03/03/2021	Submission of Test Reports of Reinforcement Steel.	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1298	05/03/2021
172	PDJHPL/IC/ICO-181/2021/2582	05/03/2021	Submission of Test Reports of Bitumen VG-40 from M/s Nayara Energy Ltd.	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1309	09/03/2021
173	PDJHPL/IC/ICO-181/2021/2594	15/03/2021	Submission of Test reports of steel & cement.	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1323	17/03/2021
174	PDJHPL/IC/ICO-181/2021/2615	02/04/2021	Submission of Test Report of Mix Design of Concrete with Nuvoco Cement & Flyash	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1363	06/04/2021
175	PDJHPL/IC/ICO-181/2021/2625	08/04/2021	Compliance on Observation of Company Profile and Credentials of 'M/s Logicmo Systems Private Limited' for the work of 'Toll Collection & Management Systems'.	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1380	16/04/2021
176	PDJHPL/IC/ICO-181/2021/2638	12/04/2021	Submission of Mix Design of M-50 Grade of Concrete with Nuvoco Cement & Sika Admixture	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1375	13/04/2021
177	PDJHPL/IC/ICO-181/2021/2640	12/04/2021	Submission of Company Profile and Credentials of 'M/s Logicmo Systems Private Limited' for the work of 'Toll Collection & Management Systems'.	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1380	20/04/2021
178	PDJHPL/IC/ICO-181/2021/2648	20/04/2021	Implementation of ICD 2.5 software & TCMS software along with ICD 2.5 software (M/s Logicmo Systems Private Limited)	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1380	20/04/2021
179	PDJHPL/IC/ICO-181/2021/2650	20/04/2021	Submission of Test Reports of Soil.	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1386	22/04/2021
180	PDJHPL/IC/ICO-181/2021/2694	12/06/2021	Submission of Mix Design of PQC with JK Cement & Sika Admixture	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1470	21/06/2021
181	PDJHPL/IC/ICO-181/2021/2701	18/06/2021	Submission of Test Report of POT-PTFE Bearing & Pin Metallic Guided Bearing of ROB @ Km 44+158 (Non-Railway Portion)		
182	PDJHPL/IC/ICO-181/2021/2705	23/06/2021	Submission of Test Report of HDPE Ducts for TCMS (M/s Logicmo Systems Pvt. Ltd).	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1472	23/06/2021
183	PDJHPL/IC/ICO-181/2021/2708	03/07/2021	Submission of Credentials of M/s RoadShield Pvt Ltd. For Supplying and Erection of Metal Beam Crash Barrier.	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1494	10/07/2021
184	PDJHPL/IC/ICO-181/2021/2713	12/07/2021	Submission of Test Reports of Bitumen Emulsion, Reinforcement Steel & Flyash.	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1501	14/07/2021
185	PDJHPL/IC/ICO-181/2021/2714	12/07/2021	Submission of Test Reports of Reinforcement Steel & Cement.	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1504	15/07/2021
186	PDJHPL/IC/ICO-181/2021/2777	25/08/2021	Submission of Company Profile & Credentials of M/s 3M (India) Ltd for Procurement of Road Stud, Pavement Marker, Solar Stud, Signboards and Delineators.	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1569	28/08/2021

[Handwritten signature]

Outgoing Letter NO.	Date of submission	Description	Approval letter no.	Date of approval
PDJHPL/IC/ICO-181/2021/2778	25/08/2021	Submission of Company Profile & Credentials of M/s 3M (India) Ltd for Procurement of Road Stud, Pavement Marker, Solar Stud, Signboards and Delineators.	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1568	28/08/2021
PDJHPL/IC/ICO-181/2021/2794	06/09/2021	Submission of Test Reports of Reinforcement Steel, Admixture & Water.	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1585	08/09/2021
PDJHPL/IC/ICO-181/2021/2912	29/10/2021	Submission of Test Report of Reinforcement Steel.	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1679	05/11/2021
PDJHPL/IC/ICO-181/2021/2913	29/10/2021	Submission of Test Report of Reinforcement Water	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1682	05/11/2021
PDJHPL/IC/ICO-181/2021/2914	29/10/2021	Submission of Test Report of Reinforcement Pondash	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1680	05/11/2021
PDJHPL/IC/ICO-181/2021/2915	29/10/2021	Submission of Test Report of Reinforcement Pondash	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1681	05/11/2021
PDJHPL/IC/ICO-181/2021/2930	25/11/2021	Regarding Submission of Test Reports of Elastomeric Bearings proposed to be used for Existing Kalisindh Bridge @ Km. 57+127 RHS.	LASA/Concessionaire/D arah- Jhalawar/IE/2021/1701	30/11/2021
PDJHPL/IC/ICO-181/2021/2941	06/12/2021	Submission of Test Report of 24F LT Single Seath Armored FO Cable for ATMS (M/s Logicmo Systems Pvt. Ltd)	LASA/Concessionaire/D arah- Jhalawar/IE/2022/1781	11/02/2022
PDJHPL/IC/ICO-181/2021/2942	09/12/2021	Submission of Test Reports of Variable Message Sign (VMS) for ATMS (M/s Logicmo Systems Pvt. Ltd).	LASA/Concessionaire/D arah- Jhalawar/IE/2022/1783	12/02/2022
PDJHPL/IC/ICO-181/2021/2967	29/12/2021	Review of Test Report of Strip Seal Expansion joint of ROB @ Km. 44+158.	LASA/Concessionaire/D arah- Jhalawar/IE/2022/1738	03/01/2022
PDJHPL/IC/ICO-181/2022/2980	19/01/2022	Submission of Test Reports of Strip Seal Expansion Joints of Existing MJB @ Km 57+127 (RHS).	LASA/Concessionaire/D arah- Jhalawar/IE/2022/1762	31/01/2022
PDJHPL/IC/ICO-181/2022/3006	03/02/2022	Submission of Test Report of PQC Core (M-40) Sample.	LASA/Concessionaire/D arah- Jhalawar/IE/2022/1771	04/02/2022
PDJHPL/IC/ICO-181/2022/3033	23/02/2022	Submission of Test Report of Soil Sample (Reinforced Zone).	LASA/Concessionaire/D arah- Jhalawar/IE/2022/1808	04/03/2022

5. Status of submitted Drawings

Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
			Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
Pipe Culvert	09+925	09+919	Submitted	Submitted	Submitted	Approved	Approved	Approved
			016 D-27.02.18, (075 D-26.06.18), (1029 D-11.05.19)			213 D-15.12.18, (499 D-23.07.19)		
Pipe Culvert	10+425	10+423	Submitted	Submitted	Submitted	Approved	Approved	Approved
			016 D-27.02.18, (075 D-26.06.18), (1029 D-11.05.19)			213 D-15.12.18, (499 D-23.07.19)		
Pipe Culvert	10+595	10+592	Submitted	Submitted	Submitted	Approved	Approved	Approved
			016 D-27.02.18, (075 D-26.06.18), (1029 D-11.05.19)			213 D-15.12.18, (499 D-23.07.19)		
Pipe	10+825	10+824	Submitted	Submitted	Submitted	Approved	Approved	Approved

S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
				Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
	Culvert			016 D-27.02.18, (075 D-26.06.18), (1029 D-11.05.19)			213 D-15.12.18, (499 D-23.07.19)		
5	Pipe Culvert	11+030	11+031	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (075 D-26.06.18), (1029 D-11.05.19)			213 D-15.12.18, (499 D-23.07.19)		
6	Box Culvert	11+605	11+605	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (463 D-20.11.18), (060 D-23.10.18), (899 D-30.03.19)			094 D-15.10.18, (134 D-14.11.18), (515 D-31.07.19)		
7	Vehicle Underpass	12+125	12+125	Submitted	Submitted	Submitted	Approved	Approved	Approved
				018 D-12.03.18, (063 D-17.11.18), (188 D-08.08.19)			(118 D-02.11.18), (123 D-10.11.18), (729 D-07.01.20)		
8	Minor Bridge	12+400	12+380	Submitted	Submitted	Submitted	Approved	Approved	Approved
				138 D-18.07.18, (1210 D-11.07.19), (1321 D-22.08.19)			489 D-17.07.19, (503), (569 D-13.09.19)		
9	Light Vehicle Underpass	12+450	12+450	Submitted	Submitted	Submitted	Not yet approved	Not yet approved	Approved
				016 D-27.02.18, (067 D-22.06.18), (1168 D-22.06.19)			092 D-15.10.18, (322 D-23.02.19)		
10	Box Culvert	13+400	13+400	Submitted	Submitted	Submitted	Not yet approved	Not yet approved	Not yet approved
				016 D-27.02.18, (463 D-20.11.18), (060 D-23.10.18)			094 D-15.10.18, (134 D-14.11.18)		
11	Box Culvert	13+980	13+980	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (463 D-20.11.18), (060 D-23.10.18)			094 D-15.10.18, (134 D-14.11.18), (481 D-11.07.19)		
12	Box Culvert	14+980	14+980	Submitted	Submitted	Submitted	Approved	Approved	Not yet approved
				016 D-27.02.18, (463 D-20.11.18), (060 D-23.10.18)			(056 D-07.09.18), (094 D-15.10.18), (134 D-14.11.18)		
13	VUP	15+725	15+725	Submitted	Submitted	Submitted	Approved	Approved	Approved
				018 D-12.03.18, (188 D-08.08.18)			(056 D-07.09.18)(123 D-10.11.18)		
14	Minor Bridge	16+050	16+060	Submitted	Submitted	Submitted	Approved	Approved	Approved
				138 D-18.07.18, (850 D-15.03.19), (1422 D-25.09.19), (1289 D-08.08.19), (1290 D-08.08.19), (1486 D-21.10.19), (1534 D-09.11.19)			353 D-16.03.19, (394 D-26.04.19), (586 D-27.09.19), (627 D-01.11.19)		
15	Box Culvert	16+600	16+580	Submitted	Submitted	Submitted	Approved	Approved	Not Approved
				016 D-27.02.18, (463 D-20.11.18), (060 D-23.10.18)			(056 D-07.09.18), 094 D-15.10.18, (134 D-14.11.18)		
16	Pipe Culvert	17+320	17+320	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
17	Light Vehicle Underpass	17+353	17+353	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.2018, (67 D-22.06.18), 1168 (D-22.06.2019)			092 D-15.10.18, (348 D-14.03.19)		

S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
				Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
18	Minor Bridge	17+950	17+890	Submitted	Submitted	Submitted	Approved	Approved	Approved
				037 D-07.06.18, (562 D-11.12.18)			394 D-26.04.19		
19	Pipe Culvert	18+210	18+206	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
20	Pipe Culvert	18+810	18+810						
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
21	VUP	19+965	19+930	Submitted	Submitted	Submitted	Not yet approved	Approved	Approved
				018 D-12.03.18, (188 D-08.08.18)			123 D-10.11.18, (747 D-09.01.20)		
22	Pipe Culvert	20+840	20+840	Submitted	Submitted	Submitted	Approved	Approved	Approved
				1377-D-10.09.2019			(1189 D-19.12.2020)		
23	Pipe Culvert	21+150	21+150	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
24	LVUP	21+180	21+183	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (67 D-22.06.18), (1168 D-22.06.19)			092 D-15.10.18 (322 D-23.02.19)		
25	Pipe Culvert	21+700	21+647	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (075 D-26.06.18), (1029 D-11.05.19)			213 D-15.12.18, (499 D-23.07.19)		
26	Pipe Culvert	22+286	22+277	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
27	Box Culvert	22+450	22+450	Submitted	Submitted	Submitted	Not Approved	Not Approved	Not Approved
				016 D-27.02.18, (463 D-20.11.18), (60 D-23.10.18)			(094 D-15.10.18), (134 D-14.11.18)		
28	Pipe Culvert	22+850	22+850	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (075 D-23.07.18), (1029 D-11.05.19), 1565 (D-21.11.19)			213 D-15.12.18, (506 D-26.07.19), (693 D-12.07.19), (698 D-12.12.19)		
29	LVUP	23+065	23+065	Submitted	Submitted	Submitted	Approved	Approved	Approved
				16 D-27.02.18, (067 D-22.06.18), (1168 D-22.06.19)			092 D-15.10.18, (322 D-23.02.19)		
30	Pipe Culvert	23+670	23+666	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18 (75 D-23.07.18) (1029 D-11.05.19)			213 D-15.12.18, (499 D-23.07.19)		
30	LVUP	23+695	23+687	Submitted	Submitted	Submitted	Approved	Approved	Approved
				16 D-27.02.18, (067 D-22.06.18), (1168 D-22.06.19)			092 D-15.10.18, (322 D-23.02.19)		
31	Pipe Culvert	23+950	23+950						
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		

(Signature)
(B. Sankar Mishra)

S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
				Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
32	LVUP	24+547	24+547	Submitted	Submitted	Submitted	Approved	Approved	Approved
				16 D-27.02.18, (067 D-22.06.18), (1168 D-22.06.19)			092 D-15.10.18, (322 D-23.02.19)		
33	Box Culvert	24+610	24+610	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18, (138 D-18.07.18), (388 D-20.10.18), (463 D-20.11.18)			093 D-15.10.18, (482 D-11.07.19) (717 D-28.12.19)		
34	VUP	25+100	25+100	Submitted	Submitted	Submitted	Approved	Approved	Approved
				018 D-12.03.18 (188 D-08.08.18)			(56 D-07.09.18), (123 D-10.11.18)		
35	Box Culvert	25+800	25+800	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18 (463 D-20.11.18), (060 D-23.10.18)			094 D-15.10.18 (134 D-14.11.18) (481 D-11.07.19)		
36	VUP	27+025	27+029	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(56 D-07.09.18), (123 D-10.11.18)		
37	Pipe Culvert	27+050	27+050	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
38	Pipe Culvert	27+600	27+600	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
39	Box Culvert	28+550	28+550	Submitted	Submitted	Submitted	Approved	Approved	Approved
				717 D-01.02.19, (1298 D-13.08.2019), (2470 D-07.12.2020)			(620 D-31.10.2019), (1189 D-19.12.2020)		
40	Box Culvert	29+000	29+000	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18 (463 D-20.11.18) (060 D-23.10.18)			094 D-15.10.18 (134 D-14.11.18) (481 D-11.07.19)		
41	Minor Bridge	29+610	29+600	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18 (138 D-18.07.18) (487 D-26.11.18) (554 D-10.12.18) (006 D-18.01.19)			107 D-29.10.18 (188 D-08.12.18) (233 D-26.12.19)		
42	Box Culvert	29+900	29+900	Submitted	Submitted	Submitted	Approved	Approved	Approved
				016 D-27.02.18 (138 D-18.07.18) (388 D-20.10.18) (463 D-20.11.18)			093 D-15.10.18, (104 D-26.10.18) (482 D-11.07.19) (714 D-28.12.19)		
43	VUP	30+075	30+078	Submitted	Submitted	Submitted	Approved	Approved	Approved
				041 D-12.06.18 (632 D-03.01.19), (1510 D-11.2.19), (1912 D-26.02.20), (1962 D-17.03.20)			479 D-09.07.19 (511 D-29.07.19) (645 D-15.11.19), (756 D-24.01.20), (729, D-07.01.20), (818 D-05.03.2020), (839 D-13.04.20)		
44	Pipe Culvert	30+100	30+100	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
45	Pipe Culvert	31+245	31+245	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
46	Pipe Culvert	31+700	31+700	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-			(1189 D-19.12.2020)		

Handwritten signature

S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
				Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
				16.03.2020)					
47	Pipe Culvert	32+130	32+150	Submitted (1377-D-10.09.2019)	Submitted (1961-D-16.03.2020)	Submitted	Approved (1189 D-19.12.2020)	Approved	Approved
48	Box Culvert	32+050	32+050	Submitted 016 D-27.02.18 (463 D-20.11.18)	Submitted (060 D-23.10.18)	Submitted	Approved (094 D-15.10.18)	Approved (134 D-14.11.18)	Approved (481 D-11.07.19)
49	Pipe Culvert	32+150	32+150	(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
50	Box Culvert	32+300	32+295	Submitted 016 D-27.02.18 (463 D-20.11.18)	Submitted (060 D-23.10.18)	Submitted	Approved (094 D-15.10.18)	Approved (134 D-14.11.18)	Approved (481 D-11.07.19)
51	Minor Bridge	33+000	33+000	Submitted 016 D-27.02.18 (037 D-06.07.18)	Submitted (564 D-11.12.19), (1640 D-10.12.19)	Submitted	Approved 505 (D-26.07.19)	Approved (512 D-30.07.19),	Approved (746 D-16.01.20)
52	Pipe Culvert	33+100	33+100	(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
53	Pipe Culvert	33+300	33+300	(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
54	RUB	33+585	33+585	Submitted	Submitted	Submitted	Approved by RLWY	Approved by RLWY	Approved by RLWY
				019 D-31.05.18 (828)			(1137 D-06.10.19)		
55	Minor Bridge	34+350	34+350	Submitted 016 D-27.02.18, (564 D-11.12.19),	Submitted (1640 D-10.12.19), (1641 D-10.12.19)	Submitted	Approved (505 D-26.07.19), (512 D-30.07.19),	Approved (745 D-16.01.20)	Approved
56	Box Culvert	35+250	35+205	Submitted (093 D-04.07.2018), (463 D-20.11.18),	Submitted	Submitted	Approved (515 D-31.07.19)	Approved	Approved
57	Major Bridge	36+105	36+070	Submitted	Submitted	Submitted	Hold (Compliance on Geotechnical report is already submitted)	Approved	Approved
				(034 D-19.04.18), (014 D-27.02.18), (037 D-07.06.18), (492 D-26.11.18), (014 D-18.03.19), (068 D-12.12.18), (1666&1705 D-27.12.19), (2227 D-24.8.20), (2285 D-15.09.20)			(341 D-03.11.19), (159 D-30.11.19), (174 D-03.12.18), (315 D-23.02.19), (720 D-02.01.2020), (826 D-17.03.20), (1012 D-07.09.20)		
58	Box Culvert	36+750	36+719	Submitted (093 D-04.07.2018), (463 D-20.11.18),	Submitted	Submitted	Not Approved	Not Approved	Not Approved
59	Pipe Culvert	37+040	37+040	1377-D-10.09.2019			(1189 D-19.12.2020)		
60	LVUP	37+050	37+053	Submitted (067 D-22.06.18), (004 D-10.01.19),	Submitted	Submitted	Approved (092 D-15.10.18), (219 D-21.12.19),	Approved	Approved

S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
				Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
				(1168 D-22.06.19)			(348 D-14.03.19)		
61	Box Culvert	37+550	37+550	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(037 D-07.06.18), (463 D-20.11.18),			481 D-11.07.19		
62	Box Culvert	38+100	38+141	Submitted	Submitted	Submitted	Not Approved	Not Approved	Not Approved
				(093 D-04.07.18), (463 D-20.11.18)					
63	Pipe Culvert	38+535	38+535	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
64	LVUP	38+545	38+547	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(067 D-22.06.18), (1168 D-22.06.19)			(092 D-15.10.18), (348 D-14.03.19)		
65	Box Culvert	39+180	39+162	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(037 D-07.06.18), (463 D-20.11.18),			(481 D-11.07.19)		
66	Pipe Culvert	39+570	39+625	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
67	Pipe Culvert	40+200	40+200	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
68	Pipe Culvert	40+600	40+600	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
69	VUP	41+095	41+102	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(041 D-12.06.18), (632 D-03.01.19), (1498 D-24.10.19), (1571 D-22.11.19), (2097 D-06.07.20), (2125 D-16.07.20)			(479 D-09.07.20), (514 D-30.07.19), (517 D-31.07.19), (729 D-07.01.20), (933 D-15.07.20), (949 D-27.07.20), (953 D-28.07.20),		
70	LVUP	41+465	41+468	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(067 D-22.06.18), (005 D-10.01.19), (1168 D-22.06.19)			(092 D-15.10.18), (220 D-21.12.19), (348 D-14.03.19)		
71	Pipe Culvert	41+478	41+481	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
72	Pipe Culvert	41+950	41+917	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
73	Pipe Culvert	42+252	42+252	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
74	LVUP	42+258	42+263	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(067 D-22.06.18), (078 D-05.01.19), (1168 D-22.06.19)			(92 D-15.10.18), (348 D-14.03.19)		
75	Pipe Culvert	42+530	42+552	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-			(1189 D-19.12.2020)		

Handwritten signature

S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
				Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
				16.03.2020)					
76	Pipe Culvert	43+220	43+221	Submitted	Submitted	Submitted	Approved	Approved	Approved
				1377-D-10.09.2019			(1189 D-19.12.2020)		
77	Pipe Culvert	43+680	43+680	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
78	LVUP	43+825	43+670	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(067 D-22.06.18), (377 D-17.10.18), (829 D-06.03.19)			(092 D-15.10.18), (335 D-05.03.19), (729 D-07.01.20)		
79	Box Culvert	44+070	44+070	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1298 D-13.08.19)			(1130 D-12.11.2020)		
80	Rail Over Bridge	44+158	44+158	Submitted	Submitted	Submitted	P-1, P-2 is approved by RLWY & A1 & A-2 (BHS) is approved by IE	P-1, P-2 is approved by RLWY & A1 & A-2 (BHS) is approved by IE	P-1, P-2 is approved by RLWY & A1 & A-2 (BHS) is approved by IE
				(118 D-09.07.18), (550 D-10.12.18), (1355 D-04.09.19), (1397 D-17.09.19), (1570 D-22.11.19)			(7504 D-06.11.18), (572 D-17.09.19), (582 D-26.09.19), (669 D-27.11.19), (797 D-20.02.20), (1038 D-25.09.20)		
81	Minor Bridge	44+900	44+910	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(146 D-23.07.18), (582 D-17.12.18), (608 D-26.12.18)			(225 D-24.12.18), (347 D-14.03.19), (394 D-26.04.19)		
82	Pipe Culvert	45+200	45+200	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(146 D-23.07.18), (075 D-26.06.18), (1029 D-11.05.19)			(499 D-23.07.19)		
83	Pipe Culvert	45+800	45+800	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(037 D-07.06.18), (075 D-26.06.18), (1029 D-11.05.19), (1565 D-21.11.19),			(213 D-15.12.18), (506 D-26.07.19), (693 D-07.12.19), (698 D-12.12.19)		
84	LVUP	45+875	45+876	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(037 D-07.06.18), (067 D-22.06.18), (1168 D-22.06.19)			(092 D-15.10.18), (348 D-14.03.19)		
85	Pipe Culvert	45+875	45+925	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
86	Pipe Culvert	46+650	46+650	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
87	Flyover	46+957	46+900 to 47+000	Submitted	Submitted	Submitted	Not Approved	Not Approved	Not Approved
				(115 D-09.07.18), (431 D-03.11.18),			(328 D-28.02.19), (487 D-15.07.19)		
88	Elevated Highway	47+830	47+830	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(037 D-07.06.18), (003 D-09.01.19),			(284 D-23.01.19)		
89	Pipe Culvert	48+220	48+221	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(146 D-23.07.18), (075 D-26.06.18),			(213 D-15.12.18), (499 D-23.07.19)		

S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
				Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
				(1029 D-11.05.19)					
90	PUP	48+260	48+260	Submitted	Submitted	Submitted	Approved	Approved	Approved
				2181-D-06.08.2020			(1202 D- 29.12.2020)		
91	Pipe Culvert	48+385	48+354	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(146 D-23.07.18), (075 D-26.06.18), (1029 D-11.05.19)			(213 D-15.12.18), (499 D-23.07.19)		
92	Pipe Culvert	48+645	48+654	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(146 D-23.07.18), (075 D-26.06.18), (1029 D-11.05.19)			(213 D-15.12.18), (499 D-23.07.19)		
93	Pipe Culvert	48+875	48+890	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(146 D-23.07.18), (075 D-26.06.18), (1029 D-11.05.19)			(213 D-15.12.18), (499 D-23.07.19)		
94	VUP	49+330	49+330	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(041 D-12.06.19), (632 D-03.01.19), (1499 D-24.10.19), (1571 D-22.11.19), (2097 D-06.07.20), (2125 D-16.07.20)			(479 D-09.07.19), (514 D-30.07.19), (518 D-31.07.19), (639 D-11.11.19), (715 D-28.12.19), (729 D-07.01.20), (950 D-27.07.20), (953 D-28.07.20)		
95	Pipe Culvert	49+290	49+290	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
96	Minor Bridge	49+775	49+785	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(317 D-29.09.18)			(394 D-26.04.19)		
97	Flyover	50+095	50+099	Submitted	Submitted	Submitted	Not Approved	Not Approved	Not Approved
				(115 D-09.07.18), (431 D-03.11.18),			(329 D-28.02.19), (487 D-15.07.19)		
98	PUP	51+450	51+450	Submitted			Approved		
				2204-D-17.08.2020, (2255 D-05.09.2020), (2480 D-16.12.2020)			(1112 D-06.11.2020), (1203 D-29.12.2020)		
99	Pipe Culvert	51+750	51+750	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(037 D-07.06.18), (075 d-26.06.18), (1029 D-11.05.19), (1565 D-21.11.19)			(213 D-15.12.18), (506 D-26.07.19), (693 D-07.12.19), (698 D-12.12.19)		
100	LVUP	51+762	51+774	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(067 D-22.06.18), (1168 D-22.06.19)			(092 D-15.10.18), (348 D-14.03.19)		
101	Pipe Culvert	52+630	52+690	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1377-D-10.09.2019), (1961-D-16.03.2020)			(1189 D-19.12.2020)		
102	Box Culvert	53+125	53+125	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(041 D-12.06.18), (463 D-20.11.18), (1533 D-09.11.19)			(482 D-11.07.19), (714 D-28.12.19)		
103	Box Culvert	53+700	53+700	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(1211 D-11.07.19), (1349 D-03.09.19)			(493 D-19.07.19), (632 D-07.11.19)		
104	Box Culvert	53+900	53+900	Submitted	Submitted	Submitted	Approved	Approved	Approved
				(041 D-12.06.18), (463 D-20.11.18),			(482 D-11.07.19), (714 D-28.12.19)		


S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site	Concessionaire Submission (Letter No.)			Independent Engineer reply/review (Letter No.)		
				Foundation Drawing	Substructure Drawing	Superstructure Drawing	Foundation Drawing	Substructure Drawing	Superstructure Drawing
				(1533 D-09.11.19)					
105	Minor Bridge	54+075	54+072	Submitted (041 D-12.06.18), (191 D-09.08.18), (830 D-06.03.19)	Submitted	Submitted	Approved (336 D-05.03.19), (347 D-14.03.19), (394 D-26.04.19)	Approved	Approved
106	Minor Bridge	54+125	54+040	Submitted (146 D-23.07.18), (763 D-15.02.19), (816 D-01.03.19)	Submitted	Submitted	Approved (314 D-21.02.19), (347 D-14.03.19), (394 D-26.04.19)	Approved	Approved
107	VUP	54+500	54+605	Submitted (041 D-12.06.18), (632 D-03.01.19), (1357 D-04.09.19), (1398 D-17.09.19), (1535 D-09.11.19), (1566 D-21.11.19)	Submitted	Submitted	Approved (565 D-11.09.19), (514 D-30.07.19), (571 D-17.09.19), (729 D-07.01.20)	Approved	Approved
108	Pipe Culvert	54+210	54+210	Submitted (1377-D-10.09.2019), (1961-D- 16.03.2020)	Submitted	Submitted	Approved (1189 D-19.12.2020)	Approved	Approved
109	Pipe Culvert	55+125	54+143	Submitted (146 D-23.07.18), (075 D-26.06.18), (1029 D-11.05.19)	Submitted	Submitted	Approved (213 D-15.12.18), (499 D-23.07.19)	Approved	Approved
110	Box Culvert	55+820	55+830	Submitted (037 D-07.06.18), (463 D-20.11.18),	Submitted	Submitted	Approved (481 D-11.07.19), (1102 D-04.11.2020)	Approved	Approved
111	Major Bridge	57+127	57+127	Submitted	Submitted	Submitted	Hold (Compliance on Geotechnical report is already submitted)	Approved	Approved
				(072 D-25.06.18), (014 D- 27.02.18), (358 D-11.10.18), (492 D- 26.11.18), (578 D-15.12.18), (701 D- 28.01.19), (820 D-02.03.19), (1356 D- 04.09.19), (1434 D-28.09.19), (1465 D- 11.10.19), (1611 D-03.12.19), (1672 D- 18.12.19), (1719 D-31.12.19), (1951 D- 11.03.20), (1559 D-19.11.19), (2227 D- 24.08.20), (2285 D-15.09.20)			(203 D-12.12.18), (081 D-04.09.18), (293 D-28.01.19), (298&299 D- 05.02.19), (316 D-23.02.19), (550 D- 03.09.19), (573 D-17.09.19), (687&692 D-12.07.19), (670 D-29.11.19), (604&607 D-15.10.19), (370&372 D- 03.04.19), (649 D-16.11.19), (826 D- 17.03.20), (657 D-21.11.19), (1012 D- 07.09.20)		
112	Flyover	58+125	58+125	Submitted (115 D-09.07.18), (431 D-03.11.18)	Submitted	Submitted	Approved (330 D-28.02.19), (356 D-19.03.19), (487 D-15.07.19)	Approved	Approved
113	PUP	32+574	32+574	(2439 D-24.11.2020), (2477 D- 15.12.2020)			(1165 D-15.12.2020), (1195 D- 22.12.2020)		
114	PUP / CUP	26+590	26+590	(2788 D-31.08.2021), (2808 D- 09.09.2021)			(1604 D-27.09.2021)		

S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site Condition	Concessionaire Submission (Letter No.)	Independent Engineer reply/review (Letter No.)
1	RE Wall Methodology (Selected Soil)			Submitted (Selected Soil) (1891 D-20.02.20), (1995 D-20.05.20), (2052 D-19.06.20)	Approved [for RE wall (Earthcon)] (860 D-14.05.20), (868 D-27.05.20), (923 D-07.07.20)
	RE Wall Methodology (Pondash)			Submitted (Pondash) (1653 D-13.12.2019), (1829 D-05.02.2020)	Approved [for RE wall (Earthcon)] ((716 D-30.12.2019), (782 D-06.02.2020)
2	RE wall	12+125 & 12+450	12+125 & 12+450	Submitted (Pond Ash) (658 D-12.01.19/RO), (916 D-05.04.19), (1103 D-04.06.19)	Not yet Approved (367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill) (2337 D-01.10.2020), (2422 D-05.11.2020), (2466 D-07.12.2020), (2487 D-23.12.2020)	Not yet Approved (1093 D-29.10.2020), 1118 (D-07.11.2020), (1205 D-29.12.2020)
3	RE wall	15+725	15+725	Submitted (Pond Ash) (200 D-11.08.18/RO), (916 D-05.04.19), (1103 D-04.06.19)	Not yet Approved (367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill) (851 D-15.03.19/R1)	Not yet Approved
4	RE wall	17+353	17+353	Submitted (Pond Ash) (201 D-11.08.18/RO), (916 D-05.04.19), (1103 D-04.06.19)	Not yet Approved (367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill) (851 D-15.03.19/R2), (1929 D-02.03.20)	Not yet Approved
5	RE wall	19+965	19+930	Submitted (Pond Ash) (659 D-12.01.19/RO), (916 D-05.04.19), (1103 D-04.06.19)	Not yet Approved (367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill) (851 D-15.03.19/R1), (2304 D-22.09.20/R2), (2492 D-26.12.2020)	Not yet Approved 1123 (D-11.11.2020), (1209 D-30.12.2020)
6	RE wall	21+180	21+183	Submitted (Pond Ash) (660 D-12.01.19/RO), (935 D-12.04.19/R1), (916 D-05.04.19), (1103 D-04.06.19)	Not yet Approved (367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Not yet submitted (Reinforced fill)	Not yet Approved
7	RE wall	23+065	23+065	Submitted (Pond Ash) (661 D-12.01.19/RO), (971 D-26.04.19/R1)	Not yet Approved (536 D-19.08.19)
				submitted (Reinforced fill) (2304 D-22.09.20/R2), (2492 D-26.12.2020)	Not yet Approved 1123 (D-11.11.2020), (1209 D-30.12.2020)
8	RE wall	23+695	23+687	Submitted (Pond Ash)	Not yet Approved

S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site Condition	Concessionaire Submission (Letter No.)	Independent Engineer reply/review (Letter No.)
				(662 D-12.01.19/RO), (978 D-27.04.19/R1), (916 D-05.04.19), (1103 D-04.06.19) submitted (Reinforced fill)	(367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19) Not yet Approved
				(2304 D-22.09.20/R2), (2492 D-26.12.2020)	1123 (D-11.11.2020), (1209 D-30.12.2020)
9	RE wall	24+547 & 25+100	24+547 & 25+100	Submitted (Pond Ash) (202 D-11.08.18/RO), (916 D-05.04.19), (1103 D-04.06.19)	Not yet Approved (367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill) (851 D-15.03.19/R1)	Not yet Approved
10	RE wall	27+025	27+029	Submitted (Pond Ash) (203 D-11.08.18/RO)	Not yet Approved (367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill) (851 D-15.03.19/R1), (1929 D-02.03.20/R3)	Not yet Approved
11	RE wall	30+075	30+078	Submitted (Pond Ash) (895 D-30.03.19/RO), (Not yet Approved (367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill) (1929 D-02.03.20/R1)	Not yet Approved
12	RE wall	37+050	37+053	Submitted (Pond Ash) (204 D-11.08.18/RO), (851 D-15.03.19/R1)	Not yet Approved (367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill) (1929 D-02.03.20/R4)	Not yet Approved
13	RE wall	38+545	38+547	Submitted (Pond Ash) (205 D-11.08.18/RO), (851 D-15.03.19/R1)	Not yet Approved (367&368 D-02.04.19), (423 D-23.05.19), (664 D-26.11.19)
				Submitted (Reinforced fill) (1929 D-02.03.20/R4)	Not yet Approved
14	RE wall	41+095 & 41+465	41+102 & 41+468	Submitted (Pond Ash) (719 D-01.02.19/P1), (2086 D-02.07.20)	Approved (243 D-01.01.19), (334 D-01.03.19), (367 D-02.04.19), (991 D-26.08.20)
				Submitted (Selected Soil) (536 D-07.12.18/P0), (078 D-05.01.19)	
15	RE wall	42+258	42+263	Submitted (Pond Ash) (720 D-01.02.19/P1), (2086 D-02.07.20)	Approved (243 D-01.01.19), (334 D-01.03.19), (367 D-02.04.19)
				Submitted (Selected Soil) (537 D-07.12.18/P0), (078 D-05.01.19)	

(Signature)
(Deepak Mishra)

S.No	Type of Structure	Chainage as per Schedule "B"	Chainage as per Site Condition	Concessionaire Submission (Letter No.)	Independent Engineer reply/review (Letter No.)
				Submitted (A1-Pondash & A2-selected soil) (2284 D-15.09.20/P3), (2305 D-22.09.20)	Not yet Approved (1026 D-16.09.20), (1128 D-12.11.2020)
16	RE wall	44+158	44+158	Submitted (Pond Ash) (1164 D-21.05.19/P0), (1603 D-30.11.19/P0) Submitted (Reinforced fill) (2087 D-02.07.20/P3), (2108 D-08.07.20), (2248 D-02.09.20/P4), (2314 D-24.09.20), (2412 D-27.10.2020)	Not yet Approved (684 D-04.12.19), (925 D-08.07.20), (940 D-20.07.20), (1021 D-11.09.20), (1140 D-18.11.2020) (1407 D-12.05.2021)
17	RE wall	45+875	45+876	Submitted (Pond Ash) (1000 D-03.05.19/P1), (1606 D-30.11.19/P2) Submitted (Reinforced fill) (2275 D-10.09.20/P3)	Approved (422 D-23.05.19), (688 D-05.12.19) Not yet Approved (1085 D-28.10.2020)
18	RE wall	49+330	49+330	Submitted (Pond Ash) (760 D-14.02.19/P1) Submitted (Reinforced fill) (534 D-07.12.18/P0), (603 D-24.12.18/P0)	Approved (243 D-01.01.19), (334 D-01.03.19), (367 D-02.04.19)
19	RE wall	50+095	50+099	Submitted (Pond Ash) (759 D-14.02.19/P1), (1590 D-27.11.19/P2) Submitted (Reinforced fill) (535 D-07.12.18/P0), (602 D-24.12.18/P0)	Approved (243 D-01.01.19), (331 D-28.02.19), (334 D-01.03.19), (367 D-02.04.19)
20	RE wall	51+762	51+774	Submitted (Pond Ash) (1001 D-03.05.19/P1) (Reinforced fill) (2490 D-26.12.2020)	Approved (416 D-21.05.19) Not yet approved (1216 D-05.01.2021)
21	RE wall	54+500	54+605	Submitted (Pond Ash) (2524 D-20.01.2021)	Not yet approved (1248 D-27.01.2021)
22	RE wall	58+125	58+125	Submitted (Reinforced fill) (2478 D-15.12.2020), (2779 D-25.08.2021), (2820 D-18.09.2021), (2857 D-05.10.2021)	Not yet approved (1192 D-21.12.2020), (1618 D-01.10.2021), (1672 D-05.11.2021),



• Status of Bearing Drawings :

S.No	Chainage	Name of Structure	Type of Bearing	Submission Letter No	Approved vide Letter No	Remarks
1	12+125	VUP	Elastomeric	Letter No. 571 dated 13.12.2018	Letter No. 525 dated 06.08.2019	
2	15+725	VUP	Elastomeric	Letter No. 571 dated 13.12.2018	Letter No. 525 dated 06.08.2019	
3	19+965	VUP	Elastomeric	Letter No. 571 dated 13.12.2018	Letter No. 525 dated 06.08.2019	
4	25+095	VUP	Elastomeric	Letter No. 571 dated 13.12.2018	Letter No. 525 dated 06.08.2019	
5	27+029	VUP	Elastomeric	Letter No. 571 dated 13.12.2018	Letter No. 525 dated 06.08.2019	
6	30+078	VUP	Elastomeric	Letter No. 1511 dated 02.11.2019	Letter No. 650 dated 16.11.2019	
7	41+102	VUP	Elastomeric	Letter No. 1511 dated 02.11.2019	Letter No. 650 dated 16.11.2019	
8	49+330	VUP	Elastomeric	Letter No. 1511 dated 02.11.2019	Letter No. 650 dated 16.11.2019	
9	30+078	VUP	Pin & Guided	Letter No. 1953 dated 11.03.2020	Letter No. 810 dated 02.03.2020	IE observation vide letter no.810 with Marked correction and it complied by Concessionaire vide letter no. 1953
10	36+070	MJB	Elastomeric	Letter No. 1391 dated 16.09.2019	Letter No. 575 dated 18.09.2019	
11	41+102	VUP	Pin & Guided	Letter No. 1953 dated 11.03.2020	Letter No. 810 dated 02.03.2020	IE observation vide letter no.810 with Marked correction and it complied by Concessionaire vide letter no. 1953
12	44+158	ROB	POT / PTFE	Letter No. 1942 dated 06.03.2020	Letter No. 1038 dated 24.09.2020	
13	46+957	Flyover	POT / PTFE	Letter No. 705 dated 28.01.2019	Letter No. 651 dated 16.11.2019	
14	47+830	Elevated Highway	POT / PTFE	Letter No. 972 dated 26.04.2019	Not yet Approved	
15	49+330	VUP	Pin & Guided	Letter No. 1953 dated 11.03.2020	Letter No. 810 dated 02.03.2020	IE observation vide letter no.810 with Marked correction and it complied by Concessionaire vide letter no. 1953
16	50+095	Flyover	POT / PTFE	Letter No. 705 dated 28.01.2019	Letter No. 651 dated 16.11.2019	
17	54+550	VUP	Elastomeric	Letter No. 1357 dated 04.09.2019	Letter No. 565 dated 11.09.2019	
18	57+127	MJB	Free, Pin & Metallic Guided	Letter No. 1465 dated 11.10.2019	Letter No. 649 dated 16.11.2019	

19	57+127	MJB	Elastomeric	Letter No. 2858 dated 05.10.2021	Letter No. 1634 dated 14.10.2021
20	58+128	Flyover	POT / PTFE	Letter No. 705 dated 28.01.2019	Letter No. 651 dated 16.11.2019

DJT – Plan & Profile and Miscellaneous Drawing Status

S.No	Types of Drawing	Availability of Drawings	Submission Status	Approval of Drawings
1	Plan & Profile (MCW)	Available	Submitted by letter no. 079 (28.06.2018) & 106 (06.07.2018)	Approved by IE Letter No.285 (23.01.2019)
2	Plan & Profile (Service Road)	Available	Submitted by letter no. 079 (28.06.2018) & 896 (30.03.2019)	Approved by IE Letter No.966 (11.08.2019)
3	Street Lightning (Electrical plan)	Available	Submitted vide letter no. 2453 D-28.11.2020	Approved by IE Letter No.1197 (23.12.2020)
4	Truck Lay-byes	Available	Submitted by (letter no 990 D-01.05.2019)	Approved by (IE Letter No.1007)
5	Bus bay	Available	Bus Bay Submitted vide (letter no. 1723 01.01.2020)	Bus Bay Approved by IE Letter no. 784 (08.02.2020)
	Bus Shelters	Available	Bus Shelter vide letter no. 2233(26.08.2020)	Not yet approved (IE replied vide letter no. 1013 D-07.09.20), (1143 D-20.11.20)
6	Rest Area	Available	Submitted vide letter no 989 (01.05.2019)	Not yet Approved (IE replied vide letter no. 724 D-04.01.20)
7	Toll Plaza Drawings	Available	Toll Plaza submitted vide letter no. 316 (29.09.2018) & 1370 (07.09.2019)	Approved (IE letter no. 098 D-17.10.2018) & 738 (11.01.2020)
8	Toll Plaza Canopy	Available	Submitted vide Letter no. 1969 (20.03.2020), 2145 (24.07.2020)	Approved (IE letter no. 1045 D-28.09.20)
9	Toll Plaza & Admin Building	Available	Toll Plaza submitted vide letter no. 316 (29.09.2018) & Admin Building submitted vide letter no. 2152 (27.07.2020)	Approved (IE letter no. 1142 D-11.11.20)
10	Traffic Aid Posts	Available	Admin Building submitted vide letter no. 2152 (27.07.2020), 2388 (D-17.10.20)	Not yet Approved (IE replied vide letter no. 1015 D-08.09.20), 1115 (D-06.11.2020)
11	Medical Aid Posts	Available	Admin Building submitted vide letter no. 2152 (27.07.2020), 2388 (D-17.10.20)	Not yet Approved (IE replied vide letter no. 1015 D-08.09.20), 1115 (D-06.11.2020)
12	Vehicle Rescue Posts	Available	Admin Building submitted vide letter no. 2152 (27.07.2020), 2388 (D-17.10.20)	Not yet Approved (IE replied vide letter no. 1015 D-08.09.20), 1115 (D-06.11.2020)
13	Landscaping and Tree Plantation	Available	Tree Plantation Submitted vide letter no. 1457 (09.10.2019).	Approved by IE Letter No. 626 (01.11.2019)

[Handwritten Signature]

14	Typical Crash Barrier of Retaining Wall	Available	Submitted vide letter no. 2397 (21.10.2020)	Approved by IE Letter No. 1104 (04.11.2020)
15	Rain Water Harvesting	Available	Submitted vide letter no. 2104 (08.07.2020)	Approved by IE letter no. 937 (18.07.2020)
16	Median Chute Drain	Available	Submitted vide letter no. 1231 (18.07.2019)	Approved by IE letter no. 936 (17.07.2020)
17	Friction Slab with Crash Barrier	Available	Submitted vide letter no. 1671 (18.12.2019)	Approved by IE letter no. 723 (04.01.2020)
18	Drainage Spout	Available	Submitted vide letter no. 2184 (07.08.2020)	Approved by IE letter no. 979 (19.08.2020) & 981 (20.08.2020)
19	RCC Railing / Parapet Wall	Available	Submitted vide letter no. 549 (10.12.2018)	Approved by IE letter no. 755 (23.01.2020)
20	Crash Barrier & Approach Slab	Available	Submitted vide letter no. 549 (10.12.2018)	Approved by IE letter no. 653 (20.11.2019)
21	Chute Drain & Stone Pitching	Available	Submitted vide letter no. 549 (10.12.2018)	Approved by IE letter no. 1515 (24.07.2021)
22	Wearing Coat	Available	Submitted vide letter no. 549 (10.12.2018)	Not yet Approved
23	Kerb	Available	Submitted vide letter no. 549 (10.12.2018)	Not yet Approved
24	Junction Drawing (Plan)	Available	Submitted vide letter no. 1618 (05.12.2019), (2450 D-28.11.2020)	Approved (Found in order with marked observation IE letter No. 710 D-23.12.2019 & 1180 D-12.12.2020).
25	Signage Plan	Available	Submitted vide letter no. 1699 (26.12.2019)	Approved by IE letter no. 1156 (D- 26.11.2020), (1210 D-31.12.2020)
26	Median Opening	Available	Submitted vide letter no. 1713 (30.12.2019)	Approved by IE letter no. 951 (27.07.2020)
27	L-shaped Retaining wall (4.5m to 5.5m)	Available	Submitted vide letter no. (2426 D-07.11.2020), (2452 D-28.11.20)	Approved by IE letter no. 1171 (08.12.2020)
28	Retaining wall (2m to 10m)	Available	Submitted vide letter no. (1487 D-21.10.2019), (2446 D-28.11.20)	Approved by IE letter no. 1169 (08.12.2020)
29	Crash Barrier details over Retaining wall	Available	Submitted vide letter no. (2397 D-21.10.2020), (2445 D-28.11.20)	Approved by IE letter no. 1170 (08.12.2020)
30	Gantry & Signage Foundation	Available	Submitted vide letter no. 2517 D- 13.01.2021	Approved by IE letter no.1241 (21.01.2021), IE letter no.1447 (02.06.2021)
31	Electric Work Plan	Available	Submitted vide letter no. 2495 D- 30.12.2020	Approved by IE letter no.1234 (14.01.2021)
32	Stair Case of ROB	Available	Submitted vide letter no. 2479 D- 17.12.2020	Approved by IE letter no.1211 (14.01.2021)
33	Strip Seal Expansion Joint for 57+127 MJB	Available	Submitted vide letter no. 2617 D- 03.04.2021	Approved by IE letter no.1382 (20.04.2021)
34	Drawings of TCMS	Available	Submitted vide letter no. 2699 D- 18.06.2021	Approved by IE letter no.1513 (24.07.2021)
35	High Mast	Available	Submitted vide letter no. 2726 D- 19.07.2021	Approved by IE letter no.1514 (24.07.2021)

Amish

35	KM Stone, 200mtr Stone, Boundary Pillar / Guard Post	Available	Submitted vide letter no. 2670 D- 20.05.2021	Approved by IE letter no.1436 (27.05.2021)
36	Poles & their Foundation for ATMS	Available	Submitted vide letter no. 27000 D- 18.06.2021	Approved by IE letter no.1517 (27.07.2021)
37	Drawings of Single Booth & Reversible Booth	Available	Submitted vide letter no. 2716 D- 12.07.2021	Approved by IE letter no.1510 (22.07.2021)
38	Stone Pitching & Chute Drain	Available	Submitted vide letter no. 2723 D- 24.07.2021	Approved by IE letter no.1515 (24.07.2021)
40	Road Delineators	Available	Submitted vide letter no. 2728 D- 24.07.2021	Approved by IE letter no.1522 (28.07.2021)
41	Strip Seal Expansion Joint for ROB	Available	Submitted vide letter no. 2756 D- 16.08.2021	Approved by IE letter no.1559 (20.08.2021)
42	Non Destructive Test & Bridge Load Test Drawing for ROB	Available	Submitted vide letter no. 2745 D- 07.08.2021	Approved by IE letter no.1560 (20.08.2021)
43	Poles & Their Foundation for ATMS	Available	Submitted vide letter no. 2790 D- 04.09.2021	Approved by IE letter no.1590 (14.09.2021)
44	Pedestrian Guard Rail	Available	Submitted vide letter no. 2795 D- 06.09.2021	Approved by IE letter no.1584 (07.09.2021)
45	Overhead & Cantilever Gantry	Available	Submitted vide letter no. 2796 D- 06.09.2021	Approved by IE letter no.1606 (28.09.2021)
46	Public Toilet at Truck Lay bye Location	Available	Submitted vide letter no. 2819 D- 18.09.2021	Approved by IE letter no.1607 (28.09.2021)
47	Pole of Compact VMS Cantilever Gantry (M/s Logicmo Systems Pvt Ltd)	Available	Submitted vide letter no. 2818 D- 18.09.2021	Approved by IE letter no.1603 (27.09.2021)
48	Gap Slab of Flyover at Km 58+128	Available	Submitted vide letter no. 2820 D- 18.09.2021	Approved by IE letter no.1618 (01.10.2021)
49	Road Delineator	Available	Submitted vide letter no. 2890 D- 18.10.2021	Approved by IE letter no.1642 (20.10.2021)
50	Toll Plaza Sign Board	Available	Submitted vide letter no. 2981 D- 19.01.2022	Approved by IE letter no.1766 (03.02.2022)
51	Major and Minor Junction	Available	Submitted vide letter no. 2833 D- 25.09.2021	Approved by IE letter no.1697 (26.11.2021)
52	Road Studs	Available	Submitted vide letter no. 2842 D- 29.09.2021	Approved by IE letter no.1676 (05.11.2021)
	Load Test Arrangement Drawings			
50	Non Destructive Test & Bridge Load Test Drawing for VUP 12+125	Available	Submitted vide letter no. 2896 D- 22.10.2021	Approved by IE letter No.1658 (29.10.2021)
51	Non Destructive Test & Bridge Load Test Drawing for VUP 15+725	Available	Submitted vide letter no. 2897 D- 22.10.2021	Approved by IE letter No.1659 (29.10.2021)

Amistm

52	Non Destructive Test & Bridge Load Test Drawing for VUP 19+965	Available	Submitted vide letter no. 2898 D- 22.10.2021	Approved by IE letter No.1660 (29.10.2021)
53	Non Destructive Test & Bridge Load Test Drawing for VUP 25+100	Available	Submitted vide letter no. 2899 D- 22.10.2021	Approved by IE letter No.1661 (29.10.2021)
54	Non Destructive Test & Bridge Load Test Drawing for VUP 27+025	Available	Submitted vide letter No. 2900 D- 22.10.2021	Approved by IE letter No.1662 (29.10.2021)
55	Non Destructive Test & Bridge Load Test Drawing for VUP 30+078	Available	Submitted vide letter no. 2847 D- 01.10.2021	Approved by IE letter no.1624 (07.10.2021)
56	Non Destructive Test & Bridge Load Test Drawing for VUP 41+102	Available	Submitted vide letter no. 2869 D- 09.10.2021	Approved by IE letter no.1644 Dt. 20.10.2021 & 1689 Dt. 20.11.2021
57	Non Destructive Test & Bridge Load Test Drawing for VUP 49+330	Available	Submitted vide letter no. 2848 D- 01.10.2021	Approved by IE letter no.1611 (29.09.2021)
58	Non Destructive Test & Bridge Load Test Drawing for VUP 54+500	Available	Submitted vide letter no. 2901 D- 22.10.2021	Approved by IE letter no.1654 Dt. 28.10.2021 & 1686 dt. 11.11.2021.
59	Non Destructive Test & Bridge Load Test Drawing for FOB 46+950	Available	Submitted vide letter no. 2870 D- 09.10.2021	Approved by IE letter no.1644 (20.10.2021)
60	Non Destructive Test & Bridge Load Test Drawing for FOB 50+095	Available	Submitted vide letter no. 2871 D- 09.10.2021	Approved by IE letter no.1656 (29.10.2021)
61	Non Destructive Test & Bridge Load Test Drawing for FOB 58+125	Available	Submitted vide letter no. 2895 D- 22.10.2021	Approved by IE letter no.1657 (29.10.2021)
62	Non Destructive Test & Bridge Load Test Drawing for MJB 36+070	Available	Submitted vide letter no. 2881 D- 13.10.2021	Approved by IE letter no.1645 (20.10.2021)
63	Non Destructive Test & Bridge Load Test Drawing for MJB 57+127	Available	Submitted vide letter no. 2845 D- 01.10.2021	Approved by IE letter no.1620 (05.10.2021)
64	Non Destructive Test & Bridge Load Test Drawing for ROB Km. 44+158	Available	Submitted vide letter no. 2849 D- 01.10.2021	Approved by IE letter no.1675 (05.11.2021)
65	Non Destructive Test & Bridge Load Test Drawing for Elevated Km. 47+830	Available	Submitted vide letter no. 2880 D- 13.10.2021	Approved by IE letter no.1674 (05.11.2021)

12. Mobilization of Manpower

Name of the Employee	Designation	Department
Atul Kumar Mishra	Sr. Project Manager	Technical
Shubhash Kumar	Dy. General Manager	Mechanical
Ajay Kumar Mahto	Asst. Manager	Mechanical
Praveen Kahar	Manager	Liasion
Balram Singh Shekhawat	Manager	Liasion
Shiv Kumar	Dy. Project Manager	Technical (Highway)
Deepak Kumar Mishra	Asst. Manager	Planning & Billing
Ravi Kumar	Asst. Manager (HR & Admin)	HR & Admin
Mahesh Pandey	Manager (Road)	Highway
Rajesh Rawal	Dy. Project Manager	QA/QC
Mukesh Kumawat	Dy. Project Manager	Structure
Kuldeep Singh	Sr.Surveyor	Survey
Ravi Kishore Pandey	Asst Manager.Accountant	Finance & Accounts
Rajan Upadhyay	Dy. Project Manager	Health & Safety
HR & ADMIN DEPARTMENT		
Ast. Manager	01 No	HR & Admin
Executive	02 Nos	HR & Admin
Ast.Executive	01 Nos	HR & Admin
Office Boy	04 Nos	HR & Admin
PLANNING & BILLING DEPARTMENT		
Sr.Engineer	01 Nos	Planning & Billing
Engineer	02 Nos	Planning & Billing
Asst. Engineer	01 Nos	Planning & Billing
QA/QC DEPARTMENT		
Lab Asst.	01 Nos	QA/QC
Asst.Lab Technician	02 Nos	QA/QC
Lab Technician	06 Nos	QA/QC
Sr. Engineer	01 No	QA/QC
Engineer	01 No	QA/QC
Jr.Engineer	01 Nos	QA/QC
HIGHWAY DEPARTMENT		
Sr. Engineer	01 Nos	Highway
Engineer	05 Nos	Highway
Asst. Engineer	10 Nos	Highway
Jr.Engineer	15 Nos	Highway
Sr. Supervisor	03 Nos	Highway
Supervisor	22 Nos	Highway
STRUCTURE DEPARTMENT		
Sr. Engineer	01 Nos	Structure
Asst. Engineer	06 Nos	Structure
Jr.Engineer	04 Nos	Structure

Supervisor	04 Nos	Structure
SURVEY DEPARTMENT		
Sr. Surveyor	03 Nos	Survey
Surveyor	09 Nos	Survey
Jr. Surveyor	02 Nos	Survey
STORE DEPARTMENT		
Sr. Executive	01 Nos	Store
Jr. Executive	12 Nos	Store
Executive	03 Nos	Store
HEALTH & SAFETY DEPARTMENT		
Dy. Manager	01 Nos	Health & Safety
Sr. Executive	01 Nos	Health & Safety
Executive	01 Nos	Health & Safety
Safety officer	03 Nos	Health & Safety
Supervisor	02 Nos	Health & Safety
IT DEPARTMENT		
Sr. Executive	02 Nos	IT
MECHANICAL DEPARTMENT		
Sr. Engineer	01 Nos	Mechanical
Supervisor	04 Nos	Mechanical
Engineer	01 Nos	Mechanical
Executive	02 Nos	Mechanical
Asst. Mechanic	03 Nos	Mechanical
Fitter	01 Nos	Mechanical
Tyre Fitter	04 Nos	Mechanical
Driver	170 Nos	Mechanical
Operator / Helper/ Mechanic	180 Nos	Mechanical
S & V		
Asst Manager	01 No	S & V
Sr. Officer	01 No	S & V

Amir

13. Mobilization of Resources (Plant and Machineries)

DETAILS OF MACHINERY			
S.No	Name of Machinery	TOTAL	Remarks
1	Excavator	15	
2	Hywa/Tipper	73	
3	Soil Compactor	9	
4	Dozer	1	
5	Water Tanker	12	
6	Diesel Dispenser	4	
7	Grader	10	
8	Loader	9	
9	Back Hoe	9	
10	Transit Mixer	16	
11	Crusher	4	
12	Concrete Batching Plant	2	
13	Weigh Bridge	4	
14	WMM Plant	1	
15	Hydra Crane	8	
16	Hot Mix Plant	1	
17	Concrete Pump	1	
18	Sand Classifier	1	
19	Tractor	14	
20	Tower Light	9	
21	DG Set	14	
22	Light Vehicle	34	
23	Trailer	4	
24	JCB	3	
25	Boom Placer	0	
26	Tandem Roller	4	
27	Baby Roller	3	
28	Mobile Service Van	2	
29	DLC Paver	2	
30	Automatic PQC Paver	1	
31	Kerb Paver	3	
32	Chilling Plant	1	
33	Bus	1	
34	Fork Lift	0	
35	Block Casting Machine	0	
36	Ambulance Van	1	
37	Tempo	2	
38	Milling Machine	1	
39	Recovery Crane	1	
	TOTAL====>>	280	

Deepak Mishra
Deepak Mishra

14. Site Progress Photo



Km. 27+700

Night view of Toll Plaza Administrative Building

LHS



Km. 27+600

Toll Plaza Administrative Building

LHS



Km. 44+500

BC Laying

RHS



Km. 15+400

Plinth Beam of Visitor Block (Rest Area) is complete

Handwritten signature



Km. 33+585 RUB

RUB Box Pushing and Relieving Girder
Checked by Railway Representatives




Km. 33+585 RUB

RUB Box Pushing and Relieving
Girder Checked by Railway
Representatives

Handwritten signature in blue ink.



Km. 24+500	Sign Board Installation at Project Site	---
------------	---	-----

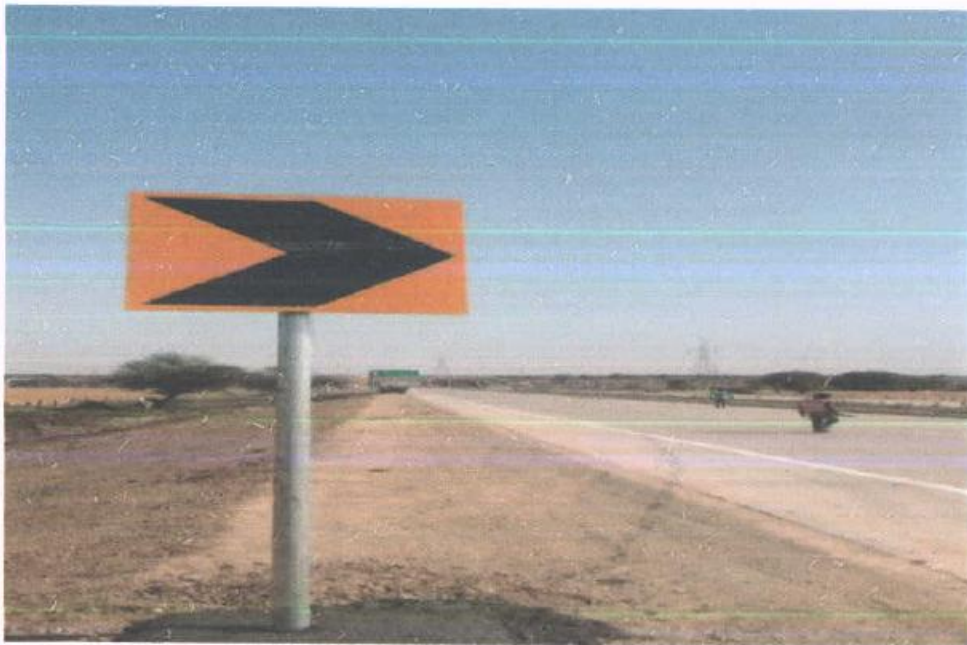

Km. 33+250	Sign Board Installation at Project Site	---
------------	---	-----



 Anisims
 (Aulpak mishi)



Km. 27+700

Toll Sign Board Installed at
Toll Plaza



Km. 44+370

DLC Laying

RHS


Handwritten signature



Km. 26+950

Manual PQC Laying

LHS

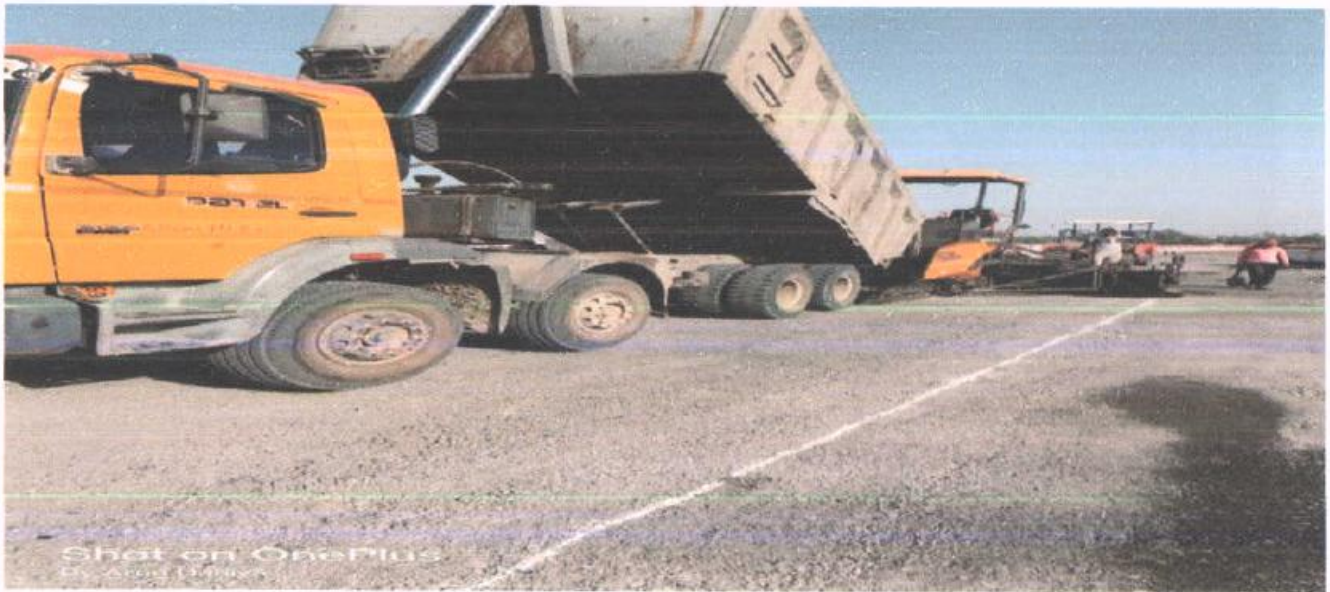

Km. 44+680

DLC Laying

LHS

Finishes



Mar 28, 2022 5:31:27 PM
Suket
Kota
Rajasthan

Breaker Marking at Suket-Kota Road



Km. 27+700

Toll Sign Board at A-2 Side of
Toll Plaza

RHS

Handwritten signature



Km. 12+450

Road Marking

LHS



Km. 9+860

Merging Road Marking

Handwritten signature



Km. 9+860

Road Marking



Km. 26+570 to
Km. 27+480

RE Wall Kerb Laying

LHS

Handwritten signature



Km. 54+540

BC Laying

LHS



Km. 44+700

BC Laying

RHS



Km. 44+840

Manual PQC Laying

LHS



Km. 27+700

Landers Visit at Toll Plaza


Handwritten signature



Km. 23+020 to
Km. 23+400

Road Marking

RHS

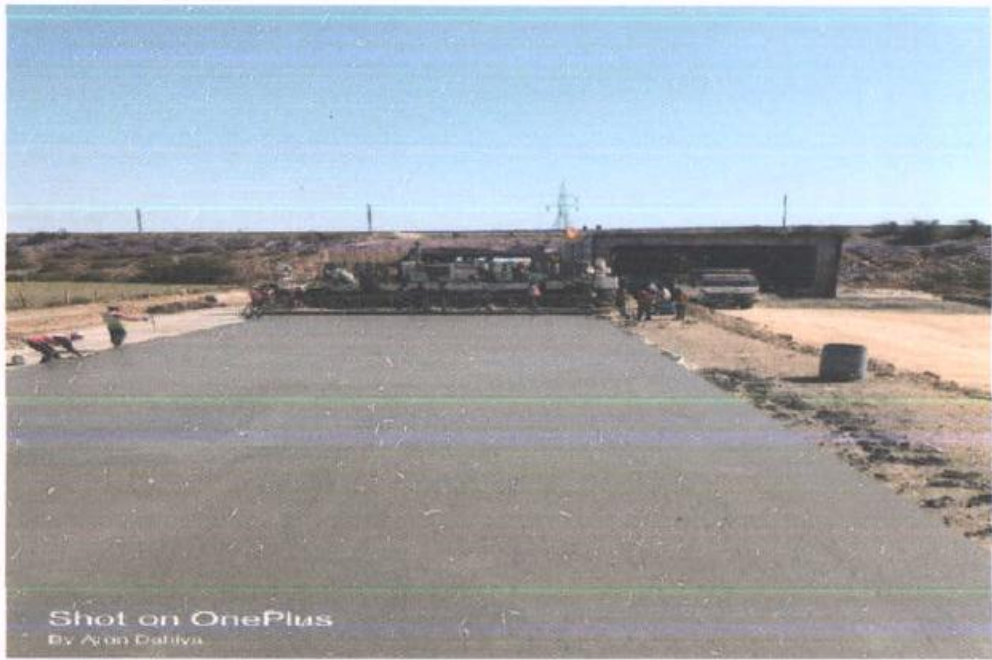

Km. 33+500

PQC Laying

LHS



Km. 44+158 ROB

A2a Gap Slab Curing

RHS



Km. 33+000 to
Km. 33+360

Road Marking

RHS

S - CURVE OF FINANCIAL PROGRESS AS PER SUBMITTED PROPOSAL

MONTH	Jan-18	Feb-18	Mar-18	Apr-18	May-18	Jun-18	Jul-18	Aug-18	Sep-18	Oct-18	Nov-18	Dec-18	Jan-19	Feb-19	Mar-19	Apr-19	May-19	Jun-19	Jul-19	Aug-19	Sep-19	Oct-19	Nov-19	Dec-19	Jan-20	Feb-20	Mar-20	Apr-20	May-20	Jun-20	Jul-20	Aug-20	Sep-20	Oct-20	Nov-20	Dec-20	Jan-21	Feb-21	Mar-21	Apr-21	May-21	Jun-21	Jul-21	Aug-21	Sep-21	Oct-21	Nov-21	Dec-21	Jan-22	Feb-22	Mar-22	Apr-22	May-22	Jun-22	Jul-22	Aug-22	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23	Mar-23	Apr-23	May-23	Jun-23	Jul-23	Aug-23	Sep-23	Oct-23	Nov-23	Dec-23	Jan-24	Feb-24	Mar-24	Apr-24	May-24	Jun-24	Jul-24	Aug-24	Sep-24	Oct-24	Nov-24	Dec-24	Jan-25	Feb-25	Mar-25	Apr-25	May-25	Jun-25	Jul-25	Aug-25	Sep-25	Oct-25	Nov-25	Dec-25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
																																																																																																	Revenue	Cost	Profit																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
Revenue	1230	1500	1700	1900	2100	2300	2500	2700	2900	3100	3300	3500	3700	3900	4100	4300	4500	4700	4900	5100	5300	5500	5700	5900	6100	6300	6500	6700	6900	7100	7300	7500	7700	7900	8100	8300	8500	8700	8900	9100	9300	9500	9700	9900	10100	10300	10500	10700	10900	11100	11300	11500	11700	11900	12100	12300	12500	12700	12900	13100	13300	13500	13700	13900	14100	14300	14500	14700	14900	15100	15300	15500	15700	15900	16100	16300	16500	16700	16900	17100	17300	17500	17700	17900	18100	18300	18500	18700	18900	19100	19300	19500	19700	19900	20100	20300	20500	20700	20900	21100	21300	21500	21700	21900	22100	22300	22500	22700	22900	23100	23300	23500	23700	23900	24100	24300	24500	24700	24900	25100	25300	25500	25700	25900	26100	26300	26500	26700	26900	27100	27300	27500	27700	27900	28100	28300	28500	28700	28900	29100	29300	29500	29700	29900	30100	30300	30500	30700	30900	31100	31300	31500	31700	31900	32100	32300	32500	32700	32900	33100	33300	33500	33700	33900	34100	34300	34500	34700	34900	35100	35300	35500	35700	35900	36100	36300	36500	36700	36900	37100	37300	37500	37700	37900	38100	38300	38500	38700	38900	39100	39300	39500	39700	39900	40100	40300	40500	40700	40900	41100	41300	41500	41700	41900	42100	42300	42500	42700	42900	43100	43300	43500	43700	43900	44100	44300	44500	44700	44900	45100	45300	45500	45700	45900	46100	46300	46500	46700	46900	47100	47300	47500	47700	47900	48100	48300	48500	48700	48900	49100	49300	49500	49700	49900	50100	50300	50500	50700	50900	51100	51300	51500	51700	51900	52100	52300	52500	52700	52900	53100	53300	53500	53700	53900	54100	54300	54500	54700	54900	55100	55300	55500	55700	55900	56100	56300	56500	56700	56900	57100	57300	57500	57700	57900	58100	58300	58500	58700	58900	59100	59300	59500	59700	59900	60100	60300	60500	60700	60900	61100	61300	61500	61700	61900	62100	62300	62500	62700	62900	63100	63300	63500	63700	63900	64100	64300	64500	64700	64900	65100	65300	65500	65700	65900	66100	66300	66500	66700	66900	67100	67300	67500	67700	67900	68100	68300	68500	68700	68900	69100	69300	69500	69700	69900	70100	70300	70500	70700	70900	71100	71300	71500	71700	71900	72100	72300	72500	72700	72900	73100	73300	73500	73700	73900	74100	74300	74500	74700	74900	75100	75300	75500	75700	75900	76100	76300	76500	76700	76900	77100	77300	77500	77700	77900	78100	78300	78500	78700	78900	79100	79300	79500	79700	79900	80100	80300	80500	80700	80900	81100	81300	81500	81700	81900	82100	82300	82500	82700	82900	83100	83300	83500	83700	83900	84100	84300	84500	84700	84900	85100	85300	85500	85700	85900	86100	86300	86500	86700	86900	87100	87300	87500	87700	87900	88100	88300	88500	88700	88900	89100	89300	89500	89700	89900	90100	90300	90500	90700	90900	91100	91300	91500	91700	91900	92100	92300	92500	92700	92900	93100	93300	93500	93700	93900	94100	94300	94500	94700	94900	95100	95300	95500	95700	95900	96100	96300	96500	96700	96900	97100	97300	97500	97700	97900	98100	98300	98500	98700	98900	99100	99300	99500	99700	99900	100100	100300	100500	100700	100900	101100	101300	101500	101700	101900	102100	102300	102500	102700	102900	103100	103300	103500	103700	103900	104100	104300	104500	104700	104900	105100	105300	105500	105700	105900	106100	106300	106500	106700	106900	107100	107300	107500	107700	107900	108100	108300	108500	108700	108900	109100	109300	109500	109700	109900	110100	110300	110500	110700	110900	111100	111300	111500	111700	111900	112100	112300	112500	112700	112900	113100	113300	113500	113700	113900	114100	114300	114500	114700	114900	115100	115300	115500	115700	115900	116100	116300	116500	116700	116900	117100	117300	117500	117700	117900	118100	118300	118500	118700	118900	119100	119300	119500	119700	119900	120100	120300	120500	120700	120900	121100	121300	121500	121700	121900	122100	122300	122500	122700	122900	123100	123300	123500	123700	123900	124100	124300	124500	124700	124900	125100	125300	125500	125700	125900	126100	126300	126500	126700	126900	127100	127300	127500	127700	127900	128100	128300	128500	128700	128900	129100	129300	129500	129700	129900	130100	130300	130500	130700	130900	131100	131300	131500	131700	131900	132100	132300	132500	132700	132900	133100	133300	133500	133700	133900	134100	134300	134500	134700	134900	135100	135300	135500	135700	135900	136100	136300	136500	136700	136900	137100	137300	137500	137700	137900	138100	138300	138500	138700	138900	139100	139300	139500	139700	139900	140100	140300	140500	140700	140900	141100	141300	141500	141700	141900	142100	142300	142500	142700	142900	143100	143300	143500	143700	143900	144100	144300	144500	144700	144900	145100	145300	145500	145700	145900	146100	146300	146500	146700	146900	147100	147300	147500	147700	147900	148100	148300	148500	148700	148900	149100	149300	149500	149700	149900	150100	150300	150500	150700	150900	151100	151300	151500	151700	151900	152100	152300	152500	152700	152900	153100	153300	153500	153700	153900	154100	154300	154500	154700	154900	155100	155300	155500	155700	155900	156100	156300	156500	156700	156900	157100	157300	157500	157700	157900	158100	158300	158500	158700	158900	159100	159300	159500	159700	159900	160100	160300	160500	160700	160900	161100	161300	161500	161700	161900	162100	162300	162500	162700	162900	163100	163300	163500	163700	163900	164100	164300	164500	164700	164900	165100	165300	165500	165700	165900	166100	166300	166500	166700	166900	167100	167300	167500	167700	167900	168100	168300	168500	168700	168900	169100	169300	169500	169700	169900	170100	170300	170500	170700	170900	171100	171300	171500	171700	171900	172100	172300	172500	172700	172900	173100	173300	173500	173700	173900	174100	174300	174500	174700	174900	175100	175300	175500	175700	175900	176100	176300	176500	176700	176900	177100	177300	177500	177700	177900	178100	178300	178500	178700	178900	179100	179300	179500	179700	179900	180100	180300	180500	180700	180900	181100	181300	181500	181700	181900	182100	182300	182500	182700	182900	183100	183300	183500	183700	183900	184100	184300	184500	184700	184900	185100	185300	185500	185700	185900	186100	186300	186500	186700	186900	187100	187300	187500	187700	187900	188100	188300	188500	188700	188900	189100	189300	189500	189700	189900	190100	190300	190500	190700	190900	191100	191300	191500	191700	191900	192100	192300	192500	192700	192900	193

Strip Chart

Darrah-Jhalawar-Teendhar section

C & G	Length	48.755Km
EMB	Length	45.82Km
SG	Length	45.82Km
GSB	Length	45.819Km
DLC	Length	45.320Km
PQC	Length	45.320Km

LHS		9800	
Chainage		9900	
C&G		10000	
EMB		10100	
SG		10200	
GSB		10300	
DLC		10400	
PQC		10500	
		10600	
		10700	
		10800	
		10900	
		11000	
		11100	
		11200	
		11300	
		11400	
		11500	
		11600	
		11700	
		11800	
		11900	
		12000	
		12100	
		12200	
		12300	
		12400	
		12500	
		12600	
		12700	
		12800	
		12900	
		13000	
		13100	
		13200	
		13300	
		13400	
		13500	
		13600	
		13700	
		13800	
		13900	
		14000	
		14100	
		14200	
		14300	
		14400	
		14500	

LHS		14500	
Chainage		14600	
C&G		14700	
EMB		14800	
SG		14900	
GSB		15000	
DLC		15100	
PQC		15200	
		15300	
		15400	
		15500	
		15600	
		15700	
		15800	
		15900	
		16000	
		16100	
		16200	
		16300	
		16400	
		16500	
		16600	
		16700	
		16800	
		16900	
		17000	
		17100	
		17200	
		17300	
		17400	
		17500	
		17600	
		17700	
		17800	
		17900	
		18000	
		18100	
		18200	
		18300	
		18400	
		18500	
		18600	
		18700	
		18800	
		18900	
		19000	
		19100	
		19200	

LHS		19200	
Chainage		19300	
C&G		19400	
EMB		19500	
SG		19600	
GSB		19700	
DLC		19800	
PQC		19900	
		20000	
		20100	
		20200	
		20300	
		20400	
		20500	
		20600	
		20700	
		20800	
		20900	
		21000	
		21100	
		21200	
		21300	
		21400	
		21500	
		21600	
		21700	
		21800	
		21900	
		22000	
		22100	
		22200	
		22300	
		22400	
		22500	
		22600	
		22700	
		22800	
		22900	
		23000	
		23100	
		23200	
		23300	
		23400	
		23500	
		23600	
		23700	
		23800	
		23900	



Index	C & G Length 48.755Km	EMB Length 45.82Km	SG Length 45.82Km	GSB Length 45.819Km	DLC Length 45.320Km	PQC Length 45.320Km
-------	--------------------------	-----------------------	----------------------	------------------------	------------------------	------------------------

Index	C & G Length 48.755Km	EMB Length 45.82Km	SG Length 45.82Km	GSB Length 45.819Km	DLC Length 45.320Km	PQC Length 45.320Km
-------	--------------------------	-----------------------	----------------------	------------------------	------------------------	------------------------

Index	C & G Length 48.755Km	EMB Length 45.82Km	SG Length 45.82Km	GSB Length 45.819Km	DLC Length 45.320Km	PQC Length 45.320Km
-------	--------------------------	-----------------------	----------------------	------------------------	------------------------	------------------------

Index	C & G Length 48.755Km	EMB Length 45.82Km	SG Length 45.82Km	GSB Length 45.819Km	DLC Length 45.320Km	PQC Length 45.320Km
-------	--------------------------	-----------------------	----------------------	------------------------	------------------------	------------------------

Index	C & G Length 48.755Km	EMB Length 45.82Km	SG Length 45.82Km	GSB Length 45.819Km	DLC Length 45.320Km	PQC Length 45.320Km
-------	--------------------------	-----------------------	----------------------	------------------------	------------------------	------------------------

Index	C & G Length 48.755Km	EMB Length 45.82Km	SG Length 45.82Km	GSB Length 45.819Km	DLC Length 45.320Km	PQC Length 45.320Km
-------	--------------------------	-----------------------	----------------------	------------------------	------------------------	------------------------

PQC	38000	38100	38200	38300	38400	38500	38600	38700	38800	38900	39000	39100	39200	39300	39400	39500	39600	39700	39800	39900	40000	40100	40200	40300	40400	40500	40600	40700	40800	40900	41000	41100	41200	41300	41400	41500	41600	41700	41800	41900	42000	42100	42200	42300	42400	42500	42600	42700							
LHS																																																							
RHS																																																							
Chainage																																																							
C&G																																																							
EMB																																																							
SG																																																							
GSB																																																							
DLC																																																							
PQC																																																							

PQC	42700	42800	42900	43000	43100	43200	43300	43400	43500	43600	43700	43800	43900	44000	44100	44200	44300	44400	44500	44600	44700	44800	44900	45000	45100	45200	45300	45400	45500	45600	45700	45800	45900	46000	46100	46200	46300	46400	46500	46600	46700	46800	46900	47000	47100	47200	47300	47400								
LHS																																																								
RHS																																																								
Chainage																																																								
C&G																																																								
EMB																																																								
SG																																																								
GSB																																																								
DLC																																																								
PQC																																																								

PQC	47400	47500	47600	47700	47800	47900	48000	48100	48200	48300	48400	48500	48600	48700	48800	48900	49000	49100	49200	49300	49400	49500	49600	49700	49800	49900	50000	50100	50200	50300	50400	50500	50600	50700	50800	50900	51000	51100	51200	51300	51400	51500	51600	51700	51800	51900	52000	52100								
LHS																																																								
RHS																																																								
Chainage																																																								
C&G																																																								
EMB																																																								
SG																																																								
GSB																																																								
DLC																																																								
PQC																																																								




	Length	40.54Km	Length	45.82Km	Length	45.819Km	Length	45.320Km	Length	45.320Km
POC										
DLC										
GSB										
SG										
EMB										
C&G										
Chainage										
C&G		52100								56800
EMB		52200								56700
SG		52300								56600
GSB		52400								56500
DLC		52500								56400
POC		52600								56300
		52700								56200
		52800								56100
		52900								56000
		53000								55900
		53100								55800
		53200								55700
		53300								55600
		53400								55500
		53500								55400
		53600								55300
		53700								55200
		53800								55100
		53900								55000
		54000								54900
		54100								54800
		54200								54700
		54300								54600
		54400								54500

	Length	45.320Km	Length	45.320Km	Length	45.320Km	Length	45.320Km
POC								
DLC								
GSB								
SG								
EMB								
C&G								
Chainage								
C&G		56800						
EMB		56900						
SG		57000						
GSB		57100						
DLC		57200						
POC		57300						
		57400						
		57500						
		57600						
		57700						
		57800						
		57900						
		58000						
		58100						
		58200						
		58300						
		58400						
		58500						
		58600						
		58700						
		58800						

End of Project




BOX CULVERT 11+605

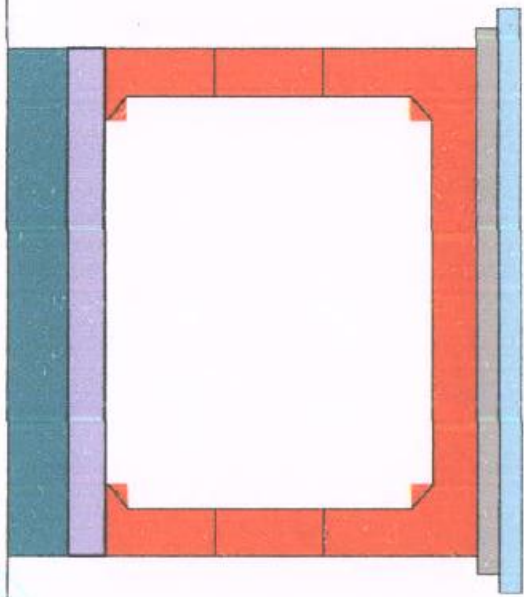


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation

BOX CULVERT 13+400

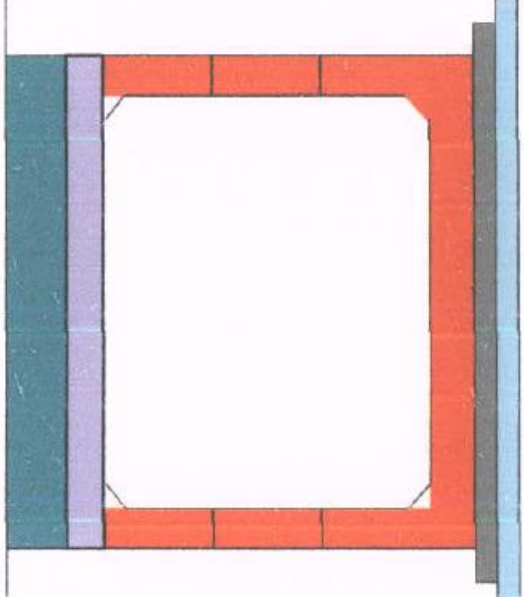


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation

BOX CULVERT 13+980

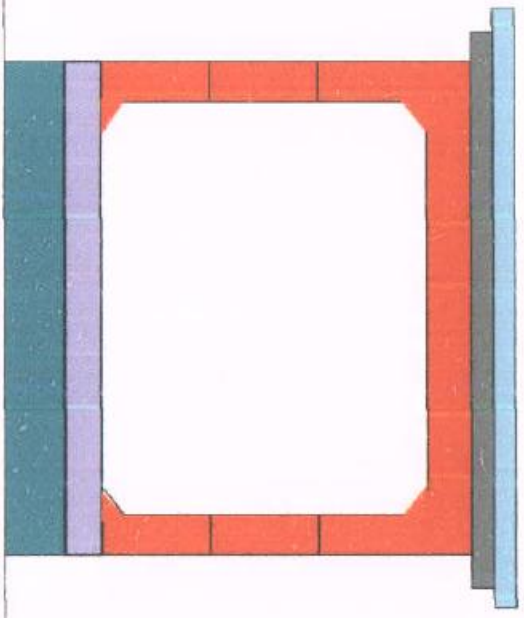


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation

BOX CULVERT 14+980

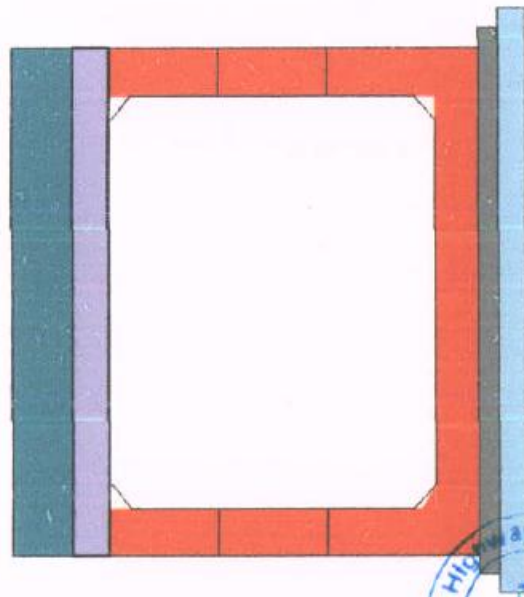


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation

BOX CULVERT 16+600

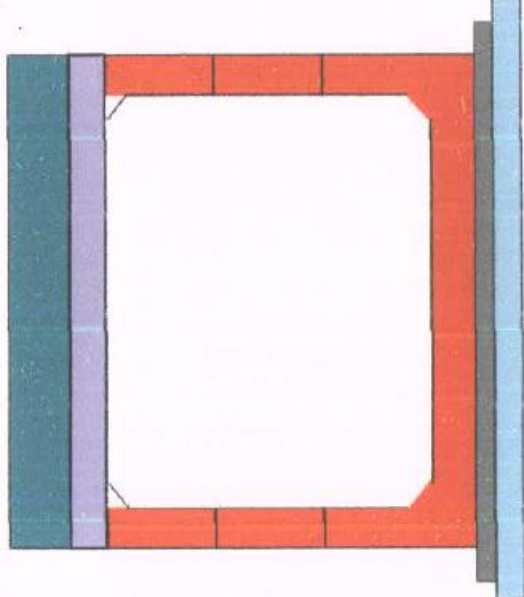

CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation

BOX CULVERT 22+450

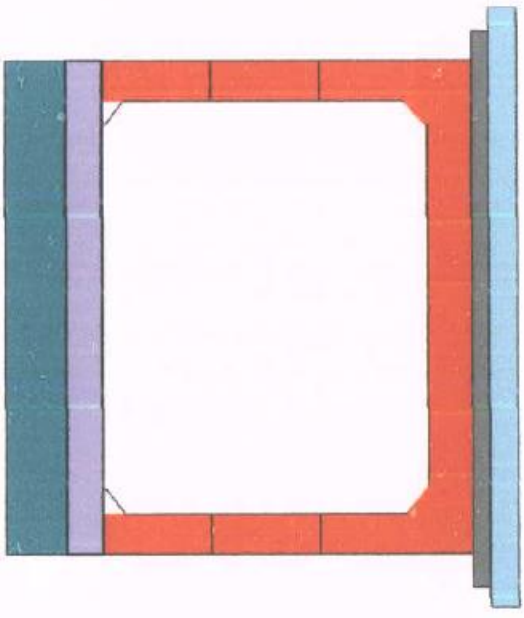


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation


Patel Darsh Patel
 Jhalawar Highway
 Patel Darsh Patel
 Patel Darsh Patel

Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Pa


BOX CULVERT 29+000

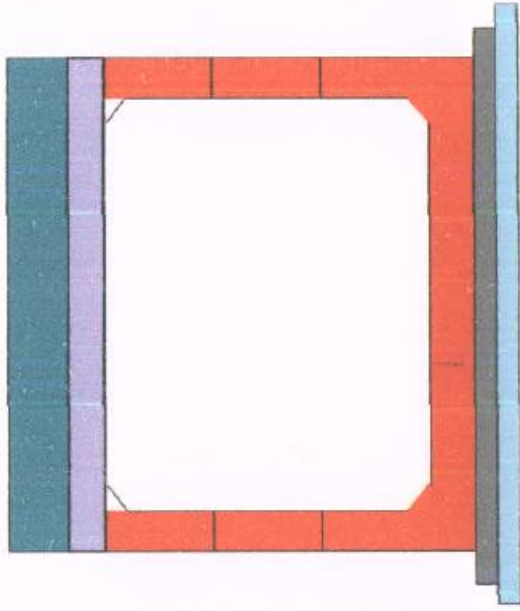

BOX CULVERT 25+800

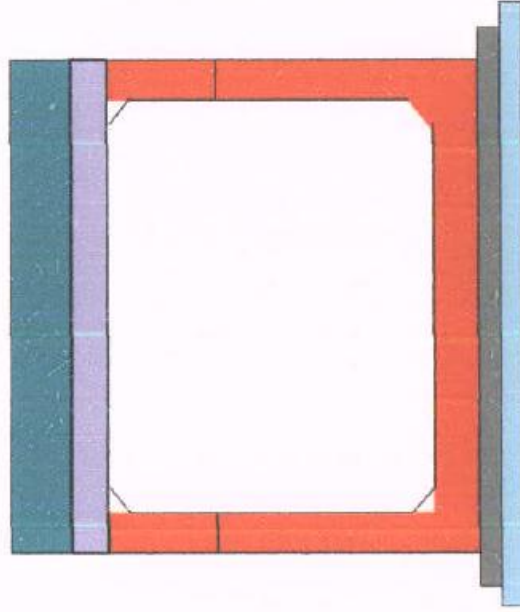


BOX CULVERT 24+610

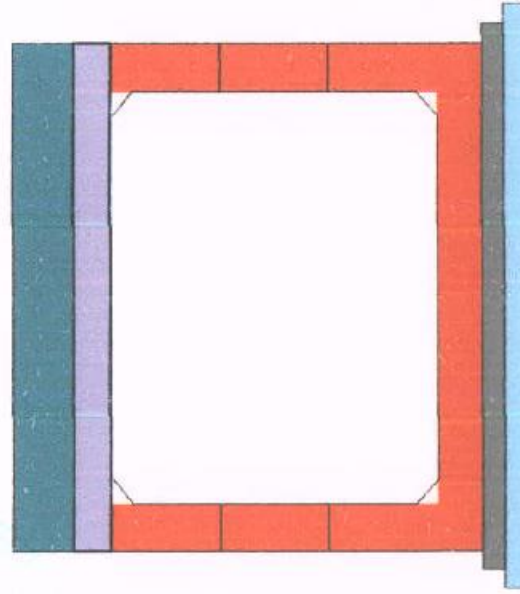


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation


BOX CULVERT 32+300

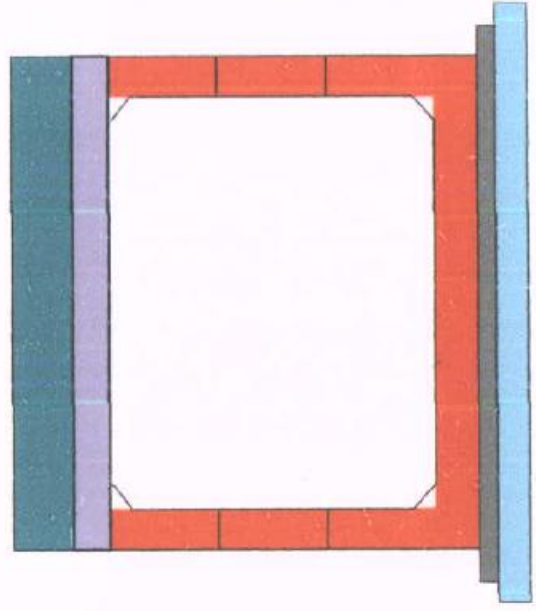

BOX CULVERT 32+050

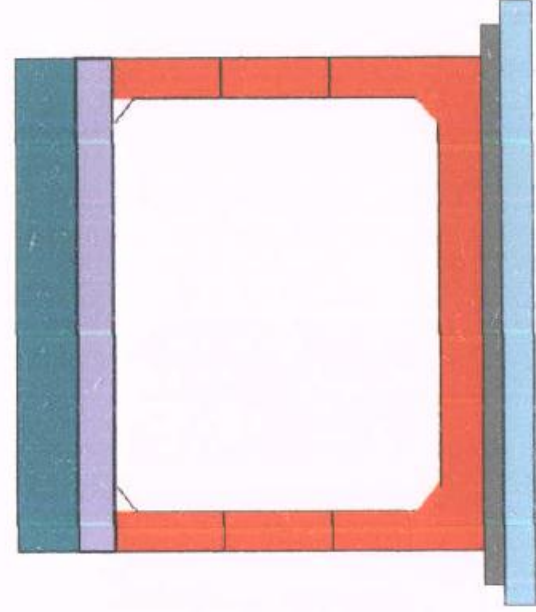

BOX CULVERT 29-600

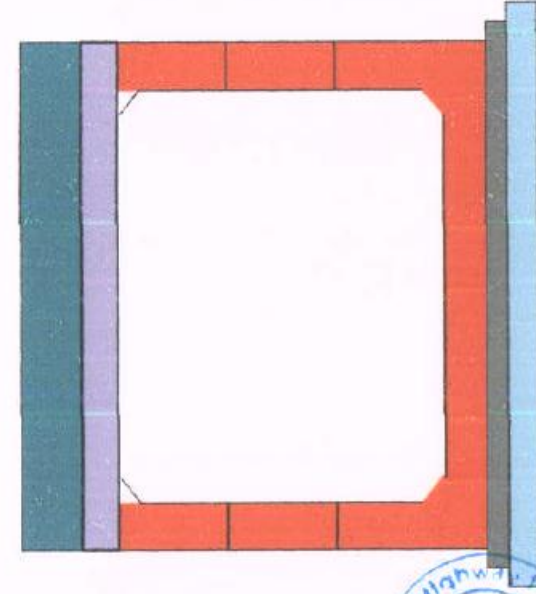


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation




Signature


BOX CULVERT 37+550

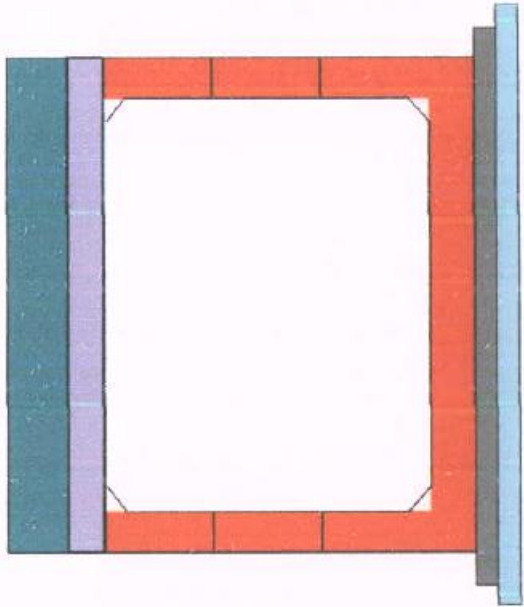

BOX CULVERT 36+719

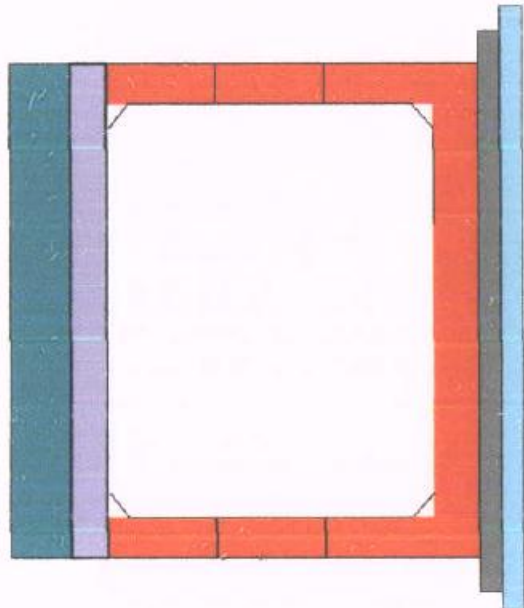


BOX CULVERT 35+205

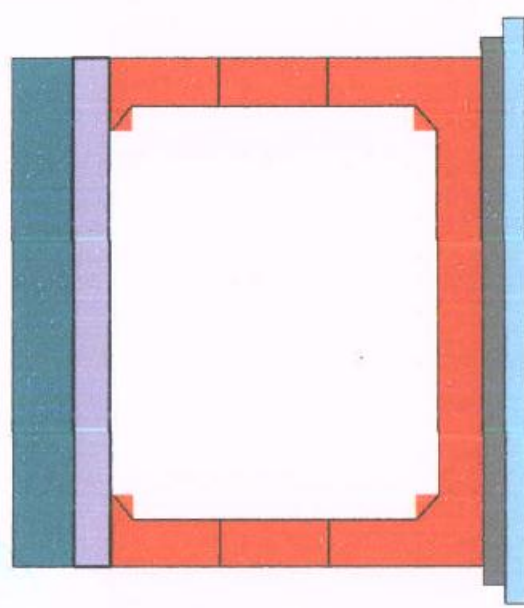


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation


BOX CULVERT 53+125

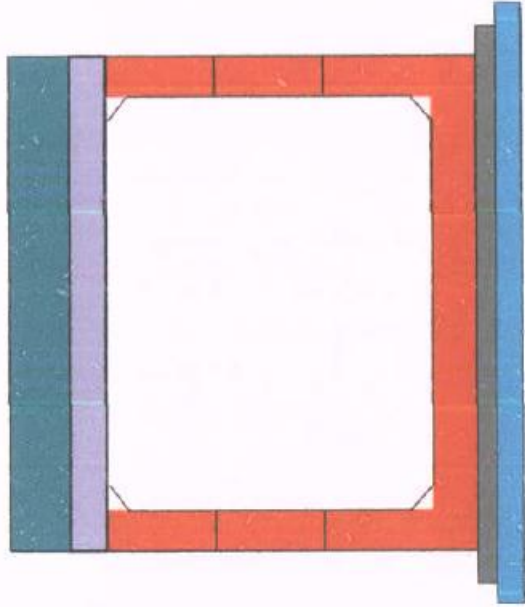

BOX CULVERT 39+180

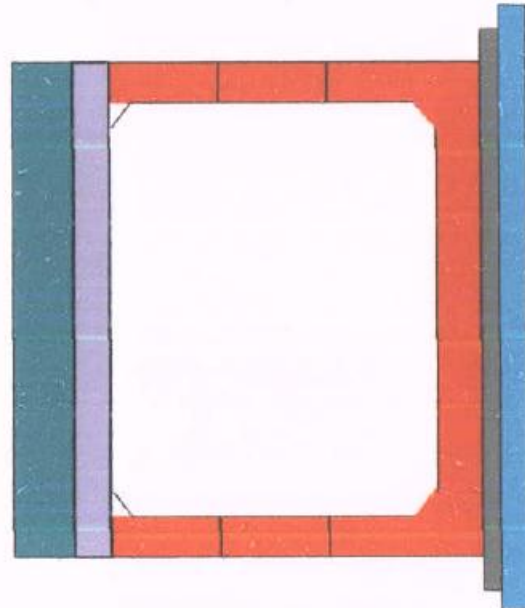

BOX CULVERT 38+100

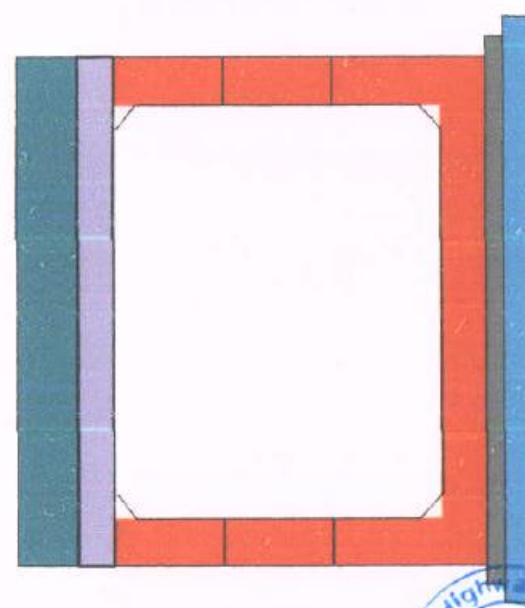


Chainage

CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation




Project: Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawat-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project (Length 48.880 Km.) -Pa


BOX CULVERT 53+700

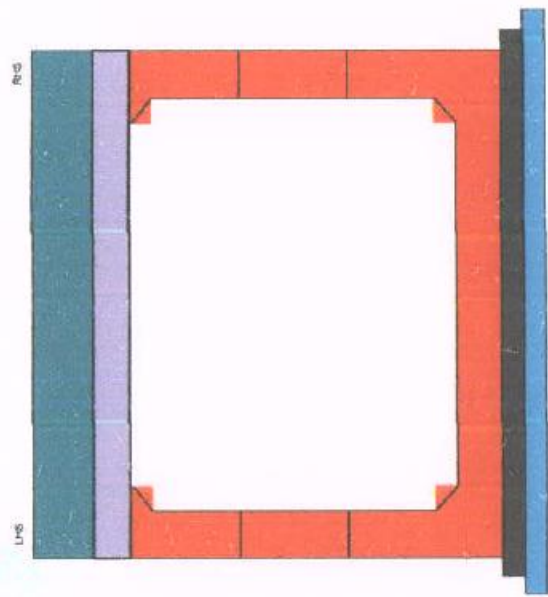

BOX CULVERT 53+900

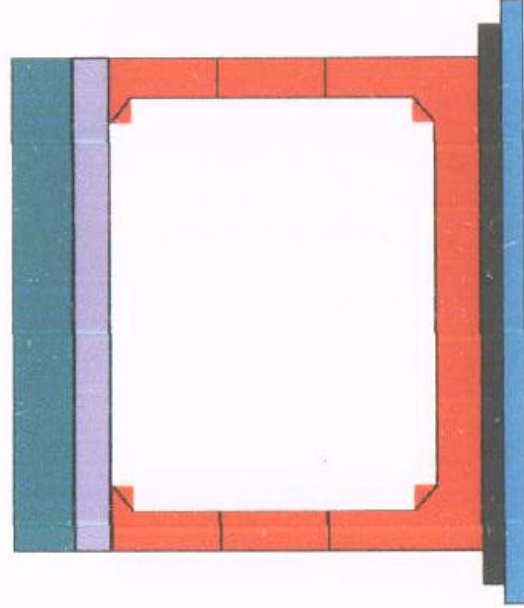


BOX CULVERT 55+820

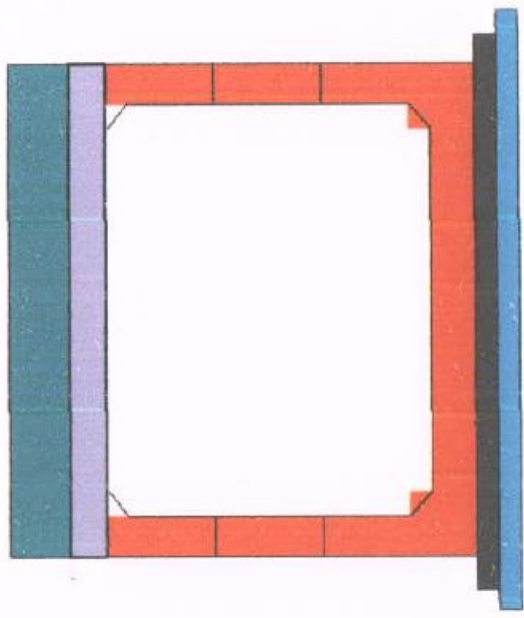


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation

Additional / SR


BOX CULVERT 28+550 (Additional)

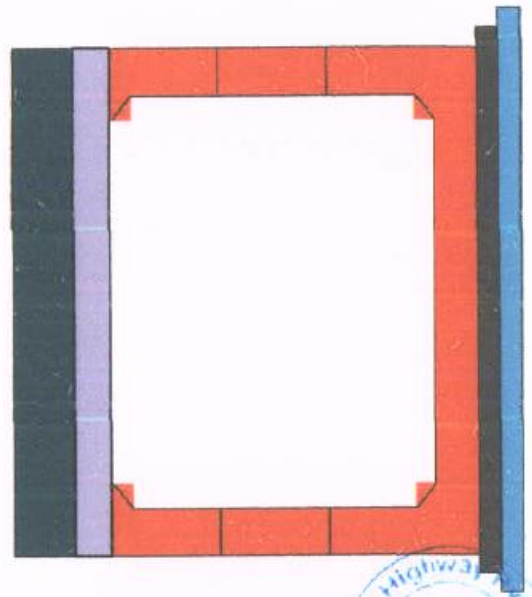

BOX CULVERT 29+900 (SR)

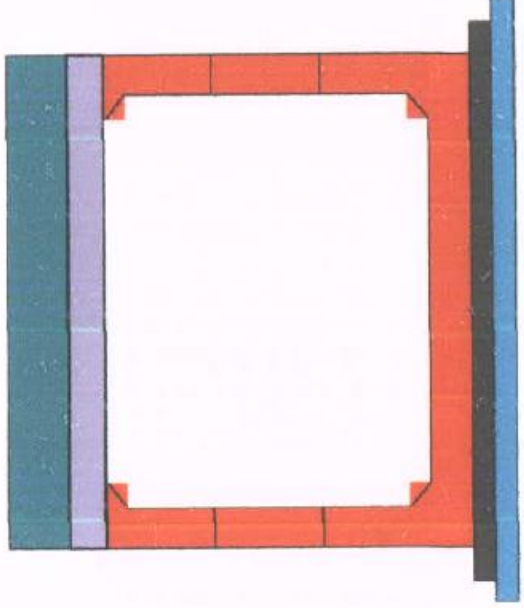




BOX CULVERT 24+610 (SR)

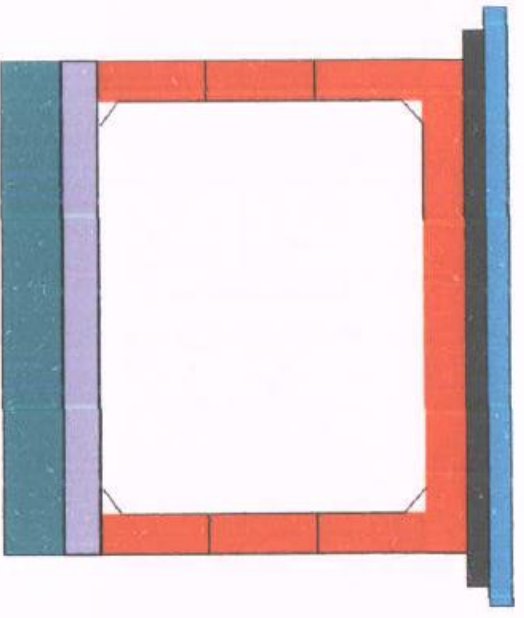

CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation



Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Pa

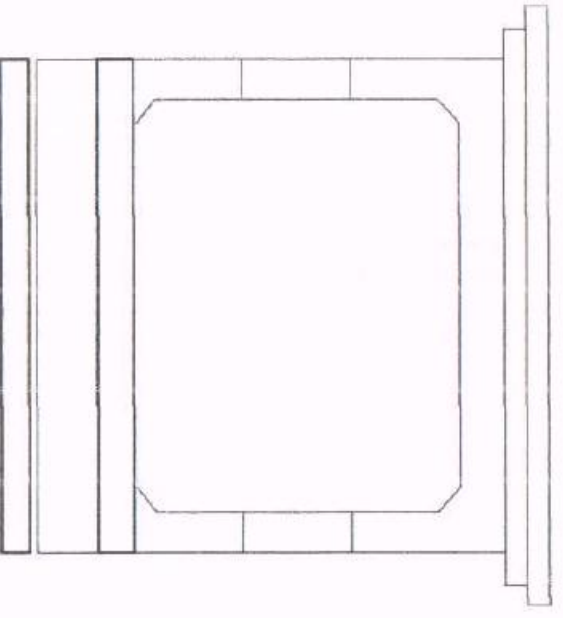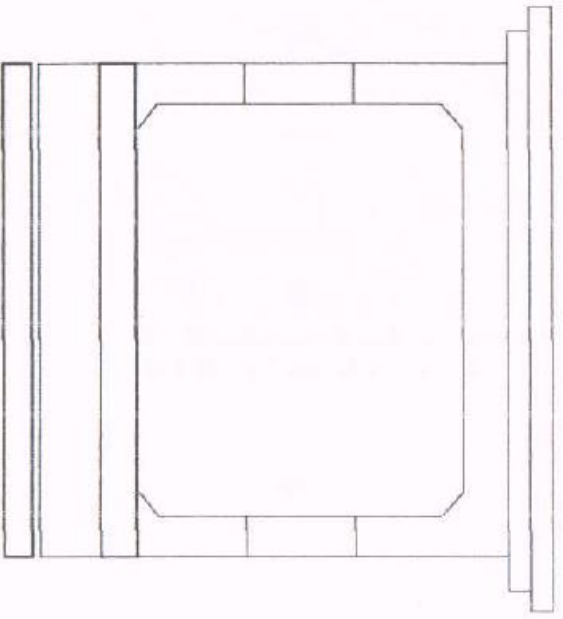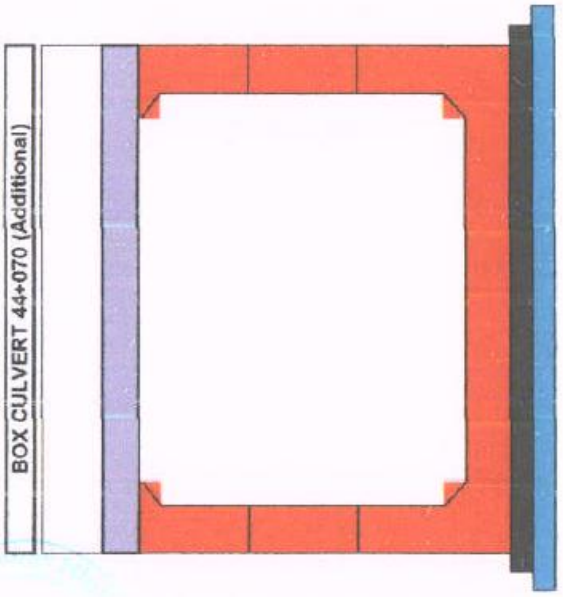


CB
Deck Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC
Excavation




Handwritten signature

MINOR BRIDGE AT KM. 12+380 RHS

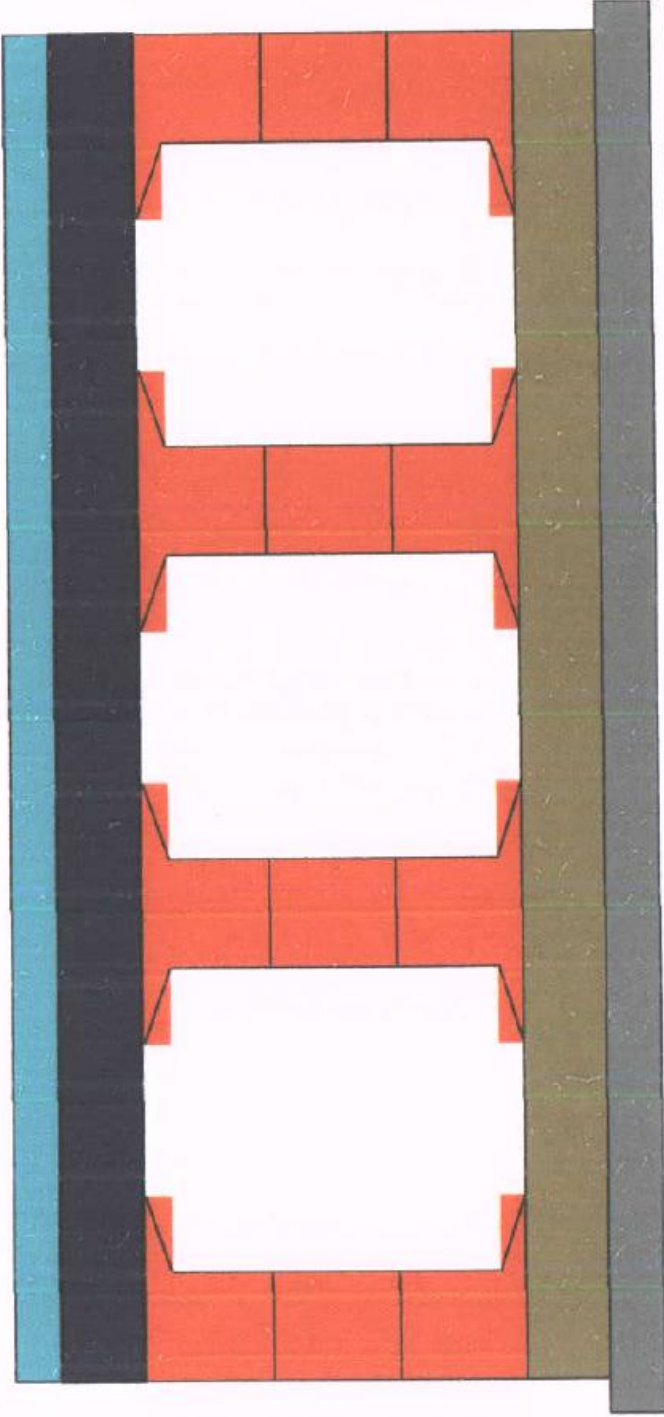

CB						
	3rd Lift					
	2nd Lift					
	1st Lift					
	Raft					
	PCC					


MINOR BRIDGE AT KM. 12+380 LHS

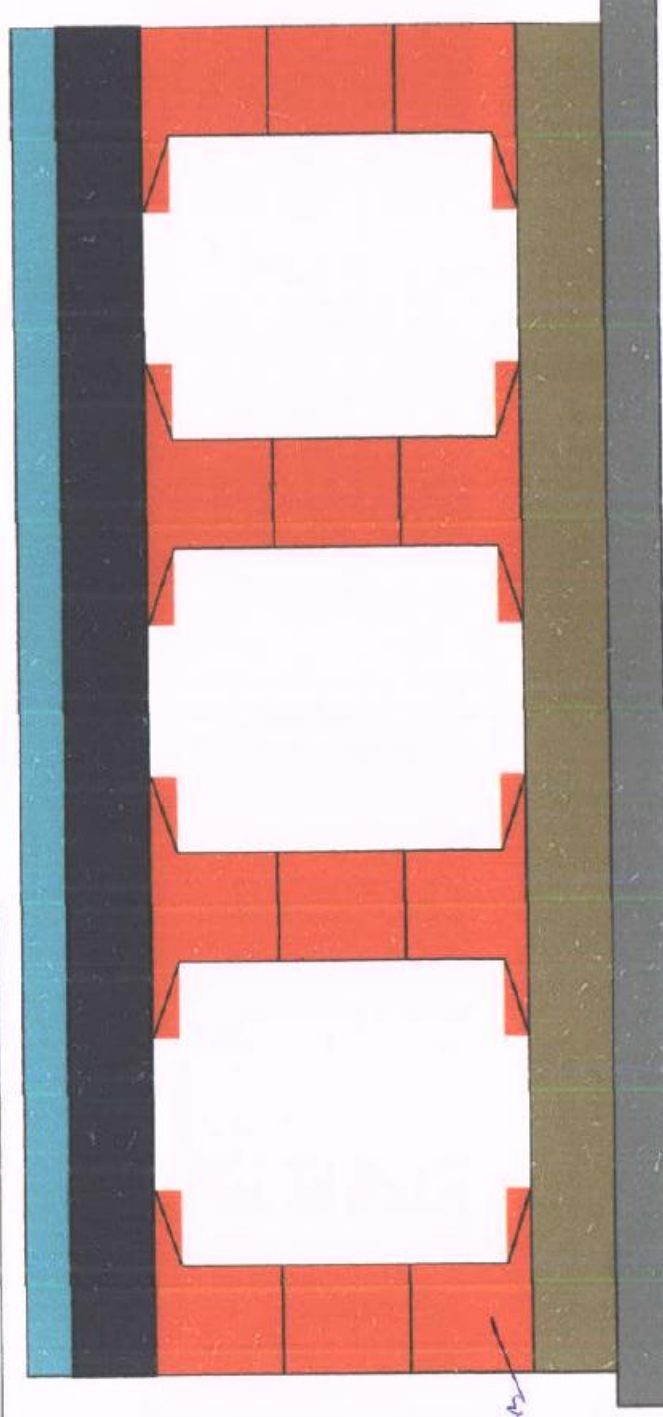

CB						
	3rd Lift					
	2nd Lift					
	1st Lift					
	Raft					
	PCC					





MINOR BRIDGE AT KM. 12+380 RHS Service Road

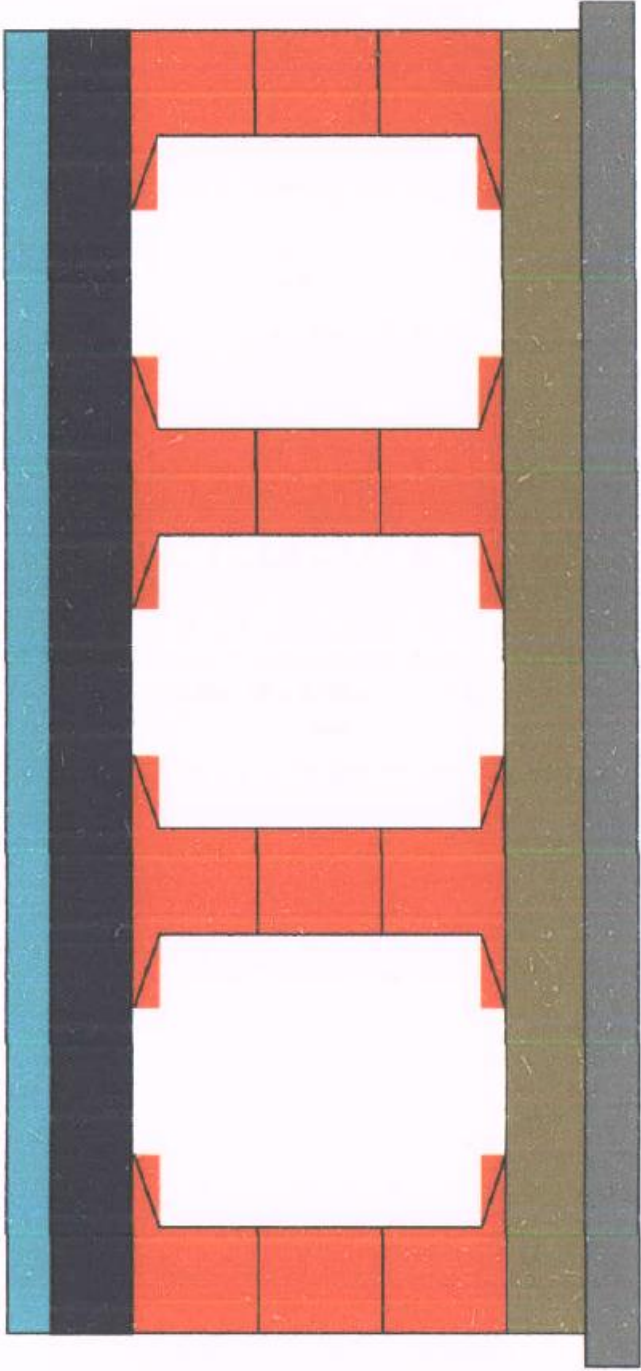

CB					
	3rd Lift				
		2nd Lift			
			1st Lift		
				Raft	
					PCC

MINOR BRIDGE AT KM. 12+380 LHS Service Road

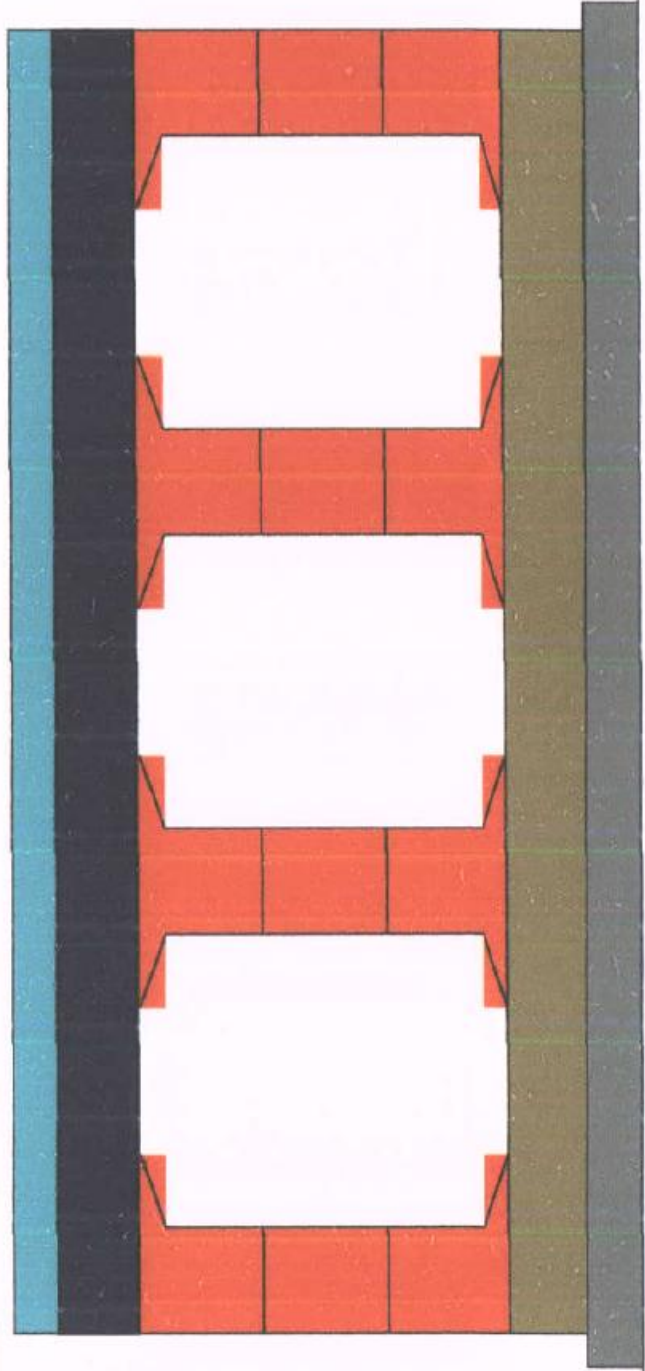


CB					
	3rd Lift				
		2nd Lift			
			1st Lift		
				Raft	
					PCC

PATEK
 Darah-Jhalawar District
 1st Lift
 Raft

Project-Construction of 4-lane Road on NH-12 (New NH-62) from Km 298.000 to 346.540 (Design Chainage from 8.860 to 68.740) (Darrah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-II on Hybrid Annuity Project(Length 48.880 Km.) -Package II


MINOR BRIDGE AT KM. 16+060 (Main Carriage Way) RHS

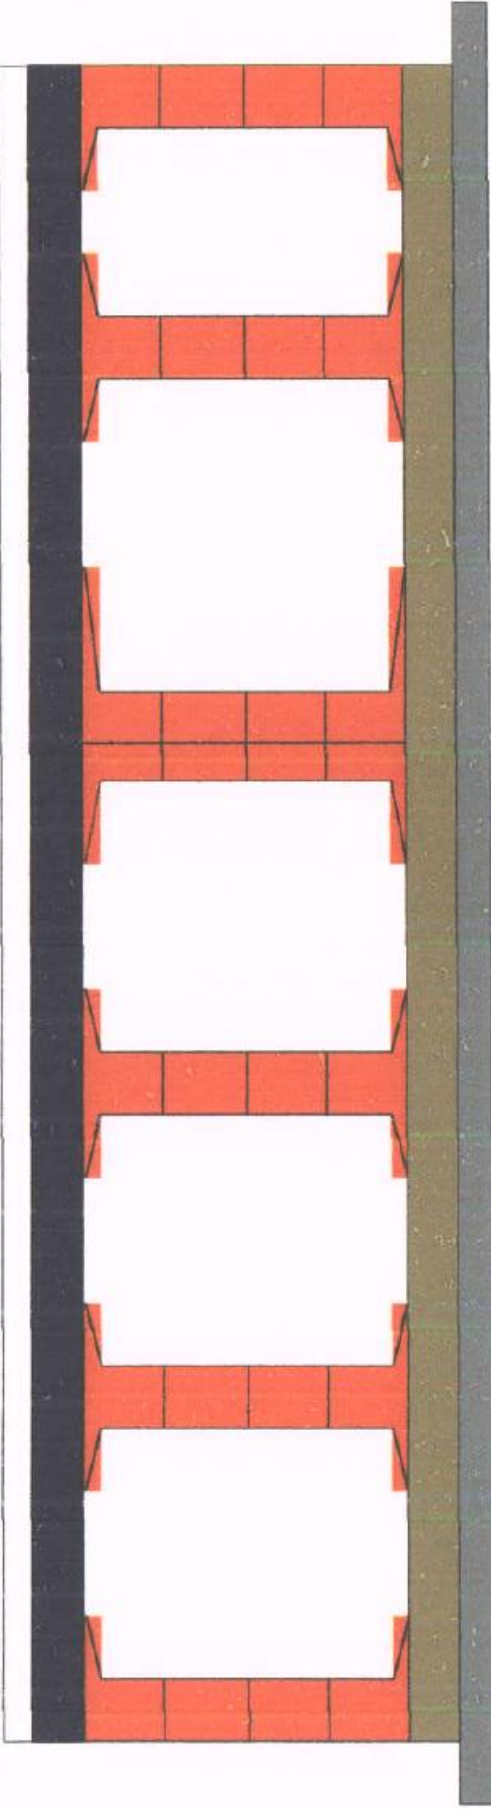

CB	
4th Lift	
3rd Lift	
2nd Lift	
1st Lift	
Raft	
PCC	

Project-Construction of 4-lane Road on NH-12 (New NH-62) from Km 298.000 to 346.540 (Design Chainage from 8.860 to 68.740) (Darrah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-II on Hybrid Annuity Project(Length 48.880 Km.) -Package II


MINOR BRIDGE AT KM. 16+060 (Main Carriage Way) LHS

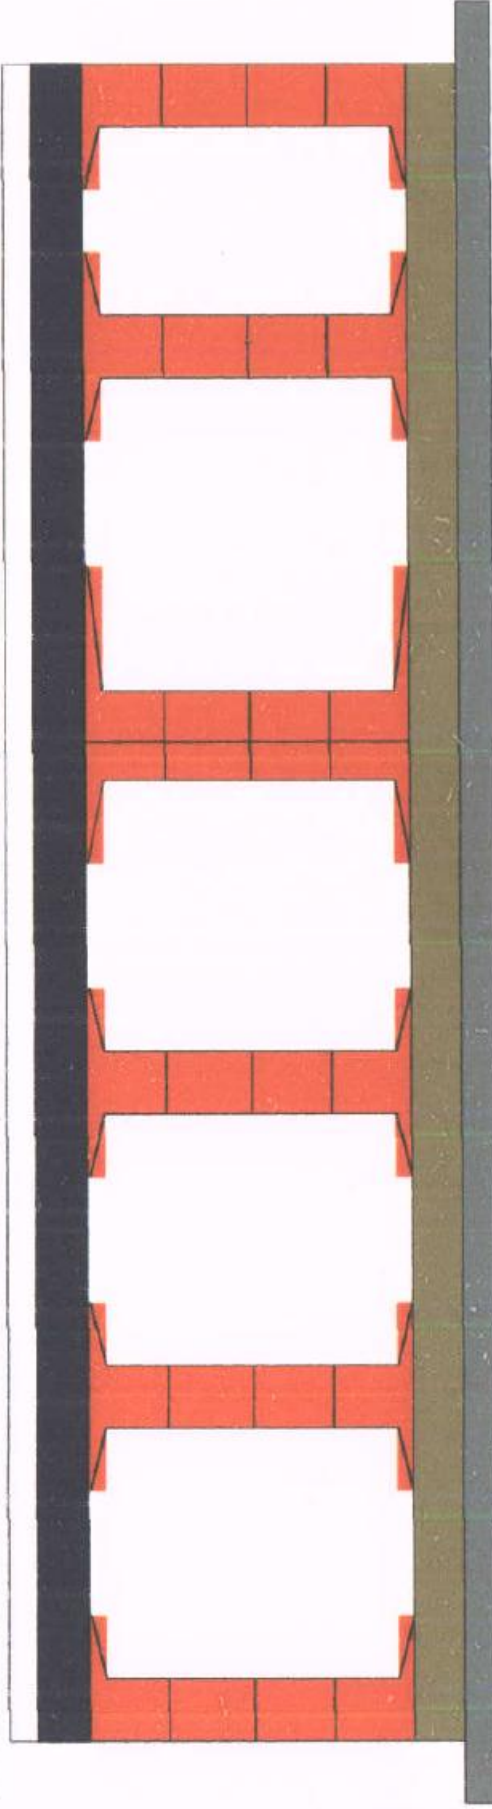

CB	
4th Lift	
3rd Lift	
2nd Lift	
1st Lift	
Raft	
PCC	




MINOR BRIDGE AT KM. 16+060 (Service Road) RHS

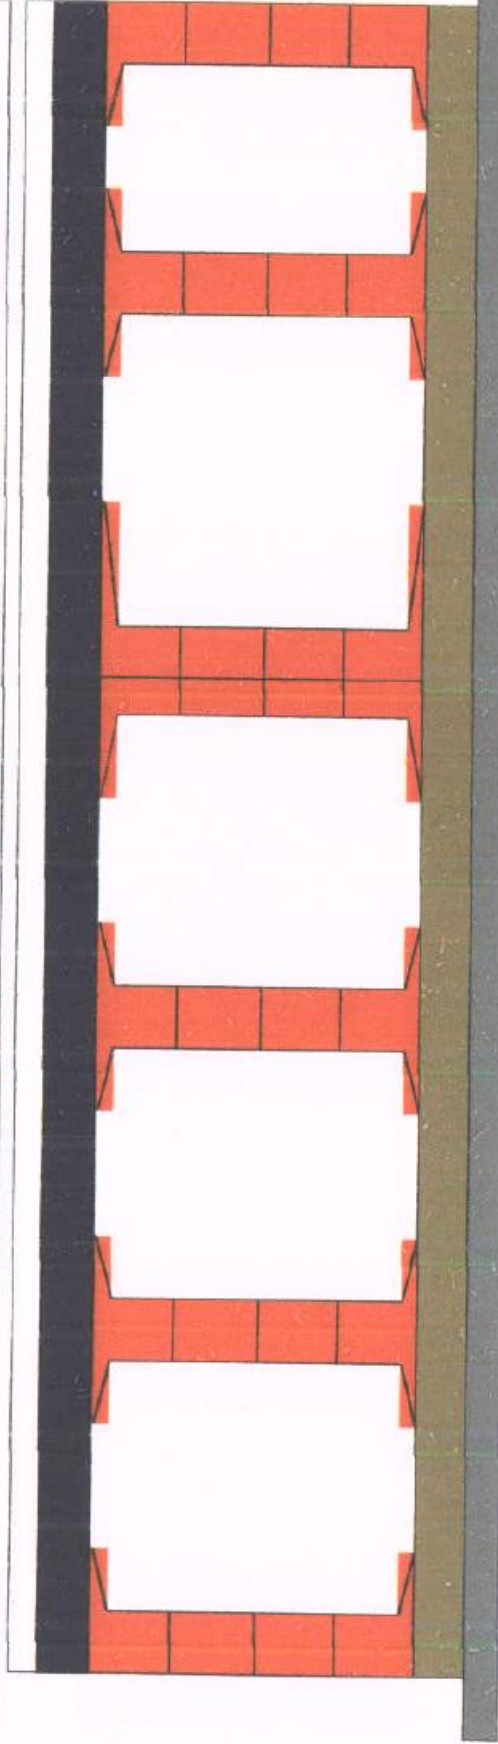

CB
4th Lift
3rd Lift
2nd Lift
1st Lift
Raft
PCC


MINOR BRIDGE AT KM. 16+060 (Service Road) LHS

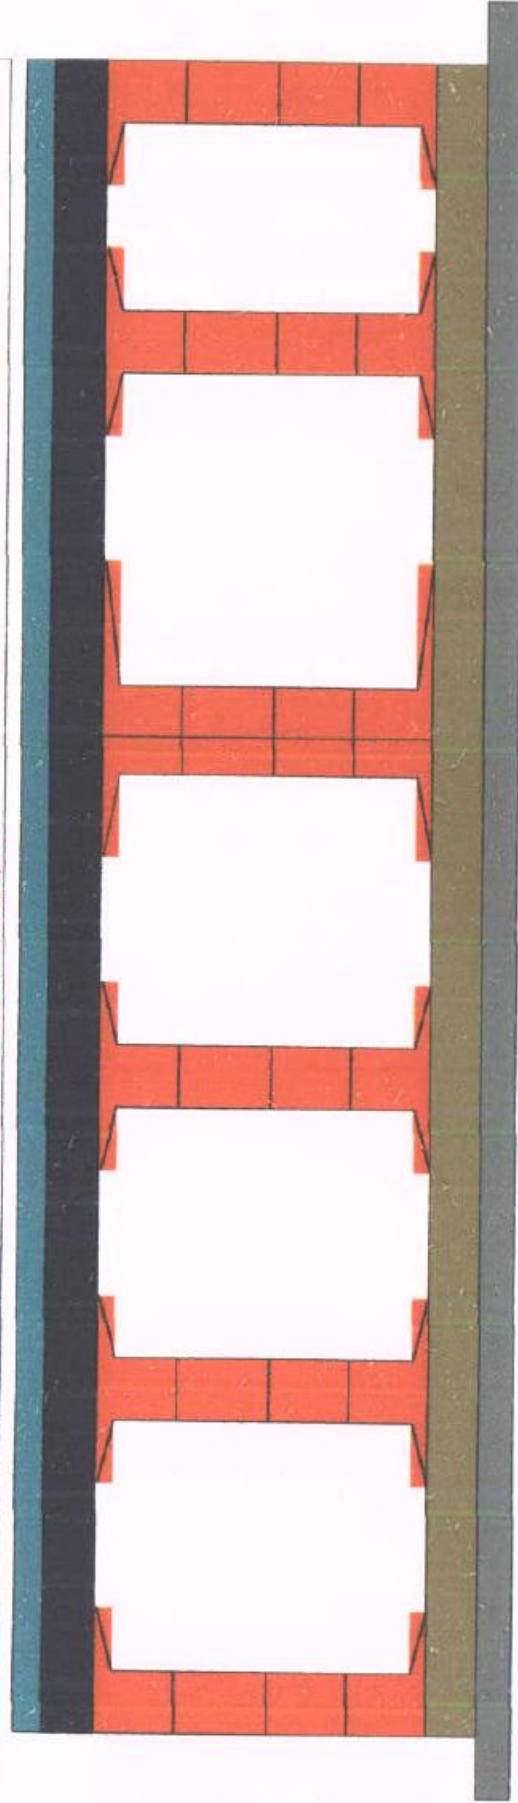

CB
4th Lift
3rd Lift
2nd Lift
1st Lift
Raft
PCC




MINOR BRIDGE AT KM. 17+880 RHS

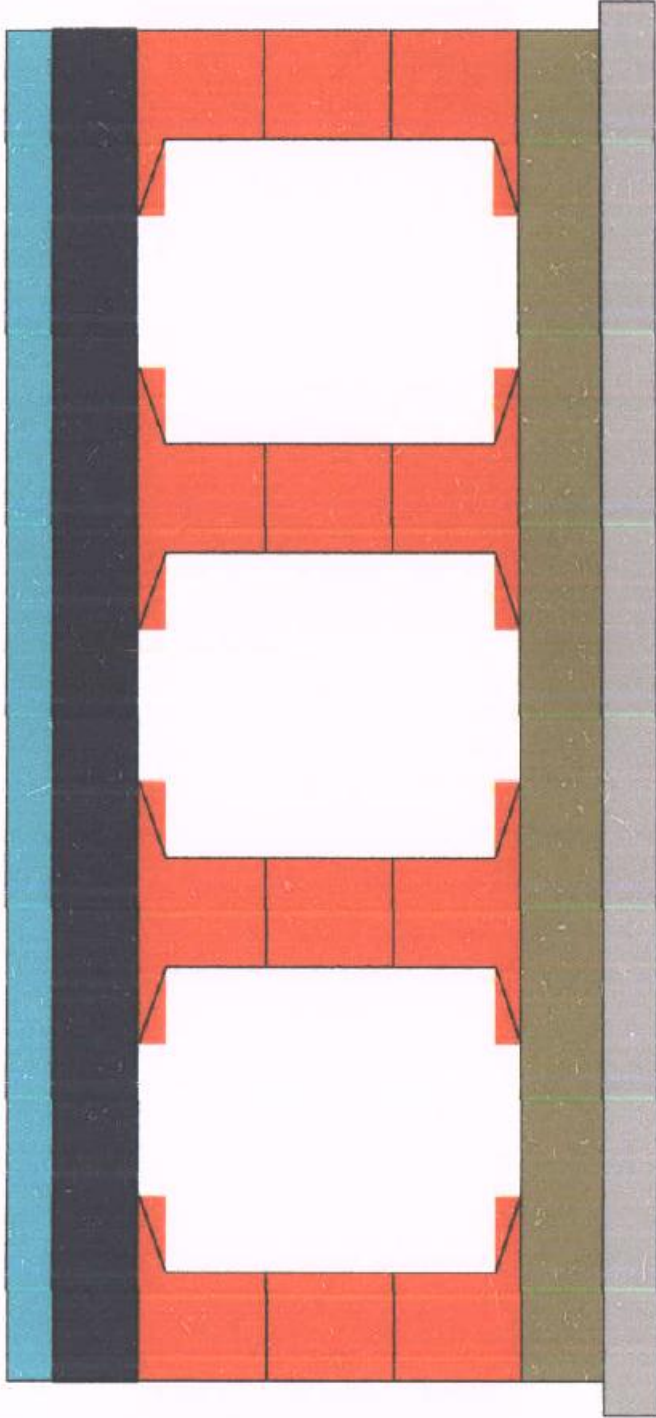

CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC


MINOR BRIDGE AT KM. 17+880 LHS

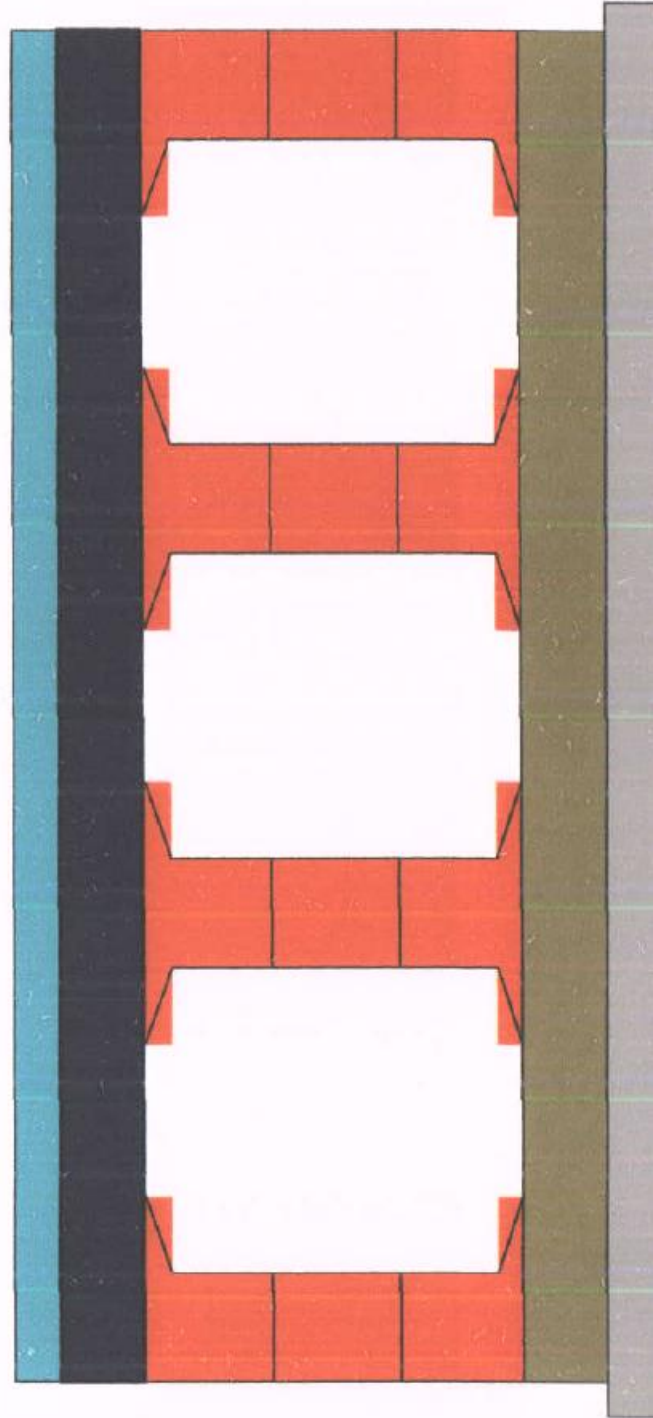

CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC


Patel Daran-Jhalavar Highway
PATEL
1st Lift
Raft
D. Patil

MINOR BRIDGE AT KM. 29+600 RHS

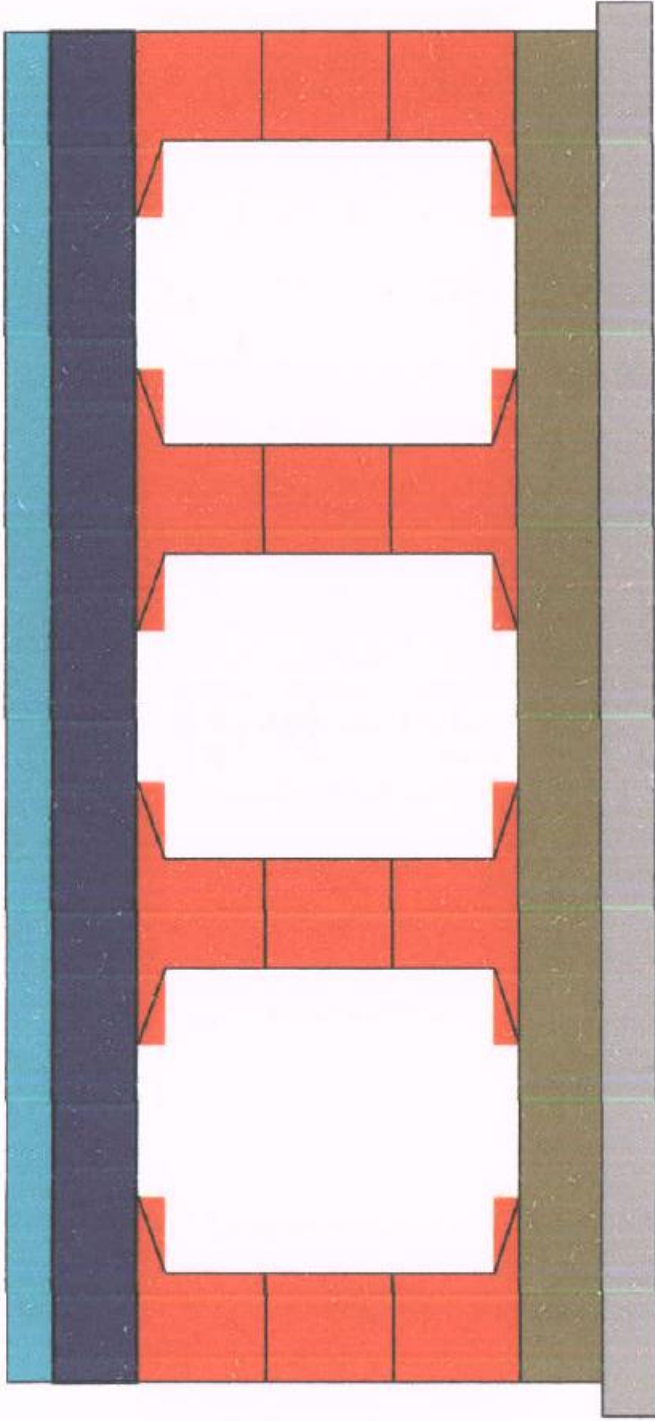

CB						
	3rd Lift					
		2nd Lift				
			1st Lift			
				Raft		
					PCC	


MINOR BRIDGE AT KM. 29+600 LHS

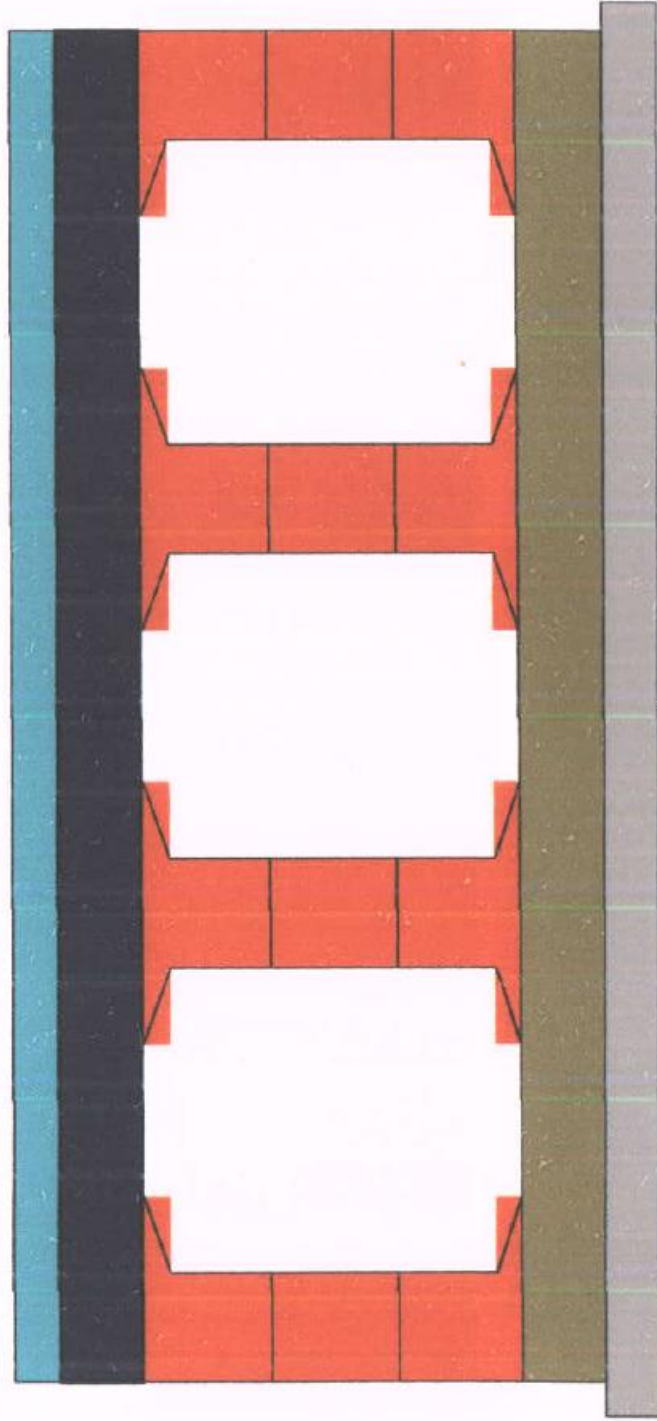

CB						
	3rd Lift					
		2nd Lift				
			1st Lift			
				Raft		
					PCC	


Gujarat Highways Department
 Gandhinagar, Gandhinagar, Gandhinagar
 PATEL
 [Signature]

MINOR BRIDGE AT KM. 33+000 RHS

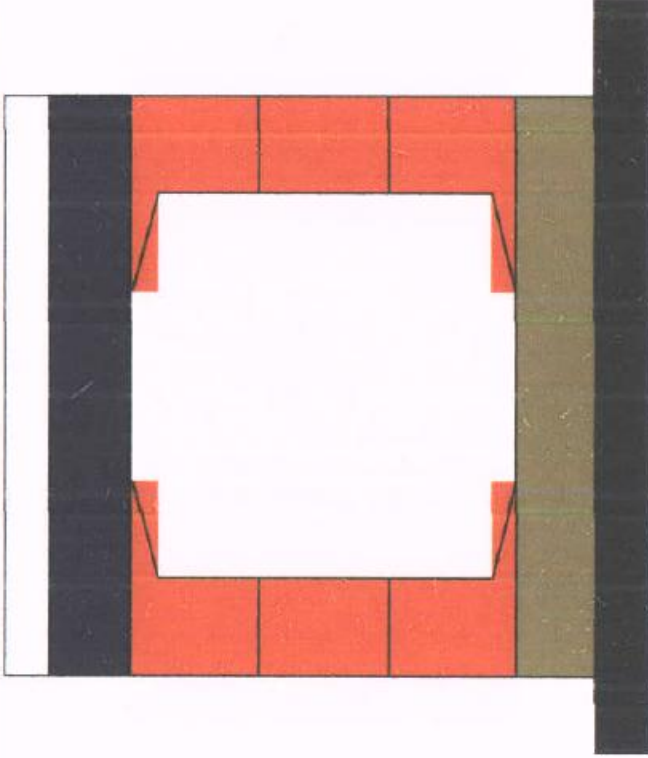

CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC


MINOR BRIDGE AT KM. 33+000 LHS

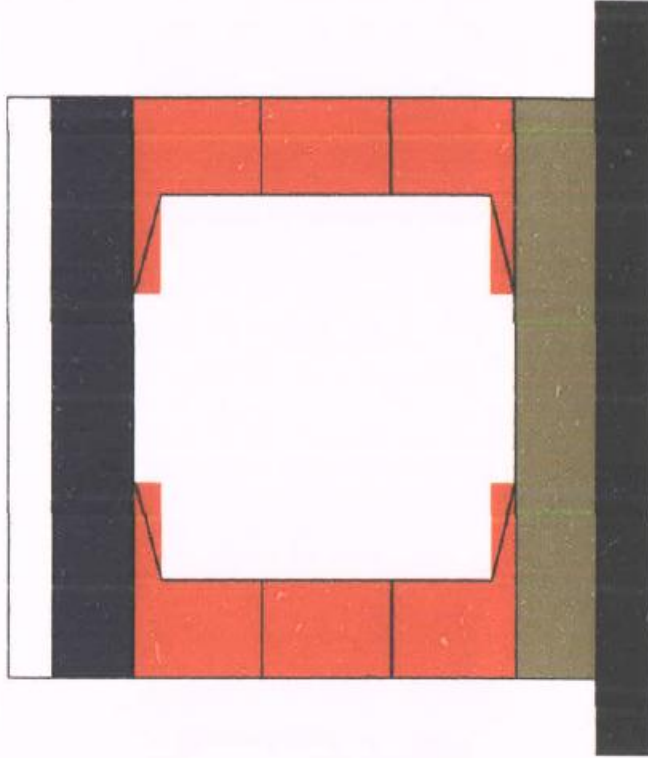

CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC




CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC

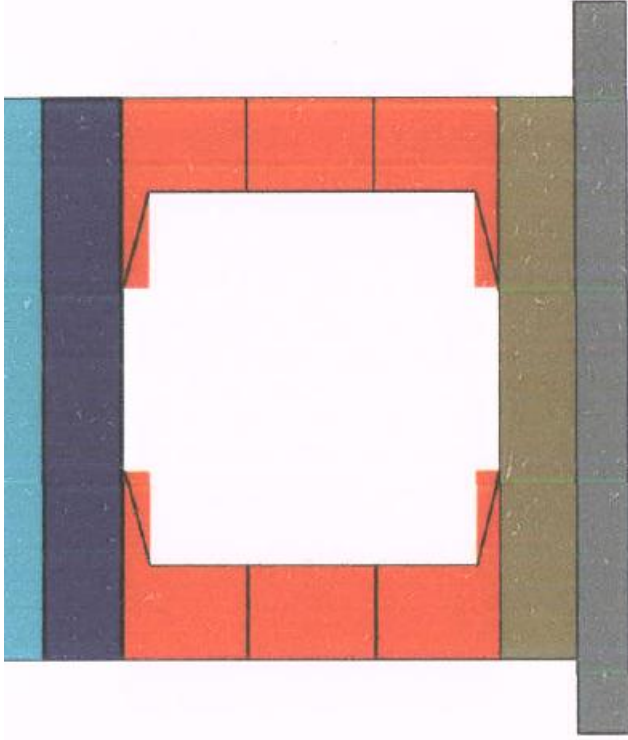


MINOR BRIDGE AT KM. 34+360 LHS

CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC

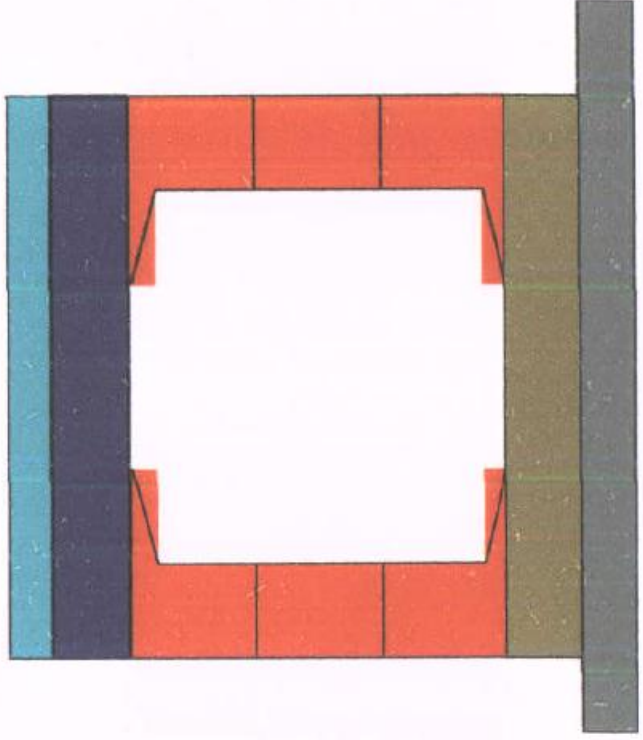



 PATEL
 Daran-Jhalawar Highway Pvt. Ltd.

MINOR BRIDGE AT KM. 44+900 RHS

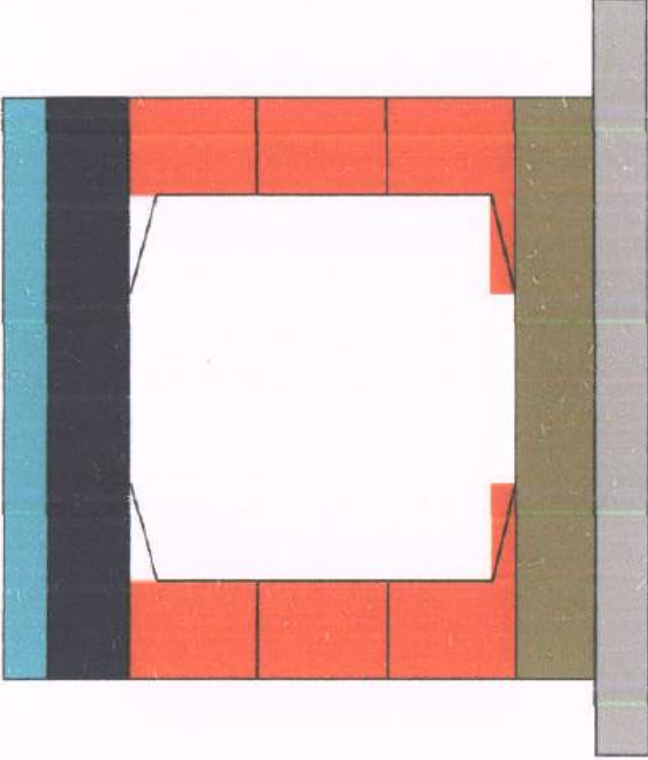

CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC

MINOR BRIDGE AT KM. 44+900 LHS

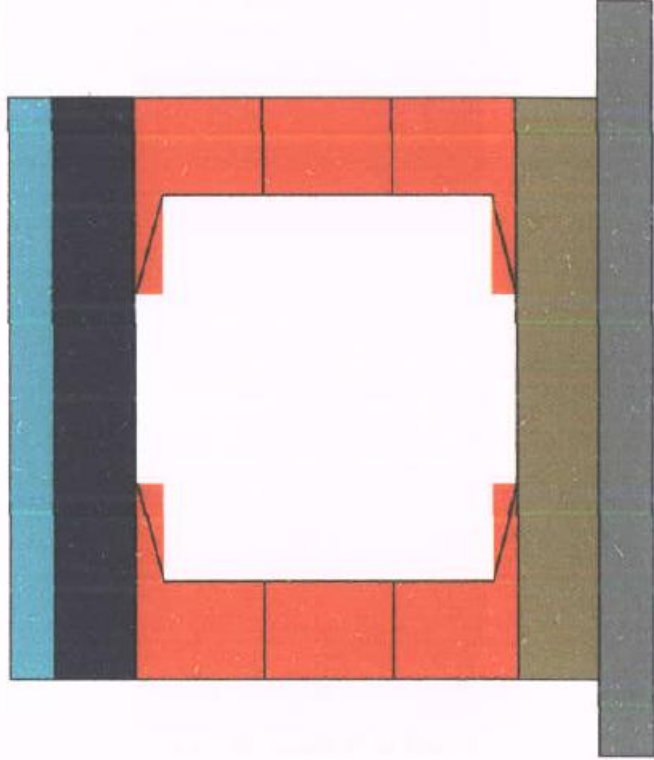


CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC



Project-Construction of 4-lane Road on NH-12 (New NH-62) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 66.740) (Daroh-Jhalawa-Tandhar section) in the State of Rajasthan under NHDP Phase-II on Hybrid Annuity Project (Length 48.880 Km.) -Package II


MINOR BRIDGE AT KM. 49+785 (Main Carriage Way) RHS

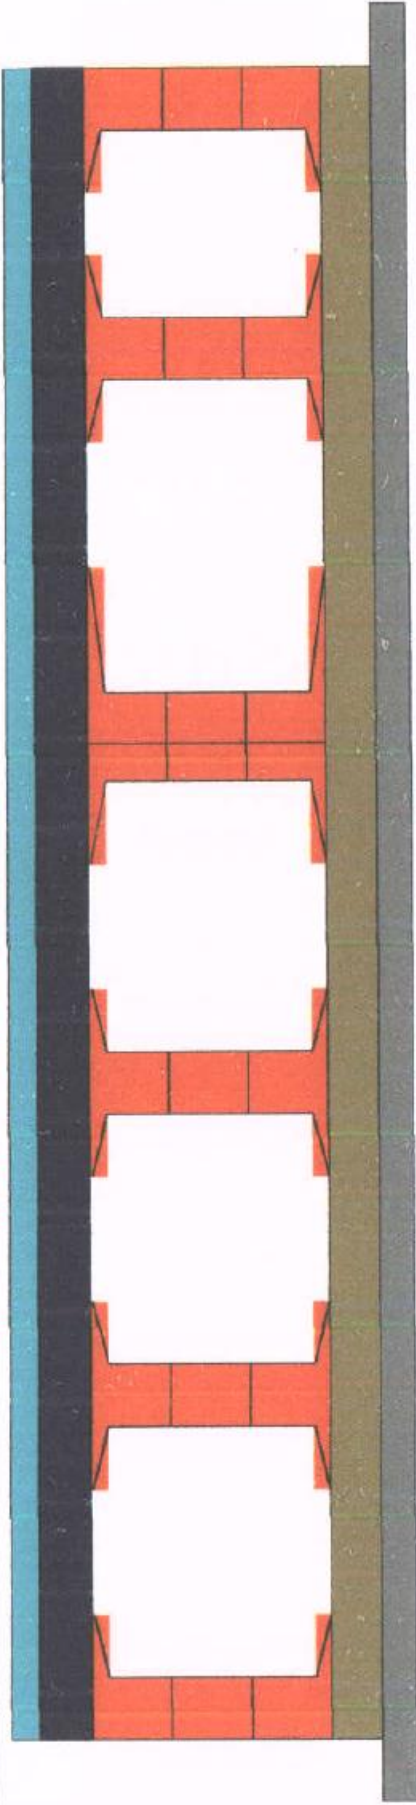

CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC

Project-Construction of 4-lane Road on NH-12 (New NH-62) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 66.740) (Daroh-Jhalawa-Tandhar section) in the State of Rajasthan under NHDP Phase-II on Hybrid Annuity Project (Length 48.880 Km.) -Package II


MINOR BRIDGE AT KM. 49+785 (Main Carriage Way) LHS

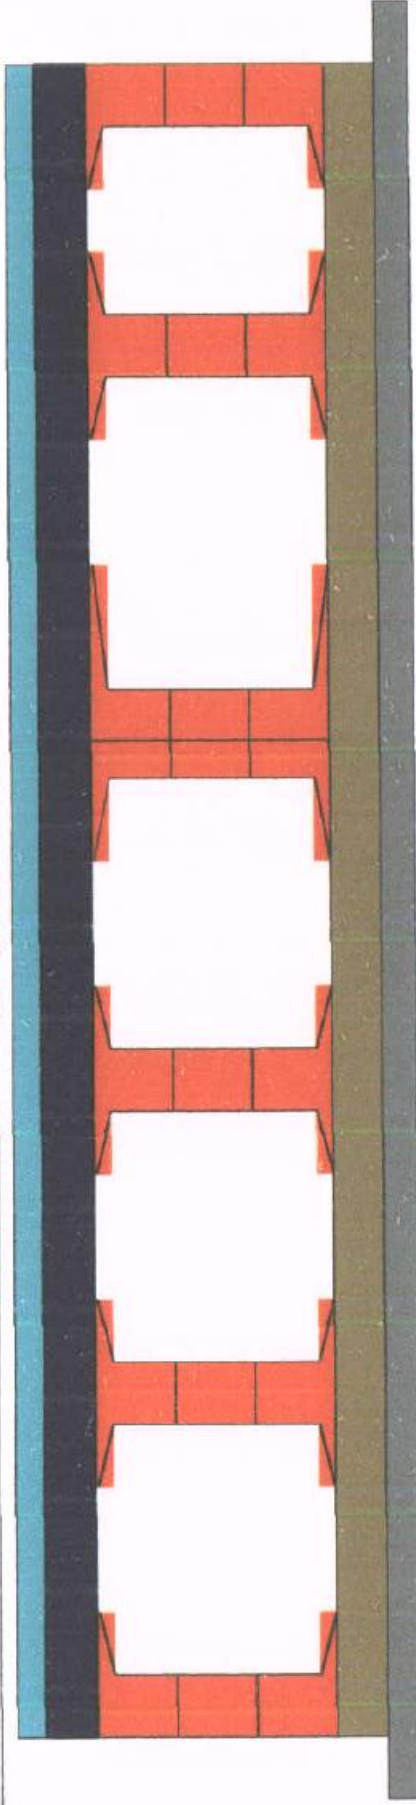

CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC




MINOR BRIDGE AT KM. 49+785 (Service Road) RHS

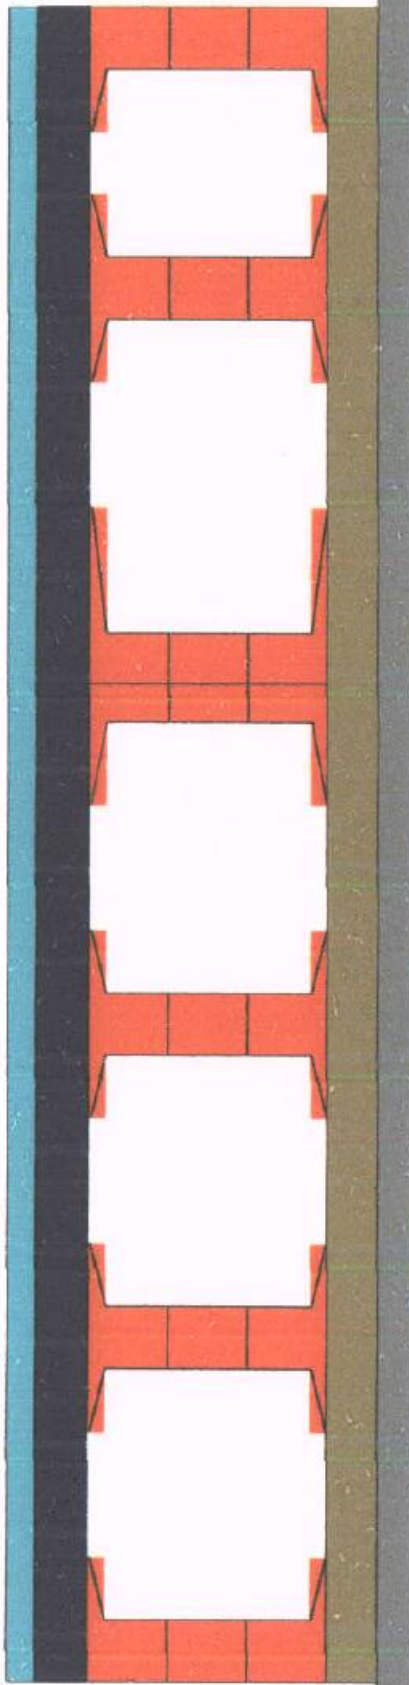

CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC

MINOR BRIDGE AT KM. 49+785 (Service Road) LHS

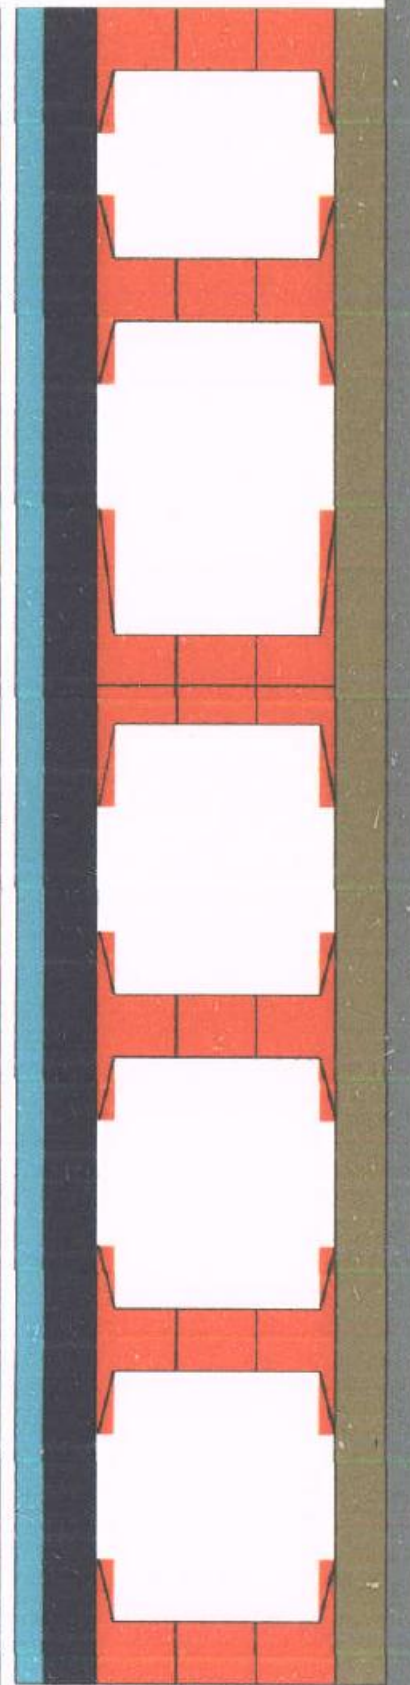


CB
3rd Lift
2nd Lift
1st Lift
Raft
PCC

Patel Narain Highway Pvt. Ltd.

 PATEL


 6/1/2025

MINOR BRIDGE AT KM. 54+040 RHS

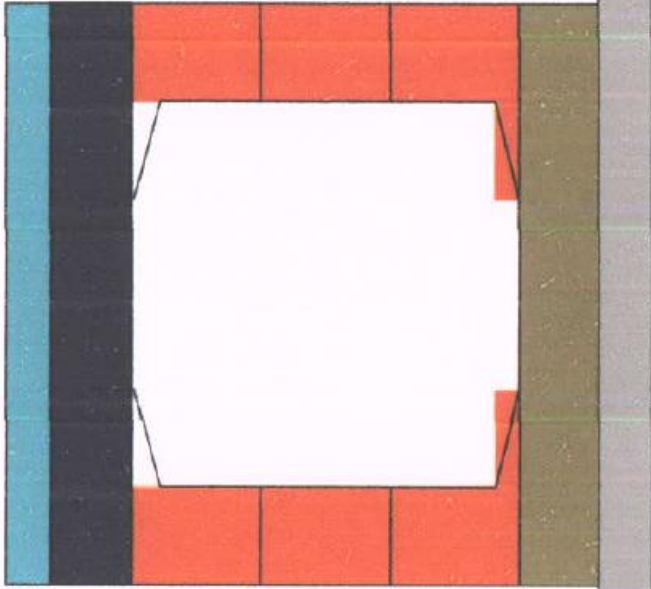

CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC


MINOR BRIDGE AT KM. 54+040 LHS

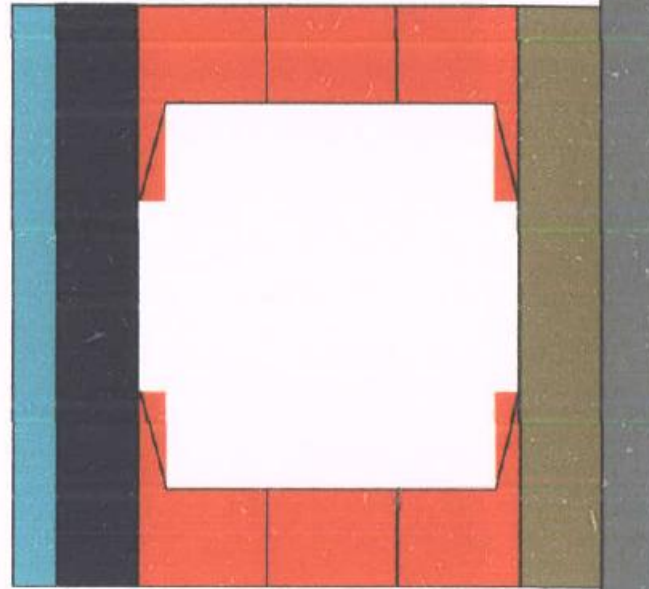

CB
Slab
3rd Lift
2nd Lift
1st Lift
Raft
PCC




MINOR BRIDGE AT KM. 54+070 RHS

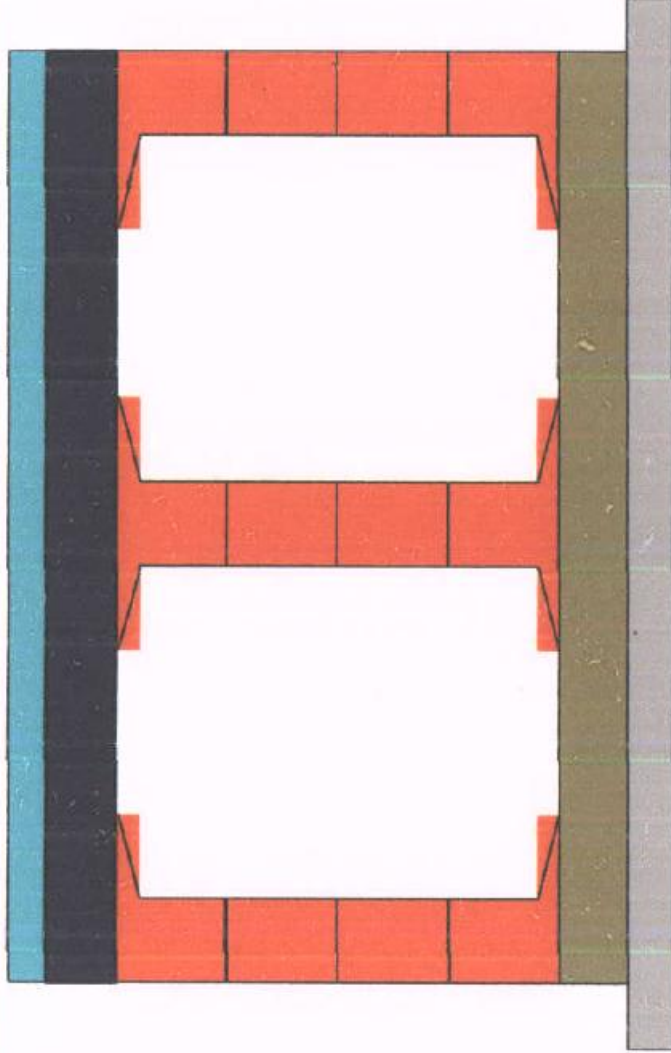

CB
Slab
4th Lift
3rd Lift
2nd Lift
1st Lift
Raft
PCC

MINOR BRIDGE AT KM. 54+070 LHS

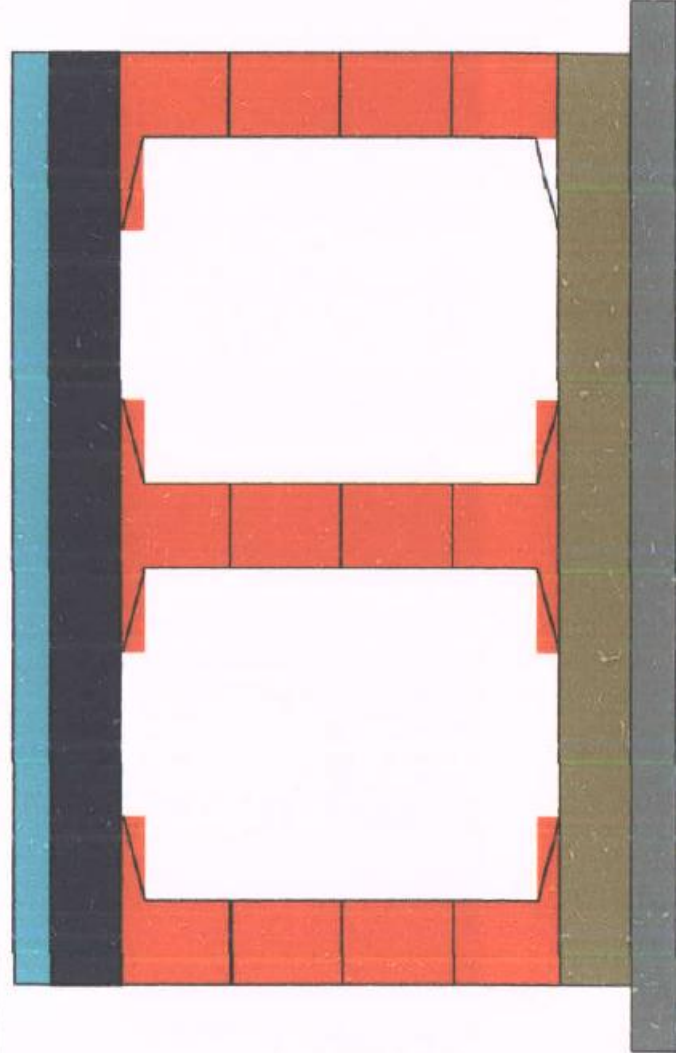


CB
Slab
4th Lift
3rd Lift
2nd Lift
1st Lift
Raft
PCC




Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 56.740) (Darrah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project (Length 48.880 Km). -Package II

VEHICULAR UNDERPASS AT 12+125 A1/A2RHS

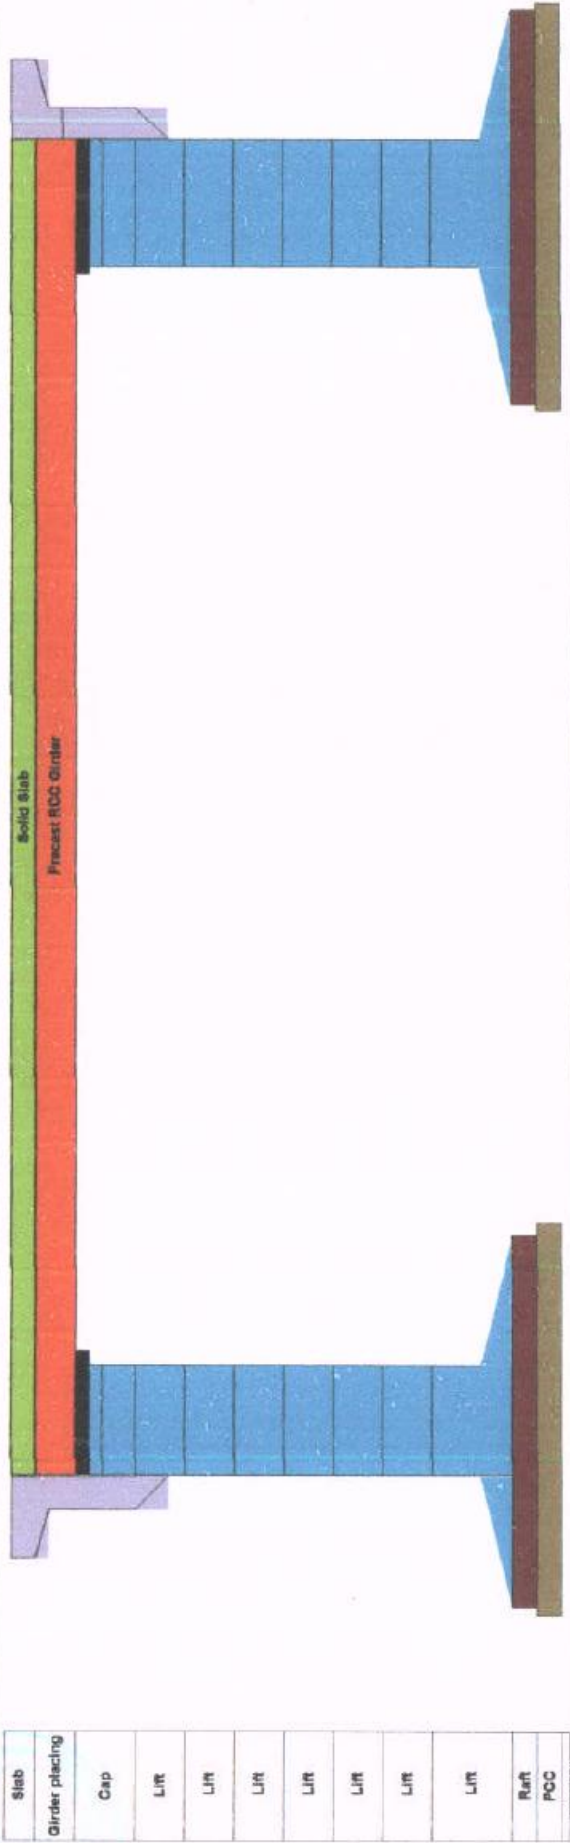

Slab
Girder placing
Cap
LIR
LIR
LIT
LIT
LIT
LIT
LIT
LIT
Raft
PCC

VEHICULAR UNDERPASS AT 12+126A1/A2 LHS

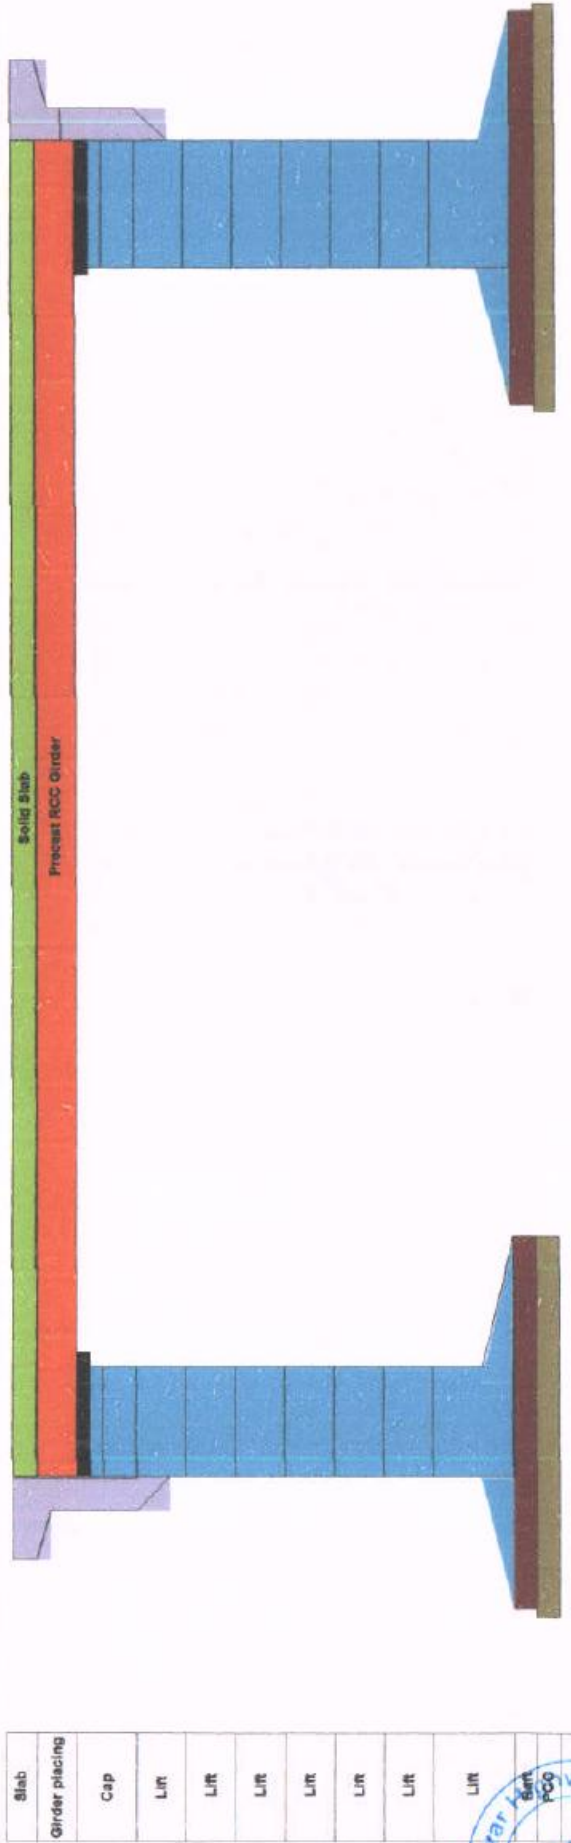


Slab
Girder placing
Cap
LIR
LIR
LIT
LIT
LIT
LIT
LIT
LIT
LIT
LIT
LIT

Stamp: PATEL Darrah-Jhalawar Highway Pvt. Ltd. with signature and date.

Project: -Construction of 4-lane Road on NH-12 (New NH-52) from Km 298.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darrah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project (Length 48.880 Km.) -Package II

VEHICULAR UNDERPASS AT 15+725 A1/A2 RHS

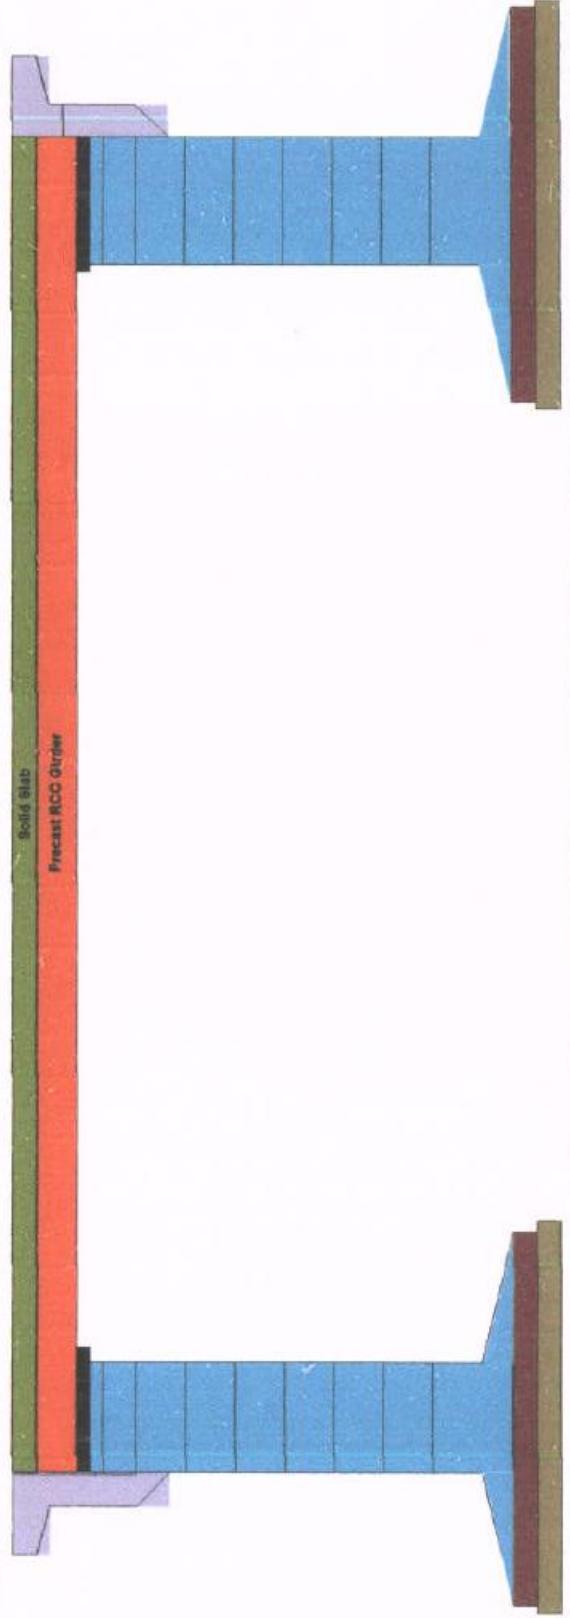

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

VEHICULAR UNDERPASS AT 15+725 A1/A2 LHS




Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

Patel

Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 289.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

VEHICULAR UNDERPASS AT 19+965 A1/ A2 LHS

Slab
Order placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Reft
PCC

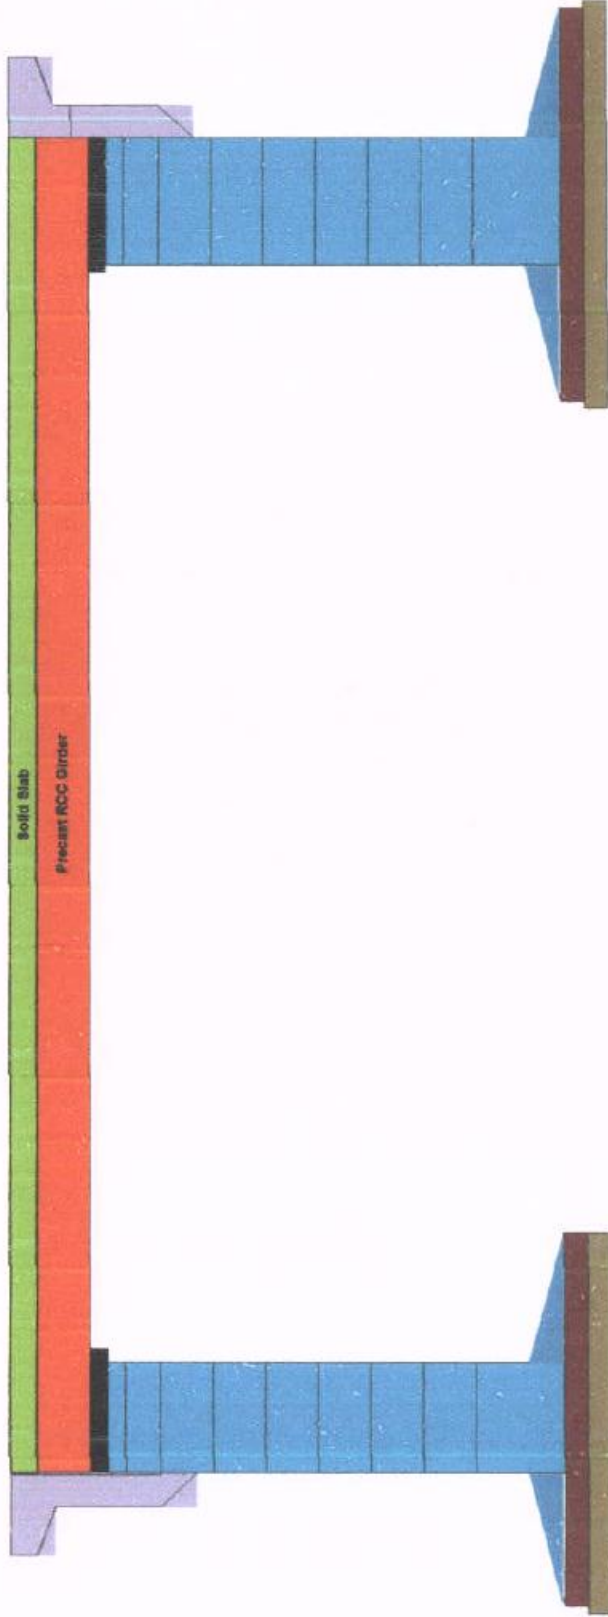

VEHICULAR UNDERPASS AT 19+965 A1 /A2RHS


Slab
Order placing
Cap
Lift
Lift
Lift
Lift
Lift
Reft
PCC



Patel Darah-Jhalawar Highway Pvt. Ltd.
 Patel
 Darah-Jhalawar Highway Pvt. Ltd.
 Patel


Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darrah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

VEHICULAR UNDERPASS AT 26+100 A1/A2 RHS

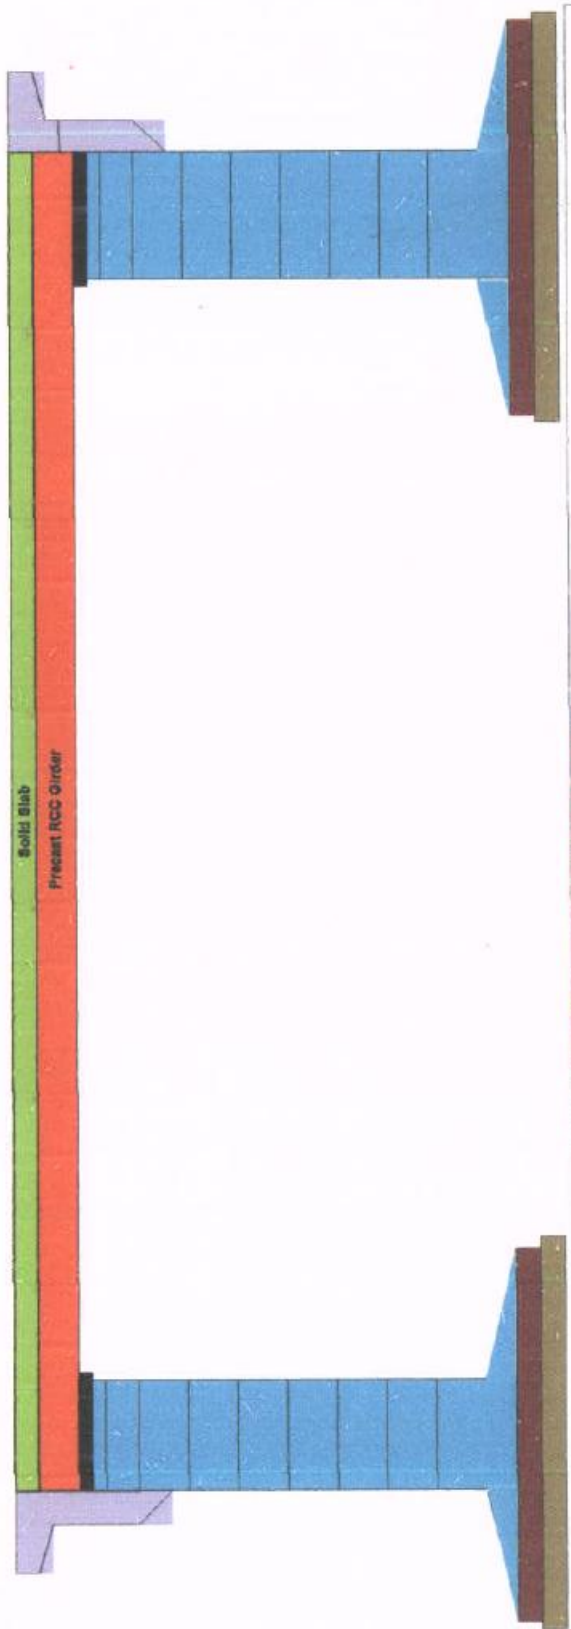

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

VEHICULAR UNDERPASS AT 25+100 A1/A2 LHS

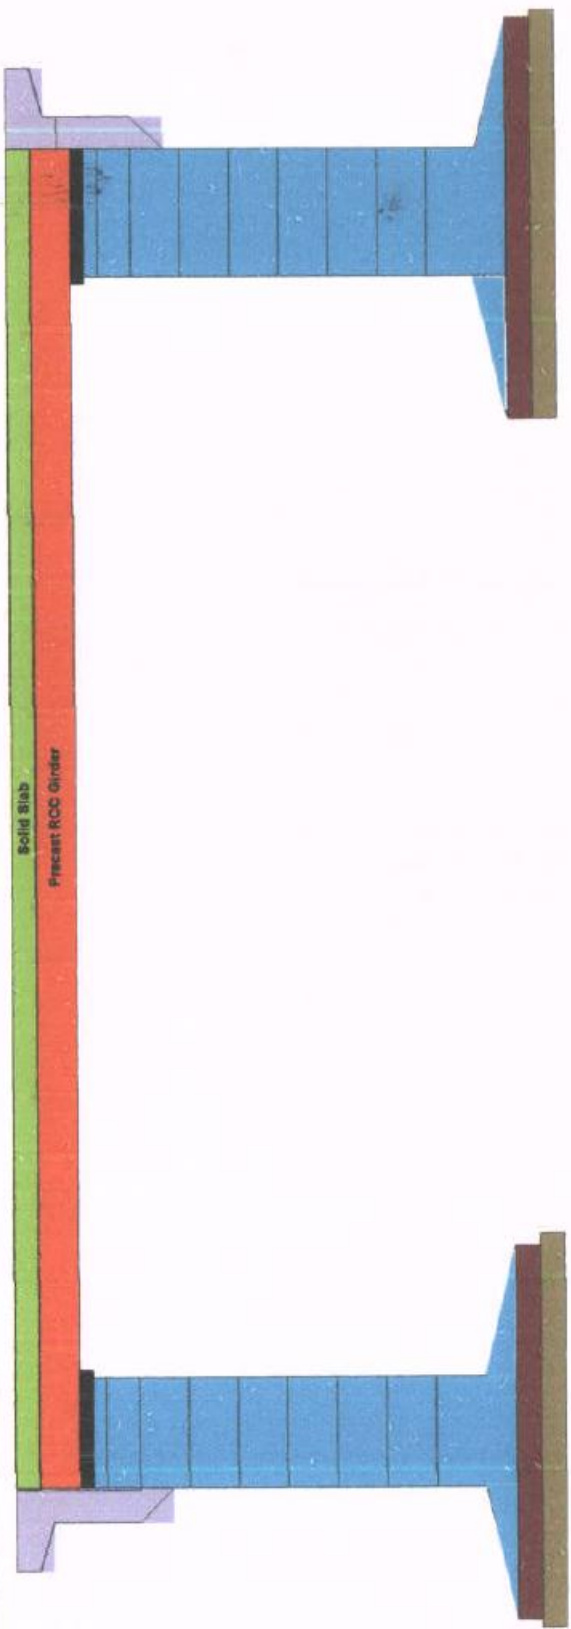

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

Patel Darrah-Jhalawar Highway Pvt. Ltd.


 PATEL

 PCC

 RAJESH KUMAR

Project: Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project (Length 48.860 Km.) - Package II

VEHICULAR UNDERPASS AT 27+029 A1/A2 RHS

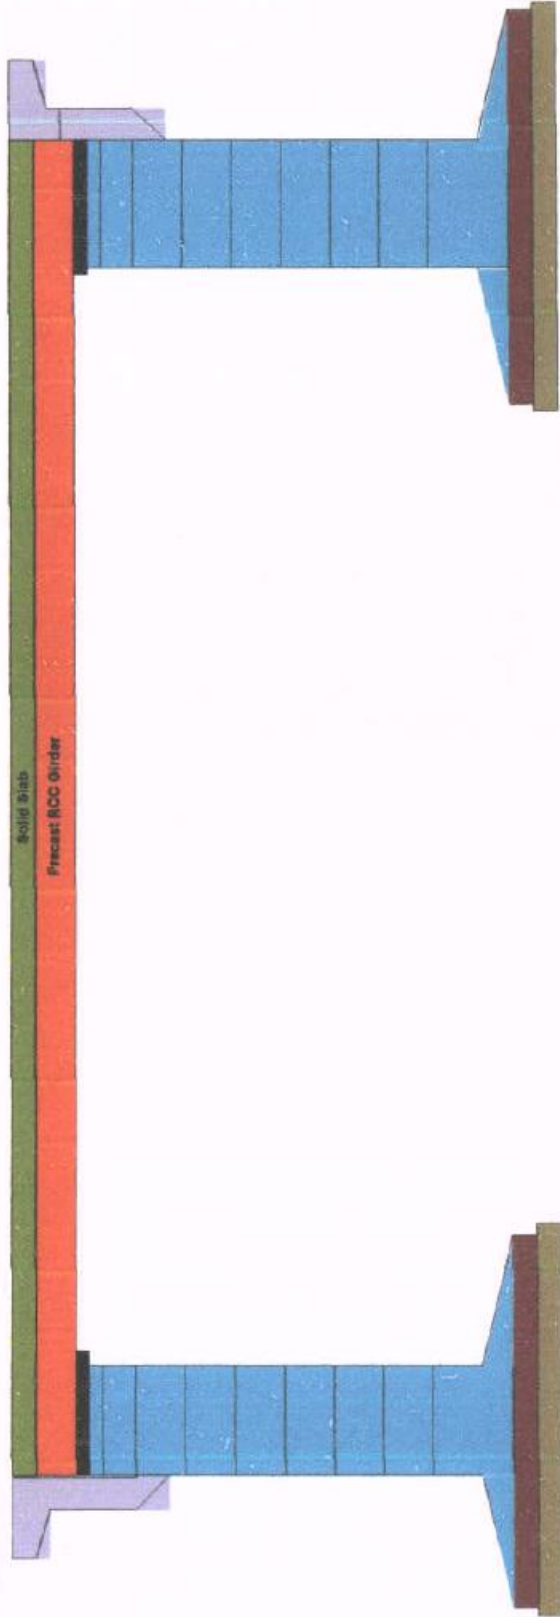

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Pier
PCC

VEHICULAR UNDERPASS AT 27+029 A1/A2 LHS




Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Pier
PCC



Handwritten signature


Project: -Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darrah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project (Length 48.880 Km.) -Package II

VEHICULAR UNDERPASS AT 30+075 A1/ A2 LHS

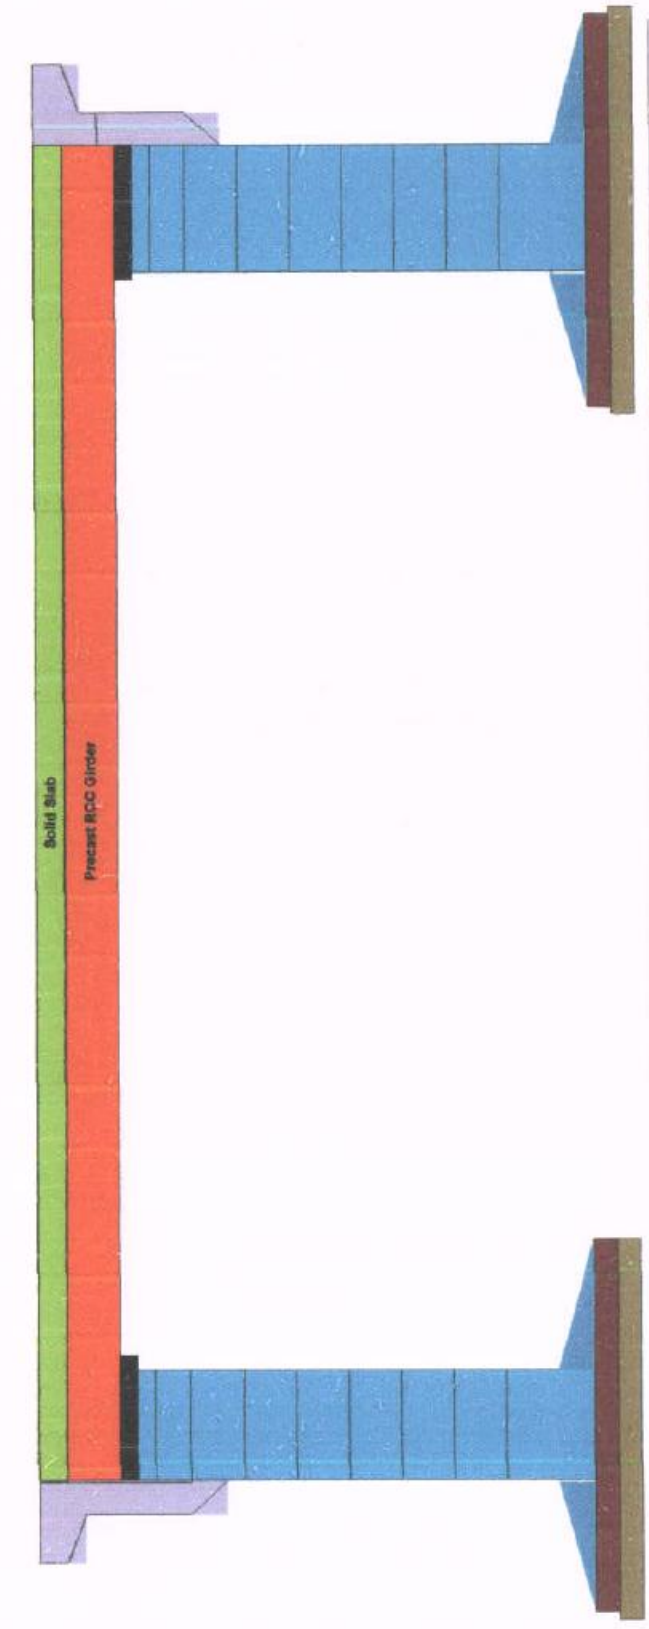

Slab
Order placing
Cap
L/R
L/R
L/R
L/R
L/R
L/R
L/R
L/R
Raft
PCC

VEHICULAR UNDERPASS AT 30+075 A1/A2RHS

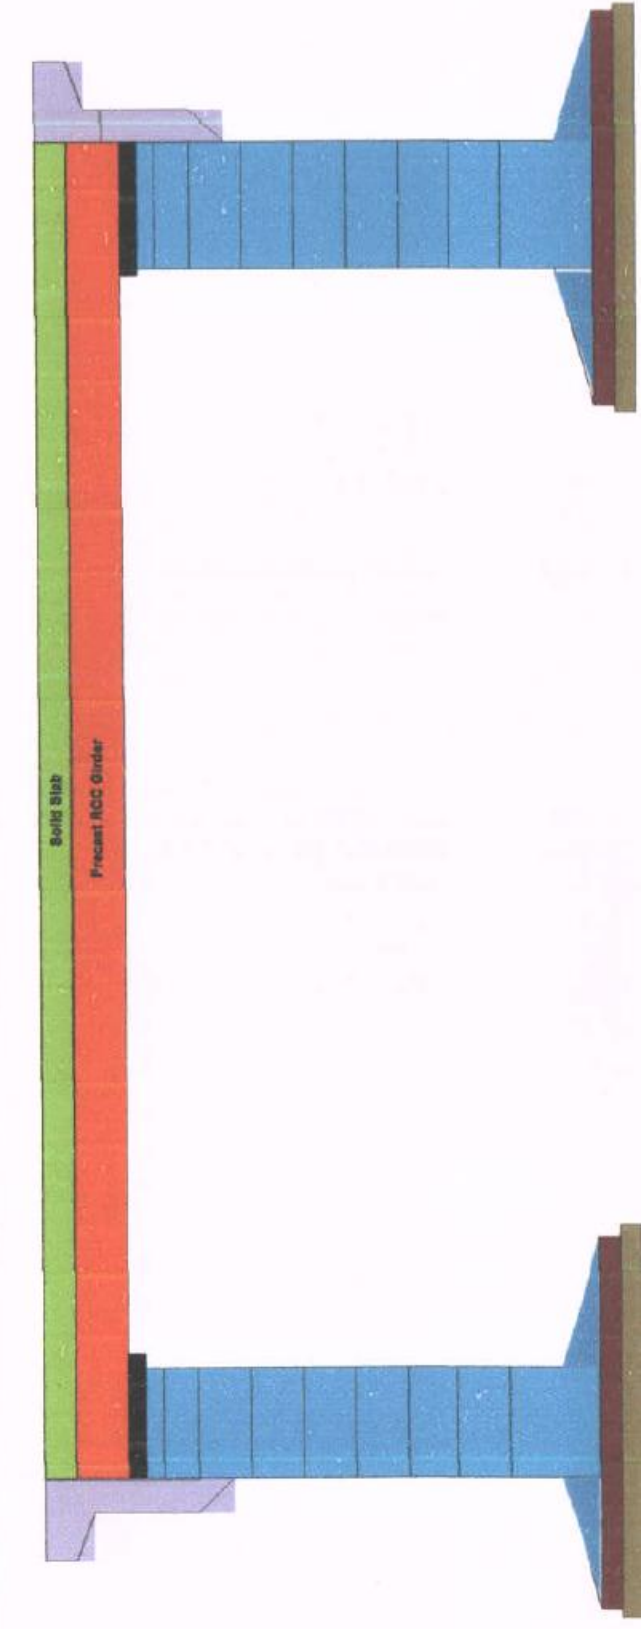

Slab
Girder placing
Cap
L/R
L/R
L/R
L/R
L/R
L/R
Raft
PCC

Patel Darrah-Jhalawar Highway Pvt. Ltd.

 PATEL


 Patel

(Handwritten signature)

Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project (Length 48.880 Km.) -Package II


VEHICULAR UNDERPASS AT 41+095 A1/ A2 LHS

Slab
Girder placing
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

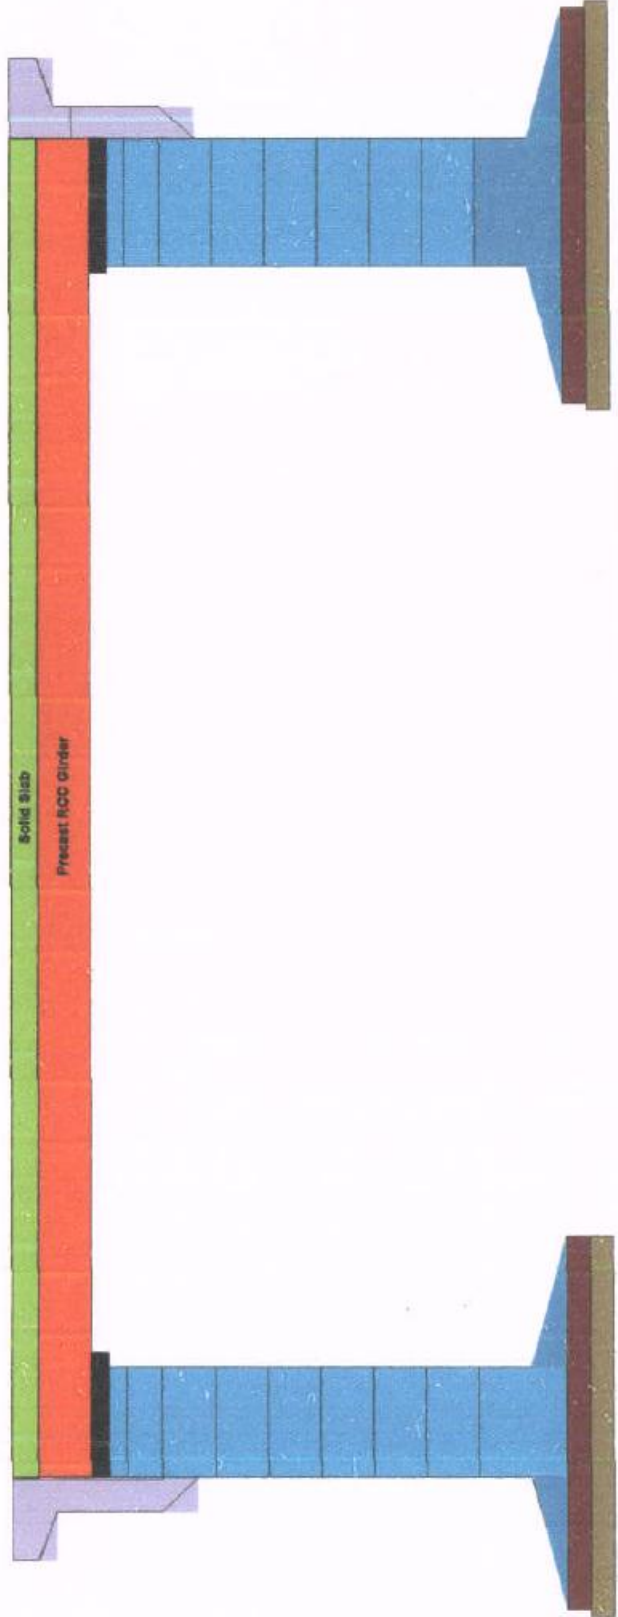

VEHICULAR UNDERPASS AT 41+095 A1 /A2RHS

Slab
Girder placing
Cap
Lift
Lift
Lift
Raft
PCC

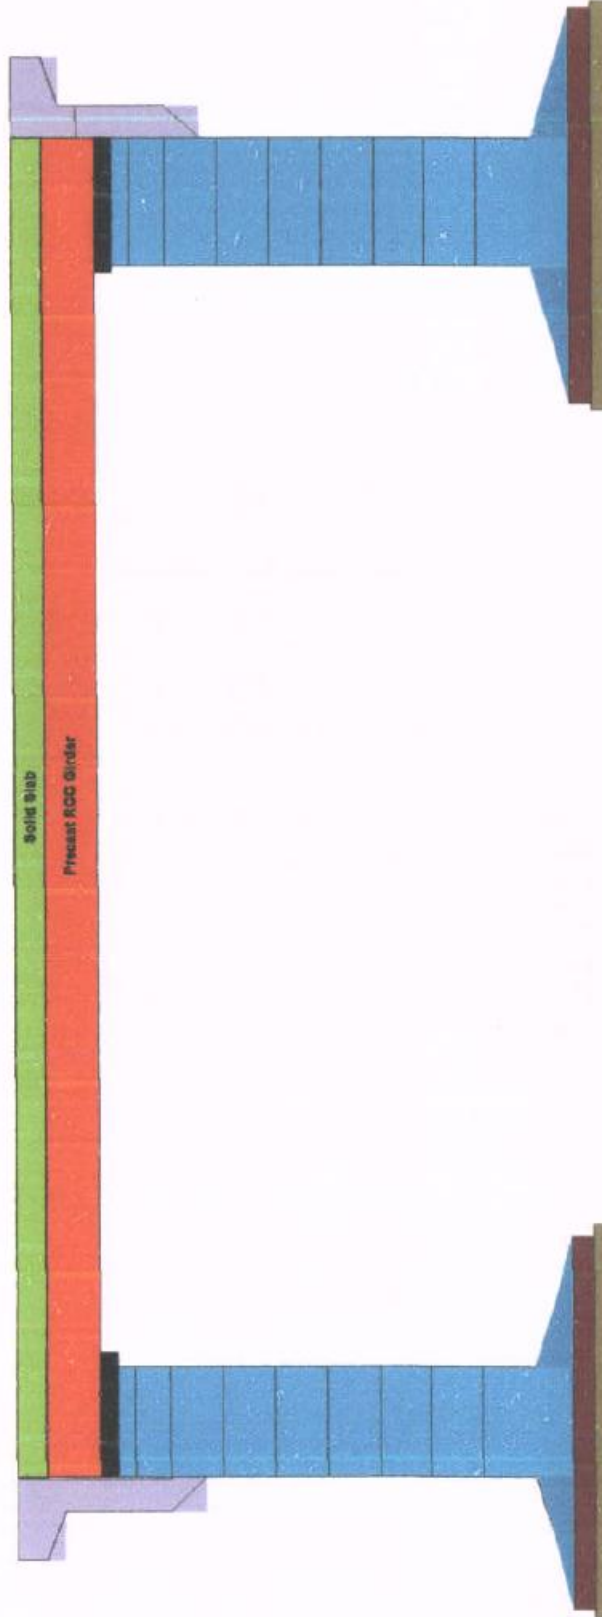


Darah-Jhalawar Highway Pvt. Ltd.
 Lift
PATEL
 Lift
 20/08/2024

Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.640 (Design Chainage from 9.860 to 68.740) (Darrah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project (Length 48.880 Km.) -Package II

VEHICULAR UNDERPASS AT 49+330A1/ A2 LHS

Slab
Girder piling
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC

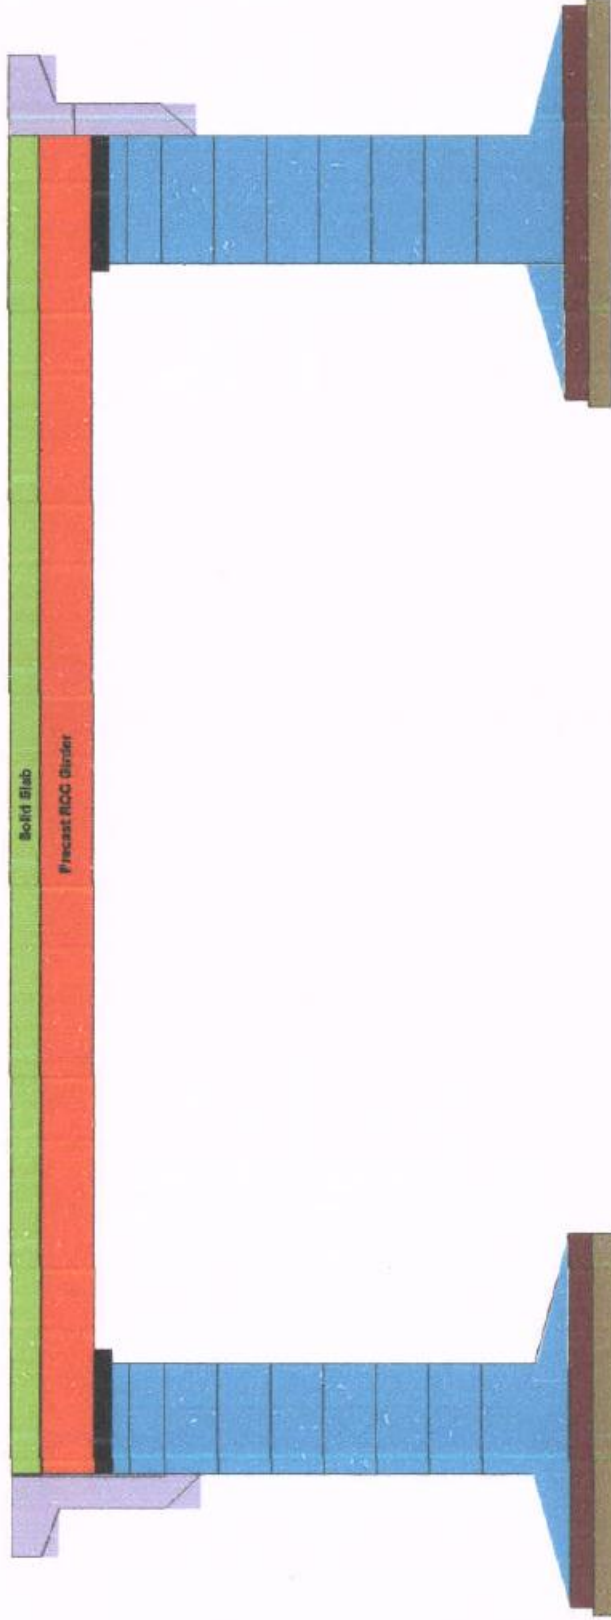

VEHICULAR UNDERPASS AT 49+330 A1 /A2RHS

Slab
Girder piling
Cap
Lift
Lift
Lift
Lift
Lift
Lift
Raft
PCC



Handwritten signature and a circular official stamp of the project engineer.

Stamp: Patel Darrah-Jhalawar Highway Pvt. Ltd. PATEL

Signature: [Handwritten Signature]

Project: Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chalmage from 9.880 to 68.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project (Length 46.880 Km.) -Package II

VEHICULAR UNDERPASS AT 54+550 A1/ A2 LHS

Slab
Girder placing
Cap
L/R
L/R
L/R
L/R
L/R
L/R
L/R
R/R
PCC






VEHICULAR UNDERPASS AT 54+560 A1/A2 RHS

Slab
Girder placing
Cap
L/R
L/R
L/R
L/R
L/R
L/R
R/R
PCC










 PATEL

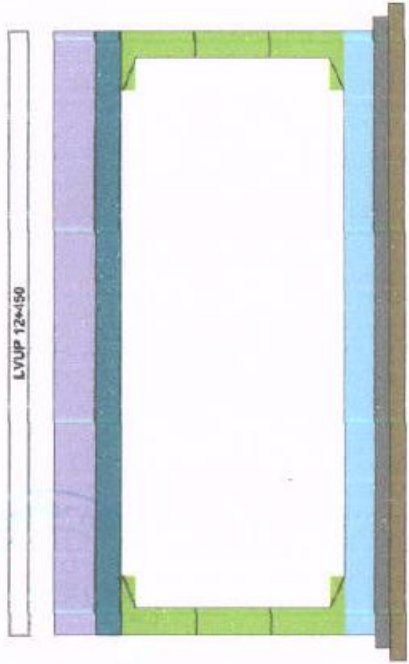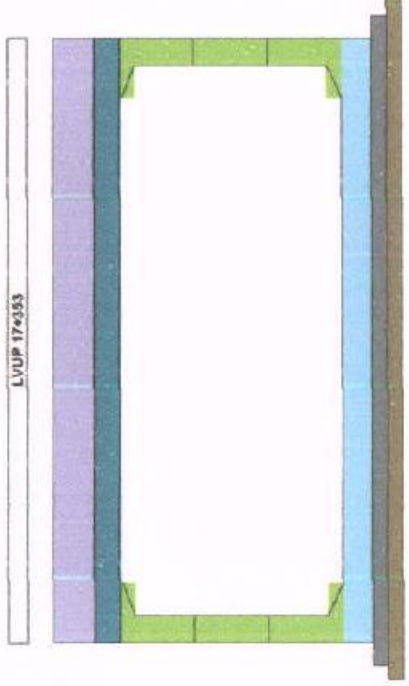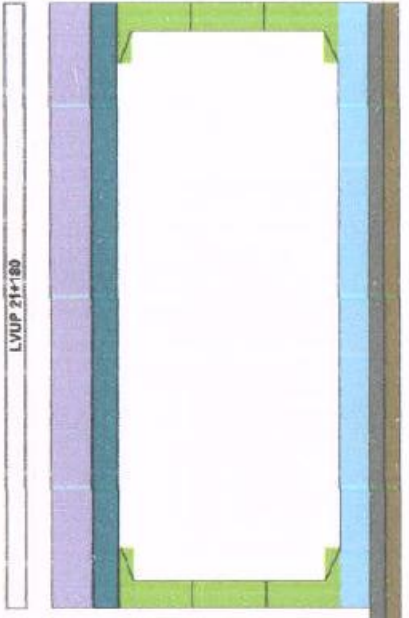

CB
Divs. Hdb.
LFH
UIC
LFH
SBFT
Excavation
Chainage

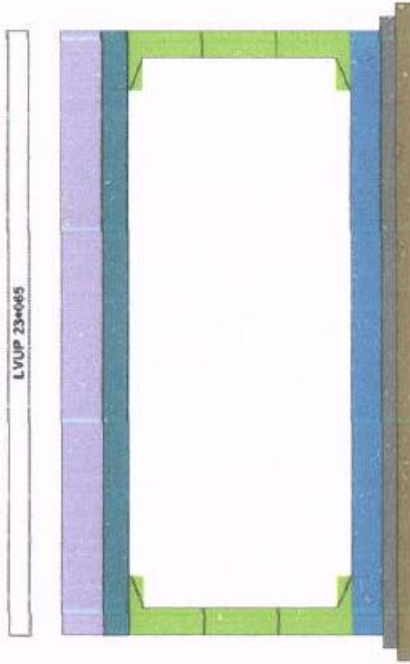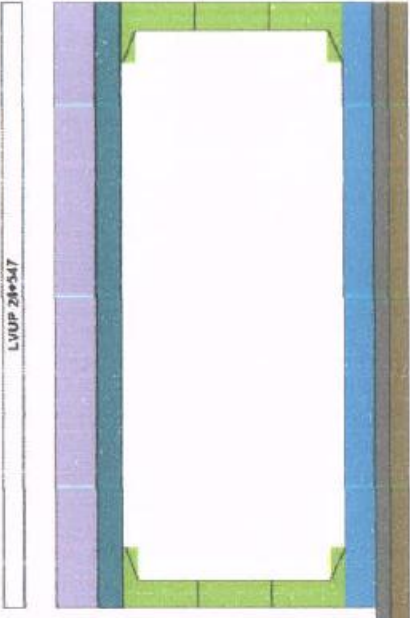




CB
Divs. Hdb.
LFH
UIC
LFH
SBFT
Excavation

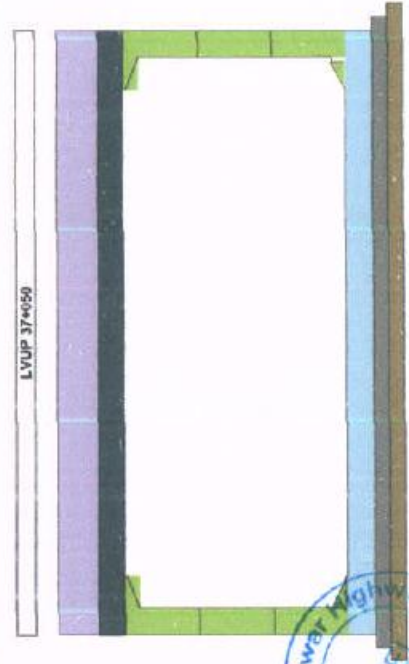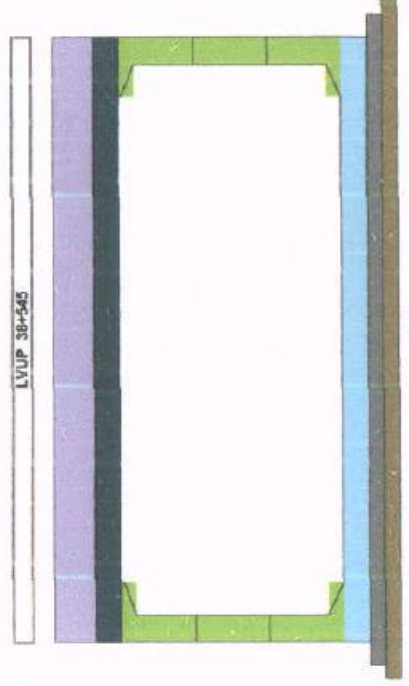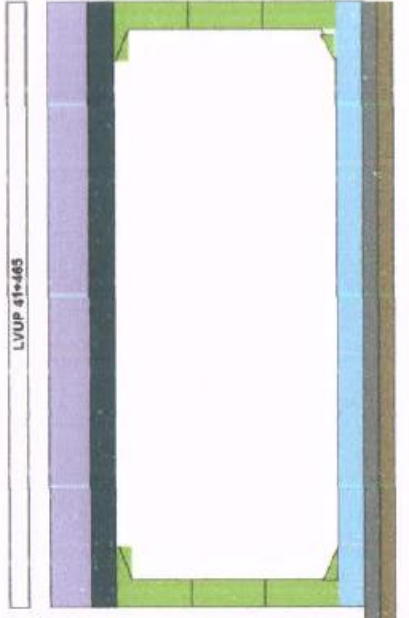


CB
Divs. Hdb.
LFH
UIC
LFH
SBFT
Excavation

Stamp: Darah-Jhalawar Highway P.W. Dept. Rajasthan
 Signature: S. K. Singh

Chainage
CB
Deck Slab
UP
UP
UP
Rest
PC-C
Excavation

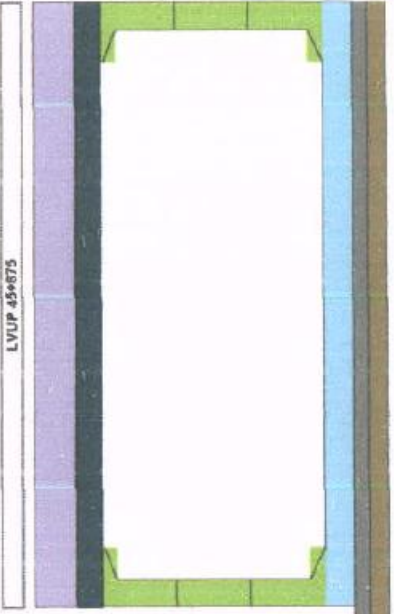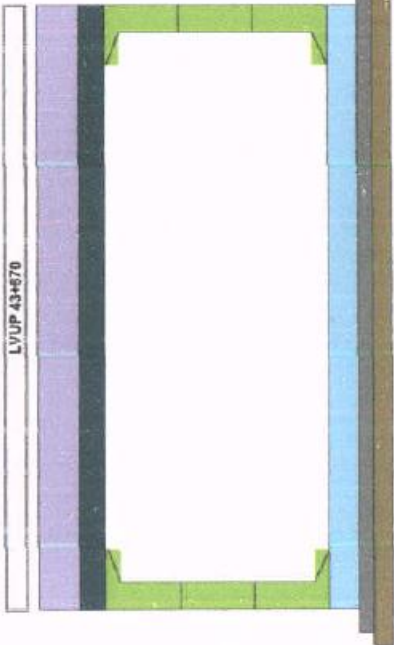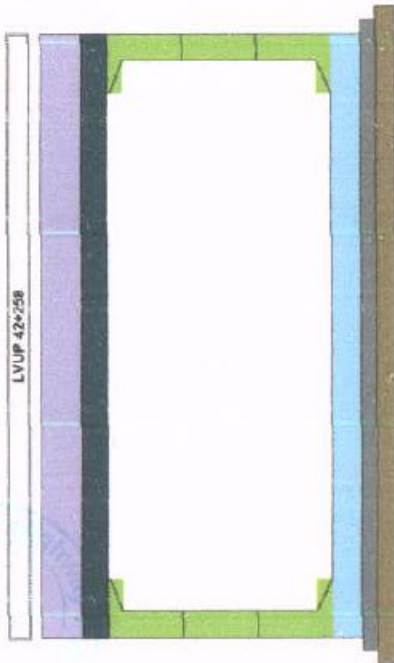


Chainage
CB
Deck Slab
UP
UP
UP
Rest
PC-C
Excavation

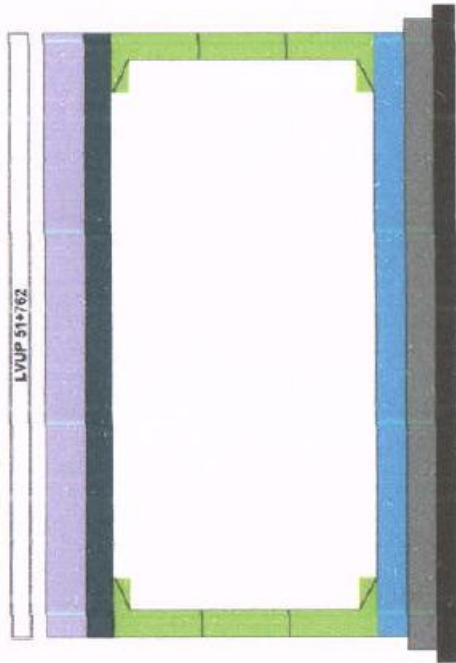


Project: Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9,850 to 58,740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project (Length 48,880 Km.) -Package II

FLYOVER (46+957)LHS

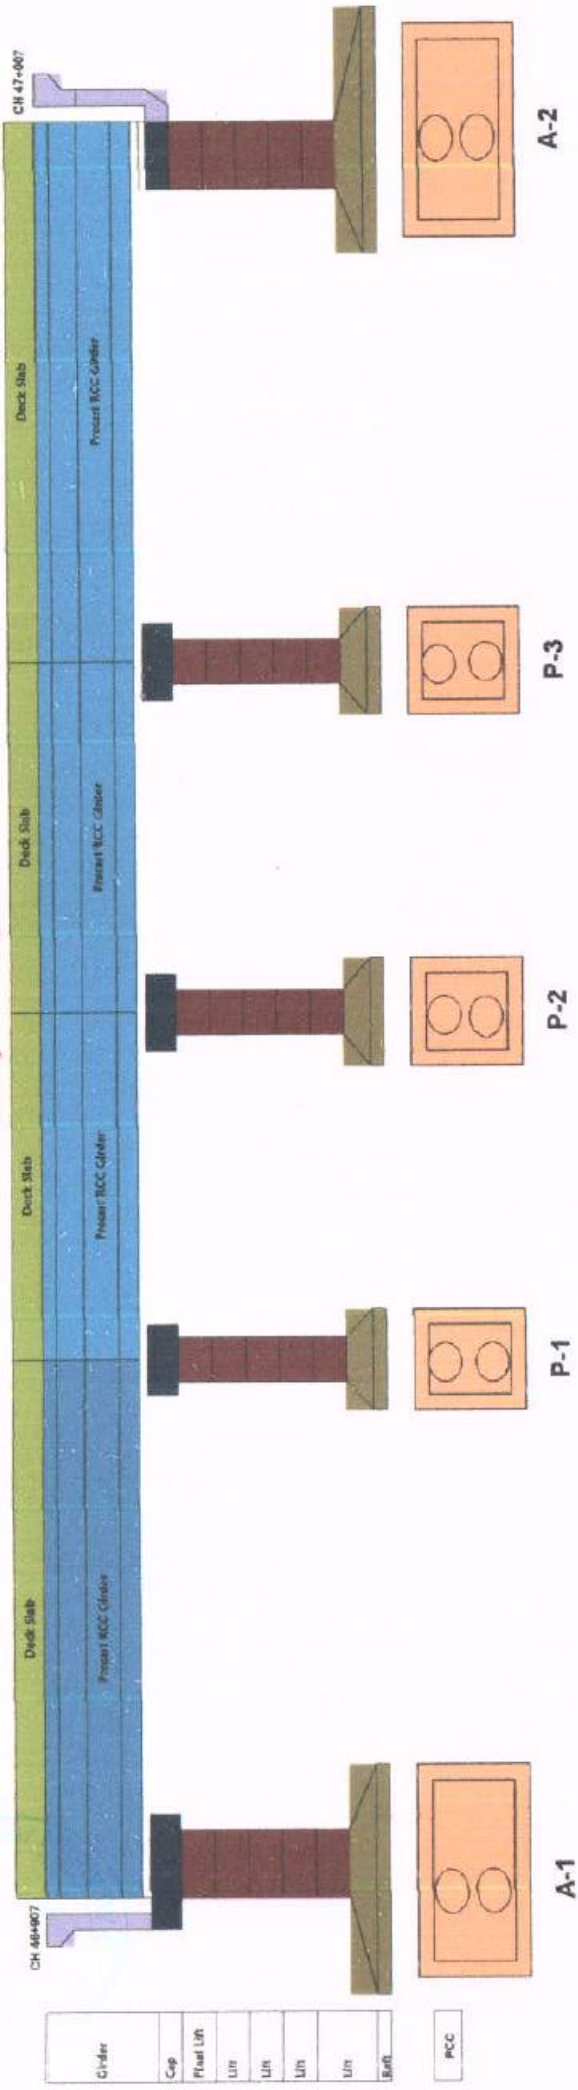


FLYOVER (46+957)RHS

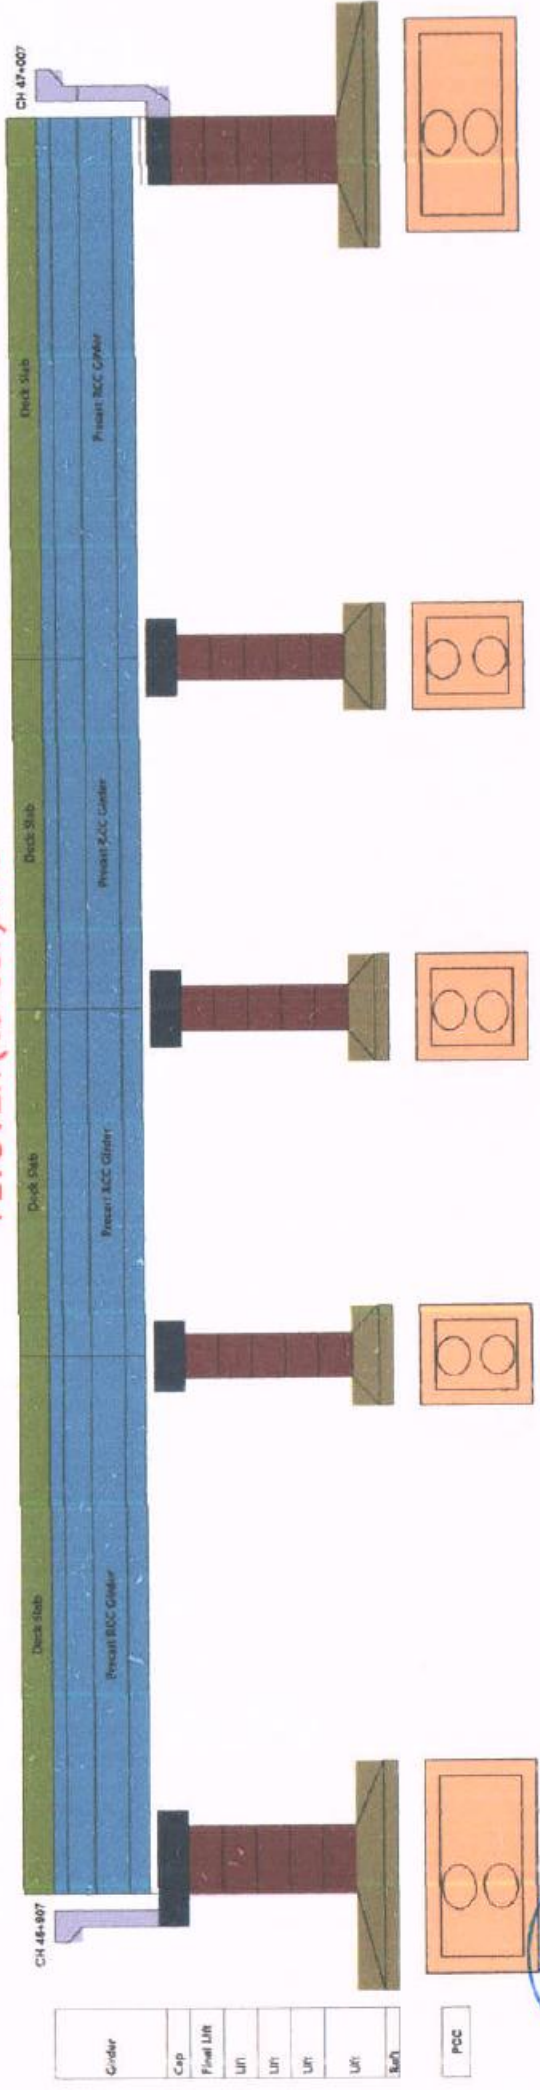


Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darrah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

FLYOVER (50+095)RHS

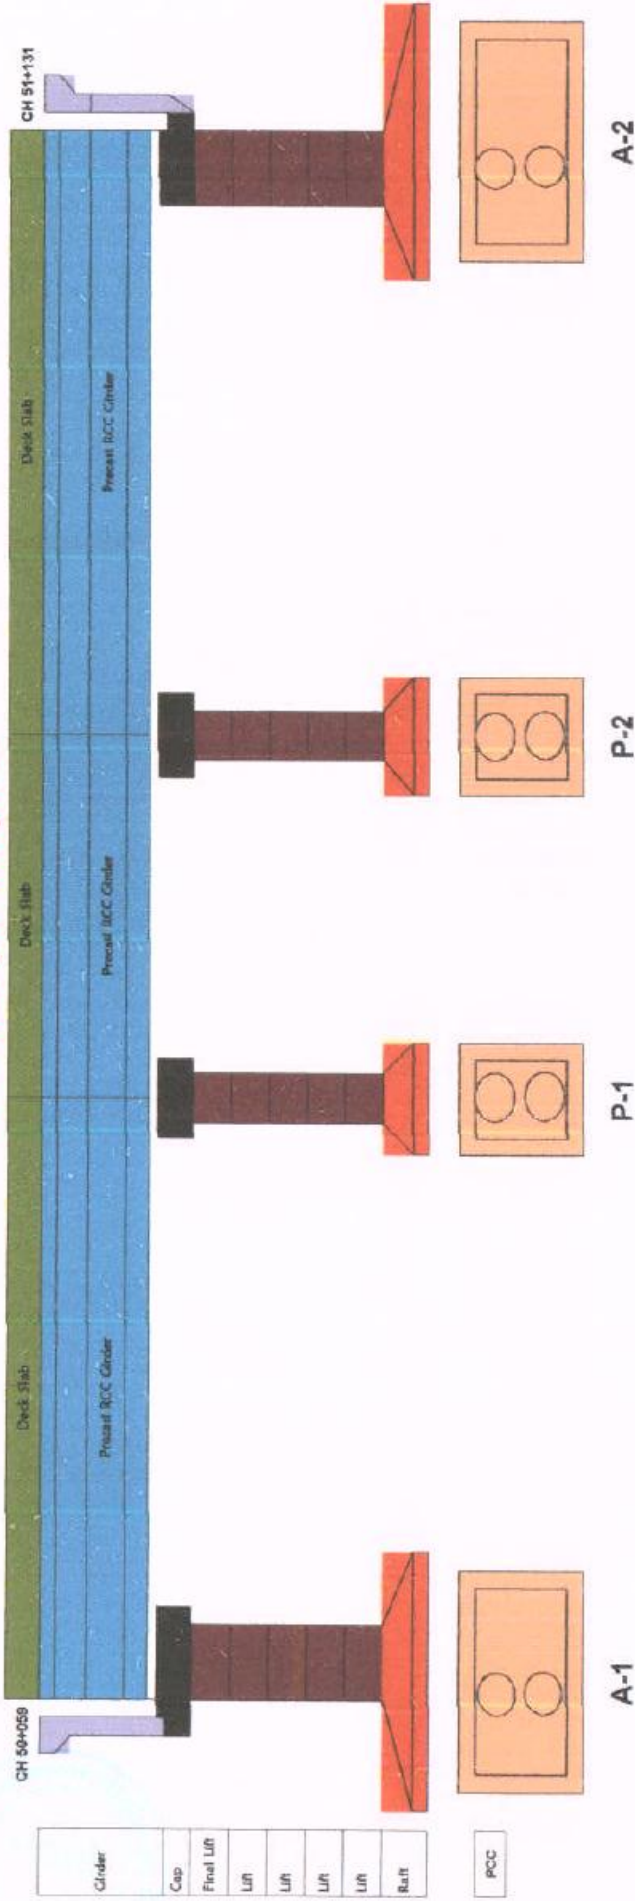


FLYOVER (50+095)LHS

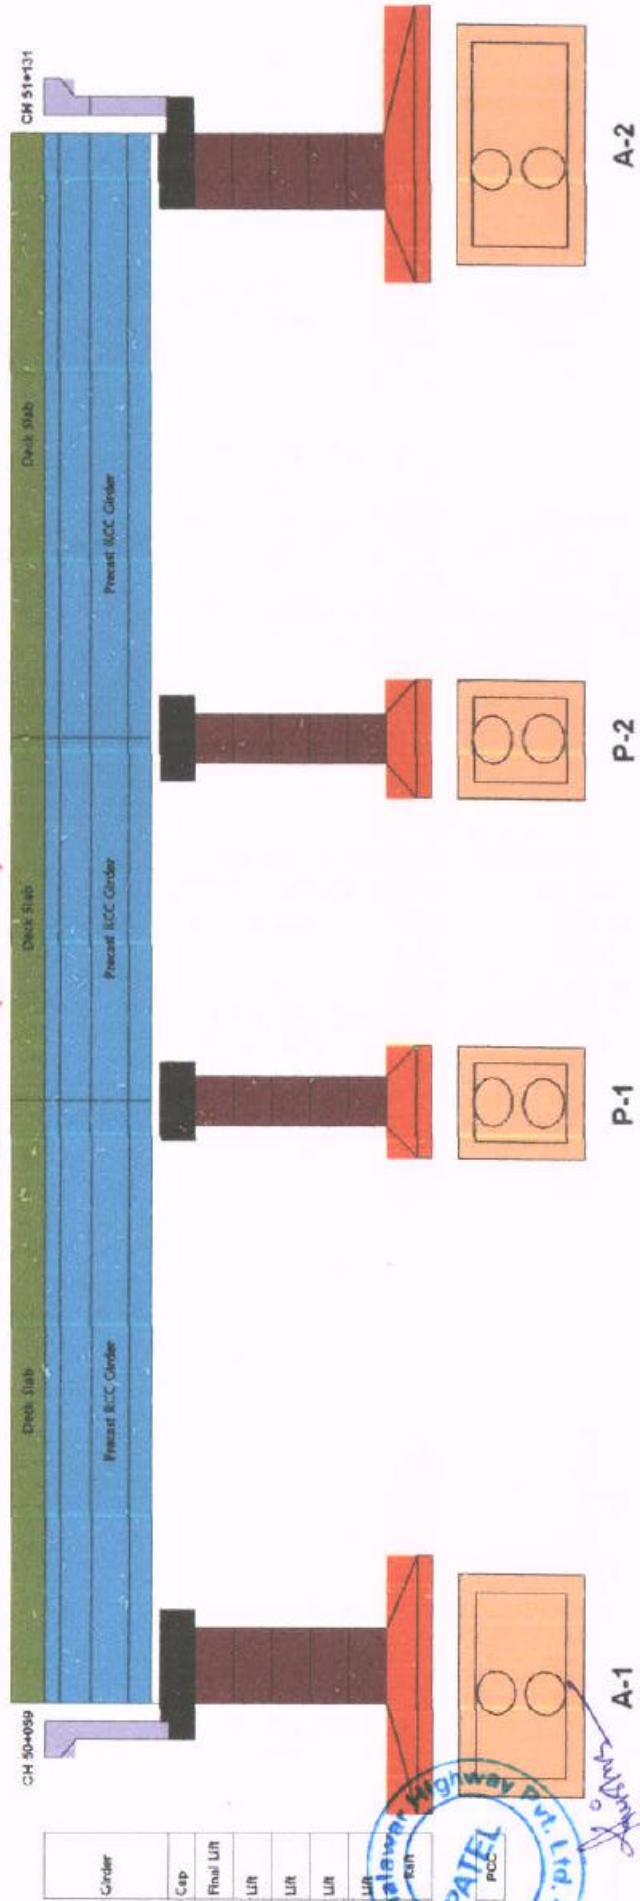


Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

FLYOVER (58+128)RHS

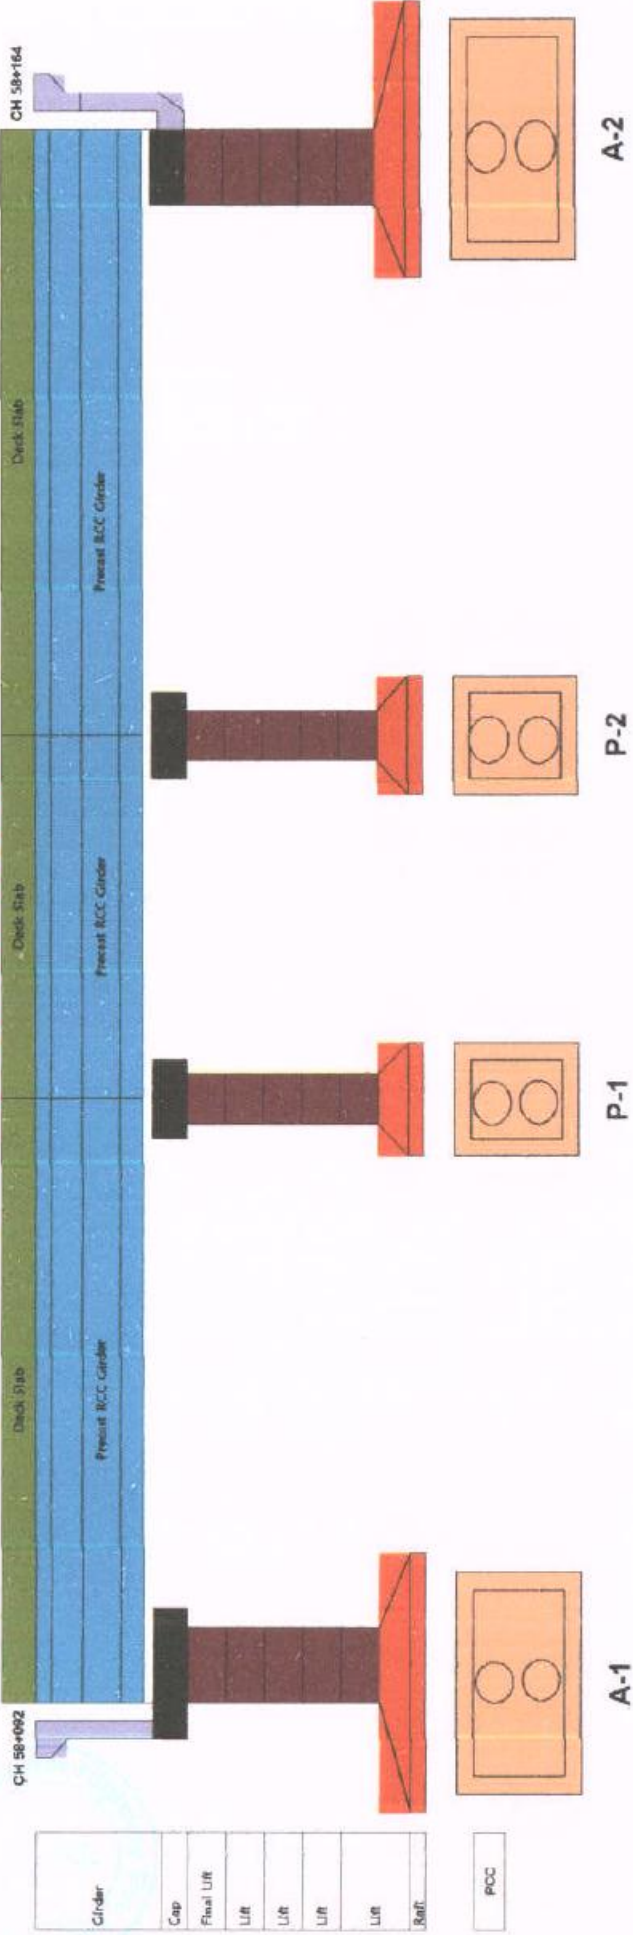


FLYOVER (58+128)LHS

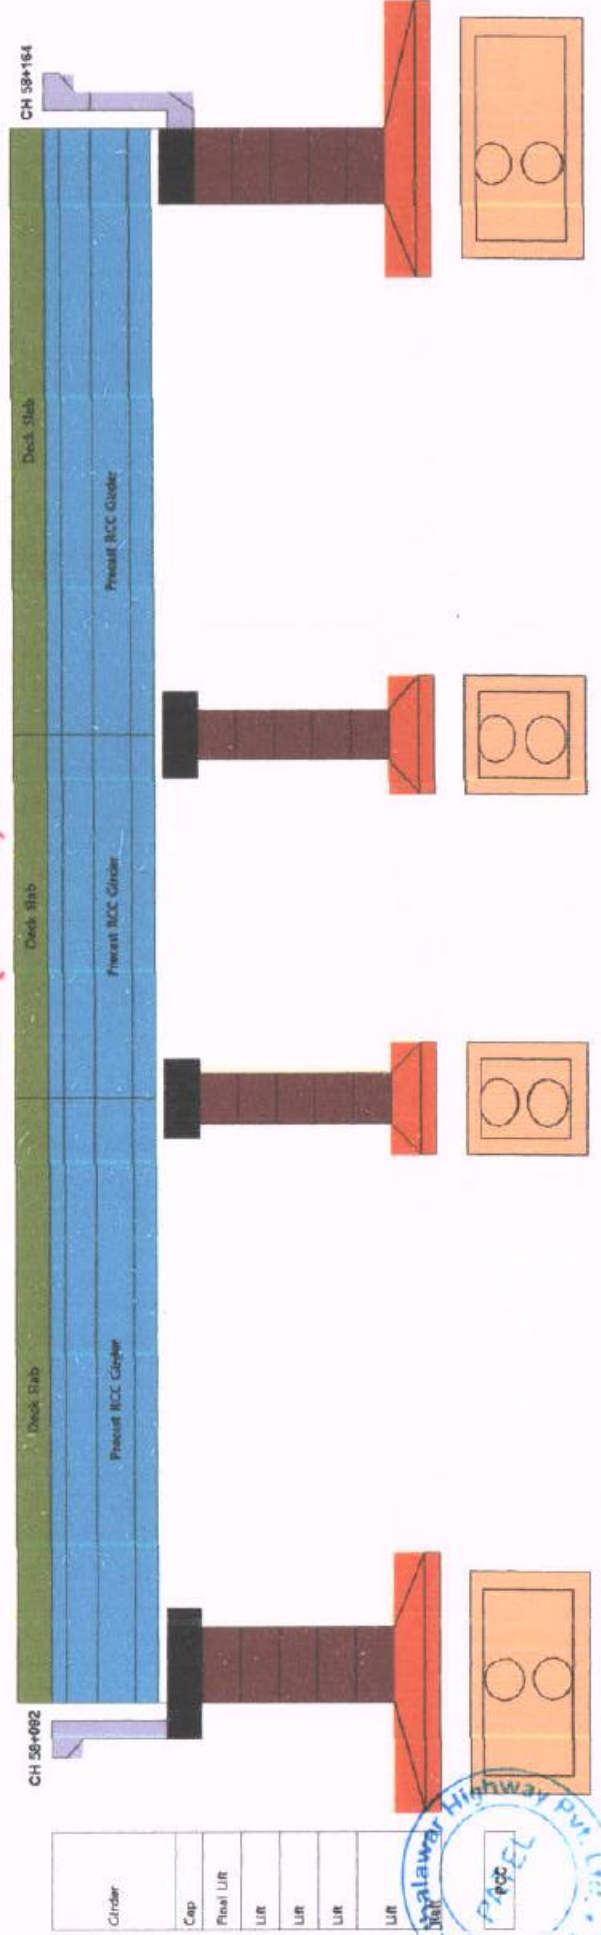


Jhalawar Highway Pvt. Ltd.
 Darah-Jhalawar-Teendhar
 Project
 20/06/2024
 Sushant


PUP 31+400

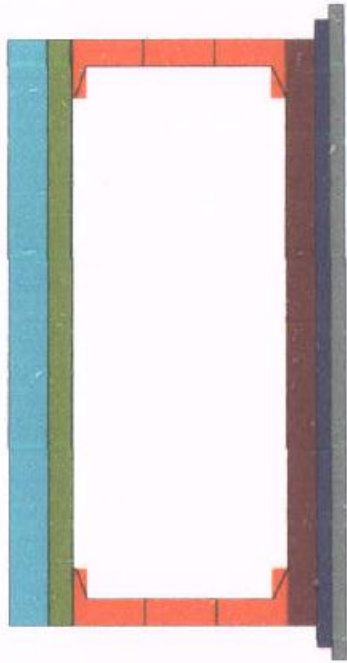


PUP 48+260

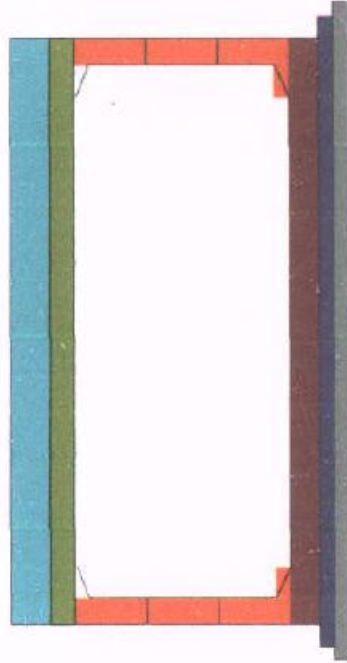

PUP 32+676

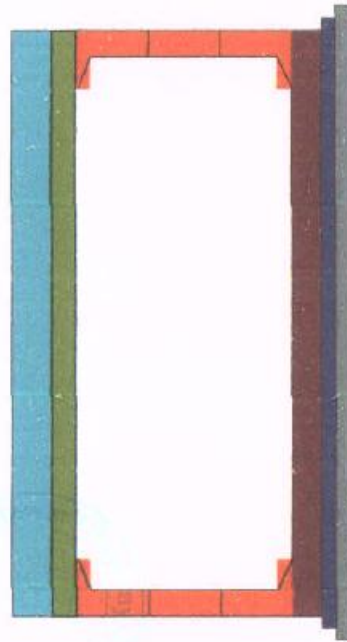

PUP 28+590

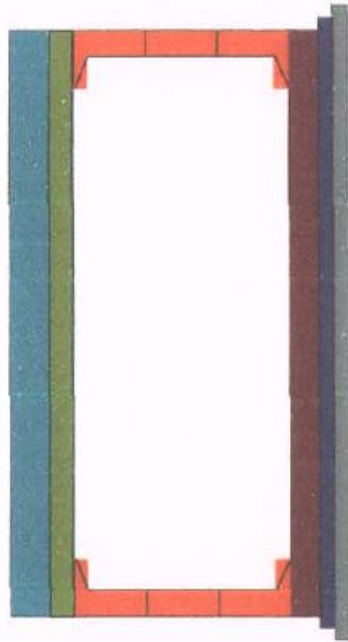


CB	
Distt. Wall	
UR	
UR	
UR	
Surf	
PCC	
Excavation	

CF	
Distt. Wall	
UR	
UR	
UR	
Surf	
PCC	
Excavation	


PAIEL
 Patel Darah-Jhalawar Highway Pvt. Ltd.
 JALAWAR

Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 53.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

MAJOR BRIDGE AT 36+070 (AHU RIVER) LHS

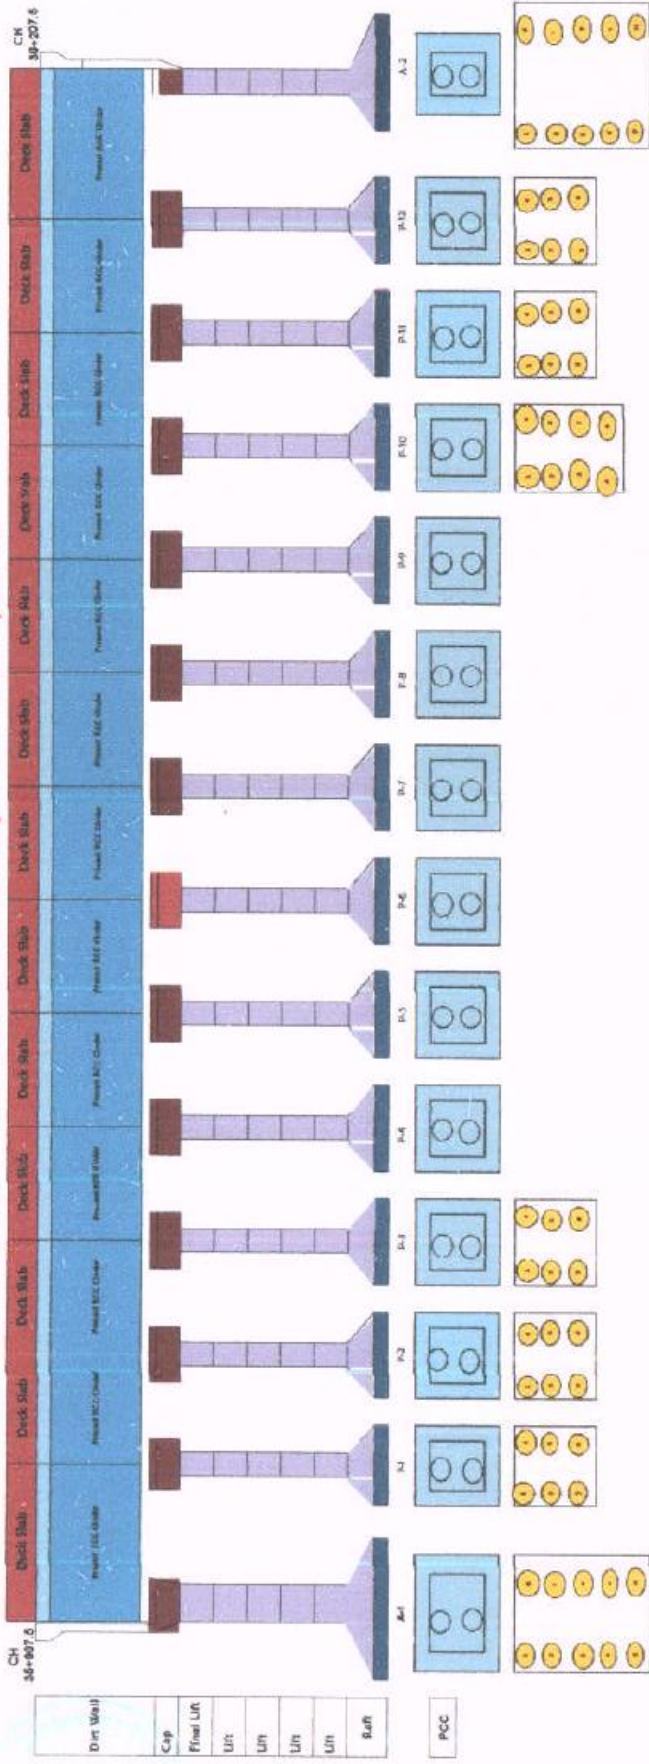

MAJOR BRIDGE AT 36+070 (AHU RIVER) RHS

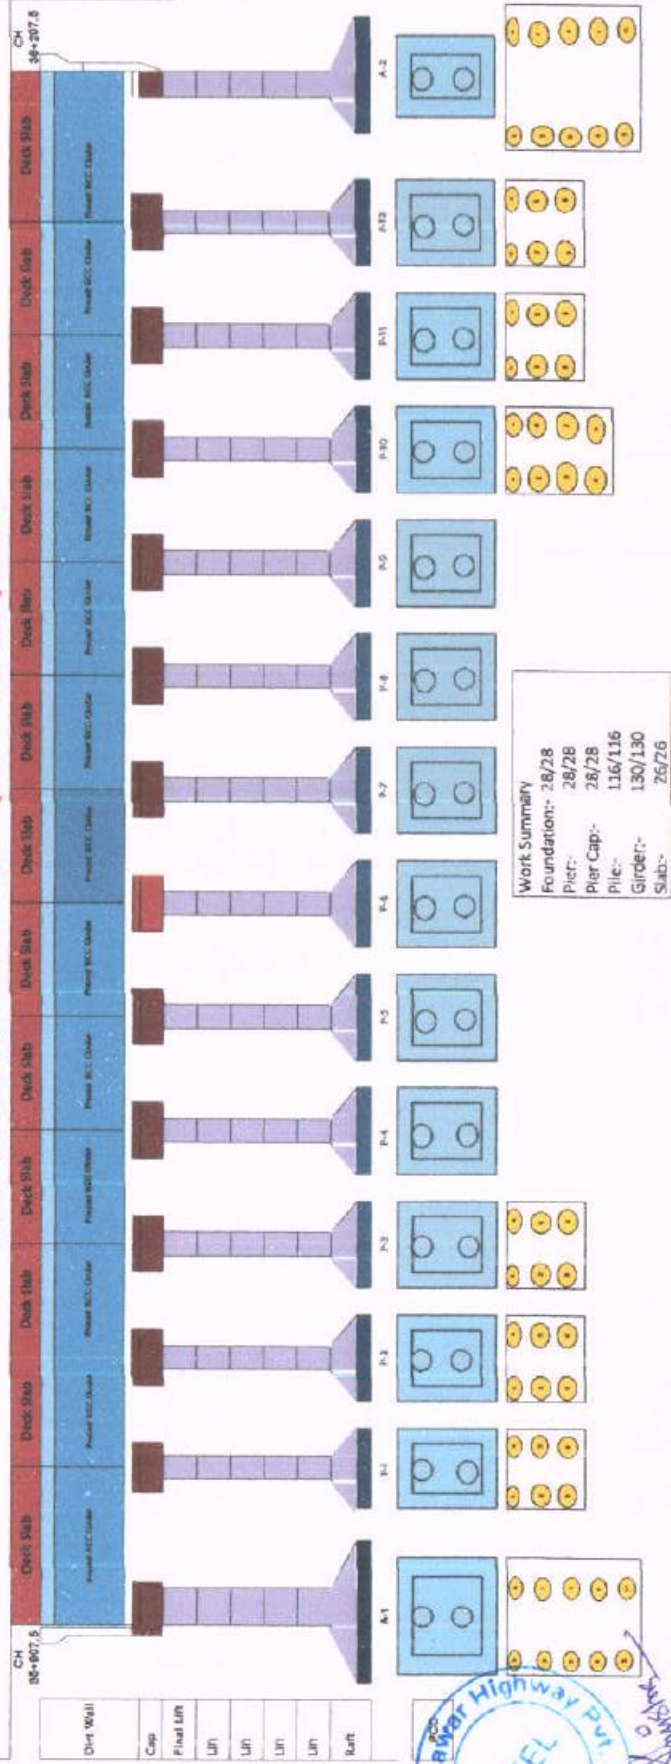

Work Summary	
Foundation:-	28/28
Pier:-	28/28
Pier Cap:-	28/28
Pile:-	116/116
Girder:-	130/130
Sub:-	76/76




Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.640 (Design Chainage from 9.860 to 58.740) (Darrah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

CH 56+902.300

MAJOR BRIDGE AT 57+127

CH 57+313.100

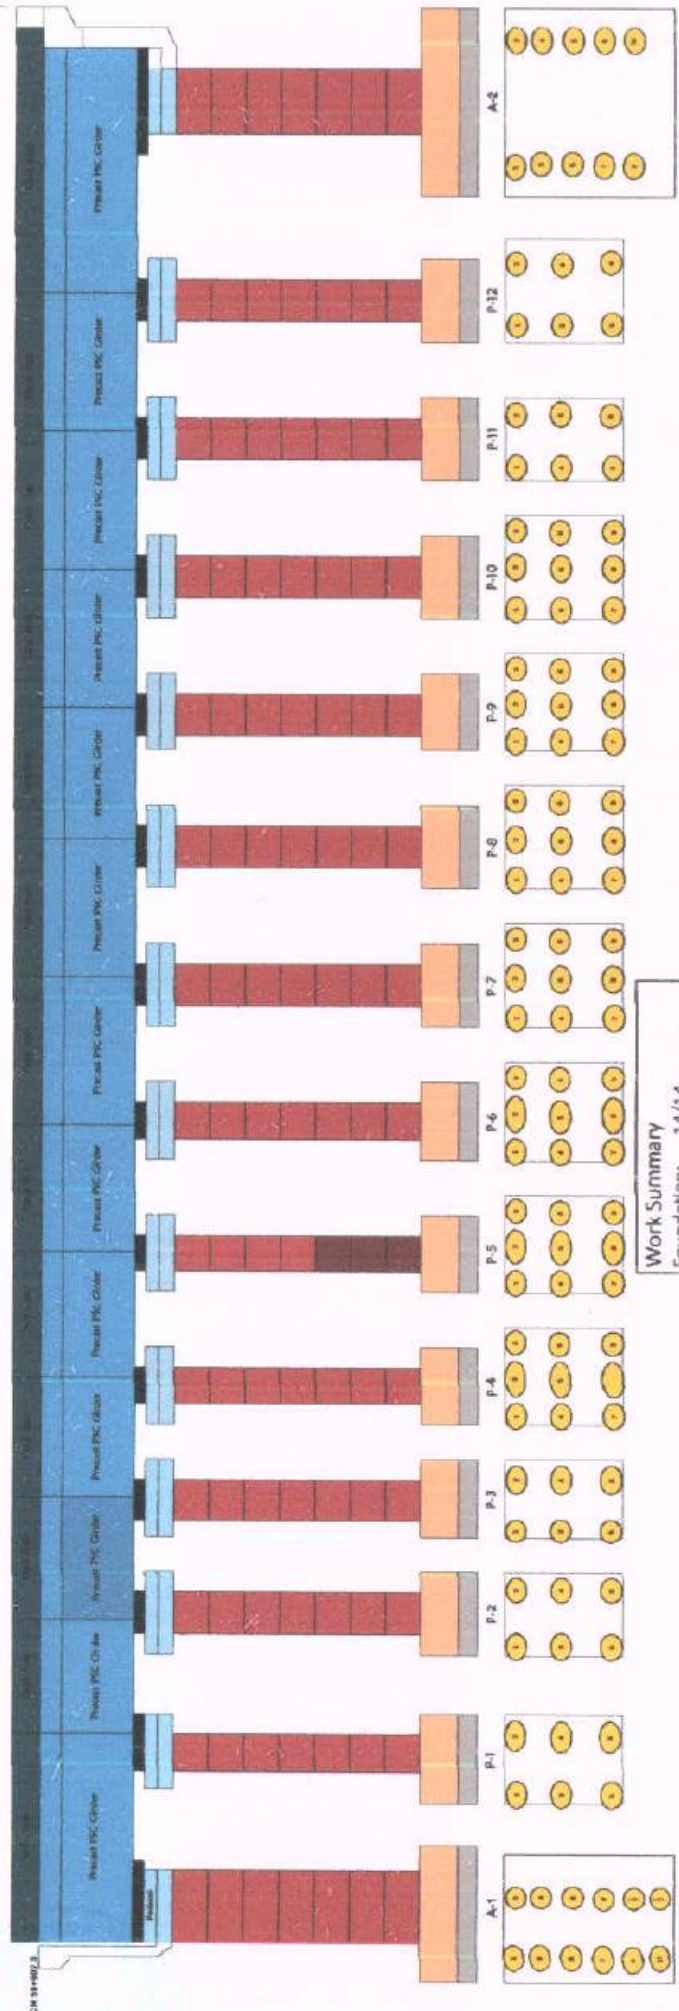

Work Summary

Foundation:-	14/14
Pile:-	115/115
Pile Cap:-	14/14
Pier:-	14/14
Pier Cap:-	14/14
Girer Casting:-	65/55


Scale	
Dist. West	
Cap	
Base	
Abut. 1st	
Abut. 2nd	
Abut. 3rd	
Abut. 4th	
Abut. 5th	
Abut. 6th	
Abut. 7th	
Abut. 8th	
Abut. 9th	
Abut. 10th	
Abut. 11th	
Abut. 12th	
Abut. 13th	
Abut. 14th	
Abut. 15th	
Abut. 16th	
Abut. 17th	
Abut. 18th	
Abut. 19th	
Abut. 20th	
Abut. 21st	
Abut. 22nd	
Abut. 23rd	
Abut. 24th	
Abut. 25th	
Abut. 26th	
Abut. 27th	
Abut. 28th	
Abut. 29th	
Abut. 30th	
Abut. 31st	
Abut. 32nd	
Abut. 33rd	
Abut. 34th	
Abut. 35th	
Abut. 36th	
Abut. 37th	
Abut. 38th	
Abut. 39th	
Abut. 40th	
Abut. 41st	
Abut. 42nd	
Abut. 43rd	
Abut. 44th	
Abut. 45th	
Abut. 46th	
Abut. 47th	
Abut. 48th	
Abut. 49th	
Abut. 50th	
Abut. 51st	
Abut. 52nd	
Abut. 53rd	
Abut. 54th	
Abut. 55th	
Abut. 56th	
Abut. 57th	
Abut. 58th	
Abut. 59th	
Abut. 60th	
Abut. 61st	
Abut. 62nd	
Abut. 63rd	
Abut. 64th	
Abut. 65th	
Abut. 66th	
Abut. 67th	
Abut. 68th	
Abut. 69th	
Abut. 70th	
Abut. 71st	
Abut. 72nd	
Abut. 73rd	
Abut. 74th	
Abut. 75th	
Abut. 76th	
Abut. 77th	
Abut. 78th	
Abut. 79th	
Abut. 80th	
Abut. 81st	
Abut. 82nd	
Abut. 83rd	
Abut. 84th	
Abut. 85th	
Abut. 86th	
Abut. 87th	
Abut. 88th	
Abut. 89th	
Abut. 90th	
Abut. 91st	
Abut. 92nd	
Abut. 93rd	
Abut. 94th	
Abut. 95th	
Abut. 96th	
Abut. 97th	
Abut. 98th	
Abut. 99th	
Abut. 100th	



Patel Daraj-Jhalawar Highway Private Limited


Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) - Package II

RUB CH. 33+585 (LHS).

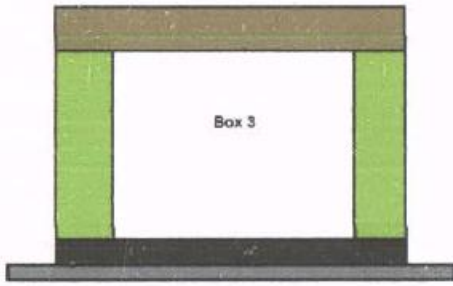


Box 3

RUB CH. 33+585 (RHS).

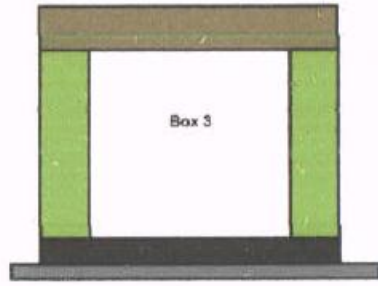


Box 3

RUB CH. 33+585

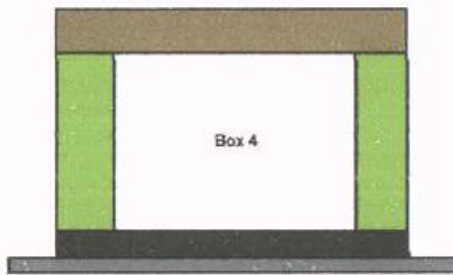


Box 4


RUB CH. 33+585

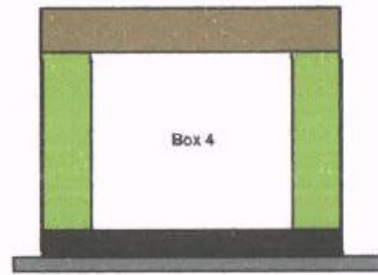


Box 4

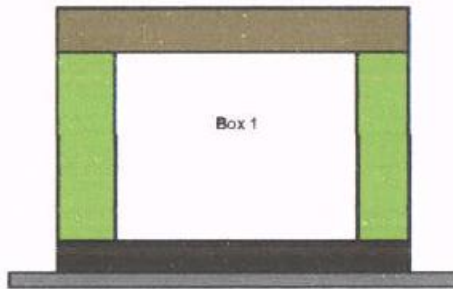


Box 1

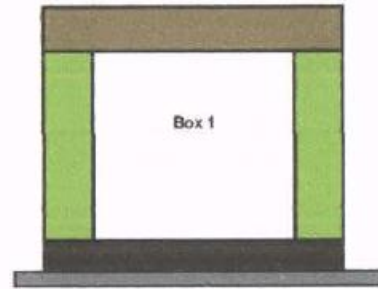


Box 1

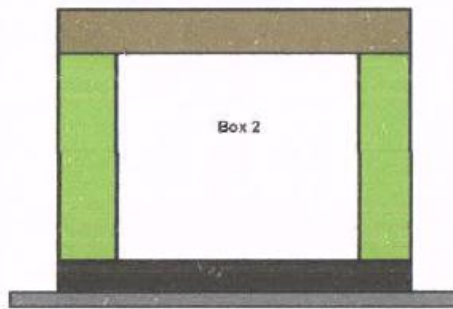


Box 2

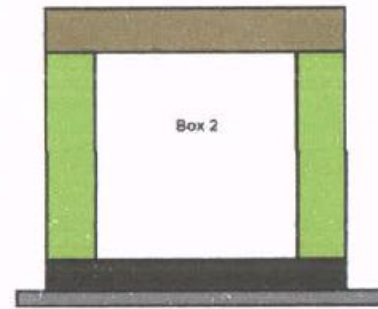

Box 2

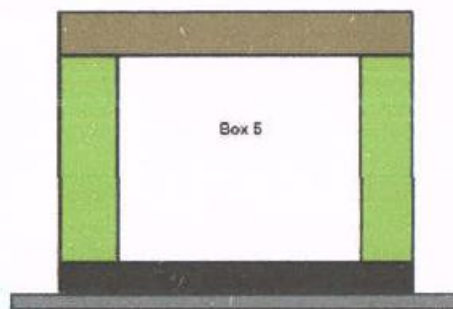

Box 5

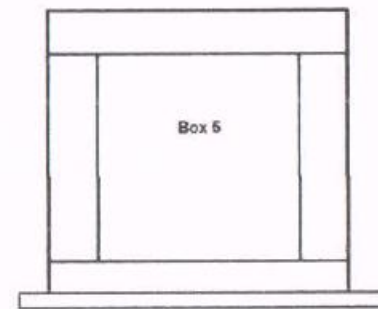


Box 5

Handwritten signature

Patel Daraj-Jhalawar Highway Private Limited

Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 298.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II
 ROB at 44+158

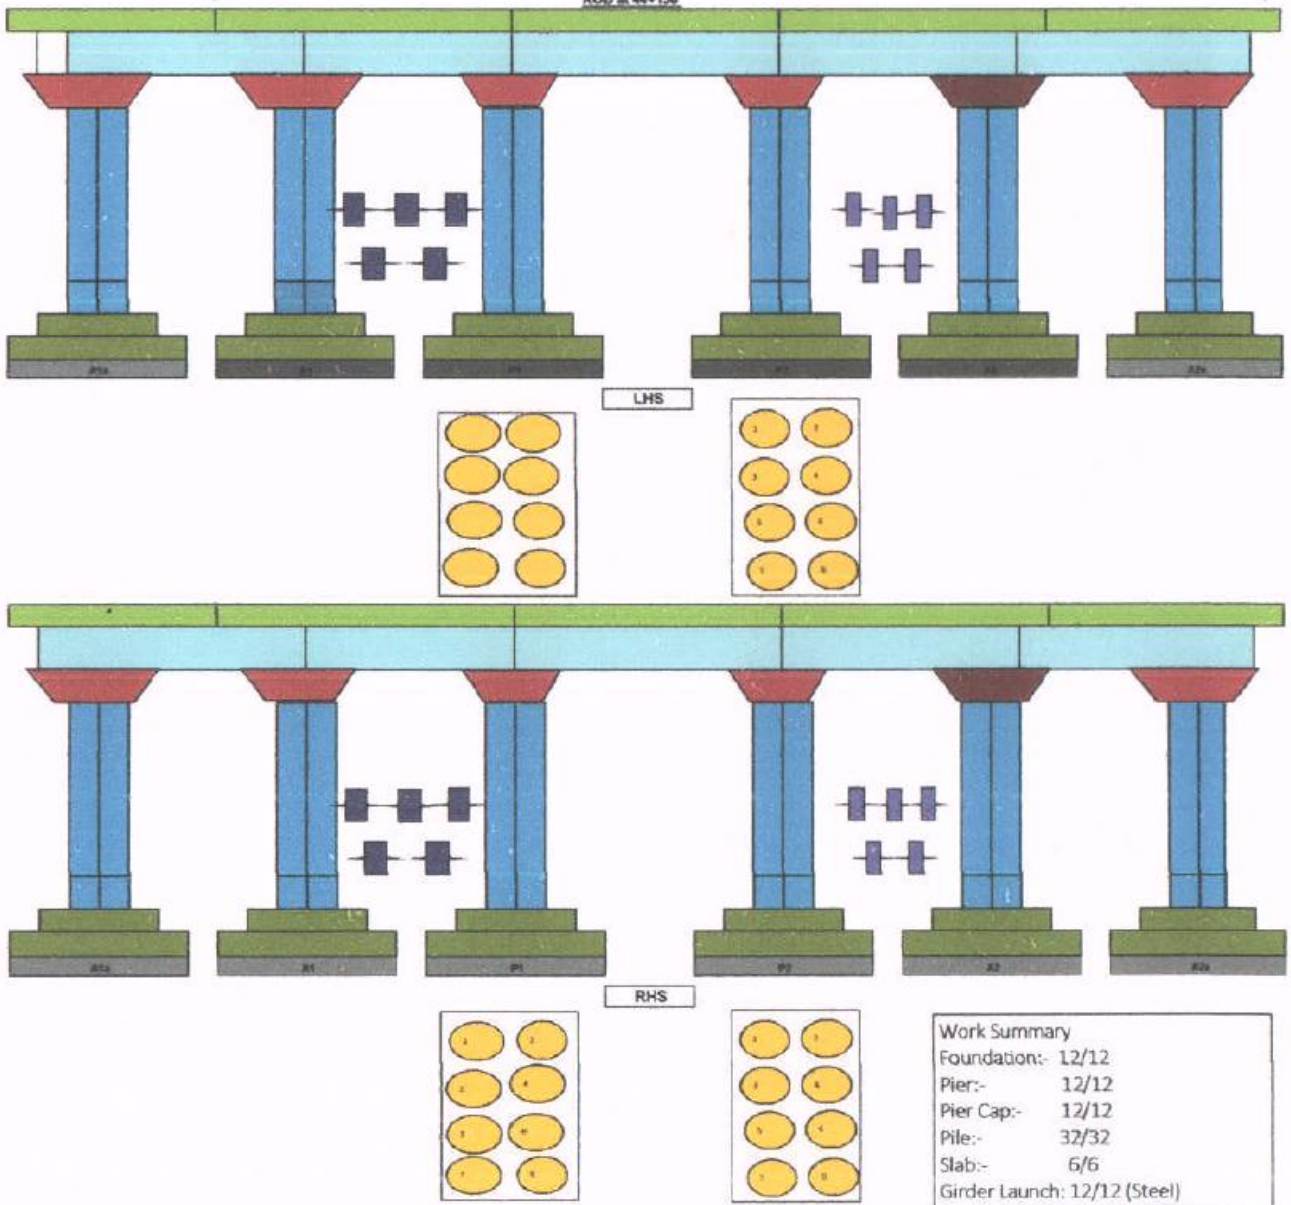


Handwritten signature

Project:-Construction of 4-lane Road on NH-12 (New NH-52) from Km 299.000 to 346.540 (Design Chainage from 9.860 to 58.740) (Darah-Jhalawar-Teendhar section) in the State of Rajasthan under NHDP Phase-III on Hybrid Annuity Project(Length 48.880 Km.) -Package II

FLY OVER + MAJOR BRIDGE(ELEVATED STRUCTURE- 47+580 TO 48+080)LHS

47+580

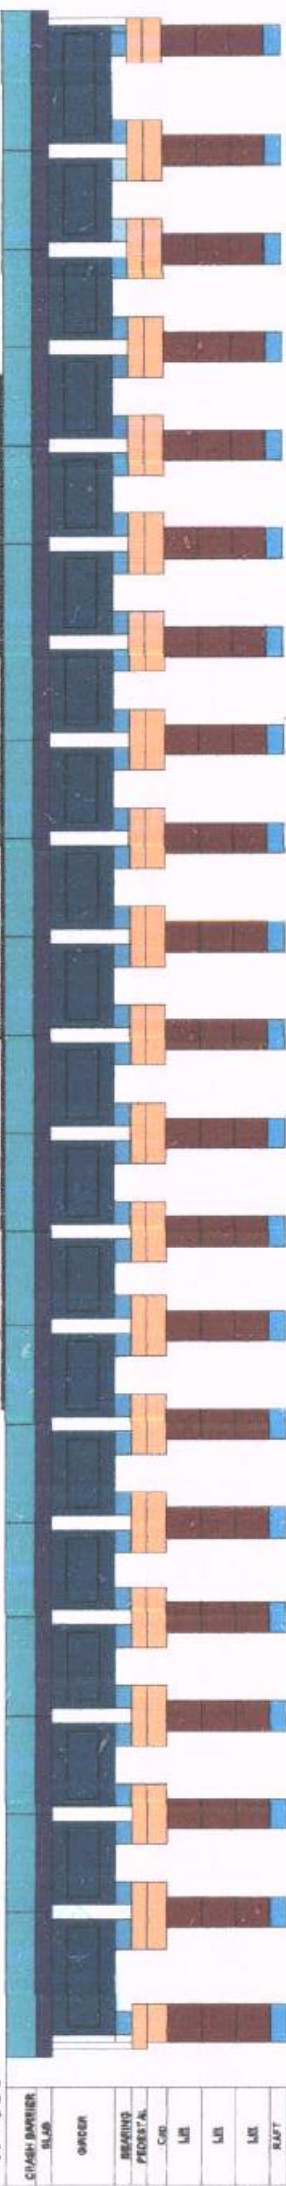


PCC

- A1
- P2
- P3
- P4
- P5
- P6
- P7
- P8
- P9
- P10
- P11
- P12
- P13
- P14
- P15
- P16
- P17
- P18
- P19
- A2

FLY OVER + MAJOR BRIDGE(ELEVATED STRUCTURE- 47+580 TO 48+080) RHS

47+580

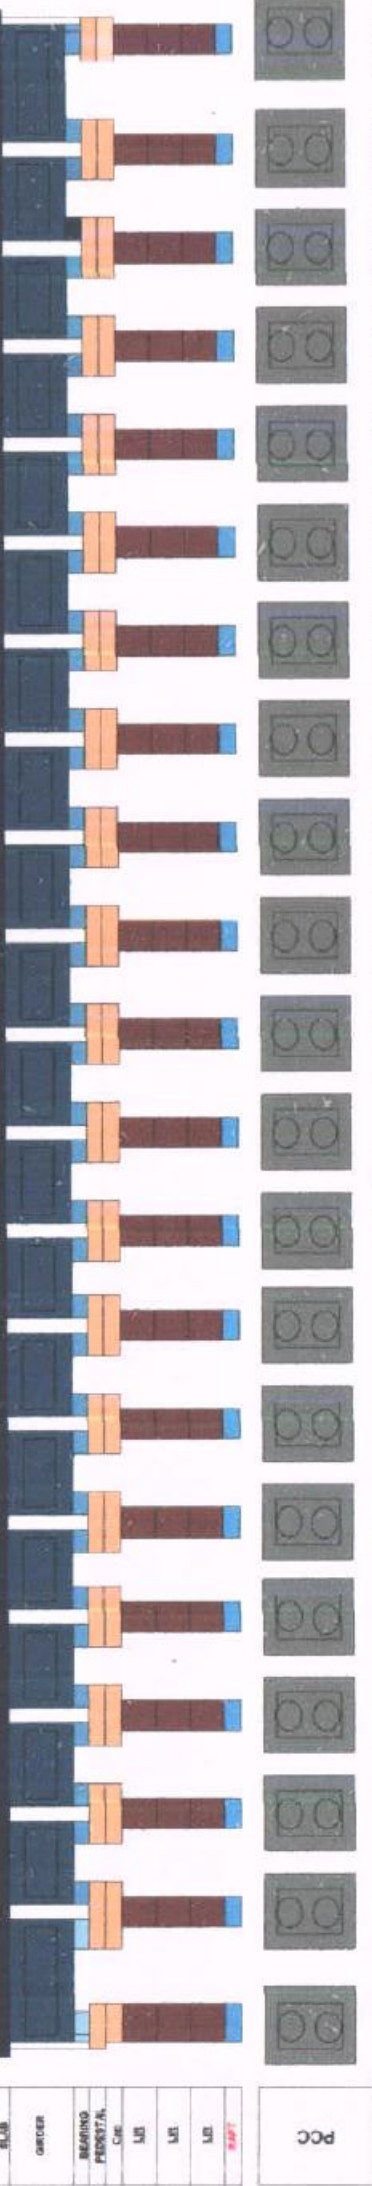


PCC

- A1
- P2
- P3
- P4
- P5
- P6
- P7
- P8
- P9
- P10
- P11
- P12
- P13
- P14
- P15
- P16
- P17
- P18
- P19
- A2

Work Summary
 Foundation:- 42/42
 Pier:- 42/42
 Pier Cap:- 42/42
 Girders:- 200/200
 Girder Launch:- 200/200



Annexure-1

Page No.		Lane	Obstruction Length (m)	Information	Photo	Remark's
From	To					
00	35+940	BHS		Land		The issue has been discussed with the land owner by concessionaire in the interest of the project and convinced him to give his consent to start the work by paying compensation from concessionaire on 01st February 2021. Issue at present resolved and work commenced from 07th feb 2021.
ii			0			

(Signature)
 (Deepak Mishra)
 Asst. Mgs. (Billing)
