



NATIONAL HIGHWAYS AUTHORITY OF INDIA (Ministry of Road Transport and Highways)

Construction of Eight lane Vadodara Kim Expressway from Km 292.00 to Km 323.00 (Manubar to Sanpa Section of Vadodara Mumbai Expressway) in the State of Gujarat under NHDP Phase - VI on Hybrid Annuity Mode (Phase IA-Package III)

MONTHLY PROGRESS REPORT 02 FOR THE MONTH OF APRIL-2019



Client : NATIONAL HIGHWAYS AUTHORITY OF INDIA.
Concessionaire : Patel Vadodara - Kim Expressway Private Limited.
Independent Engineer : Aarvee Associates Architects Engineers & Consultants Pvt. Ltd.
EPC Contractor : Patel infrastructure Limited.

Table of Contents

Contents

1.0 EXECUTIVE SUMMARY	4
1.1 Construction progress in current month.....	4
1.2 Project Synopsis	5
1.3 Strip Plan (Summary).....	6
2.0 Project Overview.....	9
2.1 Salient Features of Project	9
2.2 Project Overview	10
2.3 Project Milestones.....	11
2.4 Critical Issues & Action Log	11
3.0 Physical Progress.....	12
3.1 Detailed Scope of Work & Physical Progress by Component	13
4.0 Land Acquisition and Clearance.....	14
4.1 LA Summary: -	14
4.2 Clearances Summary: -	14
4.3 Status of utility shifting: -	15
5.0 Change of Scope.....	16
6.0 Mobilization of Resources.	17
7.0 Financial Progress Details	18
7.1 Pen Picture - Escrow.....	18
7.2 Escrow detail	18
8.0 QA/QC Report.	19
8.1 Test conducted on site.	19
8.2 Weather report.	24
9.0 Safety Features	25
9. 1 Pen picture of safety features	25
9.2 Accident report	25
10.0 Review status of drawings/design reports	26
10.1 Structure drawing status.....	26
10.2 Highway drawing status	33
10.3 Review status of source approvals.....	34

Annexure-01 Correspondence details
Annexure-02 Organization Chart
Annexure-03 RFI summary.....
Annexure-04 Project photographs
Annexure-05 Utility Status
Annexure-06 Highway Strip Chart.....
Annexure-07 Structure Stripchart.....

1.0 EXECUTIVE SUMMARY

The Patel Vadodara - Kim Expressway Private Limited. has been awarded Construction of Eight Lane Vadodara Kim Expressway from Km 292.00 to Km 323.00 (Manubar to Sanpa Section of Vadodara Mumbai Expressway) in the State of Gujarat Under NHDP Phase - VI on Hybrid Annuity Mode (Phase IA- Package III).

The road passes through plain and rolling terrain. Land use is mostly agricultural with Black Cotton soil. The entire length of the project road falls in the state of Gujarat under Bharuch Districts. The Function of expressway is to cater for movement of heavy volumes of motor traffic at high speeds. They connect major points of traffic generation and are intended to serve trips of medium and long length between large residential areas, industrial or commercial concentrations, and the central business district. They are divided highways with high standards of geometric and full or partial control of access and provided generally with grade separation at intersections. Parking, loading and unloading of goods and passengers and pedestrian traffic are not permitted on these highways.

This report covers the activities for the month of April 2019. The Embankment work of the main carriageway is started and 18.5 Km of work is in progress. The overall Physical progress as on 30th April 2019 is assessed to be approximately 0.67%. The financial progress achieved 31st March 2019 is assessed to be 0.82 %.

The Project involves the Eight Lane new alignment with divided carriageway having total 119 structures which include 1-ROB, 1-Flyover, 1-VOP, 3-MJBs.

The Major National Highways and State Highways intersecting the project corridor are NH-228, SH-161.

1.1 Construction progress in current month

Key reporting metrics	Value/ %/ Amount
Scheduled Physical Progress (%)	<i>NIL</i>
Cumulative Physical Progress up to current month (%)	<i>NIL</i>
Physical Progress during current month (%)	<i>1.02 %</i>
Financial progress (%)	<i>5.32 %</i>
Cumulative Expenditure till date (Rs Cr)	<i>91.06 Cr.</i>
Number of pending COS proposals	<i>NIL</i>
Amount for pending COS (Rs Cr)	<i>NIL</i>

1.2 Project Synopsis

National Highways Authority of India plans to undertake the Construction of new alignment 8-lane from Manubar to Sanpa from Km 292.000 to 323.000 in the State of Gujarat under NHDP Phase-VI on Hybrid Annuity Mode (Length 31.00 Km.) – Package III.

The project involves new alignment from 292.000 Km to 323.000 the 8-lane divided carriageway. It includes the construction of bridges, intersections, Connecting roads, culverts and related infrastructure, and the installation of signaling systems and signboards. The project will be developed under National Highways Development Project (NHDP) Phase-VI on Hybrid Annuity Mode.

Proposed alignment


Sr. No	Design Chainage		Length	Village	Remark
	From	To			
1	292+000	292+700	0.700	Manubar	
2	292+700	293+850	1.150	Tham	
3	293+850	296+050	2.200	Derol	
4	296+050	297+500	1.500	Tralsi	
5	297+550	300+500	2.950	Dayadara	
6	300+500	301+200	0.700	Tralsa	
7	301+200	305+550	4.350	Kelod	
8	305+550	307+750	2.200	Karela	
9	307+750	310+900	3.150	Kurchan	
10	310+900	314+300	3.400	Simartha	
11	314+300	317+200	2.900	Dora	
12	317+200	318+900	1.700	Danda	
13	318+900	321+600	2.660	Suthodara	
14	321+600	323+000	1.440	Matar Talpad	

1.3 Strip Plan (Summary)

1. Work front Unavailable & reason for Unavailability			2. Length completed by layer (MCW)			3. Length completed by layer (Service Road)		
	Length (km)	% Total Pending Length		Length (km)	% Total Length		Length (km)	% Total Length
Total Length	31.000	20.43	Total Length	-	-	Total Length	-	-
Total Work front Unavailable	6.334	20.43	Total Length Completed (Till DBM)	-	-	Total Length Completed (Till DBM)	-	-
Pending Land	6.334	20.43	BC	-	-	BC	-	-
Acq.	24.666	79.57	DBM	-	-	DBM	-	-
Pending	5.531	17.84	WMM	-	-	WMM	-	-
Clearances	25.469	82.16	GSB	-	-	GSB	-	-
Encumbrances	5.531	17.84	Sub-Grade	-	-	Sub-Grade	-	-
			C&G	-	-	C&G	-	-


Figure 1 Location MAP

323+000 End of Package-III

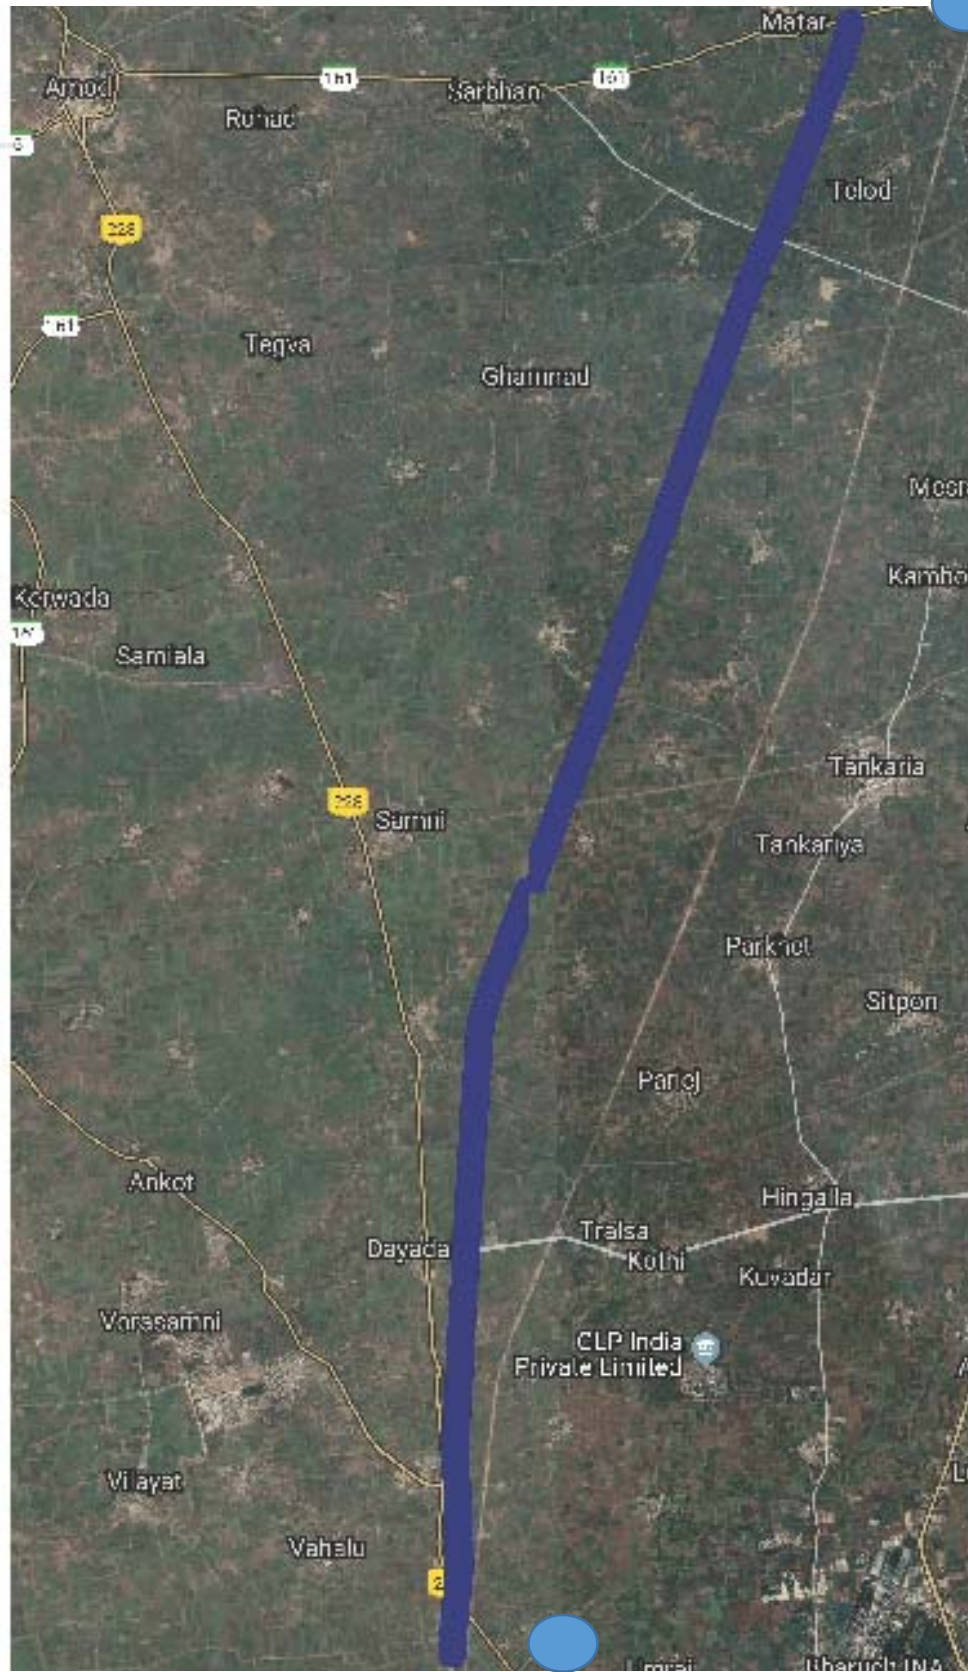

293+000 Start of Package-III

Vadodara Kim Expressway Project (Manubar to Sanpa) PKG-III From Km. 292+000 to 323+000 Linear Plan:-

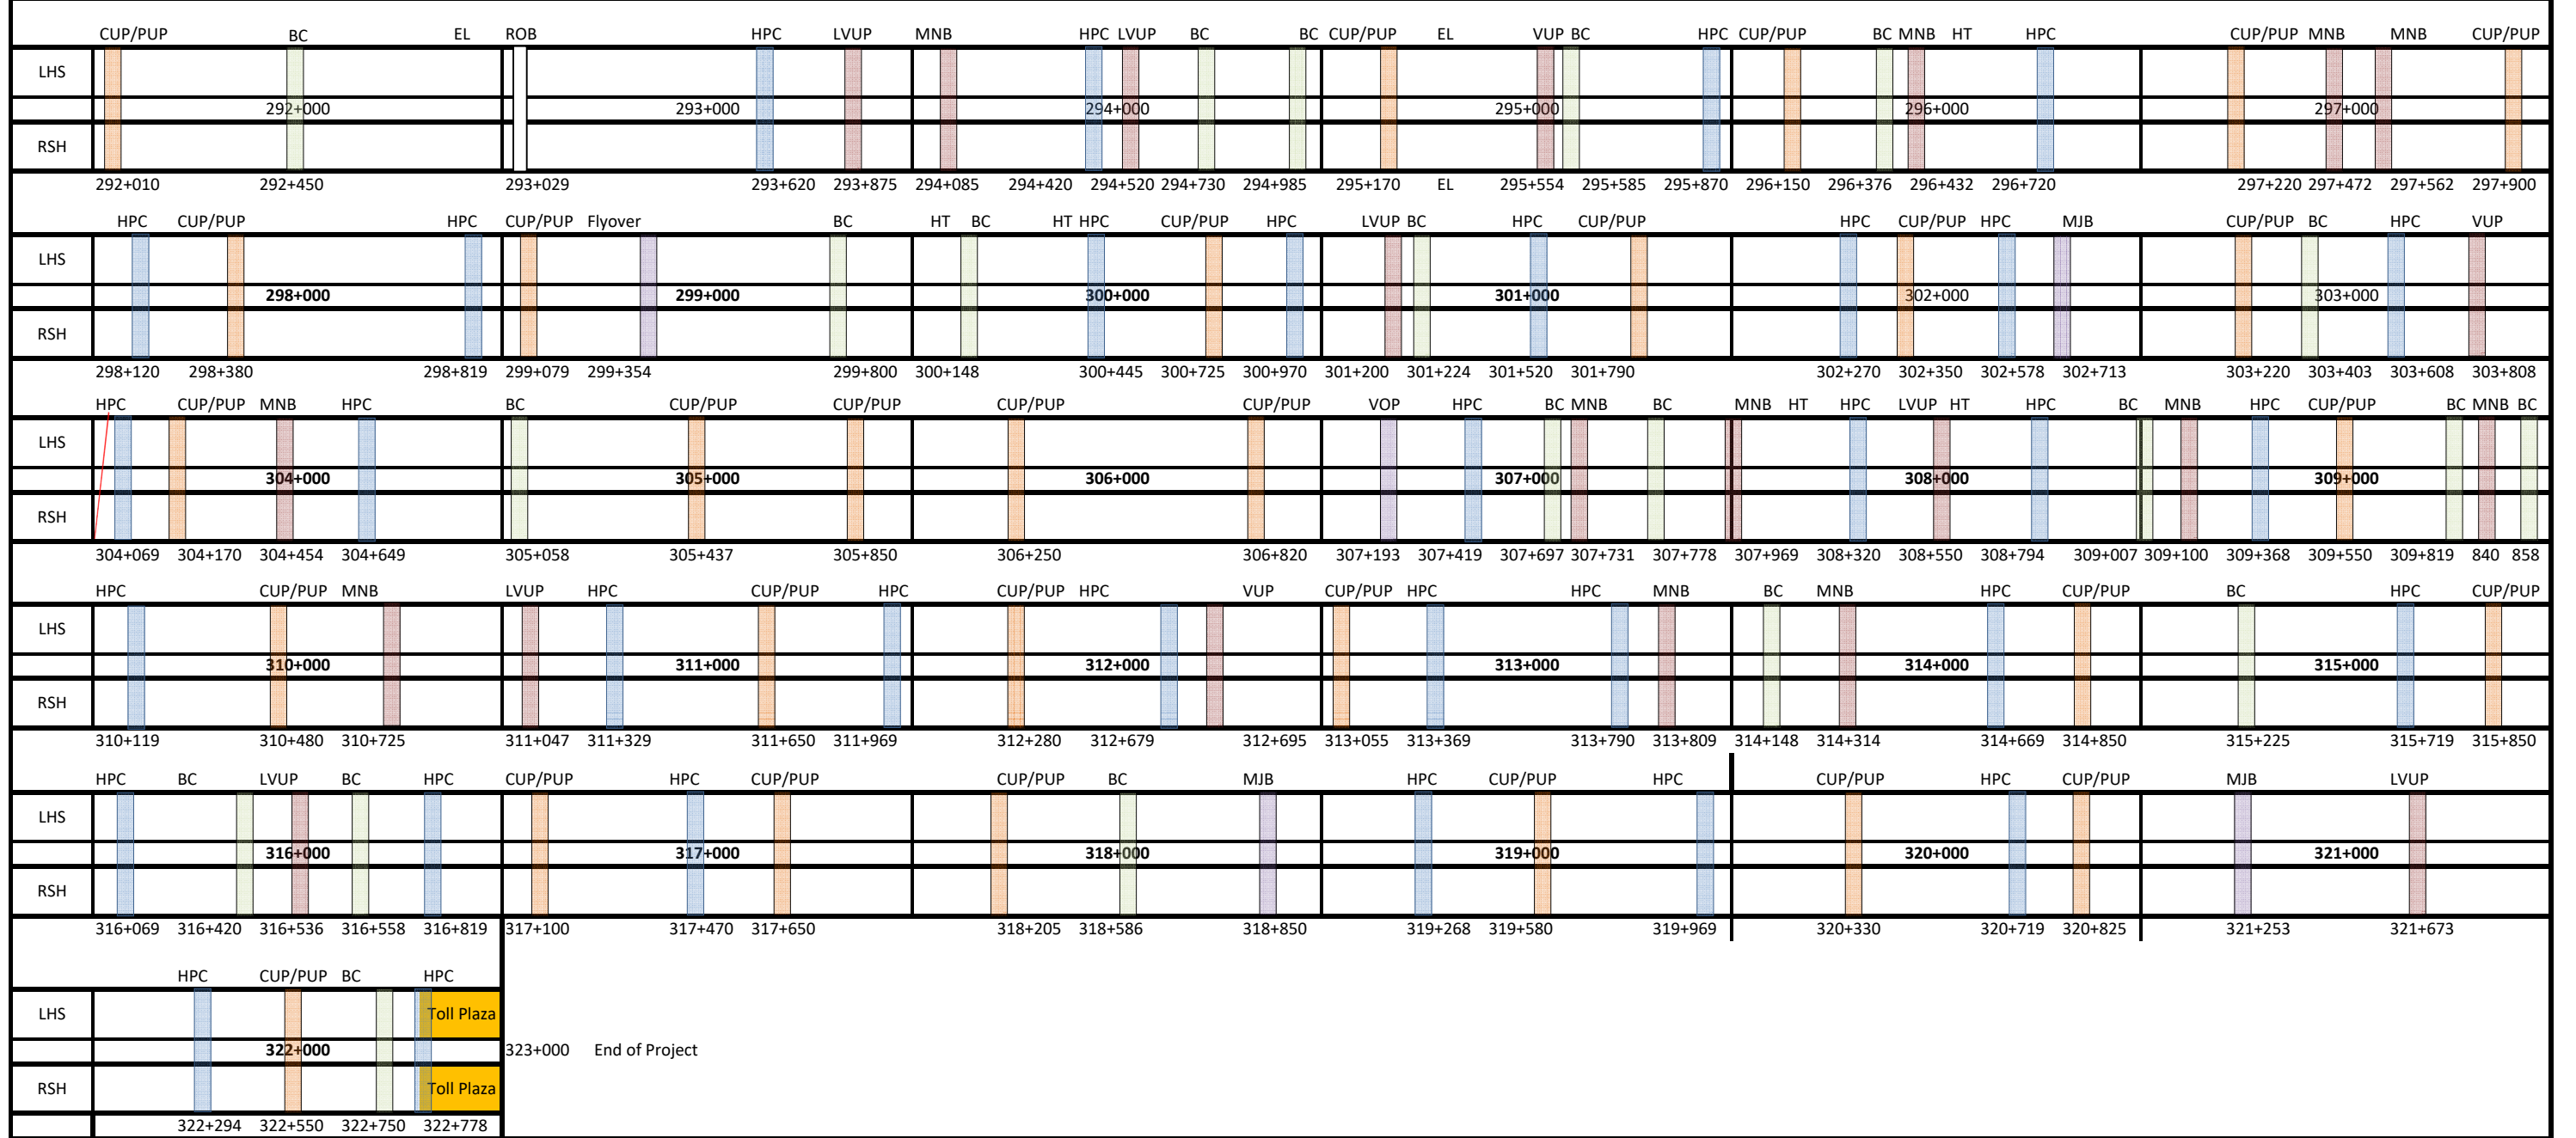

2.0 Project Overview

2.1 Salient Features of Project

Sr. No.	Component	Remarks
1	Project	Construction of Eight lane Vadodara Kim Expressway from Km 292.00 to Km 323.00 (Manubar to Sanpa Section of Vadodara Mumbai Expressway) in the State of Gujarat under NHDP Phase - VI on Hybrid Annuity Mode (Phase IA-Package III)”
2	Name of the Employer	National Highways Authority of India
3	Name of Concessionaire	Patel Vadodara Kim Expressway Pvt. Ltd.
4	Name of EPC Contractor	Patel Infrastructure Ltd.
5	Independent Engineer	Aarvee Associates Architects Engineers & Consultants Pvt. Ltd
6	Design Consultant	SPECIALIZED ENGINEERING SERVICES PVT. LTD
7	Project Length (In Km)	31.00 Km
8	Date of Concession Agreement	11th May, 2018
9	Total Project Cost as per CA	1712.00 Cr.
10	Concession Period	17 Years
11	Construction Period	2 Years
12	Appointed Date	08th March 2019
13	Scheduled Date of Completion	07th March 2021
14	Maintenance Period	15 Years

2.2 Project Overview

2.2.1 Structures

Sr. No.	Feature	Description
1	Major Bridge	03 Nos.
2	Flyover	01 No.
3	ROB	01 No.
4	Minor bridges	11 Nos.
5	Vehicular underpass	03 Nos.
6	Light Vehicular Underpasses	07 Nos.
7	Vehicular Overpasses	01 No.
8	Culverts (HP/BC)	62 Nos. (35 Nos. Pipe / 27 Nos. Box)
9	Toll Plaza	1 No.
10	Truck Parking Facility	02 Nos.
11	Toilet Facility	03 Nos.

2.2.2 Highway

Sr. No.	Feature	Description
1	Embankment	58.742 Km
2	Subgrade	58.742 Km
3	G.S.B	58.742 Km
4	D.L.C	58.742 Km
5	P.Q.C	58.742 Km

2.2.3 PROJECT LOCATION

The Project consists of new alignment of 8 lane of Manubar to Sanpa Section of Vadodara Mumbai Expressway. The project road stretch is a part of Vadodara Mumbai Expressway, which covers main cities like Vadodara, Surat, Thane and Mumbai. Major built up areas along the stretch under development are Ankleshwar, Bharuch, Valsad, and Navsari.

2.2.4 PROJECT DESCRIPTION

The road passes through plain and rolling terrain. Land use is mostly agricultural with Black Cotton soil. The entire length of the project road falls in the state of Gujarat under Bharuch Districts. The Function of expressway is to cater for movement of heavy volumes of motor traffic at high speeds. They connect major points of traffic generation and are intended to serve trips of medium and long length between large residential areas, industrial or commercial concentrations, and the central business district. They are divided highways with high standards of geometrics and fully control of access and provided generally with grade separation at intersections. Parking, loading and unloading of goods and passengers and pedestrian traffic are not permitted on these highways.

2.3 Project Milestones

Sr. No.	Project Milestone	Period to achieve the Milestone	Required % of Physical & Financial Work Completion to Achieve Milestone	Date of Milestone Achievement as per CA	Financial Progress
1	Milestone - 1	150 Th DAY	20%	05/08/2019	342.4
2	Milestone – 2	330 Th DAY	35%	01/02/2020	599.2
3	Milestone – 3	480 Th DAY	75%	30/06/2020	1284.0
4	Milestone – 4	730 Th DAY	100%	07/03/2021	1712.0

2.4 Critical Issues & Action Log

Sr.No	Issue Description	Type	Ongoing/ New Issue/ Resolved	Concerned Authority	Chainage (s) affected due to the issue	Length affected (km)	Action(s) taken till now	Action(s) suggested by the IE	Expected date/ Actual Date for resolving issue
		NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL

3.0 Physical Progress

Component	% Weightage	Physical Progress (During Current Month)	Physical Progress (Cumulative, Up to Current Month)
Road Work	45.44 %	00.00 %	00.00 %
Major Bridge Works	14.56 %	00.57 %	00.76 %
Structures	15.48 %	00.10 %	00.26 %
Others	24.52 %	00.00 %	00.00 %
Total Physical Progress		00.67 %	01.02 %

3.1 Detailed Scope of Work & Physical Progress by Component

Component	Item Description	Weightage % Component	Planned in Scope (As Per Scope of Work)	Progress Till Date km no.	Cumulative Physical Progress %	Value of Physical Progress	
Amount In Cr.	1712000000						
Road works including culverts, minor bridges, underpasses, overpasses, approaches to ROB/RUB/ Major Bridges/ Structures (but excluding service roads)	B- New realignment/bypass						
	Earthwork up to Top of Sub-Grade	25.47%	58.742 Km	00.000 Km	0.00%	-	
	Granular work (GSB)	2.03%	58.742 Km	00.000 Km	0.00%	-	
	Shoulders	0.03%	55.732 Km	00.000 Km	0.00%	-	
	DLC Work	3.44%	58.742 Km	00.000 Km	0.00%	-	
	PQC Work	14.46%	58.742 Km	00.000 Km	0.00%	-	
	C-New Culvert, MB, Underpass, Over Pass on Existing road realignment & bypass						
	Culverts	1.18%	124.000 Nos	15.000 Nos	0.14%	2,44,32,889.67	
	Minor Bridge						
	(a) Foundation	1.44%	44.000 Nos	02.000 Nos	0.07%	1,12,11,282.46	
	(b) Sub-Structure	1.40%	44.000 Nos	00.000 Nos	0.00%	-	
	(c) Super- Structure	2.93%	22.000 Nos	00.000 Nos	0.00%	-	
	Cattle/Pedestrian Underpass						
	(a) Foundation	1.54%	60.000 Nos	02.000 Nos	0.05%	88,13,814.08	
	(b) Sub-Structure	1.67%	120.000 Nos	00.000 Nos	0.00%	-	
	(c) Super- Structure	2.30%	60.000 Nos	00.000 Nos	0.00%	-	
	Grade separated structures						
	Vehicular Underpass (VUP/PUP)						
	(a) Foundation	0.50%	20.000 Nos	00.000 Nos	0.00%	-	
	(b) Sub-Structure	0.60%	40.000 Nos	00.000 Nos	0.00%	-	
	(c) Super- Structure	0.81%	20.000 Nos	00.000 Nos	0.00%	-	
	Vehicular Overpass (VOP)						
	(a) Foundation	0.11%	03.000 Nos	00.000 Nos	0.00%	-	
	(b) Sub-Structure	0.02%	03.000 Nos	00.000 Nos	0.00%	-	
	(c) Super- Structure	0.14%	02.000 Nos	00.000 Nos	0.00%	-	
	Flyover						
	(a) Foundation	0.37%	08.000 Nos	00.000 Nos	0.00%	-	
	(b) Sub-Structure	0.13%	08.000 Nos	00.000 Nos	0.00%	-	
	(c) Super- Structure	0.33%	06.000 Nos	00.000 Nos	0.00%	-	
	Major Bridge works and ROB/RUB	D- Major Bridge works and ROB/RUB					
		New Major Bridges					
		(a) Foundation					
(a) Open Foundation		0					
(b) Pile Foundation/Well Foundation		2.06%	330.000 Nos	122.000 Nos	0.76%	13,03,68,762.79	
(b) Sub-Structure		0.76%	22.000 Nos	00.000 Nos	0.00%	-	
(c) Super- Structure		1.66%	16.000 Nos	00.000 Nos	0.00%	-	
ROB							
(a) Foundation		2.47%	42.000 Nos	00.000 Nos	0.00%	-	
(b) Sub-Structure		1.00%	42.000 Nos	00.000 Nos	0.00%	-	
(c) Super- Structure		4.61%	40.000 Nos	00.000 Nos	0.00%	-	
Reinforced earth Wall		2.00%	26404.31 Sqm	00.00 Sqm	0.00%	-	
Other Works.	(i) Service roads/ Slip Roads	0.59%	02.425 Km	00.000 Km	0.00%	-	
	(ii) Toll Plaza	0.99%	02.000 Nos	00.000 Nos	0.00%	-	
	(iii) Road side drains	1.77%	119.760 Km	00.000 Km	0.00%	-	
	Road signs, markings, km stones, safety devices						
	(a) Road signs, markings, km stones, ...	2.91%	62.000 Km	00.000 Km	0.00%	-	
	(b) Concrete Crash Barrier/ W-Beam Crash Barrier in Road work	1.92%	119.760 Km	00.000 Km	0.00%	-	
	Project facilities						
	(a) Bus Bays	0.00%					
	(b) Truck Lay-byes	1.78%	02.000 Nos	00.000 Nos	0.00%	-	
	(b) Rest areas	2.67%	03.000 Nos	00.000 Nos	0.00%	-	
	Road side plantation	0.08%	62.000 Km	00.000 Km	0.00%	-	
	Protection works						
	(a) Boulder pitching on slopes	1.24%	29.010 Km	00.000 Km	0.00%	-	
	(b) Toe/Retaining wall	3.04%	02.147 Km	00.000 Km	0.00%	-	
	Miscellaneous	7.55%	01.000 Nos	00.000 Nos	0.00%	-	
	100.00%			1.02%	17,48,26,749.00		

4.0 Land Acquisition and Clearance

4.1 LA Summary: -

Sr. No	Village Name	Taluka & District	Area in Hec.	Award (RS.in.cr)	Disburse Area in Hec.	Disburse (Rs.in Cr.)	Disburse Area in%
1	Matar Talpad	Tal.- Amod Dist.- Bharuch	19.7199	10.02	16.7193	8.43	85%
2	Vanta		1.6709	1.64	0.6865	1.37	41%
3	Sunthodra		13.0293	1.77	13.0293	1.62	100%
4	Telod		3.4501	1.24	2.833	1.15	82%
5	Danda		29.1681	19.81	28.6605	19.46	98%
6	Dora		38.0178	22.58	37.0607	22.17	975%
7	Simlatha		21.219	42.05	19.6934	38.39	93%
8	Vantarsa		0.2261	0.04	0.2261	0.04	100%
9	Kurchan		18.1489	3.21	17.0847	3	94%
10	Padariya	Tal.& Dist.- Bharuch	5.7697	2.78	5.7697	2.78	1%
11	Karela		42.1435	20.7	40.8154	20.09	97%
12	Pipaliya		12.4403	3.78	12.2705	3.71	99%
13	Kelod		25.5545	24.16	24.4512	23.46	96%
14	Taralsa		16.5034	11.56	14.7986	10.39	90%
15	Dayadara		20.9353	8.48	17.1477	7.64	82%
16	Derol		35.3771	35.89	34.6392	35.12	98%
17	Tham		8.1923	4.22	7.9318	4	97%
18	Kanthariya		8.6506	11.01	6.61805	9.43	77%

4.2 Clearances Summary: -

Environment				
Proposal Description	Status	Length impacted	Current stage	Issues/Comments
Forest Land				
Proposal Description	Status	Length impacted	Current stage	Issues/Comments

4.3 Status of utility shifting: -

Utility Category	Name/ Department	Status	Length affected	Date & letter of request by Authority for estimate	Date & letter when Estimate was Received from concerned dept.	Date & letter when Estimate was Verified By IE.	Date & letter of Approval by Authority RO/ HQ	Date & letter of Deposit of supervision charge	Progress of Physical Shifting	Date of Certification from Agency for Completion	Estimate Amount	Issue/ Comments
Water	GWSSB	Estimate is under progress	80 M	-	-		-	-	-	-	-	-
	SSNNL	SSNNL asking authority to get into agreement and rent.	730 M									
Electricity	DGVCL	Revised Estimate is under progress	2640 M	-	-	#72,73 &74 on 13.02.2019	-	-	-	-	-	-
	Getco	3/6 is submitted and rest are under progress	710 M			#342 on 01.05.2019						
Others	Trees		900 M	-	-		-	-	-	-	-	-

5.0 Change of Scope

Sr. No.	Proposal Details	Date of first submission to IE	Current Status	COS Amount	Expected/Actual date of Approval
	NIL	NIL	NIL	NIL	NIL

6.0 Mobilization of Resources.

Sr. No	Equipment	Unit	Planned machinery	deployed machinery
1	Excavator	Nos	25	26
2	Motor Grader	Nos	15	16
3	Vibratory Roller	Nos	25	22
4	Wet Mix/ DLC Paver	Nos	1	-
5	Wet Mix Plant	Nos	1	-
6	PQC Paver	Nos	1	1
7	Hot Mix Plant	Nos	1	-
8	Bitumen Paver	Nos	1	-
9	Bitumen Distributor	Nos	1	-
10	Pneumatic Tyre Roller	Nos	1	-
11	Dumpers/Tippers	Nos	105	105
12	FE Loaders/JCB	Nos	15	10
13	Water Tanker	Nos	33	16
14	Batching Plant CP60	Nos	2	2
15	Batching Plant CP 120	Nos	2	1
16	Transit Mixers	Nos	15	14
17	Concrete Pump	Nos	2	1
18	Kerb Mechine	Nos	1	0

7.0 Financial Progress Details

7.1 Pen Picture - Escrow

TPC (Cr.)	Cumulative inflow to Escrow till previous month (Cr)	Cumulative outflow from Escrow till previous month (Cr)	Inflow to Escrow During the month (Cr)	Outflow from Escrow during the month (Cr)
1712	-	-	-	-

7.2 Escrow detail

TPC (Cr.)	Escrow Plan till date-Debt (HAM)(Cr)	Escrow Plan till date-Debt (HAM)(Cr)	Escrow Plan till date-Equity (HAM)(Cr)	Escrow Plan till date- VGF (HAM)(Cr)	Escrow Actual till date-Debt (HAM)(Cr)	Escrow Actual till date-Equity (HAM)(Cr)	Escrow Actual till date- YGF (HAM)(Cr)

8.0 QA/QC Report.

8.1 Test conducted on site.

Sr. No.	Name of Test	Testing Method	Frequency of Test	Specification Requirements	Number of Tests Conducted								
					Up To Previous Month			This Month			Total Upto Date		
					Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test
OGI & Cutting soil													
1	Free Swell Index	IS 2720 Part 40	2 test per 3000 m ³	50 % Max	24	0	0	0	0	0	24	0	24
2	Grain Size Analysis	IS 2720 Part 4	2 test per 3000 m ³	-	23	0	0	0	0	0	23	0	23
3	Plasticity Index	IS 2720 Part 5	2 test per 3000 m ³	L.L.= Not>50 %,PI =Not> 25 %	23	0	0	0	0	0	23	0	23
4	Max. Dry Density	IS 2720 Part 8	2 test per 3000 m ³	Up to 3m 1.52 gm./cc	24	0	0	0	0	0	24	0	24
5	CBR	IS 2720 Part 16	1 test as required	Min. 8 % or as per design	0	0	0	0	0	0	0	0	0
6	Density of Comp.Layer	IS 2720 Part 28	1 set of 10 tests/ 3000 m ²	90-95 % of lab MDD	4890	65	4955	400	0	400	5290	65	5355
Borrow Area (Embankment)													
1	Free Swell Index	IS 2720 Part 40	2 test per 3000 m ³	50 % Max	207	0	207	452	0	452	659	0	659
2	Grain Size Analysis	IS 2720 Part 4	2 test per 3000 m ³	-	207	0	207	452	0	452	659	0	659
3	Plasticity Index	IS 2720 Part 5	2 test per 3000 m ³	L.L.= Not>50 %,PI =Not> 25 %	207	0	207	452	0	452	659	0	659
4	Max. Dry Density	IS 2720 Part 8	2 test per 3000 m ³	Up to 3m 1.52 gm./cc More than 3m 1.60 gm./cc	207	0	207	452	0	452	659	0	659
5	CBR	IS 2720 Part 16	1 test per 3000 m ³	Min. 8 % as per design	2	0	2	2	0	2	4	0	4
Earthwork Field test													
1	Density of Comp.Layer (Emb.)	IS 2720 Part 28	1 set of 10 tests per 3000 m ²	95% of Lab MDD	8230	142	8372	8790	78	8868	17020	220	17240
2	Density of Comp.Layer (Sub grade & Earthen	IS 2720 Part 28	1 set of 10 tests per 2000 m ²	97% of Lab MDD	0	0	0	0	0	0	0	0	0

Sr. No.	Name of Test	Testing Method	Frequency of Test	Specification Requirements	Number of Tests Conducted								
					Up To Previous Month			This Month			Total Upto Date		
					Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test
GSB													
1	Sieve Analysis		1 Test /400M ³	As per MORT&H Table 400-1	5	0	5	10	0	10	15	0	15
2	Plasticity Index	IS 2720 Part 5	1 Test /400M ³	LL=Not>25% PI=Not>6%	5	0	5	10	0	10	15	0	15
3	Max. Dry Density	IS 2720 Part 8	1 TEST PER SOURCE		1	0	1	2	0	2	3	0	3
4	CBR	IS 2720 Part 16	As Required	30% Min.	1	0	1	1	0	1	2	0	2
5	Water Absorption	IS 2386 Part 3	As Required	2% Max.	1	0	1	12	0	12	13	0	13
6	AIV	IS 2386 (P-4) & IS 5640	As Required	40% Max	1	0	1	2	0	2	3	0	3
7	Density of Comp.Laye	IS 2720 Part 28	1 Test /1000M ²	98% of Lab MDD	0	0	0	0	0	0	0	0	0
PHYSICAL PROPERTIES OF AGGREGATE FOR CONCRETE													
1	Sieve Analysis of CA	IS 2386 Part 1	1 Test/Concreting Da	As per IS 383	23	0	23	58	0	58	81	0	81
2	Sieve Analysis of FA	IS 2386 Part 1	1 Test/Concreting Da	As per IS 383	18	0	18	29	0	29	47	0	47
3	Aggregate Impact Valu	IS 2386 Part 4	1 Test/Concreting Da	As per IS 383	16	0	16	29	0	29	45	0	45
4	Flakiness Index	IS 2386 Part 1	1 Test/Concreting Da	As per IS 383	16	0	16	29	0	29	45	0	45
5	Silt Content	IS 383	As Required		27	0	27	9	0	9	36	0	36
6	Specific Gravity & W A	IS 2386 PART 3	1 Test/Month		8	0	8	2	0	2	10	0	10


Sr. No.	Name of Test	Testing Method	Frequency of Test	Specification Requirements	Number of Tests Conducted																								
					Up To Previous Month			This Month			Total Upto Date																		
					Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test																
Concrete Mix Design (cube sets)																													
1	M15	7 Days	18 Cubes	As per MoRT&H	0	0	0	0	0	0	0	0	0																
		28 Days			9	0	0	0	0	0	9	0	9																
2	M20 Kerb	7 Days			18 Cubes	As per MoRT&H	0	0	0	0	0	0	0	0	0														
		28 Days					0	0	0	0	0	0	0	0	0														
	M20	7 Days					18 Cubes	As per MoRT&H	0	0	0	0	0	0	0	0	0												
		28 Days							9	0	0	0	0	0	9	0	9												
3	M25	7 Days							18 Cubes	As per MoRT&H	0	0	0	0	0	0	0	0	0										
		28 Days									9	0	0	0	0	0	9	0	9										
4	M30	7 Days									18 Cubes	As per MoRT&H	0	0	0	0	0	0	0	0	0								
		28 Days											9	0	0	0	0	0	9	0	9								
5	M35	7 Days											18 Cubes	As per MoRT&H	0	0	0	0	0	0	0	0	0						
		28 Days													9	0	0	0	0	0	9	0	9						
6	M35 Pile	7 Days													18 Cubes	As per MoRT&H	0	0	0	0	0	0	0	0	0				
		28 Days															9	0	0	0	0	0	9	0	9				
7	M35 RE block	7 Days															18 Cubes	As per MoRT&H	0	0	0	0	0	0	0	0	0		
		28 Days																	0	0	0	0	0	0	0	0	0		
8	M40	7 Days																	18 Cubes	As per MoRT&H	0	0	0	0	0	0	0	0	0
		28 Days																			9	0	0	0	0	0	9	0	9
9	M45	7 Days	18 Cubes	As per MoRT&H																	0	0	0	0	0	0	0	0	0
		28 Days																			0	0	0	0	0	0	0	0	0
10	M50	7 Days			18 Cubes	As per MoRT&H															0	0	0	0	0	0	0	0	0
		28 Days																			0	0	0	0	0	0	0	0	0
11	M40 PQC	7 Days					36 cubes & 30 beams	As per MoRT&H													0	0	0	0	0	0	0	0	0
		28 Days																			0	0	0	0	0	0	0	0	
12	M40 PQC Fl. Strength	7 Days							36 cubes & 30 beams	As per MoRT&H											0	0	0	0	0	0	0	0	0
		28 Days																			0	0	0	0	0	0	0	0	

Sr. No.	Name of Test	Testing Method	Frequency of Test	Specification Requirements	Number of Tests Conducted									
					Up To Previous Month			This Month			Total Upto Date			
					Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test	
Field Concrete (cube sets)														
1	M15	7 Days	IS-516	1 test - 0-5 M3 2test - 6-15 m3 3test - 16-30 m3 4 test - 31- 50 m3 +1 test for every 50m3 concrete	As per MoRT&H	27	0	27	32	0	32	59	0	59
		28 Days				13	0	13	34	0	34	47	0	47
2	M20	7 Days				0	0	0	1	0	1	1	0	1
		28 Days				0	0	0	0	0	0	0	0	0
3	M25	7 Days				0	0	0	4	0	4	4	0	4
		28 Days				0	0	0	0	0	0	0	0	0
4	M30	7 Days	IS-516	1 test - 0-5 M3 2test - 6-15 m3 3test - 16-30 m3 4 test - 31- 50 m3 +1 test for every 50m3 concrete	As per MoRT&H	2	0	2	17	0	17	19	0	19
		28 Days				0	0	0	0	0	0	0	0	0
5	M35	7 Days				0	0	0	7	0	7	7	0	7
		28 Days				0	0	0	7	0	7	7	0	7
6	M35 Pile	7 Days				0	0	0	248	0	248	248	0	248
		28 Days				41	0	41	196	0	196	237	0	237
7	M35 REblock	7 Days				0	0	0	0	0	0	0	0	0
		28 Days				0	0	0	0	0	0	0	0	0
8	M40	7 Days				0	0	0	0	0	0	0	0	0
		28 Days				0	0	0	0	0	0	0	0	0
9	M45	7 Days				0	0	0	0	0	0	0	0	0
		28 Days				0	0	0	0	0	0	0	0	0
10	M50	7 Days				0	0	0	0	0	0	0	0	0
		28 Days				0	0	0	0	0	0	0	0	0
11	M40 PQC	7 Days	IS-516	1 test of 2 cubes & 2beams for 150 m3 or Min. 6 cubes & 6 beams for the day	As per MoRT&H	0	0	0	0	0	0	0	0	0
		28 Days				0	0	0	0	0	0	0	0	
12	M40 PQC F.S	7 Days				0	0	0	0	0	0	0	0	0
		28 Days				0	0	0	0	0	0	0	0	0
13	DLC	7 Days	IS-516	et of 3cubes for 1000	Asper MoRT&H	0	0	0	0	0	0	0	0	
14	DLC	FDD	IS 2720 Part 28	1 Test /2000M ²	98% of Ref. Density	0	0	0	0	0	0	0	0	0

Sr. No.	Name of Test	Testing Method	Frequency of Test	Specification Requirements	Number of Tests Conducted								
					Up To Previous Month			This Month			Total Upto Date		
					Passed	Failed	Total No. of Test	Passed	Failed	Total No. of Test	Passed	Failed	Cum. No. of Test
Cement													
1	Fineness	IS 4031	1 Test/Week		10	0	0	4	0	4	14	0	14
2	Consistency	IS 4031	1 Test/Week		10	0	0	4	0	4	14	0	14
3	Setting Time	IS 4031	1 Test/Week		10	0	0	4	0	4	14	0	14
4	Soundness	IS 4031	1 Test/Week		0	0	0	4	0	4	4	0	4
5	Compressive Strength	IS 4031	1 Test/Week										
	a) 3 Days		01 set = 3 Cube		9	0	0	2	0	2	11	0	9
	b) 7 Days		01 set = 3 Cube		7	0	0	4	0	4	11	0	7
	c) 28 Days		01 set = 3 Cube		4	0	0	6	0	6	10	0	4

8.2 Weather report.

Sl. No.	Date	Temperature C°		Humidity %		Rainfall (mm)
		Min. Temp. (°C)	Max. Temp. (°C)	Min.	Max.	
1	01-04-19	23.1	40.1	33.4	62.7	0.0
2	02-04-19	22.5	41.7	32.6	65.4	0.0
3	03-04-19	25.5	41.2	33.7	64.2	0.0
4	04-04-19	25.1	40.4	32.1	63.9	0.0
5	05-04-19	26.4	41.7	31.6	62.1	0.0
6	06-04-19	22.3	42.0	32.6	64.1	0.0
7	07-04-19	24.1	41.6	33.4	63.9	0.0
8	08-04-19	23.2	42.2	32.6	64.1	0.0
9	09-04-19	25.8	40.6	33.4	63.6	0.0
10	10-04-19	24.4	40.8	33.7	63.9	0.0
11	11-04-19	25.1	41.2	32.5	64.0	0.0
12	12-04-19	25.8	41.7	32.6	63.2	0.0
13	13-04-19	26.1	41.4	32.3	64.2	0.0
14	14-04-19	25.1	40.8	32.9	63.9	0.0
15	15-04-19	27.9	39.9	33.6	62.4	0.0
16	16-04-19	24.1	40.2	32.2	62.1	0.0
17	17-04-19	20.1	40.2	33.1	63.7	0.0
18	18-04-19	23.1	41.4	32.2	62.9	0.0
19	19-04-19	23.5	39.7	31.4	62.3	0.0
20	20-04-19	23.5	40.5	32.4	63.4	0.0
21	21-04-19	25.1	40.0	31.5	64.5	0.0
22	22-04-19	23.5	41.5	32.5	63.5	0.0
23	23-04-19	26.8	40.5	33.0	64.8	0.0
24	24-04-19	27.1	42.2	32.5	65.1	0.0
25	25-04-19	27.6	41.9	34.5	61.2	0.0
26	26-04-19	28.6	42.5	33.8	59.5	0.0
27	27-04-19	28.1	44.8	34.5	60.4	0.0
28	28-04-19	26.9	43.5	33.9	58.9	0.0
29	29-04-19	26.6	41.9	32.5	60.2	0.0
30	30-04-19	26.5	42.4	33.9	61.4	0.0

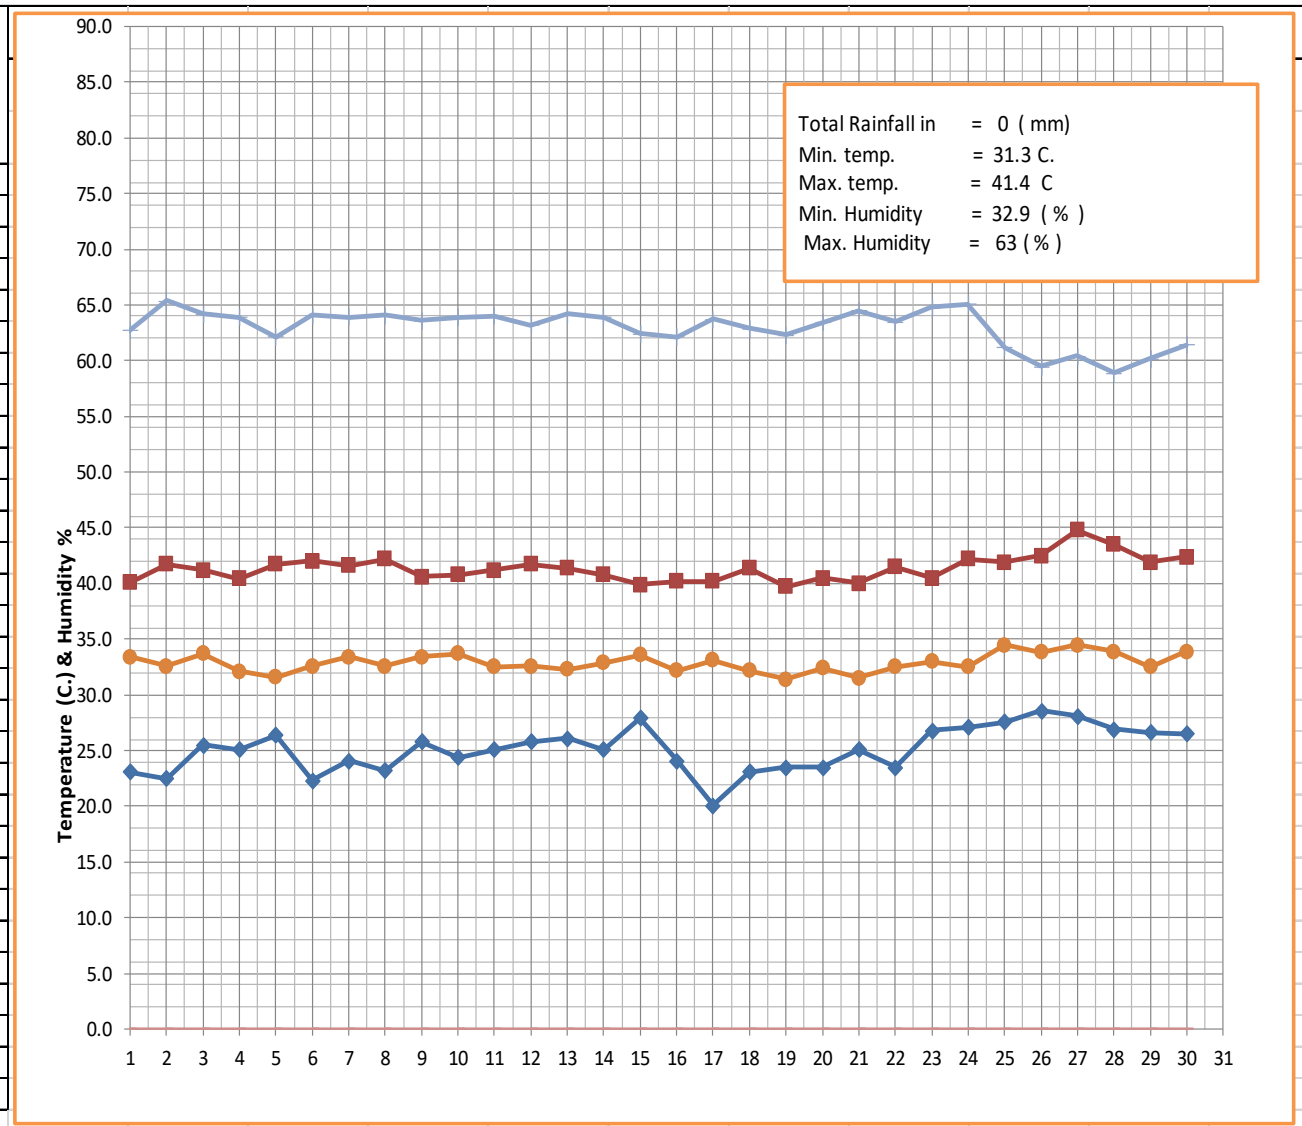

9.0 Safety Features

9.1 Pen picture of safety features

Location of Black spot	Suggested Remedial Measures with in provisions of Concession Agreement	Additional Remedial Measures (if any)	Financial implications of additional Remedial Measures for Authority
NIL			

9.2 Accident report

10.0 Review status of drawings/design reports

10.1 Structure drawing status

HPC (Total- 35 Nos.)									
Schedule Chainage (Km)						R0	R1	R2	Remark
293+620	300+970	307+419	311+969	316+819	Concessionaire Submission Letter No. and Date	#16 on 12-10-2018	# 41 on 11.04.2019		
294+420	301+520	307+969	312+679	317+470					
295+870	302+270	308+320	313+369	319+268					
296+720	302+578	308+794	313+812	319+969	IE's Coments Letter No. And Date	#5157 on 29.10.2018			
298+120	303+608	309+368	314+669	320+719					
298+819	304+069	310+119	315+719	322+294					
300+445	304+649	311+329	316+069	322+778					
Box Culvert (Total- 27 Nos.)									
Schedule Chainage (Km)						R0	R1	R2	Remark
292+450	301+247	309+892			Concessionaire Submission Letter No. and Date	#16 on 12.10.2018	HO #7 on 04.02.2019	#50 on 17.04.2019	
294+750	303+403	314+148							
295+007	305+437	316+427							
295+585	307+709	316+582			IE's Coments Letter No. And Date	#2 dated 12.01.2018	#220 on 27.03.2019		
296+376	307+789	318+612							
299+800	309+030	322+750							
300+148	309+840				Concessionaire Submission Letter No. and Date	-	#26 on 26.03.2019		
307+193	323+087								
315+247									
					IE's Coments Letter No. And Date	-	#309 on 20.04.2019		
PUP/CUP (Total- 30 Nos.)									
Schedule Chainage (Km)						R0	R1	R2	Remark
292+010	300+725	305+850	312+280	318+275	Concessionaire Submission Letter No. and Date	#21 on 22-10-2018	# 18 on 28.02.2019	12 nos Pup #49 on 17.04.2014	
295+170	301+790	306+250	313+075	319+580					
296+150	302+350	306+850	314+850	320+330					
297+220	303+245	309+550	315+870	320+825	IE's Coments Letter No. And Date	#5157 dated 29.10.2018	# 056 on 20.03.2019		
297+900	304+170	310+480	317+100	322+550					
298+380	305+085	311+650	317+650						
299+100					Concessionaire Submission Letter No. and Date	#37 on 12.12.2018			
LVUP (Total- 7 Nos.)									
Schedule Chainage (Km)						R0	R1	R2	Remark
293+895	311+073				Concessionaire Submission Letter No. and Date	#21 on 22-10-2018			
294+550	316+563								
301+240	321+700				IE's Coments Letter No. And Date	#84 on 15.02.2019			
308+550									
VUP (Total- 3 Nos.)									
Schedule Chainage (Km)						R0	R1	R2	Remark
295+575	312+720				Concessionaire Submission Letter No. and Date	#24 on 22-10-2018			
					IE's Coments Letter No. And Date	#53 on 02.02.2019			
303+830					Concessionaire Submission Letter No. and Date	#37 on 12.12.2018			
					IE's Coments Letter No. And Date	# 55 on 20.03.2019			
VOP (Total- 1 No.)									
Schedule Chainage (Km)						R0	R1	R2	Remark
307+193				Pile Load Test	Concessionaire Submission Letter No. and Date	#9 on 06.02.2019			
					IE's Comment Letter No. and Date				
				Geotech Investigation Report	Concessionaire Submission Letter No. and Date	#9 on 06.02.2019			
					IE's Comment Letter No. and Date				

MNB

Sr. no	Schedule Chainage (Km)		R0	R1	R2	Remark	
1	294+085	GAD	Concessionaire Submission Letter No. and Date	#21 on 22.10.2018	#11 on 20.02.2019	#55 on 19.04.2019	
			IE's Comment Letter No. and Date	#52 on 02.02.2019			
		Geotech Investigation Report	Concessionaire Submission Letter No. and Date			#55 on 19.04.2019	
			IE's Comment Letter No. and Date				
		Hydrology Report	Concessionaire Submission Letter No. and Date		#11 on 20.02.2019	#55 on 19.04.2019	
			IE's Comment Letter No. and Date		#150 on 03.02.2019		
		Foundation	Concessionaire Submission Letter No. and Date		#11 on 20.02.2019	#55 on 19.04.2019	
			IE's Comment Letter No. and Date				
		Substructure	Concessionaire Submission Letter No. and Date		#11 on 20.02.2019	#55 on 19.04.2019	
			IE's Comment Letter No. and Date				
		Superstructure	Concessionaire Submission Letter No. and Date		#11 on 20.02.2019	#55 on 19.04.2019	
			IE's Comment Letter No. and Date				
2	296+432	GAD	Concessionaire Submission Letter No. and Date	#37 on 12.12.2018	#28 on 28.03.2019		
			IE's Comment Letter No. and Date				
		Geotech Investigation Report	Concessionaire Submission Letter No. and Date		#28 on 28.03.2019		
			IE's Comment Letter No. and Date				
		Hydrology Report	Concessionaire Submission Letter No. and Date		#28 on 28.03.2019		
			IE's Comment Letter No. and Date				
		Foundation	Concessionaire Submission Letter No. and Date		#28 on 28.03.2019		
			IE's Comment Letter No. and Date				
		Substructure	Concessionaire Submission Letter No. and Date	#37 on 12.12.2018	#28 on 28.03.2019		
			IE's Comment Letter No. and Date				
		Superstructure	Concessionaire Submission Letter No. and Date	#37 on 12.12.2018	#28 on 28.03.2019		
			IE's Comment Letter No. and Date				
3	297+472	GAD	Concessionaire Submission Letter No. and Date	# 17 on 28.02.2019			
			IE's Comment Letter No. and Date				
		Geotech Investigation Report	Concessionaire Submission Letter No. and Date	# 17 on 28.02.2019			
			IE's Comment Letter No. and Date				
		Hydrology Report	Concessionaire Submission Letter No. and Date	# 17 on 28.02.2019			
			IE's Comment Letter No. and Date				
		Foundation	Concessionaire Submission Letter No. and Date	# 17 on 28.02.2019			
			IE's Comment Letter No. and Date				
		Substructure	Concessionaire Submission Letter No. and Date	# 17 on 28.02.2019			
			IE's Comment Letter No. and Date				
		Superstructure	Concessionaire Submission Letter No. and Date	# 17 on 28.02.2019			
			IE's Comment Letter No. and Date				

MNB

Sr. no	Schedule Chainage (Km)		R0	R1	Remark			
4	297+562	GAD	Concessionaire Submission Letter No. and Date	# 114 on 14.03.2019	#25 on 26.03.2019			
			IE's Comment Letter No. and Date					
		Geotech Investigation Report	Concessionaire Submission Letter No. and Date	# 114 on 14.03.2019				
			IE's Comment Letter No. and Date					
		Hydrology Report	Concessionaire Submission Letter No. and Date	# 114 on 14.03.2019				
			IE's Comment Letter No. and Date					
		Foundation	Concessionaire Submission Letter No. and Date	# 114 on 14.03.2019	#25 on 26.03.2019			
			IE's Comment Letter No. and Date					
		Substructure	Concessionaire Submission Letter No. and Date	# 114 on 14.03.2019	#25 on 26.03.2019			
			IE's Comment Letter No. and Date					
		Superstructure	Concessionaire Submission Letter No. and Date	# 114 on 14.03.2019	#25 on 26.03.2019			
			IE's Comment Letter No. and Date					
		5	304+450,	GAD	Concessionaire Submission Letter No. and Date		# 119 on 18.03.2019	
					IE's Comment Letter No. and Date			
Geotech Investigation Report	Concessionaire Submission Letter No. and Date				# 119 on 18.03.2019			
	IE's Comment Letter No. and Date							
Hydrology Report	Concessionaire Submission Letter No. and Date							
	IE's Comment Letter No. and Date							
Foundation	Concessionaire Submission Letter No. and Date				# 119 on 18.03.2019			
	IE's Comment Letter No. and Date							
Substructure	Concessionaire Submission Letter No. and Date				# 119 on 18.03.2019			
	IE's Comment Letter No. and Date							
Superstructure	Concessionaire Submission Letter No. and Date			# 16 on 16.10.2018	# 119 on 18.03.2019			
	IE's Comment Letter No. and Date							
6	307+731			GAD	Concessionaire Submission Letter No. and Date	# 19 on 02.03.2019	# 27 on 27.03.2019	
					IE's Comment Letter No. and Date			
		Geotech Investigation Report	Concessionaire Submission Letter No. and Date	# 19 on 02.03.2019	# 27 on 27.03.2019			
			IE's Comment Letter No. and Date					
		Hydrology Report	Concessionaire Submission Letter No. and Date		# 27 on 27.03.2019			
			IE's Comment Letter No. and Date					
		Foundation	Concessionaire Submission Letter No. and Date	# 19 on 02.03.2019	# 27 on 27.03.2019			
			IE's Comment Letter No. and Date					
		Substructure	Concessionaire Submission Letter No. and Date	# 19 on 02.03.2019	# 27 on 27.03.2019			
			IE's Comment Letter No. and Date					
		Superstructure	Concessionaire Submission Letter No. and Date	# 19 on 02.03.2019	# 27 on 27.03.2019			
			IE's Comment Letter No. and Date					

MNB

Sr. no	Schedule Chainage (Km)		R0	R1	R2	Remark
7	309+100	GAD	Concessionaire Submission Letter No. and	#135 on 05.04.2019		
			IE's Comment Letter No.			
		Geotech Investigation Report	Concessionaire Submission Letter No. and	#135 on 05.04.2019		
			IE's Comment Letter No.			
		Foundation	Concessionaire Submission Letter No. and	#135 on 05.04.2019		
IE's Comment Letter No.						
Substructure	Concessionaire Submission Letter No. and	#135 on 05.04.2019				
	IE's Comment Letter No.					
Superstructure	Concessionaire Submission Letter No. and	#135 on 05.04.2019				
	IE's Comment Letter No.					
8	309+840	GAD	Concessionaire Submission Letter No. and	# 14 on 21.10.2018	HO# 14 on 21.02.2019	
			IE's Comment Letter No.			
		Geotech Investigation Report	Concessionaire Submission Letter No. and		HO# 14 on 21.02.2019	
			IE's Comment Letter No.			
		Foundation	Concessionaire Submission Letter No. and		HO# 14 on 21.02.2019	
IE's Comment Letter No.						
Substructure	Concessionaire Submission Letter No. and	# 14 on 21.10.2018	HO# 14 on 21.02.2019			
	IE's Comment Letter No.					
Superstructure	Concessionaire Submission Letter No. and	# 14 on 21.10.2018	HO# 14 on 21.02.2019			
	IE's Comment Letter No.					
9	310+752,	GAD	Concessionaire Submission Letter No. and			
10	313+835	GAD	Concessionaire Submission Letter No. and	# 109 on 11.03.2019	# 24 on 26.03.2019	
			IE's Comment Letter No.			
		Geotech Investigation Report	Concessionaire Submission Letter No. and	# 109 on 11.03.2019		
			IE's Comment Letter No.			
		Foundation	Concessionaire Submission Letter No. and	# 109 on 11.03.2019	# 24 on 26.03.2019	
IE's Comment Letter No.						
Substructure	Concessionaire Submission Letter No. and	# 109 on 11.03.2019	# 24 on 26.03.2019			
	IE's Comment Letter No.					
Superstructure	Concessionaire Submission Letter No. and	# 16 on 16.10.2018	# 109 on 11.03.2019	# 24 on 26.03.2019		
	IE's Comment Letter No.					

MNB									
Sr. no	Schedule Chainage (Km)		R0	R1	R2	R3	R4	Remark	
11	314+314	GAD	Concessionaire	# 110 on	#42 on				
			Submission Letter No. and IE's Comment Letter No.	11.03.2018	12.04.2019				
		Geotech Investigation Report	Concessionaire	# 110 on					
			Submission Letter No. and IE's Comment Letter No.	11.03.2018					
		Hydrology Report	Concessionaire	# 110 on					
			Submission Letter No. and IE's Comment Letter No.	11.03.2018					
		Foundation	Concessionaire	# 110 on	#42 on				
			Submission Letter No. and IE's Comment Letter No.	11.03.2018	12.04.2019				
		Substructure	Concessionaire	# 110 on	#42 on				
			Submission Letter No. and IE's Comment Letter No.	11.03.2018	12.04.2019				
		Superstructure	Concessionaire	# 110 on	#42 on				
			Submission Letter No. and IE's Comment Letter No.	11.03.2018	12.04.2019				
MJB									
Sr. no	Schedule Chainage (Km)		R0	R1	R2	R3	R4	Remark	
1	302+732	GAD	Concessionaire	#24 on	# 10 on	# 13 on	# 21 on	# 29 on	
			Submission Letter No. and IE's Comment Letter No.	14.11.2018	07.02.2019	21.02.2019	06.03.2019	28.03.2019	
		Geotech Investigation Report	Concessionaire			# 13 on	# 21 on	# 29 on	
			Submission Letter No. and IE's Comment Letter No.			21.02.2019	06.03.2019	28.03.2019	
		Hydrology Report	Concessionaire			# 13 on	# 21 on	# 29 on	
			Submission Letter No. and IE's Comment Letter No.			21.02.2019	06.03.2019	28.03.2019	
		Test Pile	Concessionaire		# 10 on				# 29 on
			Submission Letter No. and IE's Comment Letter No.		07.02.2019				28.03.2019
		Foundation	Concessionaire	#24 on	# 10 on	# 13 on	# 21 on	# 29 on	
			Submission Letter No. and IE's Comment Letter No.	14.11.2018	07.02.2019	21.02.2019	06.03.2019	28.03.2019	
		Substructure Abutment	Concessionaire	#24 on	# 10 on	# 13 on	# 21 on	# 29 on	
			Submission Letter No. and IE's Comment Letter No.	14.11.2018	07.02.2019	21.02.2019	06.03.2019	28.03.2019	
		Substructure Pier	Concessionaire	#24 on	# 10 on	# 13 on	# 21 on	# 29 on	
			Submission Letter No. and IE's Comment Letter No.	14.11.2018	07.02.2019	21.02.2019	06.03.2019	28.03.2019	
		Superstructure	Concessionaire	#24 on	# 10 on	# 13 on	# 21 on	# 29 on	
			Submission Letter No. and IE's Comment Letter No.	14.11.2018	07.02.2019	21.02.2019	06.03.2019	28.03.2019	

MJB

Sr. no	Schedule Chainage (Km)		R0	R1	R2	R3	Remark	
2	318+875	GAD	Concessionaire Submission Letter No. and Date		#39 on 10.04.2019			
			IE's Comment Letter No. and Date					
		Test Pile	Concessionaire Submission Letter No. and Date	# 11 on 11.09.2019				
			IE's Comment Letter No. and Date					
		Geotech Investigation Report	Concessionaire Submission Letter No. and Date		#39 on 10.04.2019			
			IE's Comment Letter No. and Date					
		Hydrology Report	Concessionaire Submission Letter No. and Date					
			IE's Comment Letter No. and Date					
		Foundation	Concessionaire Submission Letter No. and Date		#39 on 10.04.2019			
			IE's Comment Letter No. and Date					
		Substructure	Concessionaire Submission Letter No. and Date	#37 on 12.12.2018	#39 on 10.04.2019			
			IE's Comment Letter No. and Date					
		Substructure Pier	Concessionaire Submission Letter No. and Date		#39 on 10.04.2019			
			IE's Comment Letter No. and Date					
Superstructure	Concessionaire Submission Letter No. and Date	#37 on 12.12.2018	#39 on 10.04.2019					
	IE's Comment Letter No. and Date							
3	321+280	GAD	Concessionaire Submission Letter No. and Date	HO #5 on 02.02.2019		#20 on 06.03.2019	#30 on 28.03.2019	
			IE's Comment Letter No. and Date	Need to Coordinate with IE		#171 on 09.03.2019		
		Test Pile	Concessionaire Submission Letter No. and Date	# 13 on 24.09.2018				
			IE's Comment Letter No. and Date					
		Geotech Investigation Report	Concessionaire Submission Letter No. and Date	HO #5 on 02.02.2019				
			IE's Comment Letter No. and Date			#171 on 09.03.2019		
		Hydrology Report	Concessionaire Submission Letter No. and Date	HO #5 on 02.02.2019				
			IE's Comment Letter No. and Date			#171 on 09.03.2019		
		Foundation	Concessionaire Submission Letter No. and Date	HO #5 on 02.02.2019		#20 on 06.03.2019	#30 on 28.03.2019	
			IE's Comment Letter No. and Date			#171 on 09.03.2019		
		Substructure	Concessionaire Submission Letter No. and Date	HO #5 on 02.02.2019		#20 on 06.03.2019	#30 on 28.03.2019	
			IE's Comment Letter No. and Date			#171 on 09.03.2019		
		Substructure Pier	Concessionaire Submission Letter No. and Date	HO #5 on 02.02.2019	HO #15 on 28.02.2019	#20 on 06.03.2019	#30 on 28.03.2019	
			IE's Comment Letter No. and Date			#171 on 09.03.2019		

ROB								
Sr. no	Schedule Chainage (Km)		R0	R1	Remark			
1	293+050	GAD	Concessionaire Submission Letter No. and Date	GAD Approved				
			IE's Comment Letter No. and Date					
		Test Pile	Concessionaire Submission Letter No. and Date	# 40 on 10.04.2019				
			IE's Comment Letter No. and Date					
		Geotech Investigation Report	Concessionaire Submission Letter No. and Date	#46 on 26.04.2019				
			IE's Comment Letter No. and Date					
		Hydrology Report	Concessionaire Submission Letter No. and Date	-				
			IE's Comment Letter No. and Date					
		Foundation	Concessionaire Submission Letter No. and Date	#46 on 26.04.2019				
			IE's Comment Letter No. and Date					
		Substructure	Concessionaire Submission Letter No. and Date	#46 on 26.04.2019				
			IE's Comment Letter No. and Date					
		Substructure Pier	Concessionaire Submission Letter No. and Date	#46 on 26.04.2019				
			IE's Comment Letter No. and Date					
		Superstructure	Concessionaire Submission Letter No. and Date	#46 on 26.04.2019				
			IE's Comment Letter No. and Date					
		Toe Wall & Retaining Wall						

10.2 Highway drawing status

Plan And Profile				
Sr. no	Decription	Concessionaire Submission Letter No. and Date	IE's Comment Letter No. and Date	Remark
1	MCW	# 35 on 08.04.2019		
2	Connectng Road	# 35 on 08.04.2019		
3	VOP Approaches	# 35 on 08.04.2019		

10.3 Review status of source approvals

Abstract of Pavement Design

Connecting Road / Main Carriageway & Type of Pavement			Pavement Composition	Status	Remark
connecting Roads/ Overpass Cross Roads	Flexible Pavement	New Construction (10 MSA)	40 mm BC + 50 mm DBM +250 mm WMM + 200 mm GSB + 500 mm Subgrade with 8% effective CBR	APPROVED	Letter no. AA/VKE/PVKEPL/051/18-19/Design Review/176 dated 13.03.2019
			30 mm BC + 50 mm DBM +250 mm WMM + 200 mm GSB + 500 mm Subgrade with 10% effective CBR	APPROVED	Letter no. AA/VKE/PVKEPL/051/18-19/Design Review/176 dated 13.03.2019
			30 mm BC + 50 mm DBM +100 mm WMM + 150 mm CTSB + 500 mm Subgrade with 8% effective CBR	APPROVED	Letter no. AA/VKE/PVKEPL/051/18-19/Design Review/176 dated 13.03.2019
			30 mm BC + 50 mm DBM +100 mm WMM + 150 mm CTSB + 500 mm Subgrade with 10% effective CBR	APPROVED	Letter no. AA/VKE/PVKEPL/051/18-19/Design Review/176 dated 13.03.2019
			40 mm BC + 100 mm Aggregate Layer (WMM) + 200 mm Cemented Base + 250 mm GSB + 500 mm Subgrade with 8% effective CBR	APPROVED	Letter no. AA/VKE/PVKEPL/051/18-19/Design Review/176 dated 13.03.2019
			40 mm BC + 100 mm Aggregate Layer (WMM) + 200 mm Cemented Base + 250 mm GSB + 500 mm Subgrade with 10 % effective CBR	APPROVED	Letter no. AA/VKE/PVKEPL/051/18-19/Design Review/176 dated 13.03.2019
Main Carriage	Rigid Pavement	New Construction	300 mm PQC + 150 mm DLC + 150 mm GSB+ 500 mm Subgrade with 8% effective CBR	APPROVED	Letter no. AA/VKE/PVKEPL/051/18-19/Design Review/176 dated 13.03.2019

PLANT & APPROVAL STATUS

CRUSHER:-

300 TPH @ Rajpardi for Aggregates – Functional

Batching Plant:-

1. Batching Plant (60 CUM) @ Tralsa Camp (KM 299+350 R/S) - Functional
2. Batching Plant (112 CUM) @ Tralsa Camp (KM 299+350 R/S) - Functional
3. Batching Plant (60 CUM) @ Dayadra (KM 300+000 L/S) - Functional

Source Approval:-

Course Aggregates:-

1. Rajpardi Quarry Approved vide letter no. 85 dated 15th FEB 2019

Fine Aggregates:-

- Bodeli Source Approved vide letter no. 86 dated 16th FEB 2019
Nareshwar Source Approved vide letter no. 86 dated 16th FEB 2019

Cement:-

- M/s Birla Corporation Ltd., Chanderiya, Rajasthan vide 048 dated 02th Feb 2019
M/s Ultra Tech Cement Ltd., Mumbai vide 048 dated 02th Feb 2019
M/s Udaipur Cement works lid. Vide 048 dated 02th Feb 2019
M/s Sanghi Industries Ltd., Kutch District, Gujarat. Vide 048 dated 02th Feb 2019
M/s JK Lakshmi Cement Ltd., Sirohi, Rajasthan vide 048 dated 02th Feb 2019
M/s JK Sixer Cement vide 116 dated 25th Feb 2019
M/s Gujarat Sidhee cement vide 281 dated 11th March 2019

M/s Hathi Cement

vide 289 dated 13th March 2019

Chemical Admixture:-

M/S BASF India Limited

Approved vide letter no. 062 dated 12th Feb 2019

M/S Kunal Conchem Pvt Ltd

vide letter no. 062 dated 12th Feb 2019

Reinforcement Steel:-

M/s Essar Steel Limited, Mumbai

M/s Electrosteel Steel Limited, Kolkatta

Steel Authority of India Limited (SAIL)

Tata Iron and Steel company Limited (TISCO)

Rashtriya Ispat Nigam Limited (RINL)

Jindal Steel & Power Limited (JSPL)

NP4 Hume Pipe:-

M/s Giriraj Hume Pipes Industries, Bodeli

Approved vide letter no. 066 dated 12th Feb 2019

Approved Quantity of 1200 Dia NP4 Pipes – 300 Nos.

Concrete Mix Design:-

1) M-15 PCC, M-20 PCC, M-25 RCC, M-30 RCC, M-35 RCC, M-35 Pile, M-40 RCC

With Ultratech OPC 53 Grade cement, Timba Quarry Aggregates, Bodeli and Nareshwar Sand and Kunal Con Plast Admixture. Approved vide letter no. 131 dated 25th Feb 2019.

2) M-15 PCC, M-20 PCC, M-25 RCC, M-30 RCC, M-35 RCC, M-35 Pile, M-40 RCC

With Ultratech OPC 53 Grade cement, Timba Quarry Aggregates, Bodeli and Nareshwar Sand and BASF Admixture. Approved vide letter no. 132 dated 25th Feb 2019.

Borrow Area:-

09 nos. Borrow Area approved. Qty. – 305251 CUM

08 nos. Borrow Area Submitted Qty. – 408616 CUM

Borrow area tested Qty. 795200 CUM

Independent Laboratory :-

Mukesh A Patel, Ahmedabad

Approved vide letter no. 065 dated 12th Feb 2019

NCR:-

NCR.01:- Embankment construction is carried out on review stretches without ground improvement. By Letter no. 209 on 22.03.2019 and complied Vide letter 56 on dated 19.04.2019.

NCR.02:- Embankment construction is carried out on review stretches without ground improvement. By Letter no. 253 on 08.04.2019 and complied Vide letter 56 on dated 19.04.2019.

NCR.03:- Construction of Raft is carried out 500mm below the OGL at interface of PUP at Ch. 304+170 on LHS.

NCR.04:- PCC Construction is carried out at Foundation level over un-compacted earth fill of 900mm thick for the construction of PUP at Km. 305+058 and Km. 309+550. Rectification work in progress.

NCR.05:- Construction of back fill is carried out in a single layer with embankment of 1.5m depth around the HPC at ch.303+408. Rectification work in progress.

Annexure-01 Correspondence details


Out going from PVKEPL				
Sr.No	Letter No	Description	Dete	Remarks
1	PVKEPL/VKE3/IE/126/2019	Source of Erath to be obtained form Borrow Area fir the use in Embankment.	03 April 2019	
2	PVKEPL/VKE3/IE/127/2019	Source of Erath to be obtained form Borrow Area fir the use in Embankment.	03 April 2019	
3	PVKEPL/VKE3/IE/128/2019	Source of Erath to be obtained form Borrow Area fir the use in Embankment.	03 April 2019	
4	PVKEPL/VKE3/IE/129/2019	Source of Erath to be obtained form Borrow Area fir the use in Embankment.	03 April 2019	
5	PVKEPL/VKE3/IE/130/2019	Source of Erath to be obtained form Borrow Area fir the use in Embankment.	03 April 2019	
6	PVKEPL/VKE3/IE/131/2019	Source of Erath to be obtained form Borrow Area fir the use in Embankment.	03 April 2019	
7	PVKEPL/VKE3/IE/132/2019	Source of Erath to be obtained form Borrow Area fir the use in Embankment.	03 April 2019	
8	PVKEPL/VKE3/IE/133/2019	Source of Erath to be obtained form Borrow Area fir the use in Embankment.	03 April 2019	
9	PVKEPL/VKE3/IE/134/2019	Source of Erath to be obtained form Borrow Area fir the use in Embankment.	03 April 2019	
10	PVKEPL/VKE3/IE/134/2019	Submissiun of Design & Drawings for Minor Bridge over Gas Pipeline at CH-309+082.	05 April 2019	
11	PVKEPL/VKE3/ /136/2019	Tasting of Borrow Area Soil.	11 April 2019	
12	PVKEPL/VKE3/ /137/2019	Testing of OGL Soil.	11 April 2019	
13	PVKEPL/HO/VKE3/EE/032/2019	RSJ Pole utilization in emergency work.	06 April 2019	
14	PVKEPL/HO/VKE3/IE/034/2019	Request to provide emergency shutdown permission for shifing of MGVCL eletric poles available within ROW.	08 April 2019	
15	PVKEPL/HO/VK3/IE/035/2019	Compliance to the obsevation made on Sumitted plan & profile.	08 April 2019	
16	PVKEPL/HO/VKE3/NHAI/036/2019	Regarding payment made to NHAI against 50% Reimbursement of IE Fee.	09 April 2019	
17	PVKEPL/HO/VKE3/IE/037/2019	Submission of revised Design and Drawings of 12 Nos. of PUP/CUP.	09 April 2019	
18	PVKEPL/HO/VKP3/NHAI/038/2019	Submission of evidence of Contractors All Risks insurance Policy.	10 April 2019	
19	PVKEPL/HO/VKP3/IE/039/2019	Submission of design and drawings for Major Bridge at Ch.318+870.	10 April 2019	
20	PVKEPL/HO/VKP3/IE/040/2019	Regarding Submission of Structure Design and Drawings of Test Pipe for ROB.	10 April 2019	
21	PVKEPL/HO/VKE3/IE/033/2019	Submission of Monthly progress Report for the Month of March 2019 - Reg.	10 April 2019	
22	PVKEPL/HO/VKP3/IE/041/2019	Submission of detail drawings of 35 Nos. of Pipe Culverts.	11 April 2019	
23	PVKEPL/HO/VKP3/IE/042/2019	Submission of Dasign and Drawings of Minor Bridge at Ch.314+314.	12 April 2019	
24	PVKEPL/HO/VKE3/IE/043/2019	Submission of test report of Np - 4 Hume pipe- 1200mm.	12 April 2019	
25	PVKEPL/HO/VKP3/IE/044/2019	Construction work of Box culvert across canal on Vadodara-Mumbai Expressway - Reg.	15 April 2019	
26	PVKEPL/HO/VKP3/IE/045/2019	Submission of Estimated cost for the proposed Canal crossing structure.	15 April 2019	
27	PVKEPL/HO/VKP3/IE/047/2019	Joint site inspection for testing of 1200 mm dia and 600 mm dia R.C.C. Hume pipes at M/s Giriraj Hume pipe industries.	16 April 2019	

28	PVKEPL/HO/VKE3/IE/048/2019	Compliance to observation,s made on Embankment construction - Reg.	17 April 2019	
29	PVKEPL/HO/VKP3/IE/049/2019	Submission of revised Design and Drawings of 11 Nos. of PUP/CUP.	17 April 2019	
30	PVKEPL/HO/VKP3/IE/050/2019	Submission of revised design and drawings for 21 Nos. Box Culvert.	17 April 2019	
31	PVKEPL/HO/VKP3/IE/051/2019	Submission of revised design and drawings report of Retaining wall and Teo wall.	18 April 2019	
32	PVKEPL/HO/VKP3/IE/052/2019	Submission of Geotechnical Investigation report for PUP/CUP.	19 April 2019	
33	PVKEPL/HO/VKE3/IE/053/2019	Submission of typical diversion plan for the construction of various structures on project alignment.	22 April 2019	
34	PVKEPL/HO/VKE3/IE/054/2019	Submission of Company profile and credentials of Shree Harisai Spun Pipe Factory for source approval of the Hume Pipes NP4 1200mm dia. & 600mm dia.	22 April 2019	
35	PVKEPL/HO/VKE3/IE/055/2019	Regarding Submission of revised Design and Drawings of MNB at Ch.294+085.	22 April 2019	
36	PVKEPL/HO/VKE3/IE/056/2019	Compliance to observation,s made on Embankment construction - Reg.	19 April 2019	
37	PVKEPL/HO/VKE3/IE/057/2019	Submission of Company profile and Credentials of Jindal Steel & Power Limited for procurement of TMT bars for source approval.	22 April 2019	
38	PVKEPL/HO/VKE3/IE/058/2019	Submission of Patel load Methodology - Reg.	22 April 2019	
39	PVKEPL/HO/VKE3/IE/059/2019	Submission of Contract price Weightage - Reg.	24 April 2019	
40	PVKEPL/HO/VKE3/IE/061/2019	Submission of Company Profile and Credentials of Pushti Pipe industries for procurement of HUME Pipes NP4- 1200mm Dia & 600mm Dia.	26 April 2019	
41	PVKEPL/HO/VKP3/IE/062/2019	Regarding Submission of Structure Design and Drawings of Test Pipe for ROB.	26 April 2019	
42	PVKEPL/HO/VKE3/IE/063/2019	Submission of Patel Load Test reports.	30 April 2019	
43	PVKEPL/HO/VKP3/IE/064/2019	Submission of Routine Pile load test result for Major Bridge at CH-321+253.	30 April 2019	
44	PVKEPL/HO/VKP3/IE/065/2019	Submission of test report of NP - 4 Hume Pipe - 1200mm and 600mm.	30 April 2019	

Incoming From IE

S.No	Letter No	Description	Date	Remarks
1	AA-VKE-IVKEL-063-19-20-TESTING-236	Testing of OGL soil samples	01.04.19	
2	AA-VKE-PVKEPL-064-19-20-Q&M-241	submission of mix design for concreting with cement of Ultratech and admixture of BASF	02.04.19	
3	AA-VKE-PVKEPL-065-19-20-Q&M-242	submission of mix design for concreting with cement of Ultratech and admixture of Kunal	02.04.19	
4	AA-VKE/NHAI/PVKEPL/045-19-20/ROYALTY/249	Request to recommend the exemption from royalty procedure to the prestigious Vadodara - Kim exp. Project (pare of Vadodara - Mumbai section) to expedite the progress of execution -reg	04.04.2019	
5	AA-VKE-CONCESSIONAIRE-004-19-20-COS-250	Change of Scope/variation	04.04.2019	
6	AA-VKE-PVKEPL-066-19-20-Q&M-253	Non-Conformance Report (NCR)	08.04.19	
7	AA-VKE-PVKEPL-067-19-20-Q&M-256	Execution of embankment construction without conforming to specifications and standards	09.04.19	
8	AA-VKE-PVKEPL-068-19-20-MPR-266	MPR of concessionaire	09.04.19	
9	AA-VKE-PVKEPL-069-19-20-MPR-272	Detailed construction program and contract price weightage	10.04.19	
10	AA-VKE-NHAI & PVKEPL-001-19-20-MIR-275	Programme of inspection on the project highway for month of March-19	10.04.19	
11	AA-VKE-CONCESSIONAIRE-005-19-20-FLY ASH-276	Recommendation of the expert committee for effective utilization of fly ash in nhai	10.04.19	
12	AA-VKE-CONCESSIONAIRE-006-19-20-ROAD SAFETY-277	Compliance of observation of supreme court committee on road safety	10.04.19	
13	AA-VKE-PVKEPL-071-19-20-Q&M-281	Submission of company profile of Gujarat sidhee cement ltd. For procurement of cement for sources approval -reg.	11.04.19	
14	AA-VKE-PVKEPL-071-19-20-Q&M-282	Source of Earth to be obtained from Borrow Area for use in Embankment	11.04.19	
15	AA-VKE-PVKEPL-072-19-20-Q&M-283	Submission of Company Profile of Geo Design and Research Pvt. Ltd. for testing for the project	11.04.19	
16	AA-VKE-PVKEPL-073-19-20-NCR-285	Non-Conformance Report (NCR)	12.04.19	
17	AA-VKE-CONCESSIONAIRE-007-19-20-FLY ASH-287	Utilization of FLY ash of the thermal power plants in public work -reg.	12.04.19	
18	AA-VKE-PVKEPL-073-19-20-Q&M-288	Submission of Credentials & company profile of STP Limited as a one of the source for chemical material I,e, Admixtures reg.	13.04.2019	
19	AA-VKE-PVKEPL-074-19-20-Q&M-289	Submission of Company Profile of saurashtra cement ltd for procurement of cement for source approval -reg.	13.04.2019	
20	AA-VKE-PVKEPL-075-19-20-Q&M-290	Submission of Company Profile & Credentials of M/s siddhi vinayak pipe industries for source approval for Hume pipe procurement reg.	13.04.2019	
21	AA-VKE-CONCESSIONAIRE-008-19-20/VIDEO RECORDING/298	Video recording and development of a project specific website -reg.	12.04.2019	
22	AA-VKE/PVKEPL/-076-19-20/TESTIONG/299	Testing of OGL soil samples	13.04.2019	
23	AA-VKE-PVKEPL-077-19-20/NCR/300	Non-Conformance Report (NCR)	16.04.2019	
24	AA-VKE-PVKEPL-078-19-20-MPR-302	MPR of concessionaire	18.04.2019	
25	AA-VKE-PVKEPL-079-19-20-DESIGN -309	Submission of design and drawings of BC at Km 315+225.	20.04.2019	
26	AA-VKE-/NHAI/PVKEPL-054-19-20-MPR-318	Monthly inspection report-reg.	25.04.2019	
27	AA-VKE-NHAI-058-19-20-LEAVE-335	Leave of absence of team of team leader	01.05.2019	
28	AA-VKE-PVKEPL-080--19-20-DESIGN REVIEW-337	Submission of structure design and test pile from ROB -reg.	01.05.2019	
29	AA-VKE-PVKEPL-081--19-20-DESIGN REVIEW-338	Submission of structure design of drawing for major Bridge at ch.318+870-reg.	01.05.2019	
30	AA-VKE-PVKEPL/NHAI/-060--19-20-INVOICE-340	Local currency invoice no-07 of m/s Aarvee associates architects engineers & consultant pvt.ltd for the month of April 2019-reg	01.05.2019	
31	AA-VKE-PVKEPL-083--19-20-USW-342	Construction of eight lane Vadodara Kim exp. In the state of Gujarat under NHDP phase -vi on HAM mode (phase IA-pac-III)	01.05.2019	
32	AA-VKE-PVKEPL-084--19-20-DESIGN REVIEW-344	Submission of structure design and drawing for minor bridge at Km 314+314 reg.	02.05.2019	
33	AA-VKE-PVKEPL-085--19-20-USW-GETCO/346	Shifting height raising of high tension lines from proposed Vadodara -Mumbai Exp. Corridor ch.308+419.	02.05.2019	
34	AA-VKE-PVKEPL-086--19-20-DESIGN REVIEW-347	Submission of structure design and drawing for 12 no. of PUP/cup-reg	03.05.2019	
35	AA-VKE-PVKEPL-087--19-20-DESIGN REVIEW-348	Submission of detailed drawings of 35 no. of pipe culverts -reg.	03.05.2019	
36	AA-VKE-PVKEPL-088--19-20-DESIGN REVIEW-349	submission of revised design and drawings of MNB at km 294+085 reg.	03.05.2019	

Annexure-02 Organization Chart

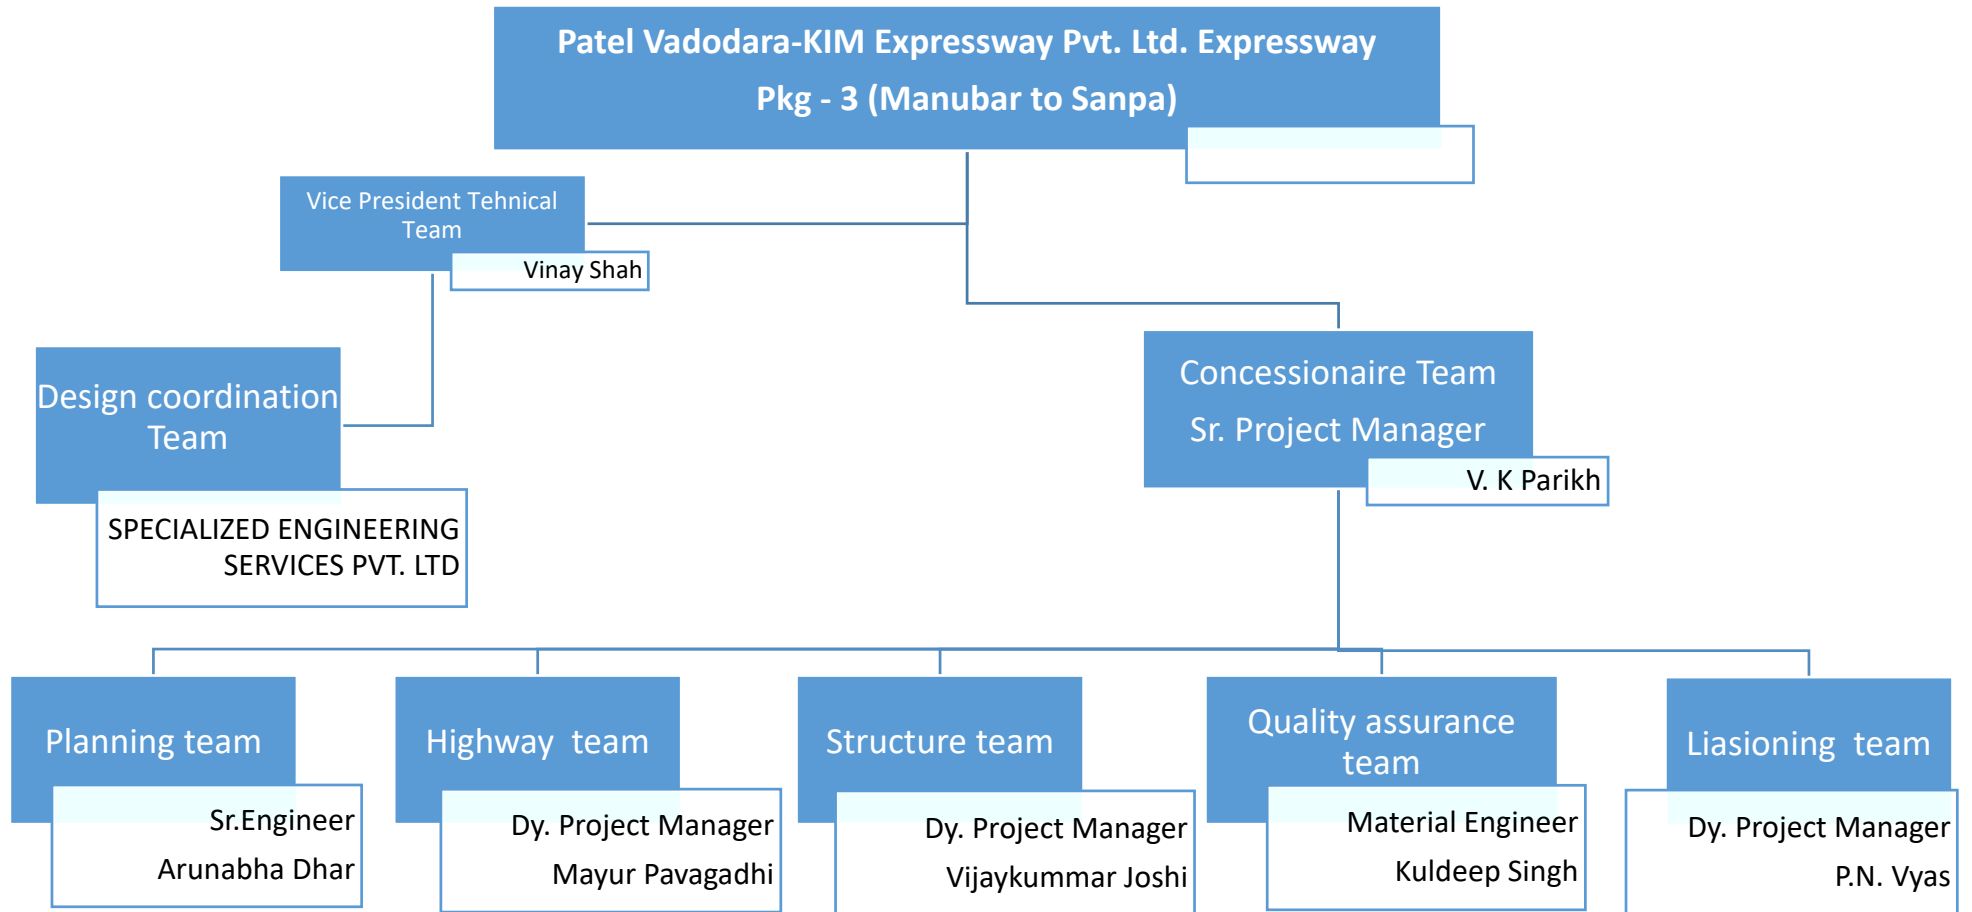

Annexure-03 RFI Summary

STRUCTURE										Status	Witness By IE	
1	VKE-3/PIL/STR/01	11-Mar-19	Pipe Culvert	Checking of Layout and Excavation for HPC	BHS	311+329	12-Mar-19	09:30AM				
1	VKE-3/PIL/STR/261	31-Mar-19	Pipe Culvert	Checking of Hume Pipe Laying 1200mm Dia.	BHS	303+608	1-Apr-19	11:00AM			Done	
2	VKE-3/PIL/STR/262	31-Mar-19	MJB	Checking of Pile Boring-A1	LHS	321+253	1-Apr-19	11:30AM		A1 LHS-Pile No.06	Done	
3	VKE-3/PIL/STR/263	31-Mar-19	MJB	Checking of Reinforcement of Pile Cage-A1	LHS	321+253	1-Apr-19	12:00PM		A1 LHS-Pile No.06	Done	
4	VKE-3/PIL/STR/264	31-Mar-19	MJB	Checking of Pile Concreting-A1	LHS	321+253	1-Apr-19	02:00PM		A1 LHS-Pile No.06	Done	
5	VKE-3/PIL/STR/265	31-Mar-19	MJB	Checking of Pile Boring-A1	LHS	321+253	1-Apr-19	03:30PM		A1 LHS-Pile No.08	Done	
6	VKE-3/PIL/STR/266	31-Mar-19	MJB	Checking of Reinforcement of Pile Cage-A1	LHS	321+253	1-Apr-19	04:30PM		A1 LHS-Pile No.08	Done	
7	VKE-3/PIL/STR/267	31-Mar-19	MJB	Checking of Pile Concreting-A1	LHS	321+253	1-Apr-19	05:30PM		A1 LHS-Pile No.08	Done	
8	VKE-3/PIL/STR/268	31-Mar-19	MJB	Checking of Pile Boring-A1	LHS	321+253	1-Apr-19	03:00PM		A1 LHS-Pile No.04	Done	
9	VKE-3/PIL/STR/269	31-Mar-19	MJB	Checking of Reinforcement of Pile Cage-A1	LHS	321+253	1-Apr-19	04:00PM		A1 LHS-Pile No.04	Done	
10	VKE-3/PIL/STR/270	31-Mar-19	MJB	Checking of Pile Concreting-A1	LHS	321+253	1-Apr-19	05:00PM		A1 LHS-Pile No.04	Done	
11	VKE-3/PIL/STR/271	1-Apr-19	PUP	Checking of Reinforcement,Shuttering and Concreting of Raft-M30	LHS	304+170	2-Apr-19	11:00AM			Done	YES
12	VKE-3/PIL/STR/272	1-Apr-19	MJB	Checking of Pile Boring-A1	RHS	321+253	2-Apr-19	08:30AM		A1 RHS-Pile No.23	Done	YES
13	VKE-3/PIL/STR/273	1-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A1	RHS	321+253	2-Apr-19	09:30AM		A1 RHS-Pile No.23	Done	YES
14	VKE-3/PIL/STR/274	1-Apr-19	MJB	Checking of Pile Concreting-A1	RHS	321+253	2-Apr-19	10:30AM		A1 RHS-Pile No.23	Done	YES
15	VKE-3/PIL/STR/275	1-Apr-19	MJB	Checking of Pile Boring-A1	RHS	321+253	2-Apr-19	10:00AM		A1 RHS-Pile No.27	Done	
16	VKE-3/PIL/STR/276	1-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A1	RHS	321+253	2-Apr-19	12:00PM		A1 RHS-Pile No.27	Done	
17	VKE-3/PIL/STR/277	1-Apr-19	MJB	Checking of Pile Concreting-A1	RHS	321+253	2-Apr-19	02:00PM		A1 RHS-Pile No.27	Done	
18	VKE-3/PIL/STR/278	1-Apr-19	MJB	Checking of Pile Boring-A1	LHS	321+253	2-Apr-19	03:00PM		A1 LHS-Pile No.05	Done	
19	VKE-3/PIL/STR/279	1-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A1	LHS	321+253	2-Apr-19	04:00PM		A1 LHS-Pile No.05	Done	
20	VKE-3/PIL/STR/280	1-Apr-19	MJB	Checking of Pile Concreting-A1	LHS	321+253	2-Apr-19	06:00PM		A1 LHS-Pile No.05	Done	
21	VKE-3/PIL/STR/281	2-Apr-19	Box Culvert	Checking of Reinforcement,Shuttering and Concreting of Raft-M30	RHS	305+437	3-Apr-19	11:00AM			Done	
22	VKE-3/PIL/STR/282	2-Apr-19	MJB	Checking of Pile Boring-A2	LHS	302+713	3-Apr-19	08:30AM		A2 LHS-Pile No.69	Done	YES
23	VKE-3/PIL/STR/283	2-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A2	LHS	302+713	3-Apr-19	09:00AM		A2 LHS-Pile No.69	Done	YES
24	VKE-3/PIL/STR/284	2-Apr-19	MJB	Checking of Pile Concreting-A2	LHS	302+713	3-Apr-19	10:00AM		A2 LHS-Pile No.69	Done	
25	VKE-3/PIL/STR/285	2-Apr-19	MJB	Checking of Pile Boring-A2	LHS	302+713	3-Apr-19	11:30AM		A2 LHS-Pile No.81	Not Done	
26	VKE-3/PIL/STR/286	2-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A2	LHS	302+713	3-Apr-19	12:00PM		A2 LHS-Pile No.81	Not Done	
27	VKE-3/PIL/STR/287	2-Apr-19	MJB	Checking of Pile Concreting-A2	LHS	302+713	3-Apr-19	02:00PM		A2 LHS-Pile No.81	Not Done	
28	VKE-3/PIL/STR/288	2-Apr-19	MJB	Checking of Pile Boring-A1	RHS	321+253	3-Apr-19	03:00PM		A1 RHS-Pile No.42	Done	YES
29	VKE-3/PIL/STR/289	2-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A1	RHS	321+253	3-Apr-19	04:00PM		A1 RHS-Pile No.42	Done	YES
30	VKE-3/PIL/STR/290	2-Apr-19	MJB	Checking of Pile Concreting-A1	RHS	321+253	3-Apr-19	06:00PM		A1 RHS-Pile No.42	Done	YES
31	VKE-3/PIL/STR/291	2-Apr-19	MJB	Checking of Pile Boring-A1	RHS	321+253	3-Apr-19	03:30PM		A1 RHS-Pile No.47	Done	
32	VKE-3/PIL/STR/292	2-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A1	RHS	321+253	3-Apr-19	04:30PM		A1 RHS-Pile No.47	Done	
33	VKE-3/PIL/STR/293	2-Apr-19	MJB	Checking of Pile Concreting-A1	RHS	321+253	3-Apr-19	05:30PM		A1 RHS-Pile No.47	Done	
34	VKE-3/PIL/STR/294	2-Apr-19	MJB	Checking of Pile Boring-A1	RHS	321+253	3-Apr-19	03:00PM		A1 RHS-Pile No.36	Done	
35	VKE-3/PIL/STR/295	2-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A1	RHS	321+253	3-Apr-19	04:00PM		A1 RHS-Pile No.36	Done	
36	VKE-3/PIL/STR/296	2-Apr-19	MJB	Checking of Pile Concreting-A1	RHS	321+253	3-Apr-19	05:00PM		A1 RHS-Pile No.36	Done	
37	VKE-3/PIL/STR/297	2-Apr-19	MJB	Checking of Pile Boring-A2	RHS	321+253	3-Apr-19	06:30PM		A2 RHS-Pile No.96	Not Done	
38	VKE-3/PIL/STR/298	2-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A2	RHS	321+253	3-Apr-19	07:30PM		A2 RHS-Pile No.96	Not Done	
39	VKE-3/PIL/STR/299	2-Apr-19	MJB	Checking of Pile Concreting-A2	RHS	321+253	3-Apr-19	08:30PM		A2 RHS-Pile No.96	Not Done	
40	VKE-3/PIL/STR/300	2-Apr-19	MJB	Checking of Pile Boring-A2	RHS	321+253	3-Apr-19	07:00PM		A2 RHS-Pile No.97	Done	
41	VKE-3/PIL/STR/301	2-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A2	RHS	321+253	3-Apr-19	08:00PM		A2 RHS-Pile No.97	Done	
42	VKE-3/PIL/STR/302	2-Apr-19	MJB	Checking of Pile Concreting-A2	RHS	321+253	3-Apr-19	09:00PM		A2 RHS-Pile No.97	Done	
43	VKE-3/PIL/STR/303	2-Apr-19	MJB	Checking of Pile Boring-A2	RHS	321+253	3-Apr-19	08:45PM		A2 RHS-Pile No.98	Done	
44	VKE-3/PIL/STR/304	2-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A2	RHS	321+253	3-Apr-19	09:30PM		A2 RHS-Pile No.98	Done	
45	VKE-3/PIL/STR/305	2-Apr-19	MJB	Checking of Pile Concreting-A2	RHS	321+253	3-Apr-19	10:30PM		A2 RHS-Pile No.98	Done	
46	VKE-3/PIL/STR/306	3-Apr-19	Box Culvert	Checking of Layout and Excavation	BHS	300+148	4-Apr-19	08:30AM			Done	YES
47	VKE-3/PIL/STR/307	3-Apr-19	Pipe Culvert	Checking of Layout and Excavation	BHS	300+445	4-Apr-19	09:00AM			Done	YES
48	VKE-3/PIL/STR/308	3-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A2	LHS	302+713	4-Apr-19	08:00AM		A2 LHS-Pile No.70	Done	YES
49	VKE-3/PIL/STR/309	3-Apr-19	MJB	Checking of Pile Boring and Pile Concreting-A2	LHS	302+713	4-Apr-19	08:45AM		A2 LHS-Pile No.70	Done	YES
50	VKE-3/PIL/STR/310	3-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A2	LHS	302+713	4-Apr-19	09:30AM		A2 LHS-Pile No.81	Not Done	
51	VKE-3/PIL/STR/311	3-Apr-19	MJB	Checking of Pile Boring and Pile Concreting-A2	LHS	302+713	4-Apr-19	10:30AM		A2 LHS-Pile No.81	Not Done	
52	VKE-3/PIL/STR/312	3-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A1	RHS	321+253	4-Apr-19	11:00AM		A1 RHS-Pile No.39	Done	
53	VKE-3/PIL/STR/313	3-Apr-19	MJB	Checking of Pile Boring and Pile Concreting-A1	RHS	321+253	4-Apr-19	12:00PM		A1 RHS-Pile No.39	Done	
54	VKE-3/PIL/STR/314	3-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A1	RHS	321+253	4-Apr-19	02:00PM		A1 RHS-Pile No.37	Done	
55	VKE-3/PIL/STR/315	3-Apr-19	MJB	Checking of Pile Boring and Pile Concreting-A1	RHS	321+253	4-Apr-19	03:00PM		A1 RHS-Pile No.37	Done	
56	VKE-3/PIL/STR/316	3-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A1	RHS	321+253	4-Apr-19	04:00PM		A1 RHS-Pile No.41	Done	YES
57	VKE-3/PIL/STR/317	3-Apr-19	MJB	Checking of Pile Boring and Pile Concreting-A1	RHS	321+253	4-Apr-19	05:00PM		A1 RHS-Pile No.41	Done	
58	VKE-3/PIL/STR/318	3-Apr-19	Box Culvert	Checking of Reinforcement,Shuttering and Concreting of Raft-M30	LHS	303+403	4-Apr-19	03:00PM			Not Done	
59	VKE-3/PIL/STR/319	4-Apr-19	PUP	Checking of Excavation and Ground Improvement	BHS	305+058	5-Apr-19	08:30AM			Done	
60	VKE-3/PIL/STR/320	4-Apr-19	MJB	Checking of Layout for Abutments A1,AZ,P1 and P2	BHS	302+713	5-Apr-19	09:00AM			Done	
61	VKE-3/PIL/STR/321	4-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A1	LHS	321+253	5-Apr-19	08:00AM		A1 LHS-Pile No.04	Done	
62	VKE-3/PIL/STR/322	4-Apr-19	MJB	Checking of Pile Boring and Pile Concreting-A1	LHS	321+253	5-Apr-19	08:45AM		A1 LHS-Pile No.04	Done	
63	VKE-3/PIL/STR/323	4-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A1	LHS	321+253	5-Apr-19	09:30AM		A1 LHS-Pile No.06	Done	
64	VKE-3/PIL/STR/324	4-Apr-19	MJB	Checking of Pile Boring and Pile Concreting-A1	LHS	321+253	5-Apr-19	10:30AM		A1 LHS-Pile No.06	Done	
65	VKE-3/PIL/STR/325	4-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A2	RHS	321+253	5-Apr-19	02:00PM		A2 RHS-Pile No.96	Done	
66	VKE-3/PIL/STR/326	4-Apr-19	MJB	Checking of Pile Boring and Pile Concreting-A2	RHS	321+253	5-Apr-19	03:00PM		A2 RHS-Pile No.96	Done	
67	VKE-3/PIL/STR/327	4-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A2	LHS	302+713	5-Apr-19	11:00AM		A2 LHS-Pile No.71	Done	
68	VKE-3/PIL/STR/328	4-Apr-19	MJB	Checking of Pile Boring and Pile Concreting-A2	LHS	302+713	5-Apr-19	12:00PM		A2 LHS-Pile No.71	Done	
69	VKE-3/PIL/STR/329	4-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A2	LHS	302+713	5-Apr-19	04:00PM		A2 LHS-Pile No.76	Done	
70	VKE-3/PIL/STR/330	4-Apr-19	MJB	Checking of Pile Boring and Pile Concreting-A2	LHS	302+713	5-Apr-19	05:00PM		A2 LHS-Pile No.76	Done	
71	VKE-3/PIL/STR/331	4-Apr-19	MJB	Checking of Reinforcement of Pile Cage-A2	LHS	302+713	5-Apr-19	06:00PM		A2 LHS-Pile No.81	Done	
72	VKE-3/PIL/STR/332	4-Apr-19	MJB	Checking of Pile Boring and Pile Concreting-A2	LHS	302+713	5-Apr-19	07:00PM		A2 LHS-Pile No.81	Done	
73	VKE-3/PIL/STR/333	4-Apr-19	Box Culvert	Checking of Reinforcement,Shuttering and Concreting of Raft-M30	LHS	303+403	5-Apr-19	03:00PM			Done	YES
74	VKE-3/PIL/STR/334	4-Apr-19	Box Culvert	Checking of Ground Improvement	BHS	300+148	5-Apr-19	08:30AM			Done	
75	VKE-3/PIL/STR/335	4-Apr-19	Pipe Culvert	Checking of Ground Improvement	BHS	300+445	5-Apr-19	09:00AM			Done	
76	VKE-3/PIL/STR/336	4-Apr-19	Pipe Culvert	Checking of Hume Pipe Laying	BHS	313+369	5-Apr-19	10:00AM			Done	
77	VKE-3/PIL/STR/337	4-Apr-19	Toe Wall	Checking of Excavation	RHS	311+530	5-Apr-19	10:30AM			Not Done	
78	VKE-3/PIL/STR/338	4-Apr-19	Toe Wall	Checking of Ground Improvement for Toe Wall	RHS	311+530	5-Apr-19	12:00PM			Not Done	
79	VKE-3/PIL/STR/339	5-Apr-19	MJB	Checking of Pile Boring and Reinforcement of Pile Cage-A1	LHS	321+253	6-Apr-19	08:00AM		A1 LHS-Pile No.01	Done	YES
80	VKE-3/PIL/STR/340	5-Apr-19	MJB	Checking of Pile Concreting-A1	LHS	321+253	6-Apr-19	08:45AM		A1 LHS-Pile No.01	Done	
81	VKE-3/PIL/STR/341	5-Apr-19	MJB	Checking of Pile Boring and Reinforcement of Pile Cage-A1	LHS	321+253	6-Apr-19	09:30AM		A1 LHS-Pile No.03	Done	
82	VKE-3/PIL/STR/342	5-Apr-19	MJB	Checking of Pile Concreting-A1	LHS	321+253	6-Apr-19	10:30AM		A1 LHS-Pile No.03	Done	
83	VKE-3/PIL/STR/343	5-Apr-19	MJB	Checking of Pile Boring and Reinforcement of Pile Cage-A2	RHS	321+253	6-Apr-19	02:00PM		A2 RHS-Pile No.99	Done	YES
84	VKE-3/PIL/STR/344	5-Apr-19	MJB	Checking of Pile Concreting-A2	RHS	321+253	6-Apr-19	03:00PM		A2 RHS-Pile No.99	Done	

STRUCTURE										Status	Witness By IE	
85	VKE-3/PIL/STR/345	5-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage-A2	LHS	302+713	6-Apr-19	11:00AM		A2 LHS-Pile No.72	Done	
86	VKE-3/PIL/STR/346	5-Apr-19	MBJ	Checking of Pile Concreting-A2	LHS	302+713	6-Apr-19	12:00PM		A2 LHS-Pile No.72	Done	
87	VKE-3/PIL/STR/347	5-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage-A2	LHS	302+713	6-Apr-19	04:00PM		A2 LHS-Pile No.82	Not Done	
88	VKE-3/PIL/STR/348	5-Apr-19	MBJ	Checking of Pile Concreting-A2	LHS	302+713	6-Apr-19	05:00PM		A2 LHS-Pile No.82	Not Done	
89	VKE-3/PIL/STR/349	5-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage-A2	RHS	302+713	6-Apr-19	06:00PM		A2 RHS-Pile No.95	Done	
90	VKE-3/PIL/STR/350	5-Apr-19	MBJ	Checking of Pile Concreting-A2	RHS	302+713	6-Apr-19	07:00PM		A2 RHS-Pile No.95	Done	
91	VKE-3/PIL/STR/351	5-Apr-19	MBJ	Checking of Layout and Excavation for Pile Cap-A2	LHS	321+253	6-Apr-19	05:30PM		A2-LHS	Done	YES
92	VKE-3/PIL/STR/352	5-Apr-19	MBJ	Checking of Pile Cap PCC-A2	LHS	321+253	6-Apr-19	06:30PM		A2-LHS	Not Done	YES
93	VKE-3/PIL/STR/353	5-Apr-19	Box Culvert	Checking of Reinforcement,Shuttering and Concreting of Haunch-M30	RHS	305+437	6-Apr-19	03:00PM			Done	
94	VKE-3/PIL/STR/354	5-Apr-19	Box Culvert	Checking of PCC	LHS	305+437	6-Apr-19	03:30PM			Done	
95	VKE-3/PIL/STR/355	5-Apr-19	Toe Wall	Checking of Excavation	RHS	311+580	6-Apr-19	10:30AM			Done	
96	VKE-3/PIL/STR/356	5-Apr-19	Toe Wall	Checking of Ground Improvement for Toe Wall	RHS	311+580	6-Apr-19	12:00PM			Done	
97	VKE-3/PIL/STR/357	6-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage-A1	RHS	321+253	7-Apr-19	08:00AM		A1 RHS-Pile No.22	Done	
98	VKE-3/PIL/STR/358	6-Apr-19	MBJ	Checking of Pile Concreting-A1	RHS	321+253	7-Apr-19	08:45AM		A1 RHS-Pile No.22	Done	YES
99	VKE-3/PIL/STR/359	6-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage-A1	RHS	321+253	7-Apr-19	09:30AM		A1 RHS-Pile No.24	Done	
100	VKE-3/PIL/STR/360	6-Apr-19	MBJ	Checking of Pile Concreting-A1	RHS	321+253	7-Apr-19	10:30AM		A1 RHS-Pile No.24	Done	
101	VKE-3/PIL/STR/361	6-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage-A1	RHS	321+253	7-Apr-19	02:00PM		A1 RHS-Pile No.30	Done	
102	VKE-3/PIL/STR/362	6-Apr-19	MBJ	Checking of Pile Concreting-A1	RHS	321+253	7-Apr-19	03:00PM		A1 RHS-Pile No.30	Done	
103	VKE-3/PIL/STR/363	6-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage-A1	RHS	321+253	7-Apr-19	11:00AM		A1 RHS-Pile No.33	Done	
104	VKE-3/PIL/STR/364	6-Apr-19	MBJ	Checking of Pile Concreting-A1	RHS	321+253	7-Apr-19	12:00PM		A1 RHS-Pile No.33	Done	
105	VKE-3/PIL/STR/365	6-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage-P1	LHS	321+253	7-Apr-19	04:00PM		P1 LHS-Pile No.52	Done	
106	VKE-3/PIL/STR/366	6-Apr-19	MBJ	Checking of Pile Concreting-P1	LHS	321+253	7-Apr-19	05:00PM		P1 LHS-Pile No.52	Done	
107	VKE-3/PIL/STR/367	6-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage-A1	LHS	321+253	7-Apr-19	06:00PM		A1 RHS-Pile No.02	Done	
108	VKE-3/PIL/STR/368	6-Apr-19	MBJ	Checking of Pile Concreting-A1	LHS	321+253	7-Apr-19	07:00PM		A1 RHS-Pile No.02	Done	
109	VKE-3/PIL/STR/369	6-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage-A2	RHS	321+253	7-Apr-19	05:30PM		A2-LHS Pile no. 101	Done	
110	VKE-3/PIL/STR/370	6-Apr-19	MBJ	Checking of Pile Concreting-A2	RHS	321+253	7-Apr-19	06:30PM		A2-LHS Pile no. 101	Done	
111	VKE-3/PIL/STR/371	6-Apr-19	MBJ	Checking of Pile Cap PCC-A2	LHS	321+253	7-Apr-19	02:00PM			Done	
112	VKE-3/PIL/STR/372	6-Apr-19	Box Culvert	Checking of Reinforcement,Shuttering and Concreting of Raft	LHS	305+437	7-Apr-19	03:00PM			Done	
113	VKE-3/PIL/STR/373	6-Apr-19	HPC	Checking of Pipe Laying	BHS	314+669	7-Apr-19	03:30PM			Done	
114	VKE-3/PIL/STR/374	6-Apr-19	HPC	Checking of shuttering and concrete pouring for cradle	BHS	314+669	7-Apr-19	03:30PM			Done	
115	VKE-3/PIL/STR/375	6-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage-A2	LHS	302+713	7-Apr-19	02:00PM		A2-LHS Pile no. 73	Done	
116	VKE-3/PIL/STR/376	6-Apr-19	MBJ	Checking of Pile Concreting-A2	LHS	302+713	7-Apr-19	03:00PM		A2-LHS Pile no. 73	Done	
117	VKE-3/PIL/STR/377	6-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage-A2	LHS	302+713	7-Apr-19	11:00AM		A2-LHS Pile no. 82	Done	
118	VKE-3/PIL/STR/378	6-Apr-19	MBJ	Checking of Pile Concreting-A2	LHS	302+713	7-Apr-19	12:00PM		A2-LHS Pile no. 82	Done	
119	VKE-3/PIL/STR/379	6-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage-A2	RHS	302+713	7-Apr-19	04:00PM		A2-RHS Pile no. 88	Not Done	
120	VKE-3/PIL/STR/380	6-Apr-19	MBJ	Checking of Pile Concreting-A2	RHS	302+713	7-Apr-19	05:00PM		A2-RHS Pile no. 88	Not Done	
121	VKE-3/PIL/STR/381	6-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage-A2	RHS	302+713	7-Apr-19	06:00PM		A2-RHS Pile no. 95	Not Done	
122	VKE-3/PIL/STR/382	6-Apr-19	MBJ	Checking of Pile Concreting-A2	RHS	302+713	7-Apr-19	07:00PM		A2-RHS Pile no. 95	Not Done	
123	VKE-3/PIL/STR/383	6-Apr-19	Toe Wall	Checking of PCC	RHS	311+580	7-Apr-19	05:30PM			Done	
124	VKE-3/PIL/STR/384	7-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	321+253	8-Apr-19	08:00AM		A1 RHS-Pile No.38	Done	
125	VKE-3/PIL/STR/385	7-Apr-19	MBJ	Checking of Pile Concreting	RHS	321+253	8-Apr-19	08:45AM		A1 RHS-Pile No.38	Done	
126	VKE-3/PIL/STR/386	7-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	321+253	8-Apr-19	09:30AM		A1 RHS-Pile No.35	Done	
127	VKE-3/PIL/STR/387	7-Apr-19	MBJ	Checking of Pile Concreting	RHS	321+253	8-Apr-19	10:30AM		A1 RHS-Pile No.35	Done	
128	VKE-3/PIL/STR/388	7-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	321+253	8-Apr-19	02:00PM		A1 RHS-Pile No.34	Done	
129	VKE-3/PIL/STR/389	7-Apr-19	MBJ	Checking of Pile Concreting	RHS	321+253	8-Apr-19	03:00PM		A1 RHS-Pile No.34	Done	
130	VKE-3/PIL/STR/390	7-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage	LHS	321+253	8-Apr-19	11:00AM		P1 RHS-Pile No.55	Done	
131	VKE-3/PIL/STR/391	7-Apr-19	MBJ	Checking of Pile Concreting	LHS	321+253	8-Apr-19	12:00PM		P1 RHS-Pile No.55	Done	
132	VKE-3/PIL/STR/392	7-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	321+253	8-Apr-19	04:00PM		A2 LHS-Pile No.102	Done	
133	VKE-3/PIL/STR/393	7-Apr-19	MBJ	Checking of Pile Concreting	RHS	321+253	8-Apr-19	05:00PM		A2 LHS-Pile No.102	Done	
134	VKE-3/PIL/STR/394	7-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage	LHS	302+713	8-Apr-19	06:00PM		A2-LHS Pile no. 79	Done	YES
135	VKE-3/PIL/STR/395	7-Apr-19	MBJ	Checking of Pile Concreting	LHS	302+713	8-Apr-19	07:00PM		A2-LHS Pile no. 79	Done	
136	VKE-3/PIL/STR/396	7-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage	LHS	302+713	8-Apr-19	05:30PM		A2-LHS Pile no. 74	Done	
137	VKE-3/PIL/STR/397	7-Apr-19	MBJ	Checking of Pile Concreting	LHS	302+713	8-Apr-19	06:30PM		A2-LHS Pile no. 74	Done	
138	VKE-3/PIL/STR/398	7-Apr-19	HPC	Checking of PCC concreting	RHS	304+649	8-Apr-19	02:00PM			Done	
139	VKE-3/PIL/STR/399	7-Apr-19	PUP	Checking of layout excavation and Gound improvement	BHS	297+900	8-Apr-19	03:00PM			Done	
140	VKE-3/PIL/STR/400	7-Apr-19	PUP	Checking of layout excavation and Gound improvement	BHS	298+380	8-Apr-19	03:30PM			Done	
141	VKE-3/PIL/STR/401	7-Apr-19	PUP	Checking of layout excavation and Gound improvement	BHS	309+550	8-Apr-19	03:30PM			Done	
142	VKE-3/PIL/STR/402	7-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	302+713	8-Apr-19	02:00PM		A2-LHS Pile no. 88	Done	
143	VKE-3/PIL/STR/403	7-Apr-19	MBJ	Checking of Pile Concreting	RHS	302+713	8-Apr-19	03:00PM		A2-LHS Pile no. 88	Done	
144	VKE-3/PIL/STR/404	7-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	302+713	8-Apr-19	11:00AM		A2-LHS Pile no. 93	Done	
145	VKE-3/PIL/STR/405	7-Apr-19	MBJ	Checking of Pile Concreting	RHS	302+713	8-Apr-19	12:00PM		A2-LHS Pile no. 93	Done	
146	VKE-3/PIL/STR/406	7-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	302+713	8-Apr-19	04:00PM		A2-RHS Pile no. 95	Done	YES
147	VKE-3/PIL/STR/407	7-Apr-19	MBJ	Checking of Pile Concreting	RHS	302+713	8-Apr-19	05:00PM		A2-RHS Pile no. 95	Done	
148	VKE-3/PIL/STR/408	7-Apr-19	PUP	Checking of PCC concreting	RHS	309+550	8-Apr-19	06:00PM			Not Done	
149	VKE-3/PIL/STR/409	7-Apr-19	Toe Wall	Checking of Reinforcement,Shuttering and Concreting of Raft	RHS	311+580	8-Apr-19	07:00PM			Not Done	
150	VKE-3/PIL/STR/410	7-Apr-19	Toe Wall	Checking of layout excavation and Gound improvement	RHS	311+600	8-Apr-19	05:30PM			Done	
151	VKE-3/PIL/STR/411	8-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	321+253	9-Apr-19	08:00AM		A1 RHS-Pile No.25	Done	
152	VKE-3/PIL/STR/412	8-Apr-19	MBJ	Checking of Pile Concreting	RHS	321+253	9-Apr-19	08:45AM		A1 RHS-Pile No.25	Done	YES
153	VKE-3/PIL/STR/413	8-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	321+253	9-Apr-19	09:30AM		A1 RHS-Pile No.26	Done	
154	VKE-3/PIL/STR/414	8-Apr-19	MBJ	Checking of Pile Concreting	RHS	321+253	9-Apr-19	10:30AM		A1 RHS-Pile No.26	Done	
155	VKE-3/PIL/STR/415	8-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	321+253	9-Apr-19	02:00PM		A2 RHS-Pile No.103	Done	
156	VKE-3/PIL/STR/416	8-Apr-19	MBJ	Checking of Pile Concreting	RHS	321+253	9-Apr-19	03:00PM		A2 RHS-Pile No.103	Done	
157	VKE-3/PIL/STR/417	8-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage	LHS	302+713	9-Apr-19	11:00AM		A2 LHS-Pile No.80	Not Done	YES
158	VKE-3/PIL/STR/418	8-Apr-19	MBJ	Checking of Pile Concreting	LHS	302+713	9-Apr-19	12:00PM		A2 LHS-Pile No.80	Not Done	
159	VKE-3/PIL/STR/419	8-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage	LHS	302+713	9-Apr-19	04:00PM		A2 LHS-Pile No.75	Done	
160	VKE-3/PIL/STR/420	8-Apr-19	MBJ	Checking of Pile Concreting	LHS	302+713	9-Apr-19	05:00PM		A2 LHS-Pile No.75	Done	
161	VKE-3/PIL/STR/421	8-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	302+713	9-Apr-19	06:00PM		A2-RHS Pile no.87	Not Done	
162	VKE-3/PIL/STR/422	8-Apr-19	MBJ	Checking of Pile Concreting	RHS	302+713	9-Apr-19	07:00PM		A2-RHS Pile no.87	Not Done	
163	VKE-3/PIL/STR/423	8-Apr-19	MBJ	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	302+713	9-Apr-19	05:30PM		A2-RHS Pile no.93	Done	
164	VKE-3/PIL/STR/424	8-Apr-19	MBJ	Checking of Pile Concreting	RHS	302+713	9-Apr-19	06:30PM		A2-RHS Pile no.93	Done	
165	VKE-3/PIL/STR/425	8-Apr-19	MBJ	Checking of Pile Group Co-ordinates	LHS	321+253	9-Apr-19	04:00PM		P1-LHS	Done	
166	VKE-3/PIL/STR/426	8-Apr-19	MBJ	Checking of Pile Group Co-ordinates	LHS	321+253	9-Apr-19	04:00PM		P2-LHS	Done	
167	VKE-3/PIL/STR/427	8-Apr-19	MBJ	Checking of Pile Cap Excavation and Layout	RHS	321+253	9-Apr-19	04:00PM		P1-RHS	Done	
168	VKE-3/PIL/STR/428	8-Apr-19	MBJ	Checking of Pile Cap PCC	RHS	321+253	9-Apr-19	05:00PM		P1-RHS	Not Done	
169	VKE-3/PIL/STR/429	8-Apr-19	Box Culvert	Checking of Reinforcement,Shuttering and Concreting of Raft-M30	RHS	314+148	9-Apr-19	09:00AM			Done	
170	VKE-3/PIL/STR/430	8-Apr-19	Toe Wall	Checking of Reinforcement,Shuttering and Concreting of Raft	RHS	311+580	9-Apr-19	07:00PM			Done	

STRUCTURE										Status	Witness By IE
171	VKE-3/PIL/STR/431	8-Apr-19	PUP	Checking of PCC Laying	LHS	305+058	9-Apr-19	02:00PM		Not Done	
172	VKE-3/PIL/STR/432	8-Apr-19	PUP	Checking of PCC Laying	LHS	309+550	9-Apr-19	03:00PM		Not Done	
173	VKE-3/PIL/STR/433	9-Apr-19	MJB	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	321+253	10-Apr-19	08:00AM	A1 RHS-Pile No.28	Not Done	
174	VKE-3/PIL/STR/434	9-Apr-19	MJB	Checking of Pile Concreting	RHS	321+253	10-Apr-19	08:45AM	A1 RHS-Pile No.28	Not Done	
175	VKE-3/PIL/STR/435	9-Apr-19	MJB	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	321+253	10-Apr-19	09:30AM	A1 RHS-Pile No.29	Not Done	
176	VKE-3/PIL/STR/436	9-Apr-19	MJB	Checking of Pile Concreting	RHS	321+253	10-Apr-19	10:30AM	A1 RHS-Pile No.29	Not Done	
177	VKE-3/PIL/STR/437	9-Apr-19	MJB	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	321+253	10-Apr-19	02:00PM	A1 RHS-Pile No.31	Not Done	
178	VKE-3/PIL/STR/438	9-Apr-19	MJB	Checking of Pile Concreting	RHS	321+253	10-Apr-19	03:00PM	A1 RHS-Pile No.31	Not Done	
179	VKE-3/PIL/STR/439	9-Apr-19	MJB	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	321+253	10-Apr-19	11:00AM	A2 RHS-Pile No.109	Done	
180	VKE-3/PIL/STR/440	9-Apr-19	MJB	Checking of Pile Concreting	RHS	321+253	10-Apr-19	12:00PM	A2 RHS-Pile No.109	Done	
181	VKE-3/PIL/STR/441	9-Apr-19	MJB	Checking of Pile Boring and Reinforcement of Pile Cage	LHS	302+713	10-Apr-19	04:00PM	A2 LHS-Pile No.80	Done	
182	VKE-3/PIL/STR/442	9-Apr-19	MJB	Checking of Pile Concreting	LHS	302+713	10-Apr-19	05:00PM	A2 LHS-Pile No.80	Done	
183	VKE-3/PIL/STR/443	9-Apr-19	MJB	Checking of Pile Boring and Reinforcement of Pile Cage	LHS	302+713	10-Apr-19	06:00PM	A2 LHS-Pile No.78	Done	
184	VKE-3/PIL/STR/444	9-Apr-19	MJB	Checking of Pile Concreting	LHS	302+713	10-Apr-19	07:00PM	A2 LHS-Pile No.78	Done	
185	VKE-3/PIL/STR/445	9-Apr-19	MJB	Checking of Pile Boring and Reinforcement of Pile Cage	LHS	302+713	10-Apr-19	05:30PM	A2 LHS-Pile No.77	Not Done	
186	VKE-3/PIL/STR/446	9-Apr-19	MJB	Checking of Pile Concreting	LHS	302+713	10-Apr-19	06:30PM	A2 LHS-Pile No.77	Not Done	
187	VKE-3/PIL/STR/447	9-Apr-19	MJB	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	302+713	10-Apr-19	06:00PM	A2-RHS pile no.87	Done	YES
188	VKE-3/PIL/STR/448	9-Apr-19	MJB	Checking of Pile Concreting	RHS	302+713	10-Apr-19	07:00PM	A2-RHS pile no.87	Done	
189	VKE-3/PIL/STR/449	9-Apr-19	MJB	Checking of Pile Boring and Reinforcement of Pile Cage	RHS	302+713	10-Apr-19	05:30PM	A2-RHS pile no.96	Done	
190	VKE-3/PIL/STR/450	9-Apr-19	MJB	Checking of Pile Concreting	RHS	302+713	10-Apr-19	06:30PM	A2-RHS pile no.96	Done	
191	VKE-3/PIL/STR/451	9-Apr-19	MJB	Checking of Pile Boring and Reinforcement of Pile Cage	LHS	302+713	10-Apr-19	05:30PM	A1 LHS-Pile No.14	Done	YES
192	VKE-3/PIL/STR/452	9-Apr-19	MJB	Checking of Pile Concreting	LHS	302+713	10-Apr-19	06:30PM	A1 LHS-Pile No.14	Done	
193	VKE-3/PIL/STR/453	9-Apr-19	MJB	Checking of Pile Cap PCC	RHS	321+253	10-Apr-19	05:00PM	P1-RHS	Done	
194	VKE-3/PIL/STR/454	9-Apr-19	PUP	Checking of S.B.C	BHS	305+058	10-Apr-19	09:00AM		Not Done	YES
195	VKE-3/PIL/STR/455	9-Apr-19	PUP	Checking of S.B.C	BHS	309+550	10-Apr-19	07:00PM		Done	
196	VKE-3/PIL/STR/456	9-Apr-19	PUP	Checking of PCC Laying	RHS	305+058	10-Apr-19	02:00PM		Done	
197	VKE-3/PIL/STR/457	9-Apr-19	PUP	Checking of PCC Laying	RHS	309+550	10-Apr-19	03:00PM		Done	
198	VKE-3/PIL/STR/458	9-Apr-19	Pipe Culvert	Checking of PCC Laying	BHS	300+445	10-Apr-19	02:00PM		Done	

Sr. NO.	RFI NO.	Inspection Time	Inspection date	Item Description	Chainage		Side	Remarks	Status	Witness By IE
					From	To				
1	VKE-3/PIL/STR/459	08:00AM	11-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	321+253		RHS	A1 RHS-Pile No.28	Done	
2	VKE-3/PIL/STR/460	08:45AM	11-Apr-19	Checking of Pile Concreting	321+253		RHS	A1 RHS-Pile No.28	Done	
3	VKE-3/PIL/STR/461	09:30AM	11-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	321+253		RHS	A1 RHS-Pile No.29	Note Done	
4	VKE-3/PIL/STR/462	10:30AM	11-Apr-19	Checking of Pile Concreting	321+253		RHS	A1 RHS-Pile No.29	Note Done	
5	VKE-3/PIL/STR/463	02:00PM	11-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	321+253		RHS	A1 RHS-Pile No.31	Note Done	
6	VKE-3/PIL/STR/464	03:00PM	11-Apr-19	Checking of Pile Concreting	321+253		RHS	A1 RHS-Pile No.31	Note Done	
7	VKE-3/PIL/STR/465	11:00AM	11-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	321+253		RHS	A2 RHS-Pile No.104	Note Done	
8	VKE-3/PIL/STR/466	12:00PM	11-Apr-19	Checking of Pile Concreting	321+253		RHS	A2 RHS-Pile No.104	Note Done	
9	VKE-3/PIL/STR/467	04:00PM	11-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		LHS	A2 LHS-Pile No.77	Note Done	
10	VKE-3/PIL/STR/468	05:00PM	11-Apr-19	Checking of Pile Concreting	302+713		LHS	A2 LHS-Pile No.77	Note Done	
11	VKE-3/PIL/STR/469	06:00PM	11-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		RHS	A2 RHS-Pile No.94	Note Done	
12	VKE-3/PIL/STR/470	07:00PM	11-Apr-19	Checking of Pile Concreting	302+713		RHS	A2 RHS-Pile No.94	Note Done	
13	VKE-3/PIL/STR/471	05:30PM	11-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		RHS	A2 RHS-Pile No.89	Note Done	
14	VKE-3/PIL/STR/472	06:30PM	11-Apr-19	Checking of Pile Concreting	302+713		RHS	A2 RHS-Pile No.89	Note Done	
15	VKE-3/PIL/STR/473	06:00PM	11-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		RHS	A2 RHS-Pile No.90	Note Done	
16	VKE-3/PIL/STR/474	07:00PM	11-Apr-19	Checking of Pile Concreting	302+713		RHS	A2 RHS-Pile No.90	Note Done	
17	VKE-3/PIL/STR/475	05:30PM	11-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		RHS	A1-RHS Pile no.28	Note Done	
18	VKE-3/PIL/STR/476	06:30PM	11-Apr-19	Checking of Pile Concreting	302+713		RHS	A1-RHS Pile no.28	Note Done	
19	VKE-3/PIL/STR/477	04:15PM	11-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		LHS	A1 LHS-Pile No.13	Note Done	
20	VKE-3/PIL/STR/478	05:15PM	11-Apr-19	Checking of Pile Concreting	302+713		LHS	A1 LHS-Pile No.13	Note Done	
21	VKE-3/PIL/STR/479	06:00PM	11-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		LHS	A1 LHS-Pile No.02	Note Done	
22	VKE-3/PIL/STR/480	07:15PM	11-Apr-19	Checking of Pile Concreting	302+713		LHS	A1 LHS-Pile No.02	Note Done	
23	VKE-3/PIL/STR/481	11:00AM	11-Apr-19	Checking of Layout and Excavation of Toe Wall	311+680	311+700	RHS	Toe Wall	Note Done	
24	VKE-3/PIL/STR/482	02:00PM	11-Apr-19	Checking of Ground Improvement of Toe Wall	311+680	311+700	RHS	Toe Wall	Note Done	
25	VKE-3/PIL/STR/483	10:00AM	11-Apr-19	Checking of Cradle Concrete-M15	314+669		RHS	HPC	Done	
26	VKE-3/PIL/STR/484	03:00PM	11-Apr-19	Checking of Reinforcement,Shuttering and Concreting of Wall 1s Lift-M30	305+437		RHS	Box Culvert	Done	
27	VKE-3/PIL/STR/485	04:00PM	11-Apr-19	Checking of Reinforcement,Shuttering and Concreting of Haunch-M30	305+437		RHS	Box Culvert	Done	
28	VKE-3/PIL/STR/486	08:00AM	12-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	321+253		RHS	A1 RHS-Pile No.29	Done	
29	VKE-3/PIL/STR/487	08:45AM	12-Apr-19	Checking of Pile Concreting	321+253		RHS	A1 RHS-Pile No.29	Done	
30	VKE-3/PIL/STR/488	09:30AM	12-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	321+253		RHS	A1 RHS-Pile No.31	Done	
31	VKE-3/PIL/STR/489	10:30AM	12-Apr-19	Checking of Pile Concreting	321+253		RHS	A1 RHS-Pile No.31	Done	
32	VKE-3/PIL/STR/490	02:00PM	12-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	321+253		RHS	A2 RHS-Pile No.104	Done	
33	VKE-3/PIL/STR/491	03:00PM	12-Apr-19	Checking of Pile Concreting	321+253		RHS	A2 RHS-Pile No.104	Done	
34	VKE-3/PIL/STR/492	04:00PM	12-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		LHS	A2 LHS-Pile No.77	Done	
35	VKE-3/PIL/STR/493	05:00PM	12-Apr-19	Checking of Pile Concreting	302+713		LHS	A2 LHS-Pile No.77	Done	
36	VKE-3/PIL/STR/494	06:00PM	12-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		RHS	A2 RHS-Pile No.94	Done	
37	VKE-3/PIL/STR/495	07:00PM	12-Apr-19	Checking of Pile Concreting	302+713		RHS	A2 RHS-Pile No.94	Done	Yes
38	VKE-3/PIL/STR/496	06:00PM	12-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		RHS	A2 RHS-Pile No.90	Done	
39	VKE-3/PIL/STR/497	07:00PM	12-Apr-19	Checking of Pile Concreting	302+713		RHS	A2 RHS-Pile No.90	Done	
40	VKE-3/PIL/STR/498	05:30PM	12-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		RHS	A1-RHS Pile no.28	Done	
41	VKE-3/PIL/STR/499	06:30PM	12-Apr-19	Checking of Pile Concreting	302+713		RHS	A1-RHS Pile no.28	Done	
42	VKE-3/PIL/STR/500	04:15PM	12-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		LHS	A1 LHS-Pile No.13	Done	
43	VKE-3/PIL/STR/501	05:15PM	12-Apr-19	Checking of Pile Concreting	302+713		LHS	A1 LHS-Pile No.13	Done	
44	VKE-3/PIL/STR/502	06:00PM	12-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		LHS	A1 LHS-Pile No.02	Done	
45	VKE-3/PIL/STR/503	07:15PM	12-Apr-19	Checking of Pile Concreting	302+713		LHS	A1 LHS-Pile No.02	Done	
46	VKE-3/PIL/STR/504	08:00AM	12-Apr-19	Checking of PCC of Toe Wall	311+600	311+620	RHS	Toe Wall	Not Done	
47	VKE-3/PIL/STR/505	02:00PM	12-Apr-19	Checking of Reinforcement,Shuttering and Concreting of Raft-M25 of Toe Wall	311+680	311+700	RHS	Toe Wall	Not Done	
48	VKE-3/PIL/STR/506	10:00AM	12-Apr-19	Checking of Cradle Concrete-M15	313+369		LHS	HPC	Done	
49	VKE-3/PIL/STR/507	03:00PM	12-Apr-19	Checking of Reinforcement,Shuttering and Concreting of Raft-M30	304+170		RHS	PUP	Done	
50	VKE-3/PIL/STR/508	02:00PM	12-Apr-19	Checking of Ground Improvement	297+900		BHS	PUP	Done	
51	VKE-3/PIL/STR/509	04:00PM	12-Apr-19	Checking of PCC Laying	305+058		LHS	PUP	Not Done	Yes
52	VKE-3/PIL/STR/510	08:00AM	13-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	321+253		RHS	A1 RHS-Pile No.32	Done	
53	VKE-3/PIL/STR/511	08:45AM	13-Apr-19	Checking of Pile Concreting	321+253		RHS	A1 RHS-Pile No.32	Done	
54	VKE-3/PIL/STR/512	09:30AM	13-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	321+253		RHS	A2 RHS-Pile No.113	Done	
55	VKE-3/PIL/STR/513	10:30AM	13-Apr-19	Checking of Pile Concreting	321+253		RHS	A2 RHS-Pile No.113	Done	
56	VKE-3/PIL/STR/514	02:00PM	13-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	321+253		RHS	A2 RHS-Pile No.114	Done	
57	VKE-3/PIL/STR/515	03:00PM	13-Apr-19	Checking of Pile Concreting	321+253		RHS	A2 RHS-Pile No.114	Done	
58	VKE-3/PIL/STR/516	04:00PM	13-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		RHS	A1 RHS-Pile No.27	Done	
59	VKE-3/PIL/STR/517	05:00PM	13-Apr-19	Checking of Pile Concreting	302+713		RHS	A1 RHS-Pile No.27	Done	
60	VKE-3/PIL/STR/518	06:00PM	13-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		RHS	A2 RHS-Pile No.91	Done	
61	VKE-3/PIL/STR/519	07:00PM	13-Apr-19	Checking of Pile Concreting	302+713		RHS	A2 RHS-Pile No.91	Done	
62	VKE-3/PIL/STR/520	06:00PM	13-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		RHS	A2 RHS-Pile No.89	Done	
63	VKE-3/PIL/STR/521	07:00PM	13-Apr-19	Checking of Pile Concreting	302+713		RHS	A2 RHS-Pile No.89	Done	
64	VKE-3/PIL/STR/522	05:30PM	13-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		LHS	A1 LHS-Pile No.04	Done	
65	VKE-3/PIL/STR/523	06:30PM	13-Apr-19	Checking of Pile Concreting	302+713		LHS	A1 LHS-Pile No.04	Done	
66	VKE-3/PIL/STR/524	04:15PM	13-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		LHS	A1 LHS-Pile No.11	Done	
67	VKE-3/PIL/STR/525	05:15PM	13-Apr-19	Checking of Pile Concreting	302+713		LHS	A1 LHS-Pile No.11	Done	
68	VKE-3/PIL/STR/526	06:00PM	13-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		LHS	A1 LHS-Pile No.10	Done	
69	VKE-3/PIL/STR/527	07:15PM	13-Apr-19	Checking of Pile Concreting	302+713		LHS	A1 LHS-Pile No.10	Done	
70	VKE-3/PIL/STR/528	08:00AM	13-Apr-19	Checking of Excavation of Toe Wall	311+680	311+700	RHS	Toe Wall	Done	
71	VKE-3/PIL/STR/529	09:00AM	13-Apr-19	Checking of Ground Improvement of Toe Wall	311+680	311+700	RHS	Toe Wall	Done	
72	VKE-3/PIL/STR/530	10:00AM	13-Apr-19	Checking of PCC of Toe Wall	311+680	311+700	RHS	Toe Wall	Done	
73	VKE-3/PIL/STR/531	02:00PM	13-Apr-19	Checking of Reinforcement,Shuttering of Wall 1st Lift of Toe Wall	311+580	311+600	RHS	Toe Wall	Done	
74	VKE-3/PIL/STR/532	10:00AM	13-Apr-19	Checking of Concreting of Wall 1st Lift-M25 of Toe Wall	311+580	311+600	RHS	Toe Wall	Done	
75	VKE-3/PIL/STR/533	02:00PM	13-Apr-19	Checking of Hume Pipe Laying	304+649		BHS	HPC	Done	
76	VKE-3/PIL/STR/534	04:00PM	13-Apr-19	Checking of PCC Laying	305+058		LHS	PUP	Done	
77	VKE-3/PIL/STR/535	08:00AM	14-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		RHS	A1 RHS-Pile No.92	Done	
78	VKE-3/PIL/STR/536	08:45AM	14-Apr-19	Checking of Pile Concreting	302+713		RHS	A1 RHS-Pile No.92	Done	
79	VKE-3/PIL/STR/537	09:30AM	14-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		RHS	A2 RHS-Pile No.84	Done	
80	VKE-3/PIL/STR/538	10:30AM	14-Apr-19	Checking of Pile Concreting	302+713		RHS	A2 RHS-Pile No.84	Done	
81	VKE-3/PIL/STR/539	02:00PM	14-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		RHS	A2 RHS-Pile No.86	Done	
82	VKE-3/PIL/STR/540	03:00PM	14-Apr-19	Checking of Pile Concreting	302+713		RHS	A2 RHS-Pile No.86	Done	
83	VKE-3/PIL/STR/541	04:00PM	14-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		LHS	A1 LHS-Pile No.05	Done	
84	VKE-3/PIL/STR/542	05:00PM	14-Apr-19	Checking of Pile Concreting	302+713		LHS	A1 LHS-Pile No.05	Done	
85	VKE-3/PIL/STR/543	06:00PM	14-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		LHS	A1 LHS-Pile No.09	Done	

Sr. NO.	RFI NO.	Inspection Time	Inspection date	Item Description	Chainage		Side	Remarks	Status	Witness By IE
					From	To				
86	VKE-3/PIL/STR/544	07:00PM	14-Apr-19	Checking of Pile Concreting	302+713		LHS	A1 LHS-Pile No.09	Done	
87	VKE-3/PIL/STR/545	06:00PM	14-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	302+713		RHS	A2 RHS-Pile No.25	Done	
88	VKE-3/PIL/STR/546	07:00PM	14-Apr-19	Checking of Pile Concreting	302+713		RHS	A2 RHS-Pile No.25	Done	
89	VKE-3/PIL/STR/547	07.30 PM	14-Apr-19	Checking of Preparation for routine load test on working pile	302+713			A2 LHS	Not Done	
90	VKE-3/PIL/STR/548	04:00PM	14-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	321+253		RHS	A1 RHS-Pile No.105	Done	
91	VKE-3/PIL/STR/549	05:00PM	14-Apr-19	Checking of Pile Concreting	321+253		RHS	A1 RHS-Pile No.105	Done	
92	VKE-3/PIL/STR/550	06:00PM	14-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	321+253		RHS	A2 RHS-Pile No.110	Done	
93	VKE-3/PIL/STR/551	07:00PM	14-Apr-19	Checking of Pile Concreting	321+253		RHS	A2 RHS-Pile No.110	Done	
94	VKE-3/PIL/STR/552	06:00PM	14-Apr-19	Checking of Pile Boring and Reinforcement of Pile Cage	321+253		RHS	A2 RHS-Pile No.111	Done	
95	VKE-3/PIL/STR/553	07:00PM	14-Apr-19	Checking of Pile Concreting	321+253		RHS	A2 RHS-Pile No.111	Done	
96	VKE-3/PIL/STR/554	09:00AM	14-Apr-19	Checking of reinforcement,formwork and concrete for Box Culvert raft	303+403		RHS	Box Culvert	Done	
97	VKE-3/PIL/STR/555	09:00AM	14-Apr-19	Checking of SBC of PUP	298+380		BHS	PUP	Done	
98	VKE-3/PIL/STR/556	10:00AM	14-Apr-19	Checking of SBC of PUP	297+900		BHS	PUP	Done	
99	VKE-3/PIL/STR/557	02:00PM	14-Apr-19	Checking of PCC Laying	297+900		LHS	PUP	Done	
100	VKE-3/PIL/STR/558	08:00AM	15-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A2 RHS-Pile No.83	Done	
101	VKE-3/PIL/STR/559	08:45AM	15-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A2 RHS-Pile No.83	Done	
102	VKE-3/PIL/STR/560	09:30AM	15-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A2 RHS-Pile No.85	Done	
103	VKE-3/PIL/STR/561	10:30AM	15-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A2 RHS-Pile No.85	Done	
104	VKE-3/PIL/STR/562	02:00PM	15-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	A1 LHS-Pile No.01	Not Done	
105	VKE-3/PIL/STR/563	03:00PM	15-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	A1 LHS-Pile No.01	Not Done	
106	VKE-3/PIL/STR/564	04:00PM	15-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	A1 LHS-Pile No.03	Done	Yes
107	VKE-3/PIL/STR/565	05:00PM	15-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	A1 LHS-Pile No.03	Done	
108	VKE-3/PIL/STR/566	06:00PM	15-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	A1 LHS-Pile No.12	Done	
109	VKE-3/PIL/STR/567	07:00PM	15-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	A1 LHS-Pile No.12	Done	
110	VKE-3/PIL/STR/568	07:00PM	15-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.20	Done	
111	VKE-3/PIL/STR/569	08:00PM	15-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.20	Done	
112	VKE-3/PIL/STR/570	05:00PM	15-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.23	Done	
113	VKE-3/PIL/STR/571	06:00PM	15-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.23	Done	
114	VKE-3/PIL/STR/572	03:00PM	15-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.26	Done	
115	VKE-3/PIL/STR/573	04:00PM	15-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.26	Done	
116	VKE-3/PIL/STR/574	07:00PM	15-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.18	Done	
117	VKE-3/PIL/STR/575	08:00PM	15-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.18	Done	
118	VKE-3/PIL/STR/576	07:00PM	15-Apr-19	Checking and Preparation for routine load test for working pile on A2 side	302+713		LHS		Done	Yes
119	VKE-3/PIL/STR/577	08:00PM	15-Apr-19	Checking of bore depth for Pile along with Reinforcement	321+253		RHS	A1 RHS-Pile No.106	Not Done	
120	VKE-3/PIL/STR/578	05:00PM	15-Apr-19	Pouring of M35 grade of Concrete for Pile Work	321+253		RHS	A1 RHS-Pile No.106	Not Done	
121	VKE-3/PIL/STR/579	06:00PM	15-Apr-19	Checking of bore depth for Pile along with Reinforcement	321+253		RHS	A2 RHS-Pile No.107	Not Done	
122	VKE-3/PIL/STR/580	07:00PM	15-Apr-19	Pouring of M35 grade of Concrete for Pile Work	321+253		RHS	A2 RHS-Pile No.107	Not Done	
123	VKE-3/PIL/STR/581	05:00PM	15-Apr-19	Checking of bore depth for Pile along with Reinforcement	321+253		RHS	A2 RHS-Pile No.108	Not Done	
124	VKE-3/PIL/STR/582	05:30PM	15-Apr-19	Pouring of M35 grade of Concrete for Pile Work	321+253		RHS	A2 RHS-Pile No.108	Not Done	
125	VKE-3/PIL/STR/583	09:00AM	15-Apr-19	Checking of center coordinate A1 for Pile	321+253		RHS	MJB	Done	
126	VKE-3/PIL/STR/584	09:00AM	15-Apr-19	Checking of center coordinate A1 for Pile	321+253		LHS	MJB	Done	
127	VKE-3/PIL/STR/585	10:00AM	15-Apr-19	Checking of Layout & Excavation for Pile Cap on A1 Side	321+253		LHS	MJB	Done	
128	VKE-3/PIL/STR/586	05:00PM	15-Apr-19	Pouring of M15 grade of Concrete for Pile Cap PCC on A1 Side	321+253		LHS	MJB	Not Done	
129	VKE-3/PIL/STR/587	05:00PM	15-Apr-19	Pouring of M15 grade of Concrete for PUP PCC work	309+550		RHS	PUP	Not Done	
130	VKE-3/PIL/STR/588	08:00AM	16-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P2 RHS-Pile No.62	Not Done	
131	VKE-3/PIL/STR/589	08:45AM	16-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P2 RHS-Pile No.62	Not Done	
132	VKE-3/PIL/STR/590	09:30AM	16-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P2 RHS-Pile No.67	Done	Yes
133	VKE-3/PIL/STR/591	10:30AM	16-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P2 RHS-Pile No.67	Done	
134	VKE-3/PIL/STR/592	02:00PM	16-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.59	Not Done	
135	VKE-3/PIL/STR/593	03:00PM	16-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.59	Not Done	
136	VKE-3/PIL/STR/594	04:00PM	16-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.54	Done	
137	VKE-3/PIL/STR/595	05:00PM	16-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.54	Done	
138	VKE-3/PIL/STR/596	06:00PM	16-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	A1 LHS-Pile No.09	Done	
139	VKE-3/PIL/STR/597	07:00PM	16-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	A1 LHS-Pile No.09	Done	
140	VKE-3/PIL/STR/598	07:00PM	16-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.15	Not Done	
141	VKE-3/PIL/STR/599	08:00PM	16-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.15	Not Done	
142	VKE-3/PIL/STR/600	05:00PM	16-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.16	Done	
143	VKE-3/PIL/STR/601	06:00PM	16-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.16	Done	
144	VKE-3/PIL/STR/602	03:00PM	16-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.24	Done	
145	VKE-3/PIL/STR/603	04:00PM	16-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.24	Done	
146	VKE-3/PIL/STR/604	07:00PM	16-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	A1 LHS-Pile No.06	Done	
147	VKE-3/PIL/STR/605	08:00PM	16-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	A1 LHS-Pile No.06	Done	
148	VKE-3/PIL/STR/606	10:00AM	16-Apr-19	Checking of Layout for Abutment on A1 and A2	307+731		BHS	MJB	Done	
149	VKE-3/PIL/STR/607	07:00PM	16-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		LHS	A1 LHS-Pile No.01	Done	
150	VKE-3/PIL/STR/608	08:00PM	16-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		LHS	A1 LHS-Pile No.01	Done	
151	VKE-3/PIL/STR/609	06:00PM	16-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		LHS	A1 LHS-Pile No.13	Done	
152	VKE-3/PIL/STR/610	07:00PM	16-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		LHS	A1 LHS-Pile No.13	Done	
153	VKE-3/PIL/STR/611	07:00PM	16-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		RHS	A1 RHS-Pile No.15	Done	
154	VKE-3/PIL/STR/612	08:00PM	16-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		RHS	A1 RHS-Pile No.15	Done	
155	VKE-3/PIL/STR/613	05:00PM	16-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		RHS	A1 RHS-Pile No.27	Done	
156	VKE-3/PIL/STR/614	06:00PM	16-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		RHS	A1 RHS-Pile No.27	Done	
157	VKE-3/PIL/STR/615	05:00PM	16-Apr-19	Pouring of M35 grade of Concrete for Pile Work	321+253		RHS	A1 RHS-Pile No.106	Done	
158	VKE-3/PIL/STR/616	06:00PM	16-Apr-19	Checking of bore depth for Pile along with Reinforcement	321+253		RHS	A2 RHS-Pile No.107	Not Done	
159	VKE-3/PIL/STR/617	07:00PM	16-Apr-19	Pouring of M35 grade of Concrete for Pile Work	321+253		RHS	A2 RHS-Pile No.107	Not Done	
160	VKE-3/PIL/STR/618	05:00PM	16-Apr-19	Checking of bore depth for Pile along with Reinforcement	321+253		RHS	A2 RHS-Pile No.108	Done	
161	VKE-3/PIL/STR/619	05:30PM	16-Apr-19	Pouring of M35 grade of Concrete for Pile Work	321+253		RHS	A2 RHS-Pile No.108	Done	
162	VKE-3/PIL/STR/620	05:00PM	16-Apr-19	Pouring of M15 grade of Concrete for Pile Cap PCC on A1 Side	321+253		LHS	MJB	Done	
163	VKE-3/PIL/STR/621	08:00AM	17-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P2 RHS-Pile No.62	Not Done	
164	VKE-3/PIL/STR/622	08:45AM	17-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P2 RHS-Pile No.62	Not Done	
165	VKE-3/PIL/STR/623	09:30AM	17-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P2 RHS-Pile No.65	Done	
166	VKE-3/PIL/STR/624	10:30AM	17-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P2 RHS-Pile No.65	Done	
167	VKE-3/PIL/STR/625	02:00PM	17-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P2 LHS-Pile No.59	Not Done	
168	VKE-3/PIL/STR/626	03:00PM	17-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P2 LHS-Pile No.59	Not Done	
169	VKE-3/PIL/STR/627	04:00PM	17-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P2 LHS-Pile No.53	Done	
170	VKE-3/PIL/STR/628	05:00PM	17-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P2 LHS-Pile No.53	Done	

Sr. No.	RFI NO.	Inspection Time	Inspection date	Item Description	Chainage		Side	Remarks	Status	Witness By IE
					From	To				
171	VKE-3/PIL/STR/629	06:00PM	17-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	A1 LHS-Pile No.07	Not Done	
172	VKE-3/PIL/STR/630	07:00PM	17-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	A1 LHS-Pile No.07	Not Done	
173	VKE-3/PIL/STR/631	07:00PM	17-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.15	Not Done	
174	VKE-3/PIL/STR/632	08:00PM	17-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.15	Not Done	
175	VKE-3/PIL/STR/633	05:00PM	17-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.23	Not Done	
176	VKE-3/PIL/STR/634	06:00PM	17-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.23	Not Done	
177	VKE-3/PIL/STR/635	03:00PM	17-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.21	Not Done	
178	VKE-3/PIL/STR/636	04:00PM	17-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.21	Not Done	
179	VKE-3/PIL/STR/637	03:00PM	17-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A2 RHS-Pile No.85	Done	
180	VKE-3/PIL/STR/638	04:00PM	17-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A2 RHS-Pile No.85	Done	
181	VKE-3/PIL/STR/639	07:00PM	17-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	A1 LHS-Pile No.08	Done	
182	VKE-3/PIL/STR/640	08:00PM	17-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	A1 LHS-Pile No.08	Done	
183	VKE-3/PIL/STR/641	05:00PM	17-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		RHS	A1 RHS-Pile No.27	Done	
184	VKE-3/PIL/STR/642	06:00PM	17-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		RHS	A1 RHS-Pile No.27	Done	
185	VKE-3/PIL/STR/643	03:00PM	17-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		RHS	A1 RHS-Pile No.28	Done	
186	VKE-3/PIL/STR/644	04:00PM	17-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		RHS	A1 RHS-Pile No.28	Done	
187	VKE-3/PIL/STR/645	10:00AM	17-Apr-19	Checking of Co-ordinates for Piles of Abutment A1	307+731		BHS	MNB	Done	
188	VKE-3/PIL/STR/646	06:00PM	17-Apr-19	Checking of bore depth for Pile along with Reinforcement	321+253		RHS	A2 RHS-Pile No.94	Done	
189	VKE-3/PIL/STR/647	07:00PM	17-Apr-19	Pouring of M35 grade of Concrete for Pile Work	321+253		RHS	A2 RHS-Pile No.94	Done	
190	VKE-3/PIL/STR/648	05:00PM	17-Apr-19	Checking of bore depth for Pile along with Reinforcement	321+253		RHS	A2 RHS-Pile No.95	Done	
191	VKE-3/PIL/STR/649	06:00PM	17-Apr-19	Pouring of M35 grade of Concrete for Pile Work	321+253		RHS	A2 RHS-Pile No.95	Done	
192	VKE-3/PIL/STR/650	05:30PM	17-Apr-19	Checking of bore depth for Pile along with Reinforcement	321+253		RHS	A2 RHS-Pile No.96	Done	
193	VKE-3/PIL/STR/651	06:30PM	17-Apr-19	Pouring of M35 grade of Concrete for Pile Work	321+253		RHS	A2 RHS-Pile No.96	Done	
194	VKE-3/PIL/STR/652	09:00AM	17-Apr-19	Checking of Reinforcement,Shuttering & Concreting of Bottom Haunch-M30	303+403		LHS	Box Culvert	Done	
195	VKE-3/PIL/STR/653	10:00AM	17-Apr-19	Checking of PCC Laying	298+120		BHS	Pipe Culvert	Done	
196	VKE-3/PIL/STR/654	02:00PM	17-Apr-19	Checking of Reinforcement,Shuttering & Concreting of Wall 1st Lift	314+148		LHS	Box Culvert-A1 Side	Done	
197	VKE-3/PIL/STR/655	03:00PM	17-Apr-19	Checking of Reinforcement,Shuttering & Concreting of Raft of Toe Wall	311+680	311+700	LHS	Toe Wall	Done	
198	VKE-3/PIL/STR/656	10:00AM	18-Apr-19	Checking of Preparation for Routine Load Test on Working Pile-A1	302+713		RHS	Abutment-A1	Not Done	
199	VKE-3/PIL/STR/657	08:00AM	18-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P2 RHS-Pile No.62	Done	
200	VKE-3/PIL/STR/658	08:45AM	18-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P2 RHS-Pile No.62	Done	
201	VKE-3/PIL/STR/659	02:00PM	18-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P2 LHS-Pile No.59	Done	
202	VKE-3/PIL/STR/660	03:00PM	18-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P2 LHS-Pile No.59	Done	
203	VKE-3/PIL/STR/661	06:00PM	18-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	A1 LHS-Pile No.07	Not Done	
204	VKE-3/PIL/STR/662	07:00PM	18-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	A1 LHS-Pile No.07	Not Done	
205	VKE-3/PIL/STR/663	07:00PM	18-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.17	Done	
206	VKE-3/PIL/STR/664	08:00PM	18-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.17	Done	
207	VKE-3/PIL/STR/665	05:00PM	18-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.23	Done	
208	VKE-3/PIL/STR/666	06:00PM	18-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.23	Done	
209	VKE-3/PIL/STR/667	03:00PM	18-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.21	Done	
210	VKE-3/PIL/STR/668	04:00PM	18-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.21	Done	
211	VKE-3/PIL/STR/669	03:00PM	18-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.22	Done	
212	VKE-3/PIL/STR/670	04:00PM	18-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.22	Done	
213	VKE-3/PIL/STR/671	05:00PM	18-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		LHS	A1 LHS-Pile No.05	Not Done	
214	VKE-3/PIL/STR/672	06:00PM	18-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		LHS	A1 LHS-Pile No.05	Not Done	
215	VKE-3/PIL/STR/673	03:00PM	18-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		LHS	A1 LHS-Pile No.11	Not Done	
216	VKE-3/PIL/STR/674	04:00PM	18-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		LHS	A1 LHS-Pile No.11	Not Done	
217	VKE-3/PIL/STR/675	03:00PM	18-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		LHS	A2 LHS-Pile No.42	Done	
218	VKE-3/PIL/STR/676	04:00PM	18-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		LHS	A2 LHS-Pile No.42	Done	
219	VKE-3/PIL/STR/677	06:00PM	18-Apr-19	Checking of bore depth for Pile along with Reinforcement	321+253		RHS	A2 RHS-Pile No.107	Not Done	
220	VKE-3/PIL/STR/678	07:00PM	18-Apr-19	Pouring of M35 grade of Concrete for Pile Work	321+253		RHS	A2 RHS-Pile No.107	Not Done	
221	VKE-3/PIL/STR/679	05:00PM	18-Apr-19	Checking of bore depth for Pile along with Reinforcement	321+253		RHS	A2 RHS-Pile No.109	Not Done	
222	VKE-3/PIL/STR/680	06:00PM	18-Apr-19	Pouring of M35 grade of Concrete for Pile Work	321+253		RHS	A2 RHS-Pile No.109	Not Done	
223	VKE-3/PIL/STR/681	05:30PM	18-Apr-19	Checking of bore depth for Pile along with Reinforcement	321+253		RHS	A2 RHS-Pile No.114	Done	
224	VKE-3/PIL/STR/682	06:30PM	18-Apr-19	Pouring of M35 grade of Concrete for Pile Work	321+253		RHS	A2 RHS-Pile No.114	Done	
225	VKE-3/PIL/STR/683	10:00AM	18-Apr-19	Checking of SBC	297+900		RHS	PUP	Done	
226	VKE-3/PIL/STR/684	11:00AM	18-Apr-19	Checking of PCC Laying	297+900		RHS	PUP	Done	
227	VKE-3/PIL/STR/685	03:00PM	18-Apr-19	Checking of Excavation & Ground Improvement of Toe Wall	311+700	311+720	RHS	Toe Wall	Done	
228	VKE-3/PIL/STR/686	08:00AM	19-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.31	Done	
229	VKE-3/PIL/STR/687	08:45AM	19-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.31	Done	
230	VKE-3/PIL/STR/688	02:00PM	19-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.37	Done	
231	VKE-3/PIL/STR/689	03:00PM	19-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.37	Done	
232	VKE-3/PIL/STR/690	06:00PM	19-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	A1 LHS-Pile No.07	Done	
233	VKE-3/PIL/STR/691	07:00PM	19-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	A1 LHS-Pile No.07	Done	
234	VKE-3/PIL/STR/692	07:00PM	19-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.17	Done	
235	VKE-3/PIL/STR/693	08:00PM	19-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.17	Done	
236	VKE-3/PIL/STR/694	05:00PM	19-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.15	Done	
237	VKE-3/PIL/STR/695	06:00PM	19-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.15	Done	
238	VKE-3/PIL/STR/696	05:00PM	19-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		LHS	A1 LHS-Pile No.05	Done	
239	VKE-3/PIL/STR/697	06:00PM	19-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		LHS	A1 LHS-Pile No.05	Done	
240	VKE-3/PIL/STR/698	03:00PM	19-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		LHS	A1 LHS-Pile No.11	Done	
241	VKE-3/PIL/STR/699	04:00PM	19-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		LHS	A1 LHS-Pile No.11	Done	
242	VKE-3/PIL/STR/700	03:00PM	19-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		LHS	A2 LHS-Pile No.30	Done	
243	VKE-3/PIL/STR/701	04:00PM	19-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		LHS	A2 LHS-Pile No.30	Done	
244	VKE-3/PIL/STR/702	08:00AM	19-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		LHS	A2 LHS-Pile No.40	Done	
245	VKE-3/PIL/STR/703	08:45AM	19-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		LHS	A2 LHS-Pile No.40	Done	
246	VKE-3/PIL/STR/704	02:00PM	19-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		RHS	A2 RHS-Pile No.56	Done	
247	VKE-3/PIL/STR/705	03:00PM	19-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		RHS	A2 RHS-Pile No.56	Done	
248	VKE-3/PIL/STR/706	06:00PM	19-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		RHS	A1 RHS-Pile No.25	Done	
249	VKE-3/PIL/STR/707	07:00PM	19-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		RHS	A1 RHS-Pile No.25	Done	
250	VKE-3/PIL/STR/708	06:00PM	19-Apr-19	Checking of bore depth for Pile along with Reinforcement	321+253		RHS	A2 RHS-Pile No.107	Done	
251	VKE-3/PIL/STR/709	07:00PM	19-Apr-19	Pouring of M35 grade of Concrete for Pile Work	321+253		RHS	A2 RHS-Pile No.107	Done	
252	VKE-3/PIL/STR/710	05:00PM	19-Apr-19	Checking of bore depth for Pile along with Reinforcement	321+253		RHS	A2 RHS-Pile No.109	Not Done	
253	VKE-3/PIL/STR/711	06:00PM	19-Apr-19	Pouring of M35 grade of Concrete for Pile Work	321+253		RHS	A2 RHS-Pile No.109	Not Done	
254	VKE-3/PIL/STR/712	04:00PM	19-Apr-19	Checking of Preparation for Routine Load Test on Working Pile-A2	321+253		LHS	A2 LHS-Pile No.74	Done	
255	VKE-3/PIL/STR/713	10:00AM	19-Apr-19	Checking of Shuttering,Reinforcement & Concreting of Wall 1st lift-M30	303+403		LHS	Box Culvert	Not Done	

Sr. NO.	RFI NO.	Inspection Time	Inspection date	Item Description	Chainage		Side	Remarks	Status	Witness By IE
					From	To				
256	VKE-3/PIL/STR/714	11:00AM	19-Apr-19	Checking of Shuttering,Reinforcement & Concreting of Wall 1st lift-M30	305+437		RHS	Box Culvert	Done	
257	VKE-3/PIL/STR/715	02:00PM	19-Apr-19	Checking of SBC	297+900		RHS	PUP	Done	
258	VKE-3/PIL/STR/716	03:30PM	19-Apr-19	Checking of PCC Laying	297+900		RHS	PUP	Done	
259	VKE-3/PIL/STR/717	03:00PM	19-Apr-19	Checking of Shuttering,Reinforcement & Concreting of Wall 1st lift-M30	314+148		LHS	Box Culvert	Done	
260	VKE-3/PIL/STR/718	02:00PM	19-Apr-19	Checking of Shuttering,Reinforcement & Concreting of Toe Wall 1st lift-M30	311+600	311+620	RHS	Toe Wall	Done	
261	VKE-3/PIL/STR/719	03:00PM	19-Apr-19	Checking of PCC Laying of Toe Wall	311+700	311+720	RHS	Toe Wall	Done	
262	VKE-3/PIL/STR/720	08:00AM	20-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.34	Done	
263	VKE-3/PIL/STR/721	08:45AM	20-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.34	Done	
264	VKE-3/PIL/STR/722	02:00PM	20-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.40	Done	
265	VKE-3/PIL/STR/723	03:00PM	20-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.40	Done	
266	VKE-3/PIL/STR/724	07:00PM	20-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P1 RHS-Pile No.50	Done	
267	VKE-3/PIL/STR/725	08:00PM	20-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P1 RHS-Pile No.50	Done	
268	VKE-3/PIL/STR/726	05:00PM	20-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P1 RHS-Pile No.51	Done	
269	VKE-3/PIL/STR/727	06:00PM	20-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P1 RHS-Pile No.51	Done	
270	VKE-3/PIL/STR/728	05:00PM	20-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		LHS	A1 LHS-Pile No.09	Done	
271	VKE-3/PIL/STR/729	06:00PM	20-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		LHS	A1 LHS-Pile No.09	Done	
272	VKE-3/PIL/STR/730	03:00PM	20-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		RHS	A1 RHS-Pile No.17	Not Done	
273	VKE-3/PIL/STR/731	04:00PM	20-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		RHS	A1 RHS-Pile No.17	Not Done	
274	VKE-3/PIL/STR/732	08:00AM	20-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		RHS	A1 RHS-Pile No.23	Not Done	
275	VKE-3/PIL/STR/733	08:45AM	20-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		RHS	A1 RHS-Pile No.23	Not Done	
276	VKE-3/PIL/STR/734	02:00PM	20-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		RHS	A2 RHS-Pile No.38	Not Done	
277	VKE-3/PIL/STR/735	03:00PM	20-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		RHS	A2 RHS-Pile No.38	Not Done	
278	VKE-3/PIL/STR/736	06:00PM	20-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+731		RHS	A1 RHS-Pile No.19	Done	
279	VKE-3/PIL/STR/737	07:00PM	20-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+731		RHS	A1 RHS-Pile No.19	Done	
280	VKE-3/PIL/STR/738	06:00PM	20-Apr-19	Checking of Vertical Dynamic Routine Load Test on Pile No.74 -A2	321+253		LHS	A2 LHS-Pile No.74	Done	
281	VKE-3/PIL/STR/739	04:00PM	20-Apr-19	Checking of Integrity Test on Pile-A2	321+253		LHS	A2 LHS-Pile No.90	Done	
282	VKE-3/PIL/STR/740	05:00PM	20-Apr-19	Checking of Shuttering,Reinforcement & Concreting of Wall 1st lift-M30	303+403		LHS	Box Culvert	Done	
283	VKE-3/PIL/STR/741	11:00AM	20-Apr-19	Checking of Shuttering,Reinforcement & Concreting of Top Slab-M30	305+437		RHS	Box Culvert	Done	
284	VKE-3/PIL/STR/742	08:30AM	20-Apr-19	Checking of Excavated Level	298+380		BHS	PUP	Done	
285	VKE-3/PIL/STR/743	04:00PM	20-Apr-19	Checking of Ground Improvement	298+380		BHS	PUP	Done	
286	VKE-3/PIL/STR/744	02:00PM	20-Apr-19	Checking of Layout and Excavation	298+819		BHS	Pipe Culvert	Done	
287	VKE-3/PIL/STR/745	03:00PM	20-Apr-19	Checking of Ground Improvement	309+550		RHS	PUP	Not Done	
288	VKE-3/PIL/STR/746	03:30PM	20-Apr-19	Checking of PCC Laying	309+550		RHS	PUP	Not Done	
289	VKE-3/PIL/STR/747	04:00PM	20-Apr-19	Checking of Shuttering,Reinforcement & Concreting of Raft-M25	317+700	317+720	RHS	Toe Wall	Not Done	
290	VKE-3/PIL/STR/748	02:00PM	20-Apr-19	Checking of Layout and Excavation of Toe Wall	311+720	311+750	RHS	Toe Wall	Done	
291	VKE-3/PIL/STR/749	05:00PM	20-Apr-19	Checking of Ground Improvement	311+720	311+750	RHS	Toe Wall	Done	
292	VKE-3/PIL/STR/750	03:00PM	20-Apr-19	Checking of PCC Laying of Toe Wall	311+720	311+750	RHS	Toe Wall	Done	
293	VKE-3/PIL/STR/751	01:00PM	20-Apr-19	Joint Verification of Utility Location	292+000	323+000			Done	
294	VKE-3/PIL/STR/752	08:00AM	21-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.30	Done	
295	VKE-3/PIL/STR/753	08:45AM	21-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.30	Done	
296	VKE-3/PIL/STR/754	02:00PM	21-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.39	Done	
297	VKE-3/PIL/STR/755	03:00PM	21-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.39	Done	
298	VKE-3/PIL/STR/756	07:00PM	21-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P1 RHS-Pile No.42	Done	
299	VKE-3/PIL/STR/757	08:00PM	21-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P1 RHS-Pile No.42	Done	
300	VKE-3/PIL/STR/758	05:00PM	21-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P1 RHS-Pile No.49	Done	
301	VKE-3/PIL/STR/759	06:00PM	21-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P1 RHS-Pile No.49	Done	
302	VKE-3/PIL/STR/760	05:00PM	21-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A1 LHS-Pile No.07	Not Done	
303	VKE-3/PIL/STR/761	06:00PM	21-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A1 LHS-Pile No.07	Not Done	
304	VKE-3/PIL/STR/762	03:00PM	21-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A1 RHS-Pile No.17	Not Done	
305	VKE-3/PIL/STR/763	04:00PM	21-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A1 RHS-Pile No.17	Not Done	
306	VKE-3/PIL/STR/764	08:00AM	21-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A1 RHS-Pile No.23	Not Done	
307	VKE-3/PIL/STR/765	08:45AM	21-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A1 RHS-Pile No.23	Not Done	
308	VKE-3/PIL/STR/766	02:00PM	21-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A2 RHS-Pile No.38	Not Done	
309	VKE-3/PIL/STR/767	03:00PM	21-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A2 RHS-Pile No.38	Not Done	
310	VKE-3/PIL/STR/768	06:00PM	21-Apr-19	Checking of Vertical Dynamic Routine Load Test on Pile No.40 -A1	321+253		LHS	P1 LHS-Pile No.40	Done	
311	VKE-3/PIL/STR/769	06:00PM	21-Apr-19	Checking of Vertical Dynamic Routine Load Test on Pile No.45 -A1	321+253		LHS	P1 LHS-Pile No.45	Done	
312	VKE-3/PIL/STR/770	06:00PM	21-Apr-19	Checking of bore depth for Pile along with Reinforcement	321+253		RHS	A2 RHS-Pile No.109	Done	
313	VKE-3/PIL/STR/771	06:00PM	21-Apr-19	Pouring of M35 grade of Concrete for Pile Work	321+253		RHS	A2 RHS-Pile No.109	Done	
314	VKE-3/PIL/STR/772	04:00PM	21-Apr-19	Checking of PCC for Pile Cap	321+253		LHS	P1-LHS	Done	
315	VKE-3/PIL/STR/773	04:00PM	21-Apr-19	Checking of Shuttering,Reinforcement & Concreting of Raft-M25	317+700	317+720	RHS	Toe Wall	Done	
316	VKE-3/PIL/STR/774	01:00PM	21-Apr-19	Joint Factory Visit for NP4 1200mm and 600mm				At Sidhvi Vinayak Ppie Industries	Not Done	
317	VKE-3/PIL/STR/775	08:00AM	22-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.33	Done	
318	VKE-3/PIL/STR/776	08:45AM	22-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.33	Done	
319	VKE-3/PIL/STR/777	02:00PM	22-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.36	Not Done	
320	VKE-3/PIL/STR/778	03:00PM	22-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.36	Not Done	
321	VKE-3/PIL/STR/779	07:00PM	22-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P1 RHS-Pile No.42	Not Done	
322	VKE-3/PIL/STR/780	08:00PM	22-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P1 RHS-Pile No.42	Not Done	
323	VKE-3/PIL/STR/781	05:00PM	22-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P1 RHS-Pile No.49	Done	
324	VKE-3/PIL/STR/782	06:00PM	22-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P1 RHS-Pile No.49	Done	
325	VKE-3/PIL/STR/783	05:00PM	22-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A1 LHS-Pile No.07	Done	
326	VKE-3/PIL/STR/784	06:00PM	22-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A1 LHS-Pile No.07	Done	
327	VKE-3/PIL/STR/785	03:00PM	22-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A1 RHS-Pile No.17	Done	
328	VKE-3/PIL/STR/786	04:00PM	22-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A1 RHS-Pile No.17	Done	
329	VKE-3/PIL/STR/787	08:00AM	22-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A1 RHS-Pile No.23	Done	
330	VKE-3/PIL/STR/788	08:45AM	22-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A1 RHS-Pile No.23	Done	
331	VKE-3/PIL/STR/789	02:00PM	22-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A2 RHS-Pile No.38	Done	
332	VKE-3/PIL/STR/790	03:00PM	22-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A2 RHS-Pile No.38	Done	
333	VKE-3/PIL/STR/791	05:00PM	22-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A2 RHS-Pile No.36	Done	
334	VKE-3/PIL/STR/792	06:00PM	22-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A2 RHS-Pile No.36	Done	
335	VKE-3/PIL/STR/793	10:00AM	22-Apr-19	Checking of SBC	297+900		RHS	PUP	Done	
336	VKE-3/PIL/STR/794	11:00AM	22-Apr-19	Checking of PCC Laying	297+900		RHS	PUP	Done	
337	VKE-3/PIL/STR/795	10:00AM	22-Apr-19	Checking of OGL	297+900		BHS	PUP	Done	
338	VKE-3/PIL/STR/796	11:00AM	22-Apr-19	Checking of OGL and Layout	300+148		BHS	Box Culvert	Done	
339	VKE-3/PIL/STR/797	12:00PM	22-Apr-19	Checking of Excavation	300+148		BHS	Box Culvert	Done	
340	VKE-3/PIL/STR/798	05:00PM	22-Apr-19	Checking of Shuttering,Reinforcement & Concreting of Haunch	303+403		RHS	Box Culvert	Done	

Sr. NO.	RFI NO.	Inspection Time	Inspection date	Item Description	Chainage		Side	Remarks	Status	Witness By IE
					From	To				
341	VKE-3/PIL/STR/799	11:00AM	22-Apr-19	Checking of Level and Excavation of PUP	309+550		RHS	PUP	Not Done	
342	VKE-3/PIL/STR/800	08:00AM	23-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.38	Done	
343	VKE-3/PIL/STR/801	08:45AM	23-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.38	Done	
344	VKE-3/PIL/STR/802	02:00PM	23-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.36	Done	
345	VKE-3/PIL/STR/803	03:00PM	23-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.36	Done	
346	VKE-3/PIL/STR/804	07:00PM	23-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P1 RHS-Pile No.42	Done	
347	VKE-3/PIL/STR/805	08:00PM	23-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P1 RHS-Pile No.42	Done	
348	VKE-3/PIL/STR/806	05:00PM	23-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P1 RHS-Pile No.43	Done	
349	VKE-3/PIL/STR/807	06:00PM	23-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P1 RHS-Pile No.43	Done	
350	VKE-3/PIL/STR/808	04:00PM	23-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P1 RHS-Pile No.47	Done	
351	VKE-3/PIL/STR/809	05:00PM	23-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P1 RHS-Pile No.47	Done	
352	VKE-3/PIL/STR/810	05:00PM	23-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A1 LHS-Pile No.05	Done	
353	VKE-3/PIL/STR/811	06:00PM	23-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A1 LHS-Pile No.05	Done	
354	VKE-3/PIL/STR/812	03:00PM	23-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A1 RHS-Pile No.21	Not Done	
355	VKE-3/PIL/STR/813	04:00PM	23-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A1 RHS-Pile No.21	Not Done	
356	VKE-3/PIL/STR/814	08:00AM	23-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A1 RHS-Pile No.15	Not Done	
357	VKE-3/PIL/STR/815	08:45AM	23-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A1 RHS-Pile No.15	Not Done	
358	VKE-3/PIL/STR/816	02:00PM	23-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A2 RHS-Pile No.34	Not Done	
359	VKE-3/PIL/STR/817	03:00PM	23-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A2 RHS-Pile No.34	Not Done	
360	VKE-3/PIL/STR/818	06:00PM	23-Apr-19	Checking of bore depth for Pile along with Reinforcement	321+253		RHS	A2 RHS-Pile No.106	Done	
361	VKE-3/PIL/STR/819	06:00PM	23-Apr-19	Pouring of M35 grade of Concrete for Pile Work	321+253		RHS	A2 RHS-Pile No.106	Done	
362	VKE-3/PIL/STR/820	05:00PM	23-Apr-19	Checking of Shuttering,Reinforcement & Concreting of Toe Wall 1st Lift	311+680	311+700	RHS	Toe Wall	Done	
363	VKE-3/PIL/STR/821	11:00AM	23-Apr-19	Checking of Level and Excavation of PUP	309+550		RHS	PUP	Not Done	
364	VKE-3/PIL/STR/822	05:00PM	23-Apr-19	Checking for Surface Bearing Capacity	298+380		BHS		Done	
365	VKE-3/PIL/STR/823	08:30AM	23-Apr-19	Removal of Earth Filling	309+550		RHS	PUP	Done	Yes
366	VKE-3/PIL/STR/824	09:00AM	23-Apr-19	Removal of Earth Filling	305+058		LHS		Done	
367	VKE-3/PIL/STR/825	10:00AM	23-Apr-19	Laying of PCC	297+900		RHS		Not Done	
368	VKE-3/PIL/STR/826	09:00AM	23-Apr-19	GSB 1st Layer Filling for Ground Improvement and Level Checking	309+550		RHS		Done	Yes
369	VKE-3/PIL/STR/827	11:00AM	23-Apr-19	GSB 2nd Layer Filling for Ground Improvement and Level Checking	309+550		RHS	PUP	Not Done	
370	VKE-3/PIL/STR/828	02:00PM	23-Apr-19	GSB 3rd Layer Filling for Ground Improvement and Level Checking	309+550		RHS		Not Done	
371	VKE-3/PIL/STR/829	04:00PM	23-Apr-19	GSB 4th Layer Filling for Ground Improvement and Level Checking	309+550		RHS		Not Done	
372	VKE-3/PIL/STR/830	11:00 AM	24-Apr-19	Checking of Reinforcement and Shuttering of Pile Cap A1	321+253		LHS	MJB		
373	VKE-3/PIL/STR/831	2:00 PM	24-Apr-19	OGI Checking	322+450	322+510	LHS		Done	
374	VKE-3/PIL/STR/832	2:00 PM	24-Apr-19	Checking of Level and Excavation of PCC	322+450	322+510	LHS	Retaining Wall	Done	
375	VKE-3/PIL/STR/833	10:00 AM	24-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A1 LHS-Pile No.03	Done	
376	VKE-3/PIL/STR/834	10:30 AM	24-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A1 LHS-Pile No.03	Done	
377	VKE-3/PIL/STR/835	11:30 AM	24-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A1 RHS-Pile No.21	Done	
378	VKE-3/PIL/STR/836	12:00 PM	24-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A1 RHS-Pile No.21	Done	
379	VKE-3/PIL/STR/837	1:00 PM	24-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A1 RHS-Pile No.15	Done	
380	VKE-3/PIL/STR/838	1:30 PM	24-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A1 RHS-Pile No.15	Done	
381	VKE-3/PIL/STR/839	2:30 PM	24-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A2 LHS-Pile No.34	Done	
382	VKE-3/PIL/STR/840	3:00 PM	24-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A2 LHS-Pile No.34	Done	
383	VKE-3/PIL/STR/841	4:00 PM	24-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A2 RHS-Pile No.44	Done	
384	VKE-3/PIL/STR/842	4:30 PM	24-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A2 RHS-Pile No.44	Done	
385	VKE-3/PIL/STR/843	11:00 AM	24-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.29	Done	
386	VKE-3/PIL/STR/844	11:30 AM	24-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.29	Done	
387	VKE-3/PIL/STR/845	1:00 PM	24-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.35	Done	
388	VKE-3/PIL/STR/846	1:30 PM	24-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.35	Done	
389	VKE-3/PIL/STR/847	2:30 PM	24-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.39	Done	
390	VKE-3/PIL/STR/848	3:00 PM	24-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.39	Done	
391	VKE-3/PIL/STR/849	8:00 AM	24-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P1 RHS-Pile No.52	Done	
392	VKE-3/PIL/STR/850	9:00 AM	24-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P1 RHS-Pile No.52	Done	
393	VKE-3/PIL/STR/851	10:00 AM	24-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.15	Not Done	
394	VKE-3/PIL/STR/852	12:00 AM	24-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.15	Not Done	
395	VKE-3/PIL/STR/853	8:30 AM	24-Apr-19	OGI and Layout checking of HPC	309+368		BHS		Done	
396	VKE-3/PIL/STR/854	9:00 AM	24-Apr-19	Excavation for HPC	309+368		BHS	HPC	Done	
397	VKE-3/PIL/STR/855	8:45 AM	24-Apr-19	OGI and Layout checking of HPC	308+794		BHS		Done	
398	VKE-3/PIL/STR/856	11:00 AM	24-Apr-19	Excavation for HPC	308+794		BHS		Done	
399	VKE-3/PIL/STR/857	5:00 PM	24-Apr-19	Removal of Earth Filling material and level checking	309+550		LHS	PUP	Not Done	
400	VKE-3/PIL/STR/858	4:00 PM	24-Apr-19	PCC Laying for Toe Wall	311+720	311+750	RHS	Toe Wall	Done	
401	VKE-3/PIL/STR/859	10:00 AM	24-Apr-19	2nd Layer of Sand Filling for Ground Improvement	309+550		RHS		Done	Yes
402	VKE-3/PIL/STR/860	2:00 PM	24-Apr-19	3rd Layer of Sand Filling for Ground Improvement	309+550		RHS	PUP	Done	Yes
403	VKE-3/PIL/STR/861	5:00 PM	24-Apr-19	4th Layer of Sand Filling for Ground Improvement	309+550		RHS		Not Done	
404	VKE-3/PIL/STR/862	10:00 AM	24-Apr-19	Laying of PCC	297+900		RHS		Done	
405	VKE-3/PIL/STR/863	11:00 AM	24-Apr-19	Checking of Safe Bearing Capacity	298+380		RHS	PUP	Not Done	
406	VKE-3/PIL/STR/864	3:00 PM	24-Apr-19	Laying of PCC	298+380		RHS		Not Done	
407	VKE-3/PIL/STR/865	11:00 AM	24-Apr-19	OGI and Layout checking of HPC	302+578		BHS	HPC	Done	
408	VKE-3/PIL/STR/866	11:00 AM	24-Apr-19	Excavation for HPC	302+578		BHS		Done	
409	VKE-3/PIL/STR/867	12:00 PM	24-Apr-19	Level checking after removal of Backfill Material	305+058		LHS	PUP	Done	Yes
410	VKE-3/PIL/STR/868	4:00 PM	24-Apr-19	Checking of Bed Level after Ground Improvement and Laying of PCC	300+148		BHS	BC	Done	
411	VKE-3/PIL/STR/869	9:00 AM	25-Apr-19	Checking of Reinforcement,Formwork and Concreting 1st lift	305+437		LHS		Done	
412	VKE-3/PIL/STR/870	9:00 AM	25-Apr-19	Checking of OGL and layout checking	305+437		RHS	BC	Done	
413	VKE-3/PIL/STR/871	9:00 AM	25-Apr-19	Excavation of Box Culvert	305+437		RHS		Done	
414	VKE-3/PIL/STR/872	10:00 AM	25-Apr-19	Checking of Reinforcement,Formwork and Concreting 2nd lift	305+437		LHS		Done	
415	VKE-3/PIL/STR/873	11:30 AM	25-Apr-19	Removal of PCC	309+550		LHS		Done	Yes
416	VKE-3/PIL/STR/874	11:00 AM	25-Apr-19	4th layer filling for Ground Improvement	309+550		LHS		Done	Yes
417	VKE-3/PIL/STR/875	3:00 PM	25-Apr-19	Checking of Safe Bearing Capacity	298+380		RHS	PUP	Done	
418	VKE-3/PIL/STR/876	4:00 PM	25-Apr-19	Laying of PCC	298+380		RHS		Done	
419	VKE-3/PIL/STR/877	11:00 AM	25-Apr-19	1st layer filling for Ground Improvement	305+058		LHS		Done	
420	VKE-3/PIL/STR/878	11:30 AM	25-Apr-19	Laying of PCC	300+148		BHS	BC	Not Done	
421	VKE-3/PIL/STR/879	3:00 PM	25-Apr-19	Checking of Reinforcement and Shuttering of Pile Cap A1	321+253		LHS		Not Done	
422	VKE-3/PIL/STR/880	3:00 PM	25-Apr-19	Lateral Load test on routine pile no. 28	321+253		LHS	MJB	Done	
423	VKE-3/PIL/STR/881	10:00 AM	25-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	A1 LHS-Pile No.15	Done	
424	VKE-3/PIL/STR/882	10:30 AM	25-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	A1 LHS-Pile No.15	Done	
425	VKE-3/PIL/STR/883	11:30 AM	25-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	A1 LHS-Pile No.17	Not Done	

Sr. NO.	RFI NO.	Inspection Time	Inspection date	Item Description	Chainage		Side	Remarks	Status	Witness By IE
					From	To				
426	VKE-3/PIL/STR/884	12:00 PM	25-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	A1 LHS-Pile No.17	Not Done	
427	VKE-3/PIL/STR/885	1:00 PM	25-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	A1 LHS-Pile No.23	Done	
428	VKE-3/PIL/STR/886	1:30 PM	25-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	A1 LHS-Pile No.23	Done	
429	VKE-3/PIL/STR/887	2:30 PM	25-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.9	Done	
430	VKE-3/PIL/STR/888	3:00 PM	25-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.9	Done	
431	VKE-3/PIL/STR/889	4:00 PM	25-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P2 LHS-Pile No.53	Done	
432	VKE-3/PIL/STR/890	4:30 PM	25-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P2 LHS-Pile No.53	Done	
433	VKE-3/PIL/STR/891	5:00 PM	25-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P2 RHS-Pile No.62	Done	
434	VKE-3/PIL/STR/892	5:30 PM	25-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P2 RHS-Pile No.62	Done	
435	VKE-3/PIL/STR/893	11:30 AM	25-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A1 LHS-Pile No.01	Done	
436	VKE-3/PIL/STR/894	12:00 PM	25-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A1 LHS-Pile No.01	Done	
437	VKE-3/PIL/STR/895	1:00 PM	25-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A1 RHS-Pile No.21	Not Done	
438	VKE-3/PIL/STR/896	1:30 PM	25-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A1 RHS-Pile No.21	Not Done	
439	VKE-3/PIL/STR/897	2:30 PM	25-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A2 LHS-Pile No.32	Done	
440	VKE-3/PIL/STR/898	3:00 PM	25-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A2 LHS-Pile No.32	Done	
441	VKE-3/PIL/STR/899	4:00 PM	25-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A2 RHS-Pile No.46	Done	
442	VKE-3/PIL/STR/900	4:30 PM	25-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A2 RHS-Pile No.46	Done	
443	VKE-3/PIL/STR/901	10:00 AM	25-Apr-19	Checking of Ground Improvement	309+368		BHS	HPC	Done	
444	VKE-3/PIL/STR/902	11:00 AM	25-Apr-19	Checking of Ground Improvement	308+794		BHS	HPC	Done	
445	VKE-3/PIL/STR/903	12:30 PM	25-Apr-19	Checking of Sand Filling for Ground Improvement 4th layer	309+550		RHS	PUP	Done	
446	VKE-3/PIL/STR/904	1:00 PM	25-Apr-19	Bottom level PCC checking	309+550		RHS	PUP	Done	
447	VKE-3/PIL/STR/905	8:30 AM	26-Apr-19	Checking of Reinforcement,Formwork and Concreting for Haunch	304+170		RHS	PUP	Done	
448	VKE-3/PIL/STR/906	8:30 AM	26-Apr-19	Checking of Reinforcement,Formwork and Concreting for Haunch	304+170		LHS	PUP	Done	
449	VKE-3/PIL/STR/907	11:00 AM	26-Apr-19	Checking of Safe Bearing Capacity	298+380		RHS	PUP	Done	
450	VKE-3/PIL/STR/908	12:00 PM	26-Apr-19	Laying of PCC	298+380		RHS	PUP	Done	
451	VKE-3/PIL/STR/909	9:00 AM	26-Apr-19	Checking of Ground Improvement	300+148		RHS	BC	Done	
452	VKE-3/PIL/STR/910	9:00 AM	26-Apr-19	Checking of Ground Improvement	300+148		LHS	BC	Done	
453	VKE-3/PIL/STR/911	11:00 AM	26-Apr-19	Laying of PCC	300+148		RHS	BC	Done	
454	VKE-3/PIL/STR/912	11:00 AM	26-Apr-19	Laying of PCC	300+148		LHS	BC	Done	
455	VKE-3/PIL/STR/913	2:00 PM	26-Apr-19	2nd Layer of Sand Filling for Ground Improvement	305+058		LHS	PUP	Not Done	
456	VKE-3/PIL/STR/914	3:00 PM	26-Apr-19	3rd Layer of Sand Filling for Ground Improvement	305+058		LHS	PUP	Not Done	
457	VKE-3/PIL/STR/915	4:00 PM	26-Apr-19	4th Layer of Sand Filling for Ground Improvement	305+058		LHS	PUP	Not Done	
458	VKE-3/PIL/STR/916	9:00 AM	26-Apr-19	Checking of PCC for Retaining Wall A1	305+437		RHS	BC	Done	
459	VKE-3/PIL/STR/917	10:00 AM	26-Apr-19	Checking of PCC for Retaining Wall A2	305+437		RHS	BC	Done	
460	VKE-3/PIL/STR/918	3:00 PM	26-Apr-19	Checking of Reinforcement and Shuttering of Pile Cap A1	321+253		LHS	MJB	Done	
461	VKE-3/PIL/STR/919	3:00 PM	26-Apr-19	Lateral Loat test on routine pile no. 46 P1	321+253		LHS	MJB	Done	
462	VKE-3/PIL/STR/920	12:30 PM	26-Apr-19	Laying of PCC	309+550		RHS	PUP	Done	Yes
463	VKE-3/PIL/STR/921	1:00 PM	26-Apr-19	Removal of Earth Filling material and Level Checking	309+550		LHS	PUP	Done	Yes
464	VKE-3/PIL/STR/922	4:00 PM	26-Apr-19	1st Layer of Sand Filling for Ground Improvement	309+550		LHS	PUP	Not Done	
465	VKE-3/PIL/STR/923	11:00 AM	26-Apr-19	Laying of PCC	309+368		RHS	HPC	Done	
466	VKE-3/PIL/STR/924	10:00 AM	26-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	A1 LHS-Pile No.7 of MJB	Done	
467	VKE-3/PIL/STR/925	10:30 AM	26-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	A1 LHS-Pile No.7 of MJB	Done	
468	VKE-3/PIL/STR/926	11:30 AM	26-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.17 of MJB	Done	
469	VKE-3/PIL/STR/927	12:00 PM	26-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.17 of MJB	Done	
470	VKE-3/PIL/STR/928	1:00 PM	26-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.21 of MJB	Done	
471	VKE-3/PIL/STR/929	1:30 PM	26-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.21 of MJB	Done	
472	VKE-3/PIL/STR/930	2:30 PM	26-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	A1 RHS-Pile No.22 of MJB	Done	
473	VKE-3/PIL/STR/931	3:00 PM	26-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	A1 RHS-Pile No.22 of MJB	Done	
474	VKE-3/PIL/STR/932	9:00 AM	26-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A1 LHS-Pile No.14 of MNB	Not Done	
475	VKE-3/PIL/STR/933	9:30 AM	26-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A1 LHS-Pile No.14 of MNB	Not Done	
476	VKE-3/PIL/STR/934	10:00 AM	26-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A1 RHS-Pile No.21 of MNB	Done	
477	VKE-3/PIL/STR/935	10:30 AM	26-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A1 RHS-Pile No.21 of MNB	Done	
478	VKE-3/PIL/STR/936	11:30 AM	26-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A2 LHS-Pile No.30 of MNB	Not Done	
479	VKE-3/PIL/STR/937	12:00 PM	26-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A2 LHS-Pile No.30 of MNB	Not Done	
480	VKE-3/PIL/STR/938	1:00 PM	26-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A2 RHS-Pile No.48 of MNB	Not Done	
481	VKE-3/PIL/STR/939	1:30 PM	26-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A2 RHS-Pile No.48 of MNB	Not Done	
482	VKE-3/PIL/STR/940	9:00 AM	26-Apr-19	Checking of Layout	293+050			ROB	Not Done	
483	VKE-3/PIL/STR/941	5:00 PM	26-Apr-19	Checking of bore depth	293+050			ROB	Not Done	
484	VKE-3/PIL/STR/942	11:00 AM	26-Apr-19	Checking of Reinforcement	293+050			ROB	Not Done	
485	VKE-3/PIL/STR/943	5:30 PM	26-Apr-19	Test pile concreting	293+050			ROB	Not Done	
486	VKE-3/PIL/STR/944	5:00 PM	27-Apr-19	Checking of Safe Bearing Capacity	309+550		LHS	PUP	Done	
487	VKE-3/PIL/STR/945	9:00 AM	27-Apr-19	Checking of Layout	293+050		LHS	PUP	Done	
488	VKE-3/PIL/STR/946	5:00 PM	27-Apr-19	Checking of bore depth	293+050		LHS	ROB	Done	Yes
489	VKE-3/PIL/STR/947	11:00 AM	27-Apr-19	Checking of Reinforcement	293+050		LHS	ROB	Done	Yes
490	VKE-3/PIL/STR/948	5:30 PM	27-Apr-19	Test pile concreting	293+050		LHS	ROB	Done	
491	VKE-3/PIL/STR/949	11:00 AM	27-Apr-19	Checking of reinforcement and Shuttering of wall 1st lift	304+170		RHS	PUP	Not Done	
492	VKE-3/PIL/STR/950	3:00 PM	27-Apr-19	Checking of concrete wall 1st lift	304+170		RHS	PUP	Not Done	
493	VKE-3/PIL/STR/951	2:00 PM	27-Apr-19	1st Layer of Sand Filling for Ground Improvement	305+058		LHS	PUP	Done	
494	VKE-3/PIL/STR/952	2:00 PM	27-Apr-19	2nd Layer of Sand Filling for Ground Improvement	305+058		LHS	PUP	Not Done	
495	VKE-3/PIL/STR/953	3:00 PM	27-Apr-19	3rd Layer of Sand Filling for Ground Improvement	305+058		LHS	PUP	Not Done	
496	VKE-3/PIL/STR/954	4:00 PM	27-Apr-19	4th Layer of Sand Filling for Ground Improvement	305+058		LHS	PUP	Not Done	
497	VKE-3/PIL/STR/955	9:00 AM	27-Apr-19	Checking of PCC for Retaining Wall A1	305+437		RHS	BC	Done	
498	VKE-3/PIL/STR/956	10:00 AM	27-Apr-19	Checking of PCC for Retaining Wall A2	305+437		RHS	BC	Done	
499	VKE-3/PIL/STR/957	3:00 PM	27-Apr-19	Checking of Safe Bearing Capacity	322+450		RHS	MJB	Not Done	
500	VKE-3/PIL/STR/958	3:00 PM	27-Apr-19	Lateral Loat test on routine pile no. 46 P1	322+450		LHS	MJB	Done	
501	VKE-3/PIL/STR/959	3:00 PM	27-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A1 LHS-Pile No.14 of MNB	Done	
502	VKE-3/PIL/STR/960	3:30 PM	27-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A1 LHS-Pile No.14 of MNB	Done	
503	VKE-3/PIL/STR/961	4:00 PM	27-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A2 LHS-Pile No.30 of MNB	Not Done	
504	VKE-3/PIL/STR/962	4:30 PM	27-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A2 LHS-Pile No.30 of MNB	Not Done	
505	VKE-3/PIL/STR/963	5:00 PM	27-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A2 RHS-Pile No.48 of MNB	Not Done	
506	VKE-3/PIL/STR/964	5:30 PM	27-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A2 RHS-Pile No.48 of MNB	Not Done	
507	VKE-3/PIL/STR/965	3:00 PM	27-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P2 LHS-Pile No.55 of MJB	Done	
508	VKE-3/PIL/STR/966	3:30 PM	27-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P2 LHS-Pile No.55 of MJB	Done	
509	VKE-3/PIL/STR/967	4:00 PM	27-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P2 LHS-Pile No.59 of MJB	Done	
510	VKE-3/PIL/STR/968	4:30 PM	27-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P2 LHS-Pile No.59 of MJB	Done	

Sr. NO.	RFI NO.	Inspection Time	Inspection date	Item Description	Chainage		Side	Remarks	Status	Witness By IE
					From	To				
511	VKE-3/PIL/STR/969	5:00 PM	27-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P2 RHS-Pile No.63 of MJB	Done	
512	VKE-3/PIL/STR/970	5:30 PM	27-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P2 RHS-Pile No.63 of MJB	Done	
513	VKE-3/PIL/STR/971	4:00 PM	27-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P2 RHS-Pile No.68 of MJB	Done	
514	VKE-3/PIL/STR/972	4:30 PM	27-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P2 RHS-Pile No.68 of MJB	Done	
515	VKE-3/PIL/STR/973	11:00 AM	27-Apr-19	1st Layer of Sand Filling for Ground Improvement	309+550		LHS	PUP	Done	Yes
516	VKE-3/PIL/STR/974	4:00 PM	27-Apr-19	2nd Layer of Sand Filling for Ground Improvement	309+550		LHS		Not Done	
517	VKE-3/PIL/STR/975	10:00 AM	28-Apr-19	Checking of Safe Bearing Capacity	322+450		RHS	Retaining wall	Not Done	
518	VKE-3/PIL/STR/976	2:00 PM	28-Apr-19	2nd Layer of Sand Filling for Ground Improvement	305+058		LHS	PUP	Done	
519	VKE-3/PIL/STR/977	5:00 PM	28-Apr-19	3rd Layer of Sand Filling for Ground Improvement	305+058		LHS		Done	
520	VKE-3/PIL/STR/978	11:00 AM	28-Apr-19	Checking of reinforcement and Shuttering of wall 1st lift	304+170		RHS		Done	
521	VKE-3/PIL/STR/979	3:00 PM	28-Apr-19	Checking of concrete wall 1st lift	304+170		RHS	Done		
522	VKE-3/PIL/STR/980	3:00 PM	28-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A1 LHS-Pile No.12 of MNB	Done	
523	VKE-3/PIL/STR/981	3:30 PM	28-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A1 LHS-Pile No.12 of MNB	Done	
524	VKE-3/PIL/STR/982	4:00 PM	28-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A1 LHS-Pile No.10 of MNB	Not Done	
525	VKE-3/PIL/STR/983	4:30 PM	28-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A1 LHS-Pile No.10 of MNB	Not Done	
526	VKE-3/PIL/STR/984	5:00 PM	28-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A2 LHS-Pile No.30 of MNB	Done	
527	VKE-3/PIL/STR/985	5:30 PM	28-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A2 LHS-Pile No.30 of MNB	Done	
528	VKE-3/PIL/STR/986	3:00 PM	28-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A2 LHS-Pile No.29 of MNB	Done	
529	VKE-3/PIL/STR/987	3:30 PM	28-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A2 LHS-Pile No.29 of MNB	Done	
530	VKE-3/PIL/STR/988	4:00 PM	28-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A2 RHS-Pile No.48 of MNB	Done	
531	VKE-3/PIL/STR/989	4:30 PM	28-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A2 RHS-Pile No.48 of MNB	Done	
532	VKE-3/PIL/STR/990	5:00 PM	28-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A2 RHS-Pile No.50 of MNB	Done	
533	VKE-3/PIL/STR/991	5:30 PM	28-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A2 RHS-Pile No.50 of MNB	Done	
534	VKE-3/PIL/STR/992	4:00 PM	28-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P2 LHS-Pile No.56 of MJB	Not Done	
535	VKE-3/PIL/STR/993	4:30 PM	28-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P2 LHS-Pile No.56 of MJB	Not Done	
536	VKE-3/PIL/STR/994	5:00 PM	28-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P2 LHS-Pile No.60 of MJB	Done	
537	VKE-3/PIL/STR/995	5:30 PM	28-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P2 LHS-Pile No.60 of MJB	Done	
538	VKE-3/PIL/STR/996	3:00 PM	28-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P2 RHS-Pile No.61 of MJB	Done	
539	VKE-3/PIL/STR/997	3:30 PM	28-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P2 RHS-Pile No.61 of MJB	Done	
540	VKE-3/PIL/STR/998	4:00 PM	28-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.32 of MJB	Done	
541	VKE-3/PIL/STR/999	4:30 PM	28-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.32 of MJB	Done	
542	VKE-3/PIL/STR/1000	5:00 PM	28-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P1 RHS-Pile No.49 of MJB	Done	
543	VKE-3/PIL/STR/1001	5:30 PM	28-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P1 RHS-Pile No.49 of MJB	Done	
544	VKE-3/PIL/STR/1002	1:00 PM	28-Apr-19	2nd Layer of Sand Filling for Ground Improvement	309+550		LHS	PUP	Done	
545	VKE-3/PIL/STR/1003	9:00 AM	28-Apr-19	OGL and layout checking for HPC	310+119		LHS	HPC	Done	
546	VKE-3/PIL/STR/1004	9:00 AM	28-Apr-19	OGL and layout checking for HPC	310+119		RHS		Done	
547	VKE-3/PIL/STR/1005	5:00 PM	28-Apr-19	Excavation for HPC	310+119		LHS	HPC	Done	
548	VKE-3/PIL/STR/1006	5:00 PM	28-Apr-19	Excavation for HPC	310+119		RHS		Done	
549	VKE-3/PIL/STR/1007	3:00 PM	28-Apr-19	PCC Laying for HPC	309+368		RHS	HPC	Done	
550	VKE-3/PIL/STR/1008	9:00 AM	28-Apr-19	Pipe Laying, Leveling and joining	298+819		BHS	HPC	Done	
551	VKE-3/PIL/STR/1009	9:00 AM	28-Apr-19	Cradle concrete	298+819		BHS		Done	
552	VKE-3/PIL/STR/1010	10:30 AM	29-Apr-19	Checking of Safe Bearing Capacity	322+450		LHS	Retaining wall	Done	
553	VKE-3/PIL/STR/1011	10:30 AM	29-Apr-19	Lateral Load test on routine pile in abutment and Pier portion	321+253		LHS	PUP	Done	Yes
554	VKE-3/PIL/STR/1012	5:00 PM	29-Apr-19	4th Layer of Sand Filling for Ground Improvement	305+058		LHS		Not Done	Yes
555	VKE-3/PIL/STR/1013	9:00 AM	29-Apr-19	3rd Layer of Sand Filling for Ground Improvement	309+550		LHS		Done	
556	VKE-3/PIL/STR/1014	5:00 PM	29-Apr-19	4th Layer of Sand Filling for Ground Improvement	309+550		LHS	PUP	Not Done	
557	VKE-3/PIL/STR/1015	4:30 PM	29-Apr-19	Checking of reinforcement and Shuttering of toe wall	311+720	311+740	RHS		toe wall	Done
558	VKE-3/PIL/STR/1016	4:30 PM	29-Apr-19	Pouring of M25 grade of Concrete for toe wall raft	311+720	311+740	RHS	HPC	Done	
559	VKE-3/PIL/STR/1017	2:00 PM	29-Apr-19	Sand Filling for Ground Improvement	310+119		LHS		Done	
560	VKE-3/PIL/STR/1018	2:15 PM	29-Apr-19	Sand Filling for Ground Improvement	310+119		RHS		Done	
561	VKE-3/PIL/STR/1019	4:00 PM	29-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A1 LHS-Pile No.10 of MNB	Done	
562	VKE-3/PIL/STR/1020	4:30 PM	29-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A1 LHS-Pile No.10 of MNB	Done	
563	VKE-3/PIL/STR/1021	5:00 PM	29-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A2 LHS-Pile No.41 of MNB	Done	
564	VKE-3/PIL/STR/1022	5:30 PM	29-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A2 LHS-Pile No.41 of MNB	Done	
565	VKE-3/PIL/STR/1023	3:00 PM	29-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A2 RHS-Pile No.50 of MNB	Done	
566	VKE-3/PIL/STR/1024	3:30 PM	29-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A2 RHS-Pile No.50 of MNB	Done	
567	VKE-3/PIL/STR/1025	4:00 PM	29-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A1 RHS-Pile No.16 of MNB	Done	
568	VKE-3/PIL/STR/1026	4:30 PM	29-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A1 RHS-Pile No.16 of MNB	Done	
569	VKE-3/PIL/STR/1027	5:00 PM	29-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A1 RHS-Pile No.28 of MNB	Done	
570	VKE-3/PIL/STR/1028	5:30 PM	29-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A1 RHS-Pile No.28 of MNB	Not Done	Yes
571	VKE-3/PIL/STR/1029	4:00 PM	29-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P2 LHS-Pile No.56 of MJB	Done	
572	VKE-3/PIL/STR/1030	4:30 PM	29-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P2 LHS-Pile No.56 of MJB	Done	
573	VKE-3/PIL/STR/1031	5:00 PM	29-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P2 LHS-Pile No.59 of MJB	Done	
574	VKE-3/PIL/STR/1032	5:30 PM	29-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P2 LHS-Pile No.59 of MJB	Done	
575	VKE-3/PIL/STR/1033	3:00 PM	29-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P2 RHS-Pile No.68 of MJB	Done	
576	VKE-3/PIL/STR/1034	3:30 PM	29-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P2 RHS-Pile No.68 of MJB	Done	
577	VKE-3/PIL/STR/1035	4:00 PM	29-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P1 LHS-Pile No.38 of MJB	Done	
578	VKE-3/PIL/STR/1036	4:30 PM	29-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P1 LHS-Pile No.38 of MJB	Done	
579	VKE-3/PIL/STR/1037	5:00 PM	29-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P1 RHS-Pile No.45 of MJB	Done	
580	VKE-3/PIL/STR/1038	5:30 PM	29-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P1 RHS-Pile No.45 of MJB	Done	
581	VKE-3/PIL/STR/1039	9:00 AM	30-Apr-19	Sand Filling for Ground Improvement	300+148		LHS	BC	Not Done	Yes
582	VKE-3/PIL/STR/1040	9:00 AM	30-Apr-19	Sand Filling for Ground Improvement	300+148		RHS		Not Done	Yes
583	VKE-3/PIL/STR/1041	4:00 PM	30-Apr-19	Laying of PCC	300+148		LHS		Not Done	
584	VKE-3/PIL/STR/1042	4:00 PM	30-Apr-19	Laying of PCC	300+148		RHS	HPC	Not Done	
585	VKE-3/PIL/STR/1043	3:00 PM	30-Apr-19	Laying of Pipe, Leveling and Jointing	298+120		LHS		Done	
586	VKE-3/PIL/STR/1044	3:00 PM	30-Apr-19	Laying of Pipe, Leveling and Jointing	298+120		RHS	Done		
587	VKE-3/PIL/STR/1045	3:00 PM	30-Apr-19	Checking of concrete wall 1st lift	304+170		RHS	PUP	Done	
588	VKE-3/PIL/STR/1046	3:00 PM	30-Apr-19	Checking of shuttering & reinforcement of retaining raft wall A1	305+437		RHS	BC	Done	
589	VKE-3/PIL/STR/1047	3:00 PM	30-Apr-19	Checking of shuttering & reinforcement of retaining raft wall A2	305+437		RHS		Done	
590	VKE-3/PIL/STR/1048	3:00 PM	30-Apr-19	Pouring of M30 grade of Concrete for retaining raft wall A1	305+437		RHS		Not Done	
591	VKE-3/PIL/STR/1049	3:00 PM	30-Apr-19	Pouring of M30 grade of Concrete for retaining raft wall A2	305+437		RHS	Not Done		
592	VKE-3/PIL/STR/1050	3:30 PM	30-Apr-19	Removal of PCC	305+058		RHS	PUP	Done	
593	VKE-3/PIL/STR/1051	3:30 PM	30-Apr-19	Removal of thick earthfill	305+058		RHS		Done	
594	VKE-3/PIL/STR/1052	9:00 AM	30-Apr-19	Checking of bore depth for Pile along with Reinforcement	293+050		LHS	A1 LHS-Pile No.1	Done	
595	VKE-3/PIL/STR/1053	9:30 AM	30-Apr-19	Pouring of M35 grade of Concrete for Pile Work	293+050		LHS	A1 LHS-Pile No.1	Done	

Sr. NO.	RFI NO.	Inspection Time	Inspection date	Item Description	Chainage		Side	Remarks	Status	Witness By IE
					From	To				
596	VKE-3/PIL/STR/1054	10:00 AM	30-Apr-19	Checking of bore depth for Pile along with Reinforcement	293+050		LHS	A1 LHS-Pile No.2	Done	
597	VKE-3/PIL/STR/1055	10:30 AM	30-Apr-19	Pouring of M35 grade of Concrete for Pile Work	293+050		LHS	A1 LHS-Pile No.2	Done	
598	VKE-3/PIL/STR/1056	11:00 AM	30-Apr-19	Checking of bore depth for Pile along with Reinforcement	293+050		LHS	A1 LHS-Pile No.7	Done	
599	VKE-3/PIL/STR/1057	11:30 AM	30-Apr-19	Pouring of M35 grade of Concrete for Pile Work	293+050		LHS	A1 LHS-Pile No.7	Done	
600	VKE-3/PIL/STR/1058	12:00 PM	30-Apr-19	OGL & Layout checking	322+778		BHS	HPC	Done	
601	VKE-3/PIL/STR/1059	12:30 PM	30-Apr-19	Excavation of HPC	322+778		BHS		Done	
602	VKE-3/PIL/STR/1060	2:00 PM	30-Apr-19	OGL & Layout checking	322+750		BHS	HPC	Done	
603	VKE-3/PIL/STR/1061	2:30 PM	30-Apr-19	Excavation of HPC	322+750		BHS		Done	
604	VKE-3/PIL/STR/1062	11:00 AM	30-Apr-19	Laying of PCC	322+450	322+470	LHS	Retaining Wall	Done	
605	VKE-3/PIL/STR/1063	4:00 PM	30-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P2 LHS-Pile No.53 of MJB	Not Done	
606	VKE-3/PIL/STR/1064	4:30 PM	30-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P2 LHS-Pile No.53 of MJB	Not Done	
607	VKE-3/PIL/STR/1065	5:00 PM	30-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P2 LHS-Pile No.59 of MJB	Done	
608	VKE-3/PIL/STR/1066	5:30 PM	30-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P2 LHS-Pile No.59 of MJB	Done	
609	VKE-3/PIL/STR/1067	3:00 PM	30-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		LHS	P2 LHS-Pile No.57 of MJB	Done	
610	VKE-3/PIL/STR/1068	3:30 PM	30-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		LHS	P2 LHS-Pile No.57 of MJB	Done	
611	VKE-3/PIL/STR/1069	4:00 PM	30-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P2 RHS-Pile No.66 of MJB	Done	
612	VKE-3/PIL/STR/1070	4:30 PM	30-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P2 RHS-Pile No.66 of MJB	Done	
613	VKE-3/PIL/STR/1071	5:00 PM	30-Apr-19	Checking of bore depth for Pile along with Reinforcement	302+713		RHS	P1 RHS-Pile No.48 of MJB	Done	
614	VKE-3/PIL/STR/1072	5:30 PM	30-Apr-19	Pouring of M35 grade of Concrete for Pile Work	302+713		RHS	P1 RHS-Pile No.48 of MJB	Done	
615	VKE-3/PIL/STR/1073	4:00 PM	30-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A1 LHS-Pile No.8 of MNB	Done	
616	VKE-3/PIL/STR/1074	4:30 PM	30-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A1 LHS-Pile No.8 of MNB	Done	
617	VKE-3/PIL/STR/1075	5:00 PM	30-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		LHS	A2 LHS-Pile No.39 of MNB	Done	
618	VKE-3/PIL/STR/1076	5:30 PM	30-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		LHS	A2 LHS-Pile No.39 of MNB	Done	
619	VKE-3/PIL/STR/1077	3:00 PM	30-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A2 RHS-Pile No.52 of MNB	Done	
620	VKE-3/PIL/STR/1078	3:30 PM	30-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A2 RHS-Pile No.52 of MNB	Done	
621	VKE-3/PIL/STR/1079	4:00 PM	30-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A1 RHS-Pile No.18 of MNB	Not Done	
622	VKE-3/PIL/STR/1080	4:30 PM	30-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A1 RHS-Pile No.18 of MNB	Not Done	
623	VKE-3/PIL/STR/1081	5:00 PM	30-Apr-19	Checking of bore depth for Pile along with Reinforcement	307+733		RHS	A1 RHS-Pile No.26 of MNB	Done	
624	VKE-3/PIL/STR/1082	5:30 PM	30-Apr-19	Pouring of M35 grade of Concrete for Pile Work	307+733		RHS	A1 RHS-Pile No.26 of MNB	Done	
625	VKE-3/PIL/STR/1083	9:00 AM	30-Apr-19	Checking of reinforcement and Shuttering	314+148		LHS	BC	Done	
626	VKE-3/PIL/STR/1084	9:30 AM	30-Apr-19	Pouring of M35 grade of Concrete for BC 2nd lift	314+148		LHS		Done	
627	VKE-3/PIL/STR/1085	8:30 AM	30-Apr-19	4th Layer of Sand Filling and Level checking for Ground Improvement	309+550		LHS	PUP	Not Done	
628	VKE-3/PIL/STR/1086	4:00 PM	30-Apr-19	Laying of PCC	309+550		LHS		Not Done	
629	VKE-3/PIL/STR/1087	11:00 AM	30-Apr-19	Checking of reinforcement and Shuttering of toe wall	311+720	311+750	RHS	Toe Wall	Done	
630	VKE-3/PIL/STR/1088	11:00 AM	30-Apr-19	Pouring of M25 grade of Concrete for toe wall raft	311+720	311+750	RHS		Done	
631	VKE-3/PIL/STR/1089	12:00 PM	30-Apr-19	Laying of PCC	309+368		BHS	HPC	Done	
632	VKE-3/PIL/STR/1090	10:00 AM	30-Apr-19	Checking of reinforcement and Shuttering	314+148		RHS	BC	Done	
633	VKE-3/PIL/STR/1091	10:30 AM	30-Apr-19	Pouring of M35 grade of Concrete for Bottom haunch	314+148		RHS		Done	

Sr. No.	RFI No	RFI Submission date	Item Head	Description of Item	Side	Chainage		Length (M)	Inspection		Status	Witness By IE
						From	To		Date	Time		
320	VKE-3/PIL/HW/320	31-Mar-19	Emb	FDD Checking of Embankment 9th Layer	LHS	303+020	303+500	480	1-Apr-19	08:30AM	Done	
321	VKE-3/PIL/HW/321	31-Mar-19	Emb	FDD Checking of Embankment 9th Layer	LHS	303+500	303+800	300	1-Apr-19	09:00AM	Done	
322	VKE-3/PIL/HW/322	31-Mar-19	Emb	FDD Checking of Embankment 8th Layer	LHS	303+820	304+000	180	1-Apr-19	10:00AM	Done	
323	VKE-3/PIL/HW/323	31-Mar-19	Emb	FDD Checking of Embankment 6th Layer	LHS	298+020	298+800	780	1-Apr-19	11:00AM	Done	
324	VKE-3/PIL/HW/324	31-Mar-19	Emb	FDD Checking of Embankment 5th Layer	LHS	298+800	299+000	200	1-Apr-19	12:00PM	Done	
325	VKE-3/PIL/HW/325	31-Mar-19	Emb	FDD Checking of Embankment 2nd Layer	LHS	300+200	300+750	550	1-Apr-19	02:00PM	Done	
326	VKE-3/PIL/HW/326	31-Mar-19	Emb	FDD Checking of Embankment 6th Layer	LHS	304+000	304+160	160	1-Apr-19	03:00PM	Done	
327	VKE-3/PIL/HW/327	31-Mar-19	Emb	FDD Checking of Embankment 6th Layer	LHS	304+200	304+420	220	1-Apr-19	04:00PM	Done	
328	VKE-3/PIL/HW/328	31-Mar-19	Emb	FDD Checking of Embankment 6th Layer	LHS	304+480	304+640	160	1-Apr-19	04:30PM	Done	
329	VKE-3/PIL/HW/329	31-Mar-19	Emb	FDD Checking of Embankment 6th Layer	LHS	304+680	305+040	360	1-Apr-19	05:00PM	Done	
330	VKE-3/PIL/HW/330	31-Mar-19	Emb	FDD Checking of Embankment 6th Layer	LHS	305+080	305+200	120	1-Apr-19	06:00PM	Done	
331	VKE-3/PIL/HW/331	31-Mar-19	Emb	FDD Checking of Embankment 2nd Layer	LHS	308+940	309+000	60	1-Apr-19	08:00AM	Done	
332	VKE-3/PIL/HW/332	31-Mar-19	Emb	FDD Checking of Embankment 4th Layer	LHS	309+040	309+500	460	1-Apr-19	09:30AM	Done	
333	VKE-3/PIL/HW/333	31-Mar-19	Emb	FDD Checking of Embankment 5th Layer	LHS	311+050	311+480	430	1-Apr-19	10:30AM	Done	
334	VKE-3/PIL/HW/334	31-Mar-19	C&G	Checking of C&G	BHS	311+480	311+650	170	1-Apr-19	11:30AM	Done	
335	VKE-3/PIL/HW/335	31-Mar-19	OGL	FDD and Level Checking of OGL	BHS	311+480	311+650	170	1-Apr-19	12:30PM	Done	
336	VKE-3/PIL/HW/336	31-Mar-19	Emb	FDD Checking of Embankment 8th Layer	LHS	311+650	311+960	310	1-Apr-19	02:30PM	Done	
337	VKE-3/PIL/HW/337	31-Mar-19	C&G	Checking of C&G	BHS	312+500	312+680	180	1-Apr-19	03:30PM	Done	
338	VKE-3/PIL/HW/338	31-Mar-19	OGL	FDD and Level Checking of OGL	BHS	312+500	312+680	180	1-Apr-19	04:45PM	Done	
339	VKE-3/PIL/HW/339	31-Mar-19	Emb	FDD Checking of Embankment 5th Layer	RHS	313+100	313+400	300	1-Apr-19	05:30PM	Done	
340	VKE-3/PIL/HW/340	31-Mar-19	Emb	FDD Checking of Embankment 2nd Layer	RHS	313+400	313+600	200	1-Apr-19	03:15PM	Done	
341	VKE-3/PIL/HW/341	31-Mar-19	Emb	FDD Checking of Embankment 9th Layer	LHS	319+800	320+400	600	1-Apr-19	09:15AM	Done	
342	VKE-3/PIL/HW/342	31-Mar-19	Emb	FDD Checking of Embankment 6th Layer	LHS	320+400	320+600	200	1-Apr-19	11:15AM	Done	
343	VKE-3/PIL/HW/343	31-Mar-19	Emb	FDD Checking of Embankment 3rd Layer	LHS	321+700	322+100	400	1-Apr-19	05:45PM	Done	
344	VKE-3/PIL/HW/344	31-Mar-19	Emb	FDD Checking of Embankment 3rd Layer	LHS	322+100	322+400	300	1-Apr-19	06:00PM	Done	
345	VKE-3/PIL/HW/345	1-Apr-19	Emb	FDD Checking of Embankment 10th Layer	LHS	303+020	303+500	480	2-Apr-19	08:30AM	Done	
346	VKE-3/PIL/HW/346	1-Apr-19	Emb	FDD Checking of Embankment 10th Layer	LHS	303+500	303+800	300	2-Apr-19	09:00AM	Done	
347	VKE-3/PIL/HW/347	1-Apr-19	Emb	FDD Checking of Embankment 9th Layer	LHS	303+820	304+000	180	2-Apr-19	10:00AM	Done	
348	VKE-3/PIL/HW/348	1-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	298+020	298+800	780	2-Apr-19	11:00AM	Done	
349	VKE-3/PIL/HW/349	1-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	298+800	299+000	200	2-Apr-19	12:00PM	Done	
350	VKE-3/PIL/HW/350	1-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	LHS	300+200	300+750	550	2-Apr-19	02:00PM	Done	
351	VKE-3/PIL/HW/351	1-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	304+000	304+160	160	2-Apr-19	03:00PM	Done	
352	VKE-3/PIL/HW/352	1-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	304+200	304+420	220	2-Apr-19	04:00PM	Done	
353	VKE-3/PIL/HW/353	1-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	304+480	304+640	160	2-Apr-19	04:30PM	Done	
354	VKE-3/PIL/HW/354	1-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	304+680	305+040	360	2-Apr-19	05:00PM	Done	
355	VKE-3/PIL/HW/355	1-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	305+080	305+200	120	2-Apr-19	06:00PM	Done	
356	VKE-3/PIL/HW/356	1-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	LHS	308+940	309+000	60	2-Apr-19	08:30AM	Done	
357	VKE-3/PIL/HW/357	1-Apr-19	Emb	FDD Checking of Embankment 5th Layer	LHS	309+040	309+500	460	2-Apr-19	09:00AM	Done	
358	VKE-3/PIL/HW/358	1-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	311+050	311+480	430	2-Apr-19	10:00AM	Done	
359	VKE-3/PIL/HW/359	1-Apr-19	Emb	FDD Checking of Embankment 1st Layer	BHS	311+480	311+650	170	2-Apr-19	11:00AM	Done	
360	VKE-3/PIL/HW/360	1-Apr-19	Emb	FDD Checking of Embankment 1st Layer	BHS	312+500	312+680	180	2-Apr-19	12:00PM	Done	
361	VKE-3/PIL/HW/361	1-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	311+650	311+960	310	2-Apr-19	02:00PM	Done	
362	VKE-3/PIL/HW/362	1-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	313+100	313+400	300	2-Apr-19	03:00PM	Done	
363	VKE-3/PIL/HW/363	1-Apr-19	Emb	FDD Checking of Embankment 4th Layer	LHS	313+400	313+800	400	2-Apr-19	04:00PM	Done	
364	VKE-3/PIL/HW/364	1-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	313+860	314+280	420	2-Apr-19	04:30PM	Done	
365	VKE-3/PIL/HW/365	1-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	314+360	314+800	440	2-Apr-19	05:00PM	Done	
366	VKE-3/PIL/HW/366	1-Apr-19	C&G	Checking of C&G	LHS	319+100	319+770	670	2-Apr-19	06:00PM	Done	
367	VKE-3/PIL/HW/367	1-Apr-19	OGL	FDD and Level Checking of OGL	LHS	319+100	319+770	670	2-Apr-19	08:00AM	Done	
368	VKE-3/PIL/HW/368	1-Apr-19	Emb	FDD Checking of Embankment 10th Layer	LHS	319+800	320+400	600	2-Apr-19	09:30AM	Done	
369	VKE-3/PIL/HW/369	1-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	320+400	320+600	200	2-Apr-19	10:30AM	Done	
370	VKE-3/PIL/HW/370	1-Apr-19	Emb	FDD Checking of Embankment 4th Layer	LHS	321+700	322+100	400	2-Apr-19	11:30AM	Done	
371	VKE-3/PIL/HW/371	1-Apr-19	Emb	FDD Checking of Embankment 4th Layer	LHS	322+100	322+400	300	2-Apr-19	12:30PM	Done	
372	VKE-3/PIL/HW/372	1-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	RHS	321+700	322+100	400	2-Apr-19	02:30PM	Done	
373	VKE-3/PIL/HW/373	1-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	RHS	322+100	322+400	300	2-Apr-19	03:30PM	Done	
374	VKE-3/PIL/HW/374	2-Apr-19	Emb	FDD Checking of Embankment 9th Layer	RHS	303+410	303+600	190	3-Apr-19	11:00AM	Done	
375	VKE-3/PIL/HW/375	2-Apr-19	Emb	FDD Checking of Embankment 4th Layer	LHS	300+400	300+500	100	3-Apr-19	09:00AM	Done	
376	VKE-3/PIL/HW/376	2-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	295+570	295+700	130	3-Apr-19	10:00AM	Done	
377	VKE-3/PIL/HW/377	2-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	295+900	296+000	100	3-Apr-19	11:00AM	Done	
378	VKE-3/PIL/HW/378	2-Apr-19	Emb	FDD Checking of Embankment 4th Layer	LHS	300+200	300+400	200	3-Apr-19	12:00PM	Done	
379	VKE-3/PIL/HW/379	2-Apr-19	Emb	FDD Checking of Embankment 8th Layer	RHS	303+820	304+000	180	3-Apr-19	10:00AM	Done	
380	VKE-3/PIL/HW/380	2-Apr-19	Emb	FDD Checking of Embankment 9th Layer	RHS	303+225	303+400	175	3-Apr-19	04:30PM	Done	
381	VKE-3/PIL/HW/381	2-Apr-19	Emb	FDD Checking and Level checking of Embankment Top	LHS	303+020	303+210	190	3-Apr-19	06:00PM	N/R	ie
382	VKE-3/PIL/HW/382	2-Apr-19	Emb	FDD Checking of Embankment 10th Layer	LHS	304+680	305+050	370	3-Apr-19	05:30PM	Done	
383	VKE-3/PIL/HW/383	2-Apr-19	Emb	FDD Checking of Embankment 1st Layer	LHS	319+400	319+500	100	3-Apr-19	04:00PM	FAIL	
384	VKE-3/PIL/HW/384	2-Apr-19	Emb	FDD Checking of Embankment 1st Layer	LHS	319+500	319+600	100	3-Apr-19	04:00PM	N/R	
385	VKE-3/PIL/HW/385	2-Apr-19	Emb	FDD Checking of Embankment 5th Layer	LHS	312+720	313+080	360	3-Apr-19	03:00PM	Done	
386	VKE-3/PIL/HW/386	2-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	313+100	313+350	250	3-Apr-19	03:00PM	N/R	
387	VKE-3/PIL/HW/387	2-Apr-19	Emb	FDD Checking of Embankment 4th Layer	RHS	322+100	322+200	100	3-Apr-19	04:00PM	FAIL	
388	VKE-3/PIL/HW/388	2-Apr-19	Emb	FDD Checking of Embankment 5th Layer	RHS	321+900	322+100	200	3-Apr-19	04:00PM	Done	ie
389	VKE-3/PIL/HW/389	2-Apr-19	Emb	FDD Checking of Embankment 9th Layer	LHS	308+500	308+800	300	3-Apr-19	05:00PM	Done	
390	VKE-3/PIL/HW/390	2-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	309+020	309+300	280	3-Apr-19	05:00PM	Done	
391	VKE-3/PIL/HW/391	2-Apr-19	Emb	FDD Checking of Embankment 2nd Layer	LHS	306+700	307+000	300	3-Apr-19	04:00PM	Done	
392	VKE-3/PIL/HW/392	2-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	295+700	295+800	100	3-Apr-19	03:30PM	N/R	
393	VKE-3/PIL/HW/393	2-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	296+500	296+700	200	3-Apr-19	04:30PM	Done	
394	VKE-3/PIL/HW/394	2-Apr-19	Emb	FDD Checking and Level checking of Embankment Top	LHS	298+560	298+700	140	3-Apr-19	11:00AM	Done	ie
395	VKE-3/PIL/HW/395	2-Apr-19	Emb	FDD Checking of Embankment 4th Layer	LHS	300+000	300+200	200	3-Apr-19	05:30PM	FAIL	
396	VKE-3/PIL/HW/396	2-Apr-19	Emb	FDD Checking of Embankment 2nd Layer	LHS	299+800	300+000	200	3-Apr-19	03:00PM	Done	
397	VKE-3/PIL/HW/397	2-Apr-19	Emb	FDD Checking of Embankment 8th Layer	RHS	303+020	303+210	190	3-Apr-19	10:30AM	Done	
398	VKE-3/PIL/HW/398	2-Apr-19	Emb	FDD Checking of Embankment 12th Layer	RHS	303+820	304+000	180	3-Apr-19	12:15PM	Done	

399	VKE-3/PIL/HW/399	2-Apr-19	C&G	Checking of C&G	BHS	302+500	302+600	100	3-Apr-19	08:30AM	N/R	ie
400	VKE-3/PIL/HW/400	2-Apr-19	OGL	FDD and Level Checking of OGL	BHS	302+500	302+600	100	3-Apr-19	11:00AM	N/R	ie
401	VKE-3/PIL/HW/401	2-Apr-19	C&G	Checking of C&G	BHS	318+200	318+500	300	3-Apr-19	08:00AM	Done	ie
402	VKE-3/PIL/HW/402	2-Apr-19	OGL	FDD and Level Checking of OGL (After Ground Improvement)	BHS	318+200	318+500	300	3-Apr-19	10:00AM	Done	ie
403	VKE-3/PIL/HW/403	2-Apr-19	Emb	FDD Checking of Embankment 6th Layer	RHS	303+610	303+800	190	3-Apr-19	03:30PM	Done	
404	VKE-3/PIL/HW/404	3-Apr-19	Emb	FDD Checking of Embankment 2nd Layer	LHS	306+800	306+900	100	4-Apr-19	03:30PM	Done	
405	VKE-3/PIL/HW/405	3-Apr-19	Emb	FDD Checking of Embankment 2nd Layer	LHS	306+500	306+700	200	4-Apr-19	05:30PM	Done	
406	VKE-3/PIL/HW/406	3-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	295+570	295+700	130	4-Apr-19	10:00AM	Done	ie
407	VKE-3/PIL/HW/407	3-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	RHS	297+160	297+260	100	4-Apr-19	04:00PM	Done	
408	VKE-3/PIL/HW/408	3-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	296+700	297+000	300	4-Apr-19	05:30PM	Done	
409	VKE-3/PIL/HW/409	3-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	LHS	300+600	300+770	170	4-Apr-19	11:00AM	FAIL	
410	VKE-3/PIL/HW/410	3-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	293+500	293+700	200	4-Apr-19	12:30PM	Done	
411	VKE-3/PIL/HW/411	3-Apr-19	Emb	FDD Checking of Embankment 10th Layer	LHS	308+800	309+000	200	4-Apr-19	02:00PM	N/R	
412	VKE-3/PIL/HW/412	3-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	309+020	309+300	280	4-Apr-19	10:00AM	Done	ie
413	VKE-3/PIL/HW/413	3-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	309+300	309+500	200	4-Apr-19	05:00PM	Done	
414	VKE-3/PIL/HW/414	3-Apr-19	Emb	FDD Checking of Embankment 1st Layer	BHS	309+500	309+700	200	4-Apr-19	05:30PM	N/R	
415	VKE-3/PIL/HW/415	3-Apr-19	Emb	FDD Checking of Embankment 4th Layer	LHS	312+200	312+270	70	4-Apr-19	11:00AM	Done	
416	VKE-3/PIL/HW/416	3-Apr-19	Emb	FDD Checking of Embankment 9th Layer	LHS	311+980	312+200	220	4-Apr-19	05:00PM	Done	
417	VKE-3/PIL/HW/417	3-Apr-19	Emb	FDD Checking of Embankment 5th Layer	LHS	311+480	311+650	170	4-Apr-19	05:30PM	Done	
418	VKE-3/PIL/HW/418	3-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	LHS	313+420	313+800	380	4-Apr-19	04:00PM	Done	ie
419	VKE-3/PIL/HW/419	3-Apr-19	Emb	FDD Checking of Embankment 10th Layer	LHS	320+200	320+400	200	4-Apr-19	04:30PM	Done	
420	VKE-3/PIL/HW/420	3-Apr-19	Emb	FDD Checking of Embankment 5th Layer	RHS	321+720	321+900	180	4-Apr-19	04:00PM	Done	
421	VKE-3/PIL/HW/421	4-Apr-19	Emb	FDD Checking of Embankment 10th Layer	LHS	304+680	305+050	370	5-Apr-19	05:00PM	FAIL	
422	VKE-3/PIL/HW/422	4-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	295+700	295+900	200	5-Apr-19	02:30PM	Done	
423	VKE-3/PIL/HW/423	4-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	295+000	295+150	150	5-Apr-19	04:00PM	N/R	
424	VKE-3/PIL/HW/424	4-Apr-19	Emb	FDD Checking of Embankment 5th Layer	LHS	297+000	297+260	260	5-Apr-19	05:00PM	Done	
425	VKE-3/PIL/HW/425	4-Apr-19	Emb	FDD Checking of Embankment 5th Layer	LHS	300+000	300+300	300	5-Apr-19	03:00PM	N/R	
426	VKE-3/PIL/HW/426	4-Apr-19	Emb	FDD & Level Checking of Embankment Top Layer	LHS	303+225	303+400	175	5-Apr-19	03:30PM	Done	ie
427	VKE-3/PIL/HW/427	4-Apr-19	Emb	FDD Checking of Embankment 2nd Layer	RHS	302+300	302+500	200	5-Apr-19	06:00PM	N/R	
428	VKE-3/PIL/HW/428	4-Apr-19	C&G	Checking of C&G	BHS	302+500	302+600	100	5-Apr-19	04:30PM	Done	ie
429	VKE-3/PIL/HW/429	4-Apr-19	OGL	FDD and Level Checking of OGL	BHS	302+500	302+600	100	5-Apr-19	05:30PM	Done	ie
430	VKE-3/PIL/HW/430	4-Apr-19	Emb	FDD Checking of Embankment 9th Layer	LHS	313+860	314+120	260	5-Apr-19	09:00AM	FAIL	
431	VKE-3/PIL/HW/431	4-Apr-19	Emb	FDD Checking of Embankment 11th Layer	LHS	311+070	311+480	410	5-Apr-19	09:30AM	Done	
432	VKE-3/PIL/HW/432	4-Apr-19	Emb	FDD Checking of Embankment 8th Layer	LHS	312+200	312+270	70	5-Apr-19	10:00AM	Done	
433	VKE-3/PIL/HW/433	4-Apr-19	Emb	FDD Checking of Embankment 5th Layer	LHS	321+900	322+100	200	5-Apr-19	11:00AM	Done	ie
434	VKE-3/PIL/HW/434	4-Apr-19	Emb	FDD Checking of Embankment 10th Layer	LHS	308+500	308+800	300	5-Apr-19	12:00PM	Done	
435	VKE-3/PIL/HW/435	4-Apr-19	Emb	FDD Checking of Embankment 8th Layer	LHS	309+020	309+450	430	5-Apr-19	02:00PM	Done	ie
436	VKE-3/PIL/HW/436	4-Apr-19	Emb	FDD Checking of Embankment 10th Layer	LHS	320+200	320+400	200	5-Apr-19	04:00PM	Done	
437	VKE-3/PIL/HW/437	4-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	319+900	320+000	100	5-Apr-19	03:00PM	Done	ie
438	VKE-3/PIL/HW/438	4-Apr-19	Emb	FDD Checking of Embankment 10th Layer	LHS	320+400	320+500	100	5-Apr-19	03:30PM	Done	
439	VKE-3/PIL/HW/439	4-Apr-19	Emb	FDD Checking of Embankment 9th Layer	LHS	311+980	312+200	220	5-Apr-19	04:00PM	Done	
440	VKE-3/PIL/HW/440	5-Apr-19	Emb	FDD Checking of Embankment 5th Layer	LHS	297+260	297+360	100	6-Apr-19	04:00PM	Done	ie
441	VKE-3/PIL/HW/441	5-Apr-19	Emb	FDD Checking of Embankment 5th Layer	LHS	300+300	300+420	120	6-Apr-19	11:00AM	Done	ie
442	VKE-3/PIL/HW/442	5-Apr-19	Emb	FDD Checking of Embankment 4th Layer	LHS	300+600	300+770	170	6-Apr-19	03:00PM	Done	
443	VKE-3/PIL/HW/443	5-Apr-19	Emb	FDD Checking of Embankment 2nd Layer	LHS	306+500	306+600	100	6-Apr-19	06:00PM	N/R	
444	VKE-3/PIL/HW/444	5-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	RHS	298+700	298+800	100	6-Apr-19	03:30PM	Done	
445	VKE-3/PIL/HW/445	5-Apr-19	Emb	FDD Checking of Embankment 4th Layer	RHS	298+500	298+700	200	6-Apr-19	04:00PM	Done	
446	VKE-3/PIL/HW/446	5-Apr-19	Emb	FDD Checking of Embankment 2nd Layer	RHS	302+100	302+300	200	6-Apr-19	05:30PM	N/R	
447	VKE-3/PIL/HW/447	5-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	296+900	297+000	100	6-Apr-19	12:30PM	Done	
448	VKE-3/PIL/HW/448	5-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	311+480	311+650	170	6-Apr-19	09:00AM	Done	ie
449	VKE-3/PIL/HW/449	5-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	RHS	312+290	312+400	110	6-Apr-19	12:00PM	Done	ie
450	VKE-3/PIL/HW/450	5-Apr-19	Emb	FDD Checking of Embankment 4th Layer	BHS	312+400	312+670	270	6-Apr-19	05:30PM	N/R	
451	VKE-3/PIL/HW/451	5-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	311+480	311+650	170	6-Apr-19	05:00PM	Done	
452	VKE-3/PIL/HW/452	5-Apr-19	Emb	FDD Checking of Embankment 11th Layer	LHS	308+500	308+800	300	6-Apr-19	05:00PM	Done	
453	VKE-3/PIL/HW/453	5-Apr-19	Emb	FDD Checking of Embankment 10th Layer	LHS	320+400	320+500	100	6-Apr-19	04:00PM	Done	
454	VKE-3/PIL/HW/454	5-Apr-19	Emb	FDD Checking of Embankment 5th Layer	LHS	321+720	321+900	180	6-Apr-19	11:00AM	Done	
455	VKE-3/PIL/HW/455	5-Apr-19	Emb	FDD Checking of Embankment 4th Layer	LHS	322+160	322+400	240	6-Apr-19	10:00AM	N/R	
456	VKE-3/PIL/HW/456	5-Apr-19	Emb	FDD Checking of Embankment 9th Layer	LHS	313+860	314+120	260	6-Apr-19	10:30AM	FAIL	
457	VKE-3/PIL/HW/457	5-Apr-19	Emb	FDD Checking of Embankment 8th Layer	LHS	314+150	314+280	130	6-Apr-19	12:00PM	Done	
458	VKE-3/PIL/HW/458	5-Apr-19	Emb	FDD Checking of Embankment 1st Layer	RHS	318+200	318+300	100	6-Apr-19	04:00PM	Done	ie
459	VKE-3/PIL/HW/459	5-Apr-19	Emb	FDD Checking of Embankment 8th Layer	LHS	309+450	309+500	50	6-Apr-19	02:00PM	Done	
460	VKE-3/PIL/HW/460	5-Apr-19	Emb	FDD Checking of Embankment 1st Layer	BHS	309+500	309+700	200	6-Apr-19	07:00PM	Done	ie
461	VKE-3/PIL/HW/461	6-Apr-19	Emb	FDD Checking of Embankment 9th Layer	LHS	313+860	314+120	260	7-Apr-19	12:00PM	Done	
462	VKE-3/PIL/HW/462	6-Apr-19	Emb	FDD Checking of Embankment 8th Layer	LHS	314+150	314+280	130	7-Apr-19	11:00AM	Done	
463	VKE-3/PIL/HW/463	6-Apr-19	Emb	FDD Checking of Embankment 1st Layer	RHS	318+200	318+300	100	7-Apr-19	11:00AM	N/R	
464	VKE-3/PIL/HW/464	6-Apr-19	Emb	FDD Checking of Embankment 5th Layer	RHS	322+100	322+400	300	7-Apr-19	02:00PM	Done	
465	VKE-3/PIL/HW/465	6-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	319+900	320+200	300	7-Apr-19	12:00PM	Done	
466	VKE-3/PIL/HW/466	6-Apr-19	Emb	FDD Checking of Embankment 8th Layer	LHS	320+500	320+600	100	7-Apr-19	02:00PM	Done	
467	VKE-3/PIL/HW/467	6-Apr-19	Emb	FDD Checking of Embankment 12th Layer	LHS	311+070	311+480	410	7-Apr-19	05:30PM	FAIL	
468	VKE-3/PIL/HW/468	6-Apr-19	Emb	FDD Checking of Embankment 4th Layer	LHS	312+400	312+670	270	7-Apr-19	09:00PM	N/R	
469	VKE-3/PIL/HW/469	6-Apr-19	Emb	FDD Checking of Embankment 8th Layer	LHS	311+380	311+650	270	7-Apr-19	05:30PM	Done	
470	VKE-3/PIL/HW/470	6-Apr-19	Emb	FDD Checking of Embankment 9th Layer	LHS	312+200	321+270	9070	7-Apr-19	09:00PM	Done	
471	VKE-3/PIL/HW/471	6-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	RHS	312+290	312+400	110	7-Apr-19	12:00PM	Done	
472	VKE-3/PIL/HW/472	6-Apr-19	Emb	FDD Checking of Embankment 5th Layer	RHS	322+100	322+400	300	7-Apr-19	02:00PM	N/R	
473	VKE-3/PIL/HW/473	6-Apr-19	Emb	FDD Checking of Embankment 9th Layer	LHS	309+020	309+300	280	7-Apr-19	05:00PM	Done	
474	VKE-3/PIL/HW/474	6-Apr-19	Emb	FDD Checking of Embankment 11th Layer	LHS	308+800	308+900	100	7-Apr-19	08:00AM	Done	
475	VKE-3/PIL/HW/475	6-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	295+000	295+150	150	7-Apr-19	04:00PM	Done	
476	VKE-3/PIL/HW/476	6-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	295+170	295+300	130	7-Apr-19	04:30PM	Done	
477	VKE-3/PIL/HW/477	6-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	293+800	293+900	100	7-Apr-19	05:00PM	Done	
478	VKE-3/PIL/HW/478	6-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	RHS	298+800	300+000	1200	7-Apr-19	03:00PM	FAIL	
479	VKE-3/PIL/HW/479	6-Apr-19	Emb	FDD Checking of Embankment 5th Layer	LHS	300+450	300+600	150	7-Apr-19	10:30AM	Done	
480	VKE-3/PIL/HW/480	6-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	BHS	299+940	300+000	60	7-Apr-19	03:30PM	Done	
481	VKE-3/PIL/HW/481	6-Apr-19	Emb	FDD Checking of Embankment 10th Layer	LHS	304+680	305+050	370	7-Apr-19	04:30PM	N/R	
482	VKE-3/PIL/HW/482	6-Apr-19	Emb	FDD Checking of Embankment 2nd Layer	RHS	306+500	306+700	200	7-Apr-19	12:30PM	Done	
483	VKE-3/PIL/HW/483	6-Apr-19	Emb	FDD Checking of Embankment 2nd Layer	RHS	306+700	307+000	300	7-Apr-19	05:30PM	Done	
484	VKE-3/PIL/HW/484	6-Apr-19	Emb	FDD Checking of Embankment 1st Layer	RHS	318+200	318+300	100	7-Apr-19	10:00 AM	Done	
485	VKE-3/PIL/HW/485	6-Apr-19	Emb	FDD Checking of Embankment 1st Layer	BHS	309+500	309+700	200	7-Apr-19	10:00 AM	Done	
486	VKE-3/PIL/HW/486	6-Apr-19	Emb	FDD Checking of Embankment 5th Layer	LHS	297+260	297+360	100	7-Apr-19	10:30AM	Done	

487	VKE-3/PIL/HW/487	7-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	296+500	296+700	200	8-Apr-19	04:00PM	Done	ie
488	VKE-3/PIL/HW/488	7-Apr-19	Emb	FDD Checking of Embankment 9th Layer	LHS	293+950	294+100	150	8-Apr-19	03:30AM	N/R	
489	VKE-3/PIL/HW/489	7-Apr-19	Emb	FDD Checking of Embankment 5th Layer	RHS	300+600	300+770	170	8-Apr-19	10:30AM	Done	ie
490	VKE-3/PIL/HW/490	7-Apr-19	Emb	FDD Checking of Embankment 6th Layer	RHS	300+450	300+600	150	8-Apr-19	03:45PM	Done	
491	VKE-3/PIL/HW/491	7-Apr-19	Emb	FDD Checking of Embankment 1st Layer	RHS	302+500	302+600	100	8-Apr-19	05:00PM	Done	
492	VKE-3/PIL/HW/492	7-Apr-19	Emb	FDD Checking of Embankment 2nd Layer	LHS	302+300	302+500	200	8-Apr-19	10:00PM	FAIL	
493	VKE-3/PIL/HW/493	7-Apr-19	Emb	FDD Checking of Embankment 2nd Layer	LHS	302+150	302+300	150	8-Apr-19	11:00PM	N/R	
494	VKE-3/PIL/HW/494	7-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	LHS	306+500	306+700	200	8-Apr-19	03:30PM	Done	
495	VKE-3/PIL/HW/495	7-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	LHS	306+700	307+000	300	8-Apr-19	05:00PM	N/R	
496	VKE-3/PIL/HW/496	7-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	319+900	320+000	100	8-Apr-19	09:00PM	Done	
497	VKE-3/PIL/HW/497	7-Apr-19	Emb	FDD Checking of Embankment 5th Layer	LHS	319+800	319+900	100	8-Apr-19	12:00PM	Done	ie
498	VKE-3/PIL/HW/498	7-Apr-19	Emb	FDD Checking of Embankment 6th Layer	RHS	321+720	322+100	380	8-Apr-19	02:00PM	Done	ie
499	VKE-3/PIL/HW/499	7-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	314+350	314+660	310	8-Apr-19	05:00PM	Done	
500	VKE-3/PIL/HW/500	7-Apr-19	Emb	FDD Checking of Embankment 1st Layer	RHS	318+300	318+500	200	8-Apr-19	08:00AM	Done	ie
501	VKE-3/PIL/HW/501	7-Apr-19	Emb	FDD Checking of Embankment 1st Layer	LHS	318+300	318+500	200	8-Apr-19	04:00PM	Done	
502	VKE-3/PIL/HW/502	7-Apr-19	Emb	FDD Checking of Embankment 13th Layer	LHS	311+070	311+480	410	8-Apr-19	04:30PM	Done	
503	VKE-3/PIL/HW/503	7-Apr-19	Emb	FDD Checking of Embankment 9th Layer	BHS	311+480	311+650	170	8-Apr-19	05:00PM	Done	
504	VKE-3/PIL/HW/504	7-Apr-19	Emb	FDD Checking of Embankment 5th Layer	BHS	312+400	312+670	270	8-Apr-19	03:00PM	Done	
505	VKE-3/PIL/HW/505	7-Apr-19	Emb	FDD Checking of Embankment 12th Layer	LHS	308+500	308+700	200	8-Apr-19	10:30AM	N/R	
506	VKE-3/PIL/HW/506	7-Apr-19	Emb	FDD Checking of Embankment 9th Layer	LHS	309+020	309+500	480	8-Apr-19	03:30PM	Done	
507	VKE-3/PIL/HW/507	7-Apr-19	Emb	FDD Checking of Embankment 1st Layer	RHS	318+200	318+520	320	8-Apr-19	04:30PM	Done	
508	VKE-3/PIL/HW/508	7-Apr-19	C&G	Checking of C&G and OGL	BHS	318+500	318+600	100	8-Apr-19	12:30PM	FAIL	
509	VKE-3/PIL/HW/509	7-Apr-19	C&G	Checking of C&G and OGL	BHS	317+800	318+000	200	8-Apr-19	05:30PM	Done	
510	VKE-3/PIL/HW/510	8-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	293+950	294+080	130	9-Apr-19	11:00AM	Done	
511	VKE-3/PIL/HW/511	8-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	295+170	295+300	130	9-Apr-19	12:30PM	Done	ie
512	VKE-3/PIL/HW/512	8-Apr-19	Emb	FDD Checking of Embankment 7th Layer	RHS	296+700	296+900	200	9-Apr-19	04:00PM	N/R	
513	VKE-3/PIL/HW/513	8-Apr-19	Emb	FDD Checking of Embankment 5th Layer	RHS	300+420	300+440	20	9-Apr-19	10:30AM	Done	
514	VKE-3/PIL/HW/514	8-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	300+155	300+420	265	9-Apr-19	11:15AM	Done	
515	VKE-3/PIL/HW/515	8-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	RHS	302+150	302+300	150	9-Apr-19	09:30AM	Done	
516	VKE-3/PIL/HW/516	8-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	RHS	302+300	302+500	200	9-Apr-19	11:30AM	Done	
517	VKE-3/PIL/HW/517	8-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	LHS	302+300	302+500	200	9-Apr-19	05:30PM	Done	
518	VKE-3/PIL/HW/518	8-Apr-19	Emb	FDD Checking of Embankment 2nd Layer	RHS	306+700	307+000	300	9-Apr-19	12:30PM	FAIL	
519	VKE-3/PIL/HW/519	8-Apr-19	Emb	FDD Checking of Embankment 5th Layer	LHS	319+800	319+900	100	9-Apr-19	03:00PM	Done	
520	VKE-3/PIL/HW/520	8-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	321+720	321+900	180	9-Apr-19	11:00AM	Done	
521	VKE-3/PIL/HW/521	8-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	321+900	322+100	200	9-Apr-19	02:00PM	Done	
522	VKE-3/PIL/HW/522	8-Apr-19	Emb	FDD Checking of Embankment 4th Layer	RHS	312+290	312+400	110	9-Apr-19	12:00PM	Done	
523	VKE-3/PIL/HW/523	8-Apr-19	Emb	FDD Checking of Embankment 10th Layer	LHS	311+980	312+270	290	9-Apr-19	06:00PM	Done	
524	VKE-3/PIL/HW/524	8-Apr-19	Emb	FDD Checking of Embankment 10th Layer	LHS	311+480	311+650	170	9-Apr-19	05:30PM	Done	
525	VKE-3/PIL/HW/525	8-Apr-19	Emb	FDD Checking of Embankment 1st Layer	LHS	318+200	318+500	300	9-Apr-19	04:30PM	Done	ie
526	VKE-3/PIL/HW/526	8-Apr-19	C&G	Checking of C&G and OGL	BHS	318+500	318+600	100	9-Apr-19	11:00AM	Done	ie
527	VKE-3/PIL/HW/527	8-Apr-19	C&G	Checking of C&G and OGL	BHS	318+100	318+200	100	9-Apr-19	11:00AM	Done	
528	VKE-3/PIL/HW/528	8-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	312+720	313+080	360	9-Apr-19	04:00PM	N/R	
529	VKE-3/PIL/HW/529	8-Apr-19	Emb	FDD Checking of Embankment 13th Layer	LHS	308+500	308+800	300	9-Apr-19	03:30PM	FAIL	
530	VKE-3/PIL/HW/530	8-Apr-19	Emb	FDD Checking of Embankment 12th Layer	LHS	308+800	308+900	100	9-Apr-19	04:30PM	Done	
531	VKE-3/PIL/HW/531	8-Apr-19	Emb	FDD Checking of Embankment 11th Layer	LHS	308+900	309+000	100	9-Apr-19	12:30PM	N/R	
532	VKE-3/PIL/HW/532	8-Apr-19	C&G	Checking of C&G and OGL	BHS	318+500	318+600	100	9-Apr-19	05:30PM	Done	ie
533	VKE-3/PIL/HW/533	8-Apr-19	Emb	FDD Checking of Embankment 10th Layer	LHS	309+020	309+500	480	9-Apr-19	12:30PM	Done	
534	VKE-3/PIL/HW/534	8-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	296+500	296+700	200	9-Apr-19	06:30PM	Done	ie
535	VKE-3/PIL/HW/535	9-Apr-19	Emb	FDD Checking of Embankment 2nd Layer	RHS	306+900	307+000	100	10-Apr-19	11:30AM	Done	
536	VKE-3/PIL/HW/536	9-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	295+450	295+540	90	10-Apr-19	02:30PM	Done	ie
537	VKE-3/PIL/HW/537	9-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	295+570	295+700	130	10-Apr-19	03:00PM	N/R	
538	VKE-3/PIL/HW/538	9-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	296+900	297+000	100	10-Apr-19	04:00PM	Done	
539	VKE-3/PIL/HW/539	9-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	297+000	297+160	160	10-Apr-19	04:30PM	Done	
540	VKE-3/PIL/HW/540	9-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	300+000	300+140	140	10-Apr-19	12:00PM	Done	
541	VKE-3/PIL/HW/541	9-Apr-19	Emb	FDD Checking of Embankment 4th Layer	LHS	299+880	300+000	120	10-Apr-19	03:40PM	Done	
542	VKE-3/PIL/HW/542	9-Apr-19	Emb	FDD Checking of Embankment 2nd Layer	BHS	302+500	302+600	100	10-Apr-19	10:00AM	Done	ie
543	VKE-3/PIL/HW/543	9-Apr-19	Emb	FDD Checking of Embankment 14th Layer	LHS	303+420	303+600	180	10-Apr-19	05:30PM	Done	
544	VKE-3/PIL/HW/544	9-Apr-19	Emb	FDD Checking of Embankment 2nd Layer	LHS	306+400	306+500	100	10-Apr-19	12:00PM	Done	
545	VKE-3/PIL/HW/545	9-Apr-19	Emb	FDD Checking of Embankment 3rd Layer	LHS	306+500	306+700	200	10-Apr-19	05:30PM	N/R	
546	VKE-3/PIL/HW/546	9-Apr-19	Emb	FDD Checking of Embankment 14th Layer	LHS	311+070	311+480	410	10-Apr-19	04:00PM	FAIL	
547	VKE-3/PIL/HW/547	9-Apr-19	Emb	FDD Checking of Embankment 10th Layer	LHS	311+480	311+650	170	10-Apr-19	05:30PM	N/R	
548	VKE-3/PIL/HW/548	9-Apr-19	Emb	FDD Checking of Embankment 6th Layer	BHS	312+500	312+670	170	10-Apr-19	06:00PM	Done	
549	VKE-3/PIL/HW/549	9-Apr-19	Emb	FDD Checking of Embankment 5th Layer	LHS	319+800	319+900	100	10-Apr-19	05:30PM	Done	ie
550	VKE-3/PIL/HW/550	9-Apr-19	Emb	FDD Checking of Embankment 5th Layer	BHS	312+400	312+500	100	10-Apr-19	04:30PM	N/R	
551	VKE-3/PIL/HW/551	9-Apr-19	Emb	FDD Checking of Embankment 1st Layer	LHS	319+700	319+850	150	10-Apr-19	11:00AM	FAIL	
552	VKE-3/PIL/HW/552	9-Apr-19	Emb	FDD Checking of Embankment 5th Layer	LHS	322+160	322+400	240	10-Apr-19	12:00PM	Done	
553	VKE-3/PIL/HW/553	9-Apr-19	Emb	FDD Checking of Embankment 6th Layer	RHS	322+100	322+400	300	10-Apr-19	04:00PM	Done	
554	VKE-3/PIL/HW/554	9-Apr-19	Emb	FDD Checking of Embankment 11th Layer	LHS	309+020	309+300	280	10-Apr-19	05:00PM	N/R	
555	VKE-3/PIL/HW/555	9-Apr-19	Emb	FDD Checking of Embankment 1st Layer	LHS	309+500	309+700	200	10-Apr-19	03:00PM	N/R	ie
556	VKE-3/PIL/HW/557	9-Apr-19	Emb	FDD Checking of Embankment 6th Layer	LHS	312+720	313+080	360	10-Apr-19	11:00AM	Done	
557	VKE-3/PIL/HW/558	9-Apr-19	Emb	FDD Checking of Embankment 7th Layer	LHS	313+100	313+350	250	10-Apr-19	11:00AM	Done	
558	VKE-3/PIL/HW/559	9-Apr-19	Emb	FDD Checking of Embankment 4th Layer	LHS	313+420	313+800	380	10-Apr-19	06:30PM	Done	

Sr. NO.	RFI NO.	Inspection Time	Inspection date	Item No.	Item Description	Chainage		Side	MCW/ CR	CA/ COS	Unit	Status	Witness By IE
						From	To						
1	VKE-3/PIL/HW/560	10:00AM	11-Apr-19		FDD Checking of Embankment 2nd Layer	302+500	302+600	RHS	MCW	CA	M	Done	
2	VKE-3/PIL/HW/561	11:00AM	11-Apr-19		FDD Checking of Embankment 6th Layer	295+450	295+540	LHS	MCW	CA	M	Done	ie
3	VKE-3/PIL/HW/562	10:30AM	11-Apr-19		FDD Checking of Embankment 7th Layer	296+700	296+900	LHS	MCW	CA	M	N/R	
4	VKE-3/PIL/HW/563	03:00PM	11-Apr-19		FDD Checking of Embankment 7th Layer	294+100	294+300	LHS	MCW	CA	M	Done	
5	VKE-3/PIL/HW/564	03:30PM	11-Apr-19		FDD Checking of Embankment 7th Layer	300+150	300+420	LHS	MCW	CA	M	Done	
6	VKE-3/PIL/HW/565	11:00AM	11-Apr-19		FDD Checking of Embankment 7th Layer	300+460	300+600	LHS	MCW	CA	M	Done	IE
7	VKE-3/PIL/HW/566	05:30PM	11-Apr-19		FDD Checking of Embankment 7th Layer	300+000	300+140	LHS	MCW	CA	M	FAIL	
8	VKE-3/PIL/HW/567	04:30PM	11-Apr-19		Checking of C&G and OGL	302+000	302+100	BHS	MCW	CA	M	Done	IE
9	VKE-3/PIL/HW/568	05:30PM	11-Apr-19		FDD Checking of Embankment 3rd Layer	302+150	302+300	LHS	MCW	CA	M	Done	
10	VKE-3/PIL/HW/569	05:30PM	11-Apr-19		FDD Checking of Embankment 3rd Layer	302+150	302+300	RHS	MCW	CA	M	FAIL	
11	VKE-3/PIL/HW/570	10:30AM	11-Apr-19		FDD Checking of Embankment 4th Layer	302+300	302+500	LHS	MCW	CA	M	Done	
12	VKE-3/PIL/HW/571	10:30AM	11-Apr-19		FDD Checking of Embankment 4th Layer	302+300	302+500	RHS	MCW	CA	M	N/R	
13	VKE-3/PIL/HW/572	05:00PM	11-Apr-19		FDD Checking of Embankment 3rd Layer	306+700	306+900	LHS	MCW	CA	M	Done	
14	VKE-3/PIL/HW/573	11:00AM	11-Apr-19		Checking of C&G and OGL	317+900	318+100	BHS	MCW	CA	M	Done	IE
15	VKE-3/PIL/HW/574	04:00PM	11-Apr-19		FDD Checking of Embankment 1st Layer	318+500	318+560	LHS	MCW	CA	M	Done	
16	VKE-3/PIL/HW/575	04:00PM	11-Apr-19		FDD Checking of Embankment 1st Layer	318+500	318+560	RHS	MCW	CA	M	Done	
17	VKE-3/PIL/HW/576	12:00PM	11-Apr-19		FDD Checking of Embankment 2nd Layer	318+200	318+500	RHS	MCW	CA	M	Done	
18	VKE-3/PIL/HW/577	04:00PM	11-Apr-19		FDD Checking of Embankment 10th Layer	313+860	314+120	LHS	MCW	CA	M	Done	
19	VKE-3/PIL/HW/578	04:00PM	11-Apr-19		FDD Checking of Embankment 9th Layer	314+150	314+280	LHS	MCW	CA	M	Done	
20	VKE-3/PIL/HW/579	11:00AM	11-Apr-19		Checking of C&G and OGL	322+400	322+500	BHS	MCW	CA	M	Done	IE
21	VKE-3/PIL/HW/580	11:00AM	11-Apr-19		FDD Checking of Embankment 7th Layer	321+900	322+100	RHS	MCW	CA	M	Done	
22	VKE-3/PIL/HW/581	04:00PM	11-Apr-19		FDD Checking of Embankment 7th Layer	321+700	321+900	RHS	MCW	CA	M	Done	
23	VKE-3/PIL/HW/582	05:00PM	11-Apr-19		FDD Checking of Embankment 11th Layer	311+980	312+200	LHS	MCW	CA	M	FAIL	
24	VKE-3/PIL/HW/583	05:30PM	11-Apr-19		FDD Checking of Embankment 11th Layer	312+200	312+270	LHS	MCW	CA	M	Done	
25	VKE-3/PIL/HW/584	08:00P	11-Apr-19		FDD Checking of Embankment 3rd Layer	311+050	311+330	RHS	MCW	CA	M	Done	
26	VKE-3/PIL/HW/585	08:00P	11-Apr-19		FDD Checking of Embankment 4th Layer	311+330	311+480	RHS	MCW	CA	M	Done	
27	VKE-3/PIL/HW/586	05:00PM	11-Apr-19		FDD Checking of Embankment 14th Layer	308+500	308+700	LHS	MCW	CA	M	N/R	
28	VKE-3/PIL/HW/587	05:30PM	11-Apr-19		FDD Checking of Embankment 11th Layer	309+220	309+500	LHS	MCW	CA	M	Done	
29	VKE-3/PIL/HW/588	02:30PM	11-Apr-19		FDD Checking of Embankment 1st Layer	319+600	319+700	LHS	MCW	CA	M	Done	IE
30	VKE-3/PIL/HW/589	04:50PM	11-Apr-19		FDD Checking of Embankment 1st Layer	319+700	319+880	LHS	MCW	CA	M	Done	
31	VKE-3/PIL/HW/590	12:00PM	11-Apr-19		FDD Checking of Embankment 6th Layer	312+500	312+670	LHS	MCW	CA	M	FAIL	
32	VKE-3/PIL/HW/591	12:00PM	11-Apr-19		FDD Checking of Embankment 6th Layer	312+500	312+670	RHS	MCW	CA	M	FAIL	
33	VKE-3/PIL/HW/592	11:00AM	11-Apr-19		FDD Checking of Embankment 1st Layer	309+500	309+700	LHS	MCW	CA	M	Done	IE
34	VKE-3/PIL/HW/593	10:30AM	11-Apr-19		FDD Checking of Embankment 4th Layer	313+420	313+800	LHS	MCW	CA	M	Done	
35	VKE-3/PIL/HW/594	12:00PM	11-Apr-19		Checking of C&G and OGL	310+420	311+000	BHS	MCW	CA	M	Done	IE
36	VKE-3/PIL/HW/595	10:00AM	12-Apr-19		FDD Checking of Embankment 7th Layer	294+200	294+300	LHS	MCW	CA	M	Done	
37	VKE-3/PIL/HW/596	05:00PM	12-Apr-19		FDD Checking of Embankment 7th Layer	295+570	295+800	LHS	MCW	CA	M	Done	
38	VKE-3/PIL/HW/597	04:30PM	12-Apr-19		FDD Checking of Embankment 3rd Layer	296+700	296+800	RHS	MCW	CA	M	Done	
39	VKE-3/PIL/HW/598	11:30AM	12-Apr-19		FDD Checking of Embankment 6th Layer	297+200	296+360	LHS	MCW	CA	M	Done	
40	VKE-3/PIL/HW/599	12:30PM	12-Apr-19		FDD Checking of Embankment 5th Layer	299+880	300+000	LHS	MCW	CA	M	FAIL	
41	VKE-3/PIL/HW/600	10:30AM	12-Apr-19		FDD Checking of Embankment 4th Layer	302+150	302+300	LHS	MCW	CA	M	FAIL	
42	VKE-3/PIL/HW/601	11:30AM	12-Apr-19		FDD Checking of Embankment 3rd Layer	302+500	302+600	LHS	MCW	CA	M	N/R	
43	VKE-3/PIL/HW/602	12:00PM	12-Apr-19		FDD Checking of Embankment 3rd Layer	302+500	302+600	RHS	MCW	CA	M	Done	
44	VKE-3/PIL/HW/603	05:30PM	12-Apr-19		FDD Checking of Embankment 15th Layer	303+420	303+600	LHS	MCW	CA	M	Done	
45	VKE-3/PIL/HW/604	06:00PM	12-Apr-19		FDD Checking of Embankment 3rd Layer	306+500	306+700	LHS	MCW	CA	M	Done	
46	VKE-3/PIL/HW/605	12:00PM	12-Apr-19		FDD Checking of Embankment 1st Layer	319+400	319+500	LHS	MCW	CA	M	Done	
47	VKE-3/PIL/HW/606	03:30PM	12-Apr-19		FDD Checking of Embankment 1st Layer	319+500	319+600	LHS	MCW	CA	M	FAIL	
48	VKE-3/PIL/HW/607	04:00PM	12-Apr-19		Checking of C&G and OGL	322+400	322+500	BHS	MCW	CA	M	N/R	
49	VKE-3/PIL/HW/608	03:00PM	12-Apr-19		FDD Checking of Embankment 7th Layer	321+900	322+100	LHS	MCW	CA	M	Done	
50	VKE-3/PIL/HW/609	11:30AM	12-Apr-19		FDD Checking of Embankment 7th Layer	321+720	321+900	LHS	MCW	CA	M	Done	
51	VKE-3/PIL/HW/610	09:00AM	12-Apr-19		FDD Checking of Embankment 7th Layer	312+400	312+500	RHS	MCW	CA	M	FAIL	
52	VKE-3/PIL/HW/611	09:30AM	12-Apr-19		FDD Checking of Embankment 6th Layer	312+290	312+400	RHS	MCW	CA	M	Done	
53	VKE-3/PIL/HW/612	05:00PM	12-Apr-19		FDD Checking of Embankment 3rd Layer	311+050	311+330	RHS	MCW	CA	M	Done	
54	VKE-3/PIL/HW/613	05:30PM	12-Apr-19		FDD Checking of Embankment 4th Layer	311+330	311+480	RHS	MCW	CA	M	Done	
55	VKE-3/PIL/HW/614	06:00PM	12-Apr-19		FDD Checking of Embankment 4th Layer	311+480	311+650	RHS	MCW	CA	M	Done	
56	VKE-3/PIL/HW/615	06:30PM	12-Apr-19		FDD Checking of Embankment 15th Layer	311+070	311+480	LHS	MCW	CA	M	FAIL	
57	VKE-3/PIL/HW/616	06:50PM	12-Apr-19		FDD Checking of Embankment 11th Layer	311+480	311+650	LHS	MCW	CA	M	Done	
58	VKE-3/PIL/HW/617	11:00AM	12-Apr-19		FDD Checking of Embankment 9th Layer	314+150	314+280	LHS	MCW	CA	M	Done	
59	VKE-3/PIL/HW/618	04:00PM	12-Apr-19		Checking of C&G and OGL	317+700	317+900	BHS	MCW	CA	M	Done	IE
60	VKE-3/PIL/HW/619	03:00PM	12-Apr-19		FDD Checking of Embankment 8th Layer	314+350	314+660	LHS	MCW	CA	M	FAIL	
61	VKE-3/PIL/HW/620	03:00PM	12-Apr-19		FDD Checking of Embankment 1st Layer	318+100	318+200	LHS	MCW	CA	M	Done	
62	VKE-3/PIL/HW/621	03:00PM	12-Apr-19		FDD Checking of Embankment 1st Layer	318+100	318+200	RHS	MCW	CA	M	Done	
63	VKE-3/PIL/HW/622	12:30PM	12-Apr-19		FDD Checking of Embankment 12th Layer	308+700	308+900	LHS	MCW	CA	M	Done	
64	VKE-3/PIL/HW/623	05:00PM	12-Apr-19		FDD Checking of Embankment 12th Layer	309+020	309+500	LHS	MCW	CA	M	Done	IE
65	VKE-3/PIL/HW/624	05:30PM	12-Apr-19		FDD Checking of Embankment 1st Layer	318+500	318+560	LHS	MCW	CA	M	FAIL	
66	VKE-3/PIL/HW/625	05:30PM	12-Apr-19		FDD Checking of Embankment 1st Layer	318+500	318+560	RHS	MCW	CA	M	N/R	
67	VKE-3/PIL/HW/626	04:00PM	12-Apr-19		FDD Checking of Embankment 11th Layer	311+980	312+200	LHS	MCW	CA	M	Done	
68	VKE-3/PIL/HW/627	03:00PM	12-Apr-19		FDD Checking of Embankment 1st Layer	319+600	319+700	LHS	MCW	CA	M	Done	
69	VKE-3/PIL/HW/628	09:50AM	12-Apr-19		FDD Checking of Embankment 1st Layer	309+500	309+700	LHS	MCW	CA	M	FAIL	
70	VKE-3/PIL/HW/629	09:50AM	12-Apr-19		FDD Checking of Embankment 1st Layer	309+500	309+700	RHS	MCW	CA	M	Done	
71	VKE-3/PIL/HW/630	03:00PM	12-Apr-19		Checking of C&G and OGL	310+420	311+000	BHS	MCW	CA	M	Done	
72	VKE-3/PIL/HW/631	09:30AM	13-Apr-19		FDD Checking of Embankment 7th Layer	300+000	300+140	LHS	MCW	CA	M	Done	IE
73	VKE-3/PIL/HW/632	04:30PM	13-Apr-19		Checking of C&G	301+960	302+000	BHS	MCW	CA	M	Done	IE
74	VKE-3/PIL/HW/633	05:30PM	13-Apr-19		Checking of OGL	301+960	302+000	BHS	MCW	CA	M	Done	IE
75	VKE-3/PIL/HW/634	05:30PM	13-Apr-19		FDD Checking of Embankment 3rd Layer	306+700	306+900	LHS	MCW	CA	M	Done	
76	VKE-3/PIL/HW/635	03:00PM	13-Apr-19		FDD Checking of Embankment 7th Layer	294+300	294+400	LHS	MCW	CA	M	Done	
77	VKE-3/PIL/HW/636	11:30AM	13-Apr-19		FDD Checking of Embankment 7th Layer	295+800	296+000	LHS	MCW	CA	M	FAIL	
78	VKE-3/PIL/HW/637	04:00PM	13-Apr-19		FDD Checking of Embankment 8th Layer	296+500	296+800	LHS	MCW	CA	M	N/R	
79	VKE-3/PIL/HW/638	11:30AM	13-Apr-19		FDD Checking of Embankment 8th Layer	300+400	300+600	LHS	MCW	CA	M	FAIL	
80	VKE-3/PIL/HW/639	03:30PM	13-Apr-19		FDD Checking of Embankment 6th Layer	299+880	300+000	LHS	MCW	CA	M	Done	
81	VKE-3/PIL/HW/640	10:15AM	13-Apr-19		FDD Checking of Embankment 5th Layer	302+300	302+500	LHS	MCW	CA	M	Done	
82	VKE-3/PIL/HW/641	11:00AM	13-Apr-19		FDD Checking of Embankment 5th Layer	302+300	302+500	RHS	MCW	CA	M	Done	
83	VKE-3/PIL/HW/642	10:30AM	13-Apr-19		Checking of C&G	302+000	302+100	BHS	MCW	CA	M	Done	IE
84	VKE-3/PIL/HW/643	05:30PM	13-Apr-19		Checking of OGL	302+000	302+100	BHS	MCW	CA	M	Done	IE
85	VKE-3/PIL/HW/644	05:30PM	13-Apr-19		FDD Checking of Embankment 4th Layer	306+400	306+500	LHS	MCW	CA	M	Done	
86	VKE-3/PIL/HW/645	05:00PM	13-Apr-19		FDD Checking of Embankment 4th Layer	306+500	306+700	LHS	MCW	CA	M	Done	
87	VKE-3/PIL/HW/646	02:30PM	13-Apr-19		FDD Checking of Embankment 3rd Layer	306+700	306+900	LHS	MCW	CA	M	Done	
88	VKE-3/PIL/HW/647	04:00PM	13-Apr-19		FDD Checking of Embankment 1st Layer	317+900	318+100	RHS	MCW	CA	M	N/R	
89	VKE-3/PIL/HW/648	11:00AM	13-Apr-19		FDD Checking of Embankment 2nd Layer	318+200	318+500	LHS	MCW	CA	M	FAIL	
90	VKE-3/PIL/HW/649	04:00PM	13-Apr-19		FDD Checking of Embankment 7th Layer	314+690	314+800	LHS	MCW	CA	M	N/R	
91	VKE-3/PIL/HW/650	03:30PM	13-Apr-19		FDD Checking of Embankment 5th Layer	311+670	311+980	RHS	MCW	CA	M	FAIL	
92	VKE-3/PIL/HW/651	04:00PM	13-Apr-19		FDD Checking of Embankment 5th Layer	311+980	312+200	RHS	MCW	CA	M	Done	
93	VKE-3/PIL/HW/652	05:30PM	13-Apr-19		FDD Checking of Embankment 6th Layer	312+200	312+270	RHS	MCW	CA	M	FAIL	
94	VKE-3/PIL/HW/653	03:00PM	13-Apr-19		FDD Checking of Embankment 7th Layer	312+290	312+400	RHS	MCW	CA	M	Done	
95	VKE-3/PIL/HW/654	05:00PM	13-Apr-19		FDD Checking of Embankment 8th Layer	312+400	312+500	RHS	MCW	CA	M	FAIL	
96	VKE-3/PIL/HW/655	04:30PM	13-Apr-19		FDD Checking of Embankment 8th Layer	312+500	312+670	RHS</					

101	VKE-3/PIL/HW/660	04:00PM	13-Apr-19		Checking of C&G	322+400	322+500	BHS	MCW	CA	M	Done	
102	VKE-3/PIL/HW/661	05:15PM	13-Apr-19		Checking of OGL	322+400	322+500	BHS	MCW	CA	M	Done	IE
103	VKE-3/PIL/HW/662	04:00PM	13-Apr-19		FDD Checking of Embankment 7th Layer	321+900	322+100	LHS	MCW	CA	M	FAIL	
104	VKE-3/PIL/HW/663	11:30AM	13-Apr-19		FDD Checking of Embankment 7th Layer	321+720	321+900	LHS	MCW	CA	M	Done	
105	VKE-3/PIL/HW/664	04:00PM	13-Apr-19		FDD Checking of Embankment 15th Layer	308+500	308+700	LHS	MCW	CA	M	Done	
106	VKE-3/PIL/HW/665	03:00PM	13-Apr-19		FDD Checking of Embankment 8th Layer	312+500	312+670	LHS	MCW	CA	M	FAIL	
107	VKE-3/PIL/HW/666	09:50AM	13-Apr-19		FDD Checking of Embankment 1st Layer	318+100	318+200	RHS	MCW	CA	M	FAIL	
108	VKE-3/PIL/HW/667	11:00AM	13-Apr-19		FDD Checking of Embankment 11th Layer	308+900	309+000	LHS	MCW	CA	M	Done	
109	VKE-3/PIL/HW/668	03:00PM	13-Apr-19		FDD Checking of Embankment 8th Layer	314+350	314+660	LHS	MCW	CA	M	FAIL	
110	VKE-3/PIL/HW/669	04:00PM	13-Apr-19		FDD Checking of Embankment 1st Layer	309+500	309+700	LHS	MCW	CA	M	FAIL	
111	VKE-3/PIL/HW/670	06:00PM	13-Apr-19		FDD Checking of Embankment 1st Layer	309+560	309+700	RHS	MCW	CA	M	Done	
112	VKE-3/PIL/HW/671	11:30AM	14-Apr-19		FDD Checking of Embankment 7th Layer	294+300	294+500	LHS	MCW	CA	M	Done	
113	VKE-3/PIL/HW/672	05:00PM	14-Apr-19		FDD Checking of Embankment 8th Layer	296+700	296+900	LHS	MCW	CA	M	Done	
114	VKE-3/PIL/HW/673	11:00AM	14-Apr-19		FDD Checking of Embankment 7th Layer	295+800	296+000	LHS	MCW	CA	M	Done	IE
115	VKE-3/PIL/HW/674	04:00PM	14-Apr-19		FDD Checking of Embankment 7th Layer	297+000	2971+000	LHS	MCW	CA	M	Done	IE
116	VKE-3/PIL/HW/675	10:30AM	14-Apr-19		FDD Checking of Embankment 4th Layer	302+500	302+600	RHS	MCW	CA	M	Done	
117	VKE-3/PIL/HW/676	11:45AM	14-Apr-19		FDD Checking of Embankment 5th Layer	302+150	302+300	RHS	MCW	CA	M	Done	
118	VKE-3/PIL/HW/677	04:30PM	14-Apr-19		FDD Checking of Embankment 5th Layer	302+200	302+300	LHS	MCW	CA	M	Done	
119	VKE-3/PIL/HW/678	05:30PM	14-Apr-19		FDD Checking of Embankment 6th Layer	302+300	302+500	LHS	MCW	CA	M	Done	
120	VKE-3/PIL/HW/679	05:30PM	14-Apr-19		FDD Checking of Embankment 17th Layer	303+500	303+600	LHS	MCW	CA	M	N/R	
121	VKE-3/PIL/HW/680	12:00PM	14-Apr-19		FDD Checking of Embankment 15th Layer	308+700	308+900	LHS	MCW	CA	M	FAIL	
122	VKE-3/PIL/HW/681	05:00 PM	14-Apr-19		FDD Checking of Embankment 2nd Layer	308+500	309+000	RHS	MCW	CA	M	FAIL	
123	VKE-3/PIL/HW/689	11:00AM	14-Apr-19		Checking of OGL along with FDD after ground improvement	301+940	302+000	BHS	MCW	CA	M	Done	
124	VKE-3/PIL/HW/682	02:30PM	14-Apr-19		FDD Checking of Embankment 3rd Layer	306+900	307+000	LHS	MCW	CA	M	FAIL	
125	VKE-3/PIL/HW/683	04:00PM	14-Apr-19		FDD Checking of Embankment 2nd Layer	318+500	318+560	RHS	MCW	CA	M	Done	
126	VKE-3/PIL/HW/684	04:00PM	14-Apr-19		FDD Checking of Embankment 2nd Layer	318+500	318+560	LHS	MCW	CA	M	Done	
127	VKE-3/PIL/HW/685	11:00AM	14-Apr-19		FDD Checking of Embankment 2nd Layer	308+500	309+000	RHS	MCW	CA	M	Done	
128	VKE-3/PIL/HW/686	04:00PM	14-Apr-19		FDD Checking of Embankment 16th Layer	308+500	308+800	LHS	MCW	CA	M	Done	
129	VKE-3/PIL/HW/687	03:30PM	14-Apr-19		FDD Checking of Embankment 4th Layer	311+050	311+330	RHS	MCW	CA	M	Done	
130	VKE-3/PIL/HW/688	04:00PM	14-Apr-19		FDD Checking of Embankment 5th Layer	311+330	331+480	RHS	MCW	CA	M	Done	
131	VKE-3/PIL/HW/689	05:30PM	14-Apr-19		FDD Checking of Embankment 5th Layer	311+480	311+650	RHS	MCW	CA	M	Done	
132	VKE-3/PIL/HW/690	03:00PM	14-Apr-19		FDD Checking of Embankment 6th Layer	322+160	322+400	LHS	MCW	CA	M	N/R	
133	VKE-3/PIL/HW/691	05:00PM	14-Apr-19		FDD Checking of Embankment 7th Layer	322+300	322+400	RHS	MCW	CA	M	FAIL	
134	VKE-3/PIL/HW/692	04:30PM	14-Apr-19		FDD Checking of Embankment 7th Layer	312+720	313+080	LHS	MCW	CA	M	Done	
135	VKE-3/PIL/HW/693	04:30PM	14-Apr-19		FDD Checking of Embankment 2nd Layer	318+500	318+560	LHS	MCW	CA	M	N/R	
136	VKE-3/PIL/HW/694	04:30PM	14-Apr-19		FDD Checking of Embankment 2nd Layer	318+500	318+560	RHS	MCW	CA	M	Done	
137	VKE-3/PIL/HW/695	03:00PM	14-Apr-19		FDD Checking of Embankment 1st Layer	319+500	319+600	LHS	MCW	CA	M	Done	
138	VKE-3/PIL/HW/696	04:00PM	14-Apr-19		FDD Checking of Embankment 1st Layer	317+900	318+100	RHS	MCW	CA	M	Done	
139	VKE-3/PIL/HW/697	05:00PM	14-Apr-19		FDD Checking of Embankment 7th Layer	314+960	314+800	LHS	MCW	CA	M	Done	
140	VKE-3/PIL/HW/698	05:00PM	14-Apr-19		FDD Checking of Embankment 6th Layer	312+200	312+270	RHS	MCW	CA	M	Done	
141	VKE-3/PIL/HW/699	05:00PM	15-Apr-19		FDD Checking of Embankment 8th Layer	300+450	300+600	LHS	MCW	CA	M	Done	
142	VKE-3/PIL/HW/700	05:30PM	15-Apr-19		FDD Checking of Embankment 6th Layer	299+880	300+000	LHS	MCW	CA	M	Done	IE
143	VKE-3/PIL/HW/701	04:00PM	15-Apr-19		FDD Checking of Embankment 7th Layer	295+000	295+150	LHS	MCW	CA	M	Done	IE
144	VKE-3/PIL/HW/702	11:00AM	15-Apr-19		FDD Checking of Embankment 7th Layer	295+800	296+000	LHS	MCW	CA	M	Done	
145	VKE-3/PIL/HW/703	04:30 PM	15-Apr-19		FDD Checking of Embankment 7th Layer	297+100	297+360	LHS	MCW	CA	M	N/R	
146	VKE-3/PIL/HW/704	05:00PM	15-Apr-19		FDD Checking of Embankment 7th Layer	294+500	294+600	LHS	MCW	CA	M	FAIL	
147	VKE-3/PIL/HW/705	11:30AM	15-Apr-19		FDD Checking of Embankment 8th Layer	300+460	300+600	LHS	MCW	CA	M	Done	
148	VKE-3/PIL/HW/706	10:15PM	15-Apr-19		FDD Checking of Embankment 6th Layer	302+150	302+300	RHS	MCW	CA	M	N/R	
149	VKE-3/PIL/HW/707	11:30AM	15-Apr-19		FDD Checking of Embankment 6th Layer	302+300	302+500	RHS	MCW	CA	M	FAIL	
150	VKE-3/PIL/HW/708	5:40PM	15-Apr-19		FDD Checking of Embankment 5th Layer	302+500	302+600	LHS	MCW	CA	M	FAIL	
151	VKE-3/PIL/HW/709	06:00 PM	15-Apr-19		FDD Checking of Embankment 5th Layer	302+500	302+600	RHS	MCW	CA	M	Done	
152	VKE-3/PIL/HW/710	10:00AM	15-Apr-19		FDD Checking of Embankment 1st Layer	317+700	317+900	RHS	MCW	CA	M	Done	
153	VKE-3/PIL/HW/711	02:30PM	15-Apr-19		FDD Checking of Embankment 4th Layer	311+050	311+330	RHS	MCW	CA	M	Done	
154	VKE-3/PIL/HW/712	04:00PM	15-Apr-19		FDD Checking of Embankment 5th Layer	311+330	311+480	RHS	MCW	CA	M	Done	
155	VKE-3/PIL/HW/713	04:30PM	15-Apr-19		FDD Checking of Embankment 5th Layer	311+480	311+650	RHS	MCW	CA	M	Done	
156	VKE-3/PIL/HW/714	11:00AM	15-Apr-19		FDD Checking of Embankment 16th Layer	311+070	311+480	LHS	MCW	CA	M	Done	IE
157	VKE-3/PIL/HW/715	04:00PM	15-Apr-19		FDD Checking of Embankment 12th Layer	311+480	311+650	LHS	MCW	CA	M	FAIL	
158	VKE-3/PIL/HW/716	03:30PM	15-Apr-19		FDD Checking of Embankment 9th Layer	312+500	312+670	LHS	MCW	CA	M	Done	
159	VKE-3/PIL/HW/717	04:00PM	15-Apr-19		FDD Checking of Embankment 9th Layer	312+500	312+670	RHS	MCW	CA	M	N/R	
160	VKE-3/PIL/HW/718	05:30PM	15-Apr-19		FDD Checking of Embankment 16th Layer	308+500	308+600	LHS	MCW	CA	M	Done	
161	VKE-3/PIL/HW/719	03:00PM	15-Apr-19		FDD Checking of Embankment 1st Layer	319+500	319+600	LHS	MCW	CA	M	Done	IE
162	VKE-3/PIL/HW/720	05:00PM	15-Apr-19		FDD Checking of Embankment 7th Layer	322+300	322+400	RHS	MCW	CA	M	Done	
163	VKE-3/PIL/HW/721	04:30PM	15-Apr-19		FDD Checking of Embankment 7th Layer	312+720	313+080	LHS	MCW	CA	M	FAIL	
164	VKE-3/PIL/HW/722	04:30PM	15-Apr-19		FDD Checking of Embankment 5th Layer	311+670	311+980	RHS	MCW	CA	M	Done	
165	VKE-3/PIL/HW/723	03:30PM	15-Apr-19		FDD Checking of Embankment 5th Layer	311+980	312+200	RHS	MCW	CA	M	Done	
166	VKE-3/PIL/HW/724	02:30PM	15-Apr-19		FDD Checking of Embankment 6th Layer	312+200	312+270	RHS	MCW	CA	M	Done	
167	VKE-3/PIL/HW/725	03:00PM	15-Apr-19		FDD Checking of Embankment 2nd Layer	308+800	308+900	RHS	MCW	CA	M	Done	
168	VKE-3/PIL/HW/726	04:00PM	15-Apr-19		FDD Checking of Embankment 16th Layer	308+500	308+700	LHS	MCW	CA	M	Done	IE
169	VKE-3/PIL/HW/727	05:00PM	15-Apr-19		FDD Checking of Embankment 7th Layer	314+690	314+800	LHS	MCW	CA	M	Done	
170	VKE-3/PIL/HW/728	04:30PM	15-Apr-19		FDD Checking of Embankment 1st Layer	319+300	319+500	LHS	MCW	CA	M	Done	
171	VKE-3/PIL/HW/729	04:30PM	16-Apr-19		FDD Checking of Embankment 8th Layer	295+600	295+800	LHS	MCW	CA	M	Done	
172	VKE-3/PIL/HW/730	05:00PM	16-Apr-19		FDD Checking of Embankment 2nd Layer	296+000	296+200	LHS	MCW	CA	M	Done	
173	VKE-3/PIL/HW/731	05:00PM	16-Apr-19		FDD Checking of Embankment 9th Layer	296+500	296+600	LHS	MCW	CA	M	Done	
174	VKE-3/PIL/HW/732	12:00PM	16-Apr-19		FDD Checking of Embankment 7th Layer	298+900	299+000	LHS	MCW	CA	M	FAIL	
175	VKE-3/PIL/HW/733	12:30PM	16-Apr-19		FDD Checking of Embankment 6th Layer	299+880	300+000	LHS	MCW	CA	M	N/R	
176	VKE-3/PIL/HW/734	11:30AM	16-Apr-19		FDD Checking of Embankment 11th Layer	298+120	298+330	LHS	MCW	CA	M	Done	
177	VKE-3/PIL/HW/735	09:30AM	16-Apr-19		FDD Checking of Embankment 1st Layer	301+940	302+100	LHS	MCW	CA	M	Done	IE
178	VKE-3/PIL/HW/736	10:30AM	16-Apr-19		FDD Checking of Embankment 1st Layer	301+940	302+100	RHS	MCW	CA	M	Done	
179	VKE-3/PIL/HW/737	11:00AM	16-Apr-19		FDD Checking of Embankment 6th Layer	302+200	302+300	LHS	MCW	CA	M	Done	IE
180	VKE-3/PIL/HW/738	04:45PM	16-Apr-19		FDD Checking of Embankment 7th Layer	302+300	302+500	LHS	MCW	CA	M	FAIL	
181	VKE-3/PIL/HW/739	11:30AM	16-Apr-19		FDD Checking of Embankment 16th Layer	303+500	303+600	LHS	MCW	CA	M	Done	IE
182	VKE-3/PIL/HW/740	04:00PM	16-Apr-19		FDD Checking of Embankment 6th Layer	297+200	297+360	LHS	MCW	CA	M	Done	
183	VKE-3/PIL/HW/741	05:00PM	16-Apr-19		FDD Checking of Embankment 5th Layer	306+100	306+320	LHS	MCW	CA	M	Done	
184	VKE-3/PIL/HW/742	06:00PM	16-Apr-19		FDD Checking of Embankment 5th Layer	306+400	306+600	LHS	MCW	CA	M	Done	
185	VKE-3/PIL/HW/743	04:30PM	16-Apr-19		FDD Checking of Embankment 7th Layer	296+900	297+000	LHS	MCW	CA	M	Done	
186	VKE-3/PIL/HW/744	11:00AM	16-Apr-19		FDD Checking of Embankment 9th Layer	312+400	312+500	RHS	MCW	CA	M	Done	
187	VKE-3/PIL/HW/745	04:00PM	16-Apr-19		FDD Checking of Embankment 5th Layer	311+480	311+650	RHS	MCW	CA	M	Done	
188	VKE-3/PIL/HW/746	03:30PM	16-Apr-19		FDD Checking of Embankment 3rd Layer	308+500	309+000	RHS	MCW	CA	M	N/R	
189	VKE-3/PIL/HW/747	04:00PM	16-Apr-19		FDD Checking of Embankment 13th Layer	309+020	309+200	LHS	MCW	CA	M	Done	
190	VKE-3/PIL/HW/748	05:30PM	16-Apr-19		FDD Checking of Embankment 8th Layer	313+100	313+350	LHS	MCW	CA	M	Done	
191	VKE-3/PIL/HW/749	03:00PM	16-Apr-19		FDD Checking of Embankment 8th Layer	321+720	321+900	RHS	MCW	CA	M	FAIL	
192	VKE-3/PIL/HW/750	05:00PM	16-Apr-19		FDD Checking of Embankment 8th Layer	321+900	322+100	RHS	MCW	CA	M	N/R	
193	VKE-3/PIL/HW/751	06:50PM	16-Apr-19		FDD Checking of Embankment 1st Layer	317+700	317+900	LHS	MCW	CA	M	Done	
194	VKE-3/PIL/HW/752	11:00AM	16-Apr-19		FDD Checking of Embankment 1st Layer	317+700	317+900	RHS	MCW	CA	M	Done	
195	VKE-3/PIL/HW/753	04:00PM	16-Apr-19		FDD Checking of Embankment 4th Layer	311+050	311+330	RHS	MCW	CA	M	Done	IE
196	VKE-3/PIL/HW/754	03:00PM	16-Apr-19		FDD Checking of Embankment 5th Layer	311+330	311+480	RHS	MCW	CA	M	Done	
197	VKE-3/PIL/HW/755	03:											

199	VKE-3/PIL/HW/757	05:00PM	16-Apr-19		FDD Checking of Embankment 2nd Layer	318+200	318+500	LHS	MCW	CA	M	Done	IE
200	VKE-3/PIL/HW/758	05:30PM	16-Apr-19		FDD Checking of Embankment 1st Layer	310+440	310+700	LHS	MCW	CA	M	Done	
201	VKE-3/PIL/HW/759	05:30PM	16-Apr-19		FDD Checking of Embankment 1st Layer	310+440	310+700	RHS	MCW	CA	M	FAIL	
202	VKE-3/PIL/HW/760	04:00PM	16-Apr-19		FDD Checking of Embankment 8th Layer	312+290	312+400	RHS	MCW	CA	M	Done	
203	VKE-3/PIL/HW/761	10:30AM	17-Apr-19		FDD Checking of Embankment 8th Layer	295+700	295+800	LHS	MCW	CA	M	Done	
204	VKE-3/PIL/HW/762	05:30PM	17-Apr-19		FDD Checking of Embankment 4th Layer	306+400	306+600	RHS	MCW	CA	M	Done	
205	VKE-3/PIL/HW/763	04:00PM	17-Apr-19		FDD Checking of Embankment 7th Layer	294+600	294+725	LHS	MCW	CA	M	N/R	
206	VKE-3/PIL/HW/764	05:00PM	17-Apr-19		FDD Checking of Embankment 8th Layer	295+000	295+150	LHS	MCW	CA	M	FAIL	
207	VKE-3/PIL/HW/765	06:00PM	17-Apr-19		FDD Checking of Embankment 2nd Layer	296+200	296+340	LHS	MCW	CA	M	N/R	
208	VKE-3/PIL/HW/766	05:30PM	17-Apr-19		FDD Checking of Embankment 9th Layer	296+600	296+800	LHS	MCW	CA	M	Done	
209	VKE-3/PIL/HW/767	12:00PM	17-Apr-19		FDD Checking of Embankment 11th Layer	298+000	298+100	LHS	MCW	CA	M	Done	
210	VKE-3/PIL/HW/768	03:00PM	17-Apr-19		FDD Checking of Embankment 4th Layer	298+000	298+350	RHS	MCW	CA	M	Done	
211	VKE-3/PIL/HW/769	10:15AM	17-Apr-19		FDD Checking of Embankment 7th Layer	302+150	302+300	RHS	MCW	CA	M	Done	
212	VKE-3/PIL/HW/770	11:30AM	17-Apr-19		FDD Checking of Embankment 7th Layer	302+300	302+500	RHS	MCW	CA	M	Done	
213	VKE-3/PIL/HW/771	05:20PM	17-Apr-19		FDD Checking of Embankment 6th Layer	302+500	302+600	LHS	MCW	CA	M	Done	
214	VKE-3/PIL/HW/772	05:40PM	17-Apr-19		FDD Checking of Embankment 6th Layer	302+500	302+600	RHS	MCW	CA	M	Done	
215	VKE-3/PIL/HW/773	11:00AM	17-Apr-19		FDD Checking of Embankment 16th Layer	303+500	303+600	LHS	MCW	CA	M	Done	
216	VKE-3/PIL/HW/774	06:00PM	17-Apr-19		FDD Checking of Embankment 1st Layer	310+700	311+040	LHS	MCW	CA	M	FAIL	
217	VKE-3/PIL/HW/775	06:00PM	17-Apr-19		FDD Checking of Embankment 1st Layer	310+700	311+040	RHS	MCW	CA	M	Done	
218	VKE-3/PIL/HW/776	04:30PM	17-Apr-19		FDD Checking of Embankment 6th Layer	311+670	311+980	RHS	MCW	CA	M	Done	
219	VKE-3/PIL/HW/777	11:00AM	17-Apr-19		FDD Checking of Embankment 6th Layer	311+980	312+200	RHS	MCW	CA	M	Done	
220	VKE-3/PIL/HW/778	04:00PM	17-Apr-19		FDD Checking of Embankment 7th Layer	312+200	312+270	RHS	MCW	CA	M	Done	
221	VKE-3/PIL/HW/779	03:30PM	17-Apr-19		FDD Checking of Embankment 2nd Layer	318+100	318+200	LHS	MCW	CA	M	N/R	
222	VKE-3/PIL/HW/780	03:30PM	17-Apr-19		FDD Checking of Embankment 2nd Layer	318+100	318+200	RHS	MCW	CA	M	Done	
223	VKE-3/PIL/HW/781	04:00PM	17-Apr-19		FDD Checking of Embankment 4th Layer	308+900	309+000	RHS	MCW	CA	M	Done	
224	VKE-3/PIL/HW/782	05:30PM	17-Apr-19		FDD Checking of Embankment 5th Layer	313+450	313+800	LHS	MCW	CA	M	Done	
225	VKE-3/PIL/HW/783	03:00PM	17-Apr-19		FDD Checking of Embankment 1st Layer	319+300	319+400	LHS	MCW	CA	M	Done	
226	VKE-3/PIL/HW/784	04:00PM	18-Apr-19		FDD Checking of Embankment 2nd Layer	296+200	296+340	LHS	MCW	CA	M	Done	
227	VKE-3/PIL/HW/785	02:00PM	18-Apr-19		FDD Checking of Embankment 8th Layer	295+000	295+150	LHS	MCW	CA	M	FAIL	
228	VKE-3/PIL/HW/786	12:30PM	18-Apr-19		FDD Checking of Embankment 4th Layer	298+400	298+500	LHS	MCW	CA	M	Done	
229	VKE-3/PIL/HW/787	04:00PM	18-Apr-19		FDD Checking of Embankment 5th Layer	298+500	298+700	LHS	MCW	CA	M	N/R	
230	VKE-3/PIL/HW/788	10:15AM	18-Apr-19		FDD Checking of Embankment 7th Layer	302+200	302+300	LHS	MCW	CA	M	Done	IE
231	VKE-3/PIL/HW/789	11:30AM	18-Apr-19		FDD Checking of Embankment 8th Layer	302+300	302+500	LHS	MCW	CA	M	Done	
232	VKE-3/PIL/HW/790	05:45PM	18-Apr-19		FDD Checking of Embankment 2nd Layer	301+940	302+100	LHS	MCW	CA	M	Done	
233	VKE-3/PIL/HW/791	06:00PM	18-Apr-19		FDD Checking of Embankment 4th Layer	306+800	307+000	RHS	MCW	CA	M	Done	
234	VKE-3/PIL/HW/792	06:00PM	18-Apr-19		FDD Checking of Embankment 5th Layer	311+050	311+330	RHS	MCW	CA	M	Done	
235	VKE-3/PIL/HW/793	06:00PM	18-Apr-19		FDD Checking of Embankment 6th Layer	311+330	311+650	RHS	MCW	CA	M	Done	
236	VKE-3/PIL/HW/794	04:30PM	18-Apr-19		FDD Checking of Embankment 10th Layer	312+500	312+670	LHS	MCW	CA	M	Done	
237	VKE-3/PIL/HW/795	04:30PM	18-Apr-19		FDD Checking of Embankment 10th Layer	312+500	312+670	RHS	MCW	CA	M	Done	
238	VKE-3/PIL/HW/796	11:00AM	18-Apr-19		FDD Checking of Embankment 2nd Layer	317+900	318+100	LHS	MCW	CA	M	Done	
239	VKE-3/PIL/HW/797	04:00PM	18-Apr-19		FDD Checking of Embankment 10th Layer	313+860	314+120	LHS	MCW	CA	M	Done	
240	VKE-3/PIL/HW/798	03:30PM	18-Apr-19		FDD Checking of Embankment 8th Layer	321+720	321+900	LHS	MCW	CA	M	N/R	
241	VKE-3/PIL/HW/799	03:30PM	18-Apr-19		FDD Checking of Embankment 8th Layer	321+900	322+100	LHS	MCW	CA	M	Done	
242	VKE-3/PIL/HW/800	04:00PM	18-Apr-19		FDD Checking of Embankment 7th Layer	322+300	322+400	RHS	MCW	CA	M	Done	
243	VKE-3/PIL/HW/786	12:30PM	19-Apr-19		FDD Checking of Embankment 4th Layer	298+400	298+500	RHS	MCW	CA	M	Repeat RFI(DONE)	
244	VKE-3/PIL/HW/787	04:00PM	19-Apr-19		FDD Checking of Embankment 5th Layer	298+500	298+700	RHS	MCW	CA	M	Repeat RFI(DONE)	
245	VKE-3/PIL/HW/801	04:30PM	19-Apr-19		FDD Checking of Embankment 8th Layer	295+700	295+800	LHS	MCW	CA	M	Done	
246	VKE-3/PIL/HW/802	03:30PM	19-Apr-19		FDD Checking of Embankment 5th Layer	306+400	306+500	LHS	MCW	CA	M	Fail	
247	VKE-3/PIL/HW/803	10:30AM	19-Apr-19		FDD Checking of Embankment 7th Layer	294+600	294+725	LHS	MCW	CA	M	Done	
248	VKE-3/PIL/HW/804	04:45PM	19-Apr-19		FDD Checking of Embankment 8th Layer	295+000	295+150	LHS	MCW	CA	M	Done	
249	VKE-3/PIL/HW/805	11:00AM	19-Apr-19		FDD Checking of Embankment 6th Layer	302+500	302+600	LHS	MCW	CA	M	Done	
250	VKE-3/PIL/HW/806	11:20AM	19-Apr-19		FDD Checking of Embankment 6th Layer	302+500	302+600	RHS	MCW	CA	M	Done	
251	VKE-3/PIL/HW/807	03:00PM	19-Apr-19		FDD Checking of Embankment 8th Layer	295+900	296+000	LHS	MCW	CA	M	Done	
252	VKE-3/PIL/HW/808	11:30AM	19-Apr-19		FDD Checking of Embankment 7th Layer	294+730	294+800	LHS	MCW	CA	M	Done	
253	VKE-3/PIL/HW/809	11:00AM	19-Apr-19		FDD Checking of Embankment 3rd Layer	296+700	296+800	RHS	MCW	CA	M	Done	
254	VKE-3/PIL/HW/810	02:30PM	19-Apr-19		FDD Checking of Embankment 4th Layer	297+160	297+260	RHS	MCW	CA	M	Done	
255	VKE-3/PIL/HW/811	12:00PM	19-Apr-19		FDD Checking of Embankment 8th Layer	297+000	297+200	LHS	MCW	CA	M	Done	
256	VKE-3/PIL/HW/812	02:00PM	19-Apr-19		FDD Checking of Embankment 4th Layer	298+160	298+350	RHS	MCW	CA	M	Done	
257	VKE-3/PIL/HW/813	05:00PM	19-Apr-19		FDD Checking of Embankment 4th Layer	298+700	298+800	RHS	MCW	CA	M	Done	
258	VKE-3/PIL/HW/814	04:30PM	19-Apr-19		FDD Checking of Embankment 8th Layer	302+150	302+300	RHS	MCW	CA	M	Done	
259	VKE-3/PIL/HW/815	05:30PM	19-Apr-19		FDD Checking of Embankment 8th Layer	302+300	302+500	RHS	MCW	CA	M	Done	
260	VKE-3/PIL/HW/816	05:00PM	19-Apr-19		FDD Checking of Embankment 3rd Layer	306+400	306+700	RHS	MCW	CA	M	Done	
261	VKE-3/PIL/HW/817	06:00PM	19-Apr-19		FDD Checking of Embankment 9th Layer	312+290	312+400	RHS	MCW	CA	M	Done	
262	VKE-3/PIL/HW/818	04:30PM	19-Apr-19		FDD Checking of Embankment 10th Layer	312+400	312+500	RHS	MCW	CA	M	Done	
263	VKE-3/PIL/HW/819	11:00AM	19-Apr-19		FDD Checking of Embankment 13th Layer	311+670	311+980	LHS	MCW	CA	M	Done	
264	VKE-3/PIL/HW/820	04:00PM	19-Apr-19		FDD Checking of Embankment 7th Layer	322+160	322+400	LHS	MCW	CA	M	Done	
265	VKE-3/PIL/HW/821	03:30PM	19-Apr-19		FDD Checking of Embankment 2nd Layer	317+900	318+100	RHS	MCW	CA	M	Fail	
266	VKE-3/PIL/HW/822	04:00PM	19-Apr-19		FDD Checking of Embankment 10th Layer	314+150	314+280	LHS	MCW	CA	M	Done	
267	VKE-3/PIL/HW/823	05:00PM	20-Apr-19		FDD Checking of Embankment 2nd Layer	296+000	296+200	RHS	MCW	CA	M	Done	ie
268	VKE-3/PIL/HW/824	11:00AM	20-Apr-19		FDD Checking of Embankment 3rd Layer	297+000	297+160	RHS	MCW	CA	M	Done	
269	VKE-3/PIL/HW/825	10:00AM	20-Apr-19		FDD Checking of Embankment 4th Layer	297+200	297+300	RHS	MCW	CA	M	Done	ie
270	VKE-3/PIL/HW/826	04:00PM	20-Apr-19		FDD Checking of Embankment 8th Layer	297+200	297+360	LHS	MCW	CA	M	Done	
271	VKE-3/PIL/HW/827	02:30PM	20-Apr-19		FDD Checking of Embankment 2nd Layer	298+820	298+940	RHS	MCW	CA	M	Done	
272	VKE-3/PIL/HW/828	03:00PM	20-Apr-19		FDD Checking of Embankment 5th Layer	298+400	298+500	RHS	MCW	CA	M	Done	
273	VKE-3/PIL/HW/829	04:00PM	20-Apr-19		FDD Checking of Embankment 12th Layer	298+000	298+100	LHS	MCW	CA	M	Done	
274	VKE-3/PIL/HW/830	05:30PM	20-Apr-19		FDD Checking of Embankment 7th Layer	302+500	302+600	LHS	MCW	CA	M	Done	
275	VKE-3/PIL/HW/831	05:45PM	20-Apr-19		FDD Checking of Embankment 7th Layer	302+500	302+600	RHS	MCW	CA	M	Done	
276	VKE-3/PIL/HW/832	10:00AM	20-Apr-19		FDD Checking of Embankment 2nd Layer	296+000	296+200	LHS	MCW	CA	M	Done	
277	VKE-3/PIL/HW/833	11:00AM	20-Apr-19		FDD Checking of Embankment 8th Layer	302+300	302+500	LHS	MCW	CA	M	Done	
278	VKE-3/PIL/HW/834	05:30PM	20-Apr-19		FDD Checking of Embankment 5th Layer	306+800	307+000	LHS	MCW	CA	M	Done	
279	VKE-3/PIL/HW/835	05:00PM	20-Apr-19		FDD Checking of Embankment 2nd Layer	301+940	302+100	RHS	MCW	CA	M	Done	
280	VKE-3/PIL/HW/836	10:30AM	20-Apr-19		FDD Checking of Embankment 8th Layer	295+800	295+900	LHS	MCW	CA	M	Done	
281	VKE-3/PIL/HW/837	10:40AM	20-Apr-19		FDD Checking of Embankment 8th Layer	321+900	322+100	LHS	MCW	CA	M	Done	
282	VKE-3/PIL/HW/838	11:50AM	20-Apr-19		FDD Checking of Embankment 2nd Layer	310+440	310+700	LHS	MCW	CA	M	Done	ie
283	VKE-3/PIL/HW/839	12:00PM	20-Apr-19		FDD Checking of Embankment 2nd Layer	310+440	310+700	RHS	MCW	CA	M	Done	
284	VKE-3/PIL/HW/840	03:30PM	20-Apr-19		FDD Checking of Embankment 2nd Layer	317+700	317+900	RHS	MCW	CA	M	Done	
285	VKE-3/PIL/HW/841	04:00PM	20-Apr-19		FDD Checking of Embankment 2nd Layer	309+570	309+700	LHS	MCW	CA	M	N/R	ie
286	VKE-3/PIL/HW/842	04:30PM	20-Apr-19		FDD Checking of Embankment 2nd Layer	309+570	309+700	RHS	MCW	CA	M	N/R	ie
287	VKE-3/PIL/HW/843	05:00PM	20-Apr-19		FDD Checking of Embankment 9th Layer	314+350	314+660	LHS	MCW	CA	M	Done	
288	VKE-3/PIL/HW/844	10:00AM	20-Apr-19		FDD Checking of Embankment 4th Layer	308+800	308+900	RHS	MCW	CA	M	Done	
289	VKE-3/PIL/HW/845	11:00AM	20-Apr-19		FDD Checking of Embankment 5th Layer	308+900	309+000	RHS	MCW	CA	M	Done	
290	VKE-3/PIL/HW/846	08:00AM	20-Apr-19		FDD Checking of Embankment 17th Layer	308+500	308+700	LHS	MCW	CA	M	Done	
291	VKE-3/PIL/HW/847	08:30AM	20-Apr-19		FDD Checking of Embankment 6th Layer	311+480	311+650	RHS	MCW	CA	M	Fail	
292	VKE-3/PIL/HW/848	04:30PM	20-Apr-19		FDD Checking of Embankment 4th Layer	308+500	308+800	RHS	MCW	CA	M	Done	
293	VKE-3/PIL/HW/849	11:30AM	21-Apr-19		FDD Checking of Embankment 7th Layer	302+200	302+300	LHS	MCW	CA	M	Done	
294	VKE-3/PIL/HW/850	11:00AM	21-Apr-19		FDD Checking of Embankment 7th Layer	294+600	294+725	LHS	MCW	CA	M	Done	
295	VKE-3/PIL/HW/851	0											

297	VKE-3/PIL/HW/853	02:00PM	21-Apr-19		FDD Checking of Embankment 3rd Layer	295+000	295+150	RHS	MCW	CA	M	Done	
298	VKE-3/PIL/HW/854	02:15PM	21-Apr-19		FDD Checking of Embankment 2nd Layer	296+200	296+340	RHS	MCW	CA	M	Done	
299	VKE-3/PIL/HW/855	02:30PM	21-Apr-19		FDD Checking of Embankment 3rd Layer	296+700	296+800	RHS	MCW	CA	M	Done	
300	VKE-3/PIL/HW/856	12:00PM	21-Apr-19		FDD Checking of Embankment 4th Layer	297+000	297+160	RHS	MCW	CA	M	Done	
301	VKE-3/PIL/HW/857	04:00PM	21-Apr-19		FDD Checking of Embankment 9th Layer	296+800	297+000	LHS	MCW	CA	M	Done	
302	VKE-3/PIL/HW/858	04:15PM	21-Apr-19		FDD Checking of Embankment 2nd Layer	296+800	296+900	RHS	MCW	CA	M	Done	
303	VKE-3/PIL/HW/859	05:15PM	21-Apr-19		FDD Checking of Embankment 12th Layer	298+120	298+350	LHS	MCW	CA	M	Done	
304	VKE-3/PIL/HW/860	05:30PM	21-Apr-19		FDD Checking of Embankment 9th Layer	302+300	302+500	LHS	MCW	CA	M	Done	
305	VKE-3/PIL/HW/861	11:45AM	21-Apr-19		FDD Checking of Embankment 4TH Layer	301+940	302+100	RHS	MCW	CA	M	Done	
306	VKE-3/PIL/HW/862	12:15PM	21-Apr-19		FDD Checking of Embankment 4TH Layer	301+940	302+100	LHS	MCW	CA	M	Done	
307	VKE-3/PIL/HW/863	05:45PM	21-Apr-19		FDD Checking of Embankment 9th Layer	304+680	305+050	LHS	MCW	CA	M	N/R	
308	VKE-3/PIL/HW/864	03:30PM	21-Apr-19		FDD Checking of Embankment 5th Layer	306+800	306+950	LHS	MCW	CA	M	Done	
309	VKE-3/PIL/HW/865	10:30AM	21-Apr-19		FDD Checking of Embankment 1st & 2nd Layer for HPC backfill	303+605		BHS	MCW	CA	M		
310	VKE-3/PIL/HW/866	02:30PM	21-Apr-19		Checking of Sand Filling 1st Layer Beside HPC	303+605		BHS	MCW	CA	M	HPC	
311	VKE-3/PIL/HW/867	04:30PM	21-Apr-19		FDD Checking of Embankment 2nd Layer	298+940	299+050	RHS	MCW	CA	M	Done	
312	VKE-3/PIL/HW/868	05:00PM	21-Apr-19		FDD Checking of Embankment 2nd Layer	297+260	297+360	RHS	MCW	CA	M	FAIL	
313	VKE-3/PIL/HW/869	11:30AM	21-Apr-19		FDD Checking of Embankment 2nd Layer	296+200	296+340	RHS	MCW	CA	M	Done	
314	VKE-3/PIL/HW/870	12:00PM	21-Apr-19		FDD Checking of Embankment 12th Layer	298+120	298+350	LHS	MCW	CA	M	Done	
315	VKE-3/PIL/HW/871	04:00PM	21-Apr-19		FDD Checking of Embankment 5th Layer	298+300	298+350	RHS	MCW	CA	M	Done	
316	VKE-3/PIL/HW/872	04:30PM	21-Apr-19		FDD Checking of Embankment 3rd Layer	310+700	311+040	LHS	MCW	CA	M	Done	
317	VKE-3/PIL/HW/873	04:45PM	21-Apr-19		FDD Checking of Embankment 8th Layer	314+690	314+800	LHS	MCW	CA	M	N/R	
318	VKE-3/PIL/HW/874	05:00PM	21-Apr-19		FDD Checking of Embankment 2nd Layer	317+700	317+900	LHS	MCW	CA	M	Done	
319	VKE-3/PIL/HW/875	06:00PM	21-Apr-19		FDD Checking of Embankment 1st Layer	319+200	319+300	LHS	MCW	CA	M	N/R	
320	VKE-3/PIL/HW/876	04:00PM	21-Apr-19		FDD Checking of Embankment 9th Layer	321+720	321+900	RHS	MCW	CA	M	Done	
321	VKE-3/PIL/HW/877	03:30PM	21-Apr-19		FDD Checking of Embankment 9th Layer	321+900	322+100	RHS	MCW	CA	M	Done	
322	VKE-3/PIL/HW/878	05:30PM	21-Apr-19		FDD Checking of Embankment 5th Layer	322+100	322+150	LHS	MCW	CA	M	Done	
323	VKE-3/PIL/HW/879	04:30PM	21-Apr-19		FDD Checking of Embankment 5th Layer	308+500	308+800	LHS	MCW	CA	M	Done	
324	VKE-3/PIL/HW/880	05:00PM	22-Apr-19		FDD Checking of Embankment 7th Layer	294+800	294+980	LHS	MCW	CA	M	Done	
325	VKE-3/PIL/HW/881	12:30PM	22-Apr-19		FDD Checking of Embankment 5th Layer	306+950	307+000	LHS	MCW	CA	M	FAIL	
326	VKE-3/PIL/HW/882	04:00PM	22-Apr-19		FDD Checking of Embankment 2nd Layer	295+170	295+240	RHS	MCW	CA	M	Done	
327	VKE-3/PIL/HW/883	11:30AM	22-Apr-19		FDD Checking of Embankment 5th Layer	298+400	298+500	RHS	MCW	CA	M	Done	
328	VKE-3/PIL/HW/884	04:30PM	22-Apr-19		FDD Checking of Embankment 5th Layer	298+120	298+300	RHS	MCW	CA	M	Done	
329	VKE-3/PIL/HW/885	10:30AM	22-Apr-19		FDD Checking of Embankment 9th Layer	302+150	302+500	RHS	MCW	CA	M	Done	ie
330	VKE-3/PIL/HW/886	11:30AM	22-Apr-19		FDD Checking of Embankment 9th Layer	302+150	302+500	RHS	MCW	CA	M	Done	
331	VKE-3/PIL/HW/887	05:30PM	22-Apr-19		FDD Checking of Embankment 7th Layer	302+200	302+300	LHS	MCW	CA	M	Done	
332	VKE-3/PIL/HW/888	10:00AM	22-Apr-19		FDD Checking of Embankment 3rd Layer	306+700	307+000	RHS	MCW	CA	M	N/R	ie
333	VKE-3/PIL/HW/889	12:00PM	22-Apr-19		FDD Checking of Embankment 2nd Layer	297+260	297+360	RHS	MCW	CA	M	N/R	
334	VKE-3/PIL/HW/890	11:00AM	22-Apr-19		FDD Checking of Embankment 2nd Layer	296+900	297+000	RHS	MCW	CA	M	Done	
335	VKE-3/PIL/HW/891	10:00AM	22-Apr-19		FDD Checking of Embankment 1st Layer for HPC backfilling	303+608		BHS	MCW	CA	M		
336	VKE-3/PIL/HW/892	11:00AM	22-Apr-19		FDD Checking of Embankment 2nd Layer for HPC backfilling	303+608		BHS	MCW	CA	M		
337	VKE-3/PIL/HW/893	10:00AM	22-Apr-19		Checking of Sand Filling 1st Layer Beside HPC	303+808		BHS	MCW	CA	M	HPC	
338	VKE-3/PIL/HW/894	04:00PM	22-Apr-19		Checking of Sand Filling 2nd Layer Beside HPC	303+808		BHS	MCW	CA	M	HPC	
339	VKE-3/PIL/HW/895	03:00PM	22-Apr-19		FDD Checking of Embankment 6th Layer	308+500	308+800	RHS	MCW	CA	M	Done	
340	VKE-3/PIL/HW/896	05:30PM	22-Apr-19		FDD Checking of Embankment 6th Layer	308+900	309+000	RHS	MCW	CA	M	Done	
341	VKE-3/PIL/HW/897	05:30PM	22-Apr-19		FDD Checking of Embankment 2nd Layer	309+560	309+700	LHS	MCW	CA	M	Done	ie
342	VKE-3/PIL/HW/898	05:30PM	22-Apr-19		FDD Checking of Embankment 2nd Layer	309+560	309+700	RHS	MCW	CA	M	Done	ie
343	VKE-3/PIL/HW/899	04:00PM	22-Apr-19		FDD Checking of Embankment 6th Layer	311+050	311+330	RHS	MCW	CA	M	Done	ie
344	VKE-3/PIL/HW/900	05:00PM	22-Apr-19		FDD Checking of Embankment 7th Layer	311+330	311+650	RHS	MCW	CA	M	Done	
345	VKE-3/PIL/HW/901	06:00PM	22-Apr-19		FDD Checking of Embankment 13th Layer	311+670	311+980	LHS	MCW	CA	M	Done	
346	VKE-3/PIL/HW/902	04:00PM	22-Apr-19		FDD Checking of Embankment 3rd Layer	318+300	318+500	LHS	MCW	CA	M	Done	
347	VKE-3/PIL/HW/903	03:30PM	22-Apr-19		FDD Checking of Embankment 6th Layer	313+450	313+800	LHS	MCW	CA	M	Done	
348	VKE-3/PIL/HW/904	03:00PM	22-Apr-19		FDD Checking of Embankment 9th Layer	321+720	321+900	LHS	MCW	CA	M	Done	
349	VKE-3/PIL/HW/905	04:00PM	22-Apr-19		FDD Checking of Embankment 9th Layer	321+900	322+100	LHS	MCW	CA	M	Done	ie
350	VKE-3/PIL/HW/906	04:00PM	22-Apr-19		FDD Checking of Embankment 7th Layer	322+100	322+160	LHS	MCW	CA	M	Done	
351	VKE-3/PIL/HW/907	04:30PM	22-Apr-19		FDD Checking of Embankment 7th Layer	322+100	322+300	RHS	MCW	CA	M	Done	ie
352	VKE-3/PIL/HW/908	03:00PM	22-Apr-19		FDD Checking of Embankment 7th Layer	320+000	320+200	LHS	MCW	CA	M	Done	
353	VKE-3/PIL/HW/909	09:30AM	23-Apr-19		FDD Checking of Embankment 12th Layer	298+120	298+350	LHS	MCW	CA	M	Done	
354	VKE-3/PIL/HW/910	10:00AM	23-Apr-19		FDD Checking of Embankment 17th Layer	298+120	298+200	LHS	MCW	CA	M	Done	
355	VKE-3/PIL/HW/911	05:00PM	23-Apr-19		FDD Checking of Embankment 3rd Layer	298+950	299+050	RHS	MCW	CA	M	Done	ie
356	VKE-3/PIL/HW/912	04:00PM	23-Apr-19		FDD Checking of Embankment 2nd Layer	295+240	295+380	RHS	MCW	CA	M	Done	ie
357	VKE-3/PIL/HW/913	05:15PM	23-Apr-19		FDD Checking of Embankment 3rd Layer	296+000	296+340	RHS	MCW	CA	M	N/R	
358	VKE-3/PIL/HW/914	05:30PM	23-Apr-19		FDD Checking of Embankment 3rd Layer	296+500	296+600	RHS	MCW	CA	M	Done	
359	VKE-3/PIL/HW/915	02:40PM	23-Apr-19		FDD Checking of Embankment 5th Layer	298+000	298+100	RHS	MCW	CA	M	Done	
360	VKE-3/PIL/HW/916	04:30PM	23-Apr-19		FDD Checking of Embankment 13th Layer	298+000	298+100	LHS	MCW	CA	M	Done	
361	VKE-3/PIL/HW/917	10:30AM	23-Apr-19		FDD Checking of Embankment 8th Layer	302+200	302+300	LHS	MCW	CA	M	Done	
362	VKE-3/PIL/HW/918	11:30AM	23-Apr-19		FDD Checking of Embankment 10th Layer	302+300	302+500	LHS	MCW	CA	M	Done	
363	VKE-3/PIL/HW/919	05:30PM	23-Apr-19		FDD Checking of Embankment 10th Layer	302+150	302+300	RHS	MCW	CA	M	Done	
364	VKE-3/PIL/HW/920	05:00PM	23-Apr-19		FDD Checking of Embankment 8th Layer	302+500	302+600	LHS	MCW	CA	M	Done	
365	VKE-3/PIL/HW/921	06:00PM	23-Apr-19		FDD Checking of Embankment 8th Layer	302+500	302+600	RHS	MCW	CA	M	Done	
366	VKE-3/PIL/HW/922	03:00PM	23-Apr-19		FDD Checking of Embankment 3rd Layer	295+000	295+150	RHS	MCW	CA	M	N/R	
367	VKE-3/PIL/HW/923	04:00PM	23-Apr-19		FDD Checking of Embankment 3rd Layer	306+700	307+000	RHS	MCW	CA	M	N/R	ie
368	VKE-3/PIL/HW/924	10:00AM	23-Apr-19		FDD Checking of Embankment 1st Layer for HPC backfilling	303+608		BHS	MCW	CA	M		
369	VKE-3/PIL/HW/925	11:00AM	23-Apr-19		FDD Checking of Embankment 2nd Layer for HPC backfilling	303+608		BHS	MCW	CA	M		
370	VKE-3/PIL/HW/926	10:00AM	23-Apr-19		Checking of Sand Filling 1st Layer Beside HPC	303+808		BHS	MCW	CA	M	HPC	
371	VKE-3/PIL/HW/927	04:00PM	23-Apr-19		Checking of Sand Filling 2nd Layer Beside HPC	303+808		BHS	MCW	CA	M	HPC	
372	VKE-3/PIL/HW/928	12:00PM	23-Apr-19		FDD Checking of Embankment 7th Layer	308+500	308+800	RHS	MCW	CA	M	Done	
373	VKE-3/PIL/HW/929	02:00PM	23-Apr-19		FDD Checking of Embankment 5th Layer	308+800	308+900	RHS	MCW	CA	M	Done	
374	VKE-3/PIL/HW/930	05:00PM	23-Apr-19		FDD Checking of Embankment 7th Layer	308+900	309+000	RHS	MCW	CA	M	Done	
375	VKE-3/PIL/HW/931	04:00PM	23-Apr-19		FDD Checking of Embankment 7th Layer	311+670	311+980	RHS	MCW	CA	M	Done	ie
376	VKE-3/PIL/HW/932	05:00PM	23-Apr-19		FDD Checking of Embankment 7th Layer	311+980	312+200	RHS	MCW	CA	M	Done	ie
377	VKE-3/PIL/HW/933	06:00PM	23-Apr-19		FDD Checking of Embankment 8th Layer	312+200	312+270	RHS	MCW	CA	M	Done	ie
378	VKE-3/PIL/HW/934	04:30PM	23-Apr-19		FDD Checking of Embankment 2nd Layer	310+700	311+040	RHS	MCW	CA	M	Done	
379	VKE-3/PIL/HW/935	04:00PM	23-Apr-19		FDD Checking of Embankment 3rd Layer	318+300	318+400	LHS	MCW	CA	M	Done	
380	VKE-3/PIL/HW/936	04:00PM	23-Apr-19		FDD Checking of Embankment 8th Layer	312+720	313+080	LHS	MCW	CA	M	Done	
381	VKE-3/PIL/HW/937	03:00PM	23-Apr-19		FDD Checking of Embankment 7th Layer	319+900	320+000	LHS	MCW	CA	M	Done	
382	VKE-3/PIL/HW/938	03:30PM	23-Apr-19		FDD Checking of Embankment 6th Layer	319+800	319+900	LHS	MCW	CA	M	Done	
383	VKE-3/PIL/HW/939	06:00PM	23-Apr-19		FDD Checking of Embankment 7th Layer	322+100	322+160	RHS	MCW	CA	M	FAIL	
384	VKE-3/PIL/HW/940	4:00 PM	24-Apr-19		FDD Checking of Embankment 10th Layer	312+290	312+400	RHS	MCW	CA	M	Done	
385	VKE-3/PIL/HW/941	5:00 PM	24-Apr-19		FDD Checking of Embankment 11th Layer	312+400	312+500	RHS	MCW	CA	M	Done	
386	VKE-3/PIL/HW/942	6:00 PM	24-Apr-19		FDD Checking of Embankment 11th Layer	312+500	312+670	LHS	MCW	CA	M	Done	
387	VKE-3/PIL/HW/943	6:00 PM	24-Apr-19		FDD Checking of Embankment 11th Layer	312+500	312+670	RHS	MCW	CA	M	Done	
388	VKE-3/PIL/HW/944	11:00 AM	24-Apr-19		FDD Checking of Embankment 10th Layer	321+720	321+900	RHS	MCW	CA	M	FAIL	
389	VKE-3/PIL/HW/945	4:00 PM	24-Apr-19		FDD Checking of Embankment 10th Layer	321+900	322+100	RHS	MCW	CA	M	Done	
390	VKE-3/PIL/HW/946	4:00 PM	24-Apr-19		FDD Checking of Embankment 8th Layer	322+300	322+400	RHS	MCW	CA	M	N/R	
391	VKE-3/PIL/HW/947	5:00 PM	24-Apr-19		FDD Checking of Embankment 3rd Layer	309+560	309+700	LHS	MCW	CA	M	Done	
392	VKE-3/PIL/HW/948	5:30 PM	24-Apr-19		FDD Checking of Embankment 3rd Layer	309+560	309+700	RHS	MCW	CA	M	Done	
393	VKE-3/PIL/HW/949	6:00 PM	24-Apr-19		FDD Checking of Embankment 8th Layer	3							

395	VKE-3/PIL/HW/951	4:00 PM	24-Apr-19		FDD Checking of Embankment 3rd Layer	317+900	318+300	LHS	MCW	CA	M	Done	ie
396	VKE-3/PIL/HW/952	4:30 PM	24-Apr-19		FDD Checking of Embankment 11th Layer	320+200	320+400	LHS	MCW	CA	M	N/R	
397	VKE-3/PIL/HW/953	10:00 PM	24-Apr-19		FDD Checking of Embankment 7th Layer	311+670	311+980	RHS	MCW	CA	M	Done	ie
398	VKE-3/PIL/HW/954	10:30 AM	24-Apr-19		FDD Checking of Embankment 2nd Layer	297+260	297+360	RHS	MCW	CA	M	Done	
399	VKE-3/PIL/HW/955	2:30 PM	24-Apr-19		FDD Checking of Embankment 3rd Layer	295+000	295+150	RHS	MCW	CA	M	N/R	
400	VKE-3/PIL/HW/956	10:00 AM	24-Apr-19		FDD Checking of Embankment 3rd Layer	306+700	307+000	RHS	MCW	CA	M	Done	ie
401	VKE-3/PIL/HW/957	10:00 AM	24-Apr-19		Excavation for Filling soil upto Cradde top of HPC	303+608		BHS	MCW	CA	M	HPC	
402	VKE-3/PIL/HW/958	11:30 AM	24-Apr-19		FDD Checking of Embankment 1st Layer with sand filling around	303+608		BHS	MCW	CA	M	HPC	
403	VKE-3/PIL/HW/959	2:30 PM	24-Apr-19		FDD Checking of Embankment 2nd Layer with sand filling around	303+608		BHS	MCW	CA	M	HPC	
404	VKE-3/PIL/HW/960	5:00 PM	24-Apr-19		FDD Checking of Embankment 3rd Layer with sand filling around	303+608		BHS	MCW	CA	M	HPC	
405	VKE-3/PIL/HW/961	4:00 PM	24-Apr-19		FDD Checking of Embankment 3rd Layer	295+570	295+700	RHS	MCW	CA	M	FAIL	
406	VKE-3/PIL/HW/962	4:30 PM	24-Apr-19		FDD Checking of Embankment 3rd Layer	296+600	296+700	RHS	MCW	CA	M	Done	
407	VKE-3/PIL/HW/963	3:30 PM	24-Apr-19		FDD Checking of Embankment 3rd Layer	296+800	296+900	RHS	MCW	CA	M	Done	ie
408	VKE-3/PIL/HW/964	12:00 PM	24-Apr-19		FDD Checking of Embankment 13th Layer	298+120	298+350	LHS	MCW	CA	M	Done	
409	VKE-3/PIL/HW/965	3:00 PM	24-Apr-19		FDD Checking of Embankment 5th Layer	298+700	298+800	RHS	MCW	CA	M	Done	
410	VKE-3/PIL/HW/966	5:50 PM	24-Apr-19		FDD Checking of Embankment 10th Layer	302+300	302+500	RHS	MCW	CA	M	FAIL	
411	VKE-3/PIL/HW/967	6:30 PM	24-Apr-19		FDD Checking of Embankment 2nd Layer	305+550	305+750	LHS	MCW	CA	M	N/R	ie
412	VKE-3/PIL/HW/968	11:00 AM	24-Apr-19		FDD Checking of Embankment 3rd Layer	306+700	307+000	RHS	MCW	CA	M	Done	
413	VKE-3/PIL/HW/969	4:30 PM	24-Apr-19		FDD Checking of Embankment 9th Layer	304+680	605+050	LHS	MCW	CA	M	Done	
414	VKE-3/PIL/HW/970	11:00 AM	24-Apr-19		Resampling of Borrow Area No.10-B	302+400		RHS		CA	M	FAIL	
415	VKE-3/PIL/HW/971	3:30 PM	24-Apr-19		FDD Checking of Embankment 6th Layer	298+000	298+120	RHS	MCW	CA	M	Done	
416	VKE-3/PIL/HW/972	4:00 PM	24-Apr-19		FDD Checking of Embankment 6th Layer	298+400	298+590	RHS	MCW	CA	M	N/R	
417	VKE-3/PIL/HW/973	6:00 PM	24-Apr-19		FDD Checking of Embankment 6th Layer	298+600	298+700	RHS	MCW	CA	M	Done	
418	VKE-3/PIL/HW/974	5:50 PM	24-Apr-19		FDD Checking of Embankment 4th Layer	298+820	299+050	RHS	MCW	CA	M	Done	
419	VKE-3/PIL/HW/975	4:45 PM	24-Apr-19		FDD Checking of Embankment 16th Layer	303+610	303+780	LHS	MCW	CA	M	FAIL	
420	VKE-3/PIL/HW/976	3:50 PM	24-Apr-19		FDD Checking of Embankment 12th Layer	303+820	304+000	LHS	MCW	CA	M	Done	
421	VKE-3/PIL/HW/977	5:00 PM	24-Apr-19		FDD Checking of Embankment 8th Layer	303+820	304+000	RHS	MCW	CA	M	Done	
422	VKE-3/PIL/HW/978	5:30 PM	25-Apr-19		FDD Checking of Embankment 3rd Layer	310+440	310+700	LHS	MCW	CA	M	Done	
423	VKE-3/PIL/HW/979	5:30 PM	25-Apr-19		FDD Checking of Embankment 3rd Layer	310+440	310+700	RHS	MCW	CA	M	Done	
424	VKE-3/PIL/HW/980	11:00 AM	25-Apr-19		FDD Checking of Embankment 8th Layer	322+160	322+400	LHS	MCW	CA	M	Done	
425	VKE-3/PIL/HW/981	11:00 AM	25-Apr-19		FDD Checking of Embankment 8th Layer	322+300	322+400	RHS	MCW	CA	M	Done	
426	VKE-3/PIL/HW/982	4:00 PM	25-Apr-19		FDD Checking of Embankment 10th Layer	321+900	322+100	LHS	MCW	CA	M	Done	
427	VKE-3/PIL/HW/983	3:00 PM	25-Apr-19		FDD Checking of Embankment 3rd Layer	318+500	318+560	LHS	MCW	CA	M	Done	
428	VKE-3/PIL/HW/984	3:00 PM	25-Apr-19		FDD Checking of Embankment 3rd Layer	318+500	318+560	RHS	MCW	CA	M	Done	
429	VKE-3/PIL/HW/985	3:00 PM	25-Apr-19		FDD Checking of Embankment 7th Layer	313+450	313+800	LHS	MCW	CA	M	Done	ie
430	VKE-3/PIL/HW/986	4:00 PM	25-Apr-19		FDD Checking of Embankment 6th Layer	308+800	308+900	RHS	MCW	CA	M	Done	
431	VKE-3/PIL/HW/987	5:30 PM	25-Apr-19		FDD Checking of Embankment 8th Layer	308+500	308+800	RHS	MCW	CA	M	N/R	ie
432	VKE-3/PIL/HW/988	5:30 PM	25-Apr-19		FDD Checking of Embankment 11th Layer	320+400	320+500	LHS	MCW	CA	M	Done	
433	VKE-3/PIL/HW/989	6:00 PM	25-Apr-19		FDD Checking of Embankment 9th Layer	320+500	320+600	LHS	MCW	CA	M	Done	
434	VKE-3/PIL/HW/990	4:00 PM	25-Apr-19		FDD Checking of Embankment 6th Layer	298+120	298+350	RHS	MCW	CA	M	Done	ie
435	VKE-3/PIL/HW/991	2:00 PM	25-Apr-19		FDD Checking of Embankment 9th Layer	302+200	302+300	LHS	MCW	CA	M	Done	
436	VKE-3/PIL/HW/992	4:00 PM	25-Apr-19		FDD Checking of Embankment 9th Layer	302+500	302+600	LHS	MCW	CA	M	Done	ie
437	VKE-3/PIL/HW/993	4:45 PM	25-Apr-19		FDD Checking of Embankment 9th Layer	302+500	302+600	RHS	MCW	CA	M	N/R	ie
438	VKE-3/PIL/HW/994	5:30 PM	25-Apr-19		FDD Checking of Embankment 5th Layer	301+940	302+100	LHS	MCW	CA	M	Done	
439	VKE-3/PIL/HW/995	6:30 PM	25-Apr-19		FDD Checking of Embankment 5th Layer	301+940	302+100	RHS	MCW	CA	M	Done	
440	VKE-3/PIL/HW/996	6:30 PM	25-Apr-19		FDD Checking of Embankment 2nd Layer	305+550	305+850	LHS	MCW	CA	M	Done	
441	VKE-3/PIL/HW/997	3:30 PM	25-Apr-19		FDD Checking of Embankment 6th Layer	298+000	298+100	RHS	MCW	CA	M	Done	
442	VKE-3/PIL/HW/998	4:00 PM	25-Apr-19		FDD Checking of Embankment 6th Layer	298+400	298+590	RHS	MCW	CA	M	Done	
443	VKE-3/PIL/HW/999	6:00 PM	25-Apr-19		FDD Checking of Embankment 6th Layer	298+610	298+700	RHS	MCW	CA	M	FAIL	
444	VKE-3/PIL/HW/1000	5:50 PM	25-Apr-19		FDD Checking of Embankment 4th Layer	298+820	299+050	RHS	MCW	CA	M	Done	
445	VKE-3/PIL/HW/1001	4:45 PM	25-Apr-19		FDD Checking of Embankment 16th Layer	303+610	303+780	LHS	MCW	CA	M	Done	
446	VKE-3/PIL/HW/1002	3:50 PM	25-Apr-19		FDD Checking of Embankment 12th Layer	303+820	304+000	LHS	MCW	CA	M	N/R	
447	VKE-3/PIL/HW/1003	5:00 PM	25-Apr-19		FDD Checking of Embankment 8th Layer	303+820	304+000	RHS	MCW	CA	M	N/R	
448	VKE-3/PIL/HW/1004	12:00 PM	26-Apr-19		FDD Checking of Embankment 13th Layer	298+120	298+350	LHS	MCW	CA	M	Done	
449	VKE-3/PIL/HW/1005	2:00 PM	26-Apr-19		FDD Checking of Embankment 3rd Layer	295+000	295+150	RHS	MCW	CA	M	Done	
450	VKE-3/PIL/HW/1006	3:00 PM	26-Apr-19		FDD Checking of Embankment 3rd Layer	295+570	295+700	RHS	MCW	CA	M	N/R	
451	VKE-3/PIL/HW/1007	4:00 PM	26-Apr-19		FDD Checking of Embankment 9th Layer	303+020	303+200	RHS	MCW	CA	M	Done	
452	VKE-3/PIL/HW/1008	4:15 PM	26-Apr-19		FDD Checking of Embankment 2nd Layer	293+500	293+700	RHS	MCW	CA	M	Done	ie
453	VKE-3/PIL/HW/1009	4:40 PM	26-Apr-19		FDD Checking of Embankment 3rd Layer	295+570	295+700	RHS	MCW	CA	M	N/R	
454	VKE-3/PIL/HW/1010	4:45 PM	26-Apr-19		FDD Checking of Embankment 6th Layer	296+500	296+700	RHS	MCW	CA	M	Done	ie
455	VKE-3/PIL/HW/1011	3:30 PM	26-Apr-19		FDD Checking of Embankment 14th Layer	298+000	298+100	LHS	MCW	CA	M	Done	
456	VKE-3/PIL/HW/1012	5:00 PM	26-Apr-19		FDD Checking of Embankment 11th Layer	298+400	298+500	LHS	MCW	CA	M	FAIL	
457	VKE-3/PIL/HW/1013	5:30 PM	26-Apr-19		FDD Checking of Embankment 7th Layer	298+120	298+350	RHS	MCW	CA	M	Done	
458	VKE-3/PIL/HW/1014	6:00 PM	26-Apr-19		FDD Checking of Embankment 5th Layer	298+700	298+800	RHS	MCW	CA	M	Done	
459	VKE-3/PIL/HW/1015	4:40 PM	26-Apr-19		FDD Checking of Embankment 10th Layer	302+500	302+570	RHS	MCW	CA	M	Done	
460	VKE-3/PIL/HW/1016	4:50 PM	26-Apr-19		FDD Checking of Embankment 10th Layer	302+500	302+570	LHS	MCW	CA	M	Done	ie
461	VKE-3/PIL/HW/1017	5:30 PM	26-Apr-19		FDD Checking of Embankment 3rd Layer	302+100	302+150	RHS	MCW	CA	M	Done	
462	VKE-3/PIL/HW/1018	5:15 PM	26-Apr-19		FDD Checking of Embankment 9th Layer	303+225	303+400	RHS	MCW	CA	M	Done	
463	VKE-3/PIL/HW/1019	5:00 PM	26-Apr-19		FDD Checking of Embankment 9th Layer	303+410	303+600	RHS	MCW	CA	M	Done	
464	VKE-3/PIL/HW/1020	6:00 PM	26-Apr-19		FDD Checking of Embankment 7th Layer	303+610	303+780	RHS	MCW	CA	M	Done	
465	VKE-3/PIL/HW/1021	11:00 AM	26-Apr-19		1st Layer of Backfilling with Sand around HPC	303+608		LHS	MCW	CA	M		
466	VKE-3/PIL/HW/1022	11:00 AM	26-Apr-19		1st Layer of Backfilling with Sand around HPC	303+608		RHS	MCW	CA	M	HPC	
467	VKE-3/PIL/HW/1023	4:00 PM	26-Apr-19		2nd Layer of Backfilling with Sand around HPC	303+608		LHS	MCW	CA	M		
468	VKE-3/PIL/HW/1024	4:00 PM	26-Apr-19		2nd Layer of Backfilling with Sand around HPC	303+608		RHS	MCW	CA	M		
469	VKE-3/PIL/HW/1025	12:00 PM	26-Apr-19		FDD Checking of Embankment 3rd Layer	317+700	317+900	LHS	MCW	CA	M	Done	
470	VKE-3/PIL/HW/1026	11:00 AM	26-Apr-19		FDD Checking of Embankment 10th Layer	321+900	322+100	LHS	MCW	CA	M	Done	
471	VKE-3/PIL/HW/1027	3:00 PM	26-Apr-19		FDD Checking of Embankment 10th Layer	321+720	321+900	LHS	MCW	CA	M	Done	
472	VKE-3/PIL/HW/1028	10:00 AM	26-Apr-19		FDD Checking of Embankment 11th Layer	313+860	314+120	LHS	MCW	CA	M	Done	
473	VKE-3/PIL/HW/1029	4:00 PM	26-Apr-19		FDD Checking of Embankment 9th Layer	312+720	313+080	LHS	MCW	CA	M	Done	
474	VKE-3/PIL/HW/1030	12:00 PM	26-Apr-19		FDD Checking of Embankment 4th Layer	310+700	311+040	BHS	MCW	CA	M	Done	
475	VKE-3/PIL/HW/1031	5:00 PM	26-Apr-19		FDD Checking of Embankment 8th Layer	311+052	311+330	RHS	MCW	CA	M	Done	ie
476	VKE-3/PIL/HW/1032	6:00 PM	26-Apr-19		FDD Checking of Embankment 8th Layer	311+330	311+480	RHS	MCW	CA	M	N/R	
477	VKE-3/PIL/HW/1033	10:30 AM	26-Apr-19		FDD Checking of Embankment 13th Layer	311+670	311+980	LHS	MCW	CA	M	Done	
478	VKE-3/PIL/HW/1034	6:00 PM	26-Apr-19		FDD Checking of Embankment 9th Layer	311+480	311+650	RHS	MCW	CA	M	FAIL	
479	VKE-3/PIL/HW/1035	5:00 PM	26-Apr-19		FDD Checking of Embankment 2nd Layer	319+400	319+500	LHS	MCW	CA	M	Done	
480	VKE-3/PIL/HW/1036	5:30 PM	26-Apr-19		FDD Checking of Embankment 2nd Layer	319+500	319+600	LHS	MCW	CA	M	Done	
481	VKE-3/PIL/HW/1037	5:30 PM	26-Apr-19		FDD Checking of Embankment 7th Layer	308+800	308+900	LHS	MCW	CA	M	Done	
482	VKE-3/PIL/HW/1038	6:00 PM	26-Apr-19		FDD Checking of Embankment 9th Layer	308+900	309+000	LHS	MCW	CA	M	Done	
483	VKE-3/PIL/HW/1039	6:00 PM	26-Apr-19		FDD Checking of Embankment 8th Layer	308+500	308+800	RHS	MCW	CA	M	Done	ie
484	VKE-3/PIL/HW/1040	4:00 PM	27-Apr-19		FDD Checking of Embankment 2nd Layer	293+700	293+800	RHS	MCW	CA	M	FAIL	
485	VKE-3/PIL/HW/1041	5:00 PM	27-Apr-19		FDD Checking of Embankment 3rd Layer	295+700	295+800	RHS	MCW	CA	M	Done	
486	VKE-3/PIL/HW/1042	12:00 PM	27-Apr-19		FDD Checking of Embankment 12th Layer	296+700	297+000	RHS	MCW	CA	M	Done	ie
487	VKE-3/PIL/HW/1043	5:00 PM	27-Apr-19		FDD Checking of Embankment 3rd Layer	297+260	297+360	RHS	MCW	CA	M	N/R	
488	VKE-3/PIL/HW/1044	4:30 PM	27-Apr-19		FDD Checking of Embankment 9th Layer	298+700	298+800	LHS	MCW	CA	M	FAIL	
489	VKE-3/PIL/HW/1045	5:00 PM	27-Apr-19		FDD Checking of Embankment 6th Layer	298+000	298+100	RHS	MCW	CA	M	Done	
490	VKE-3/PIL/HW/1046	5:30 PM	27-Apr-19		FDD Checking of Embankment 6th Layer	301+940	302+100	RHS	MCW	CA	M	Done	
491	VKE-3/PIL/HW/1047	5:50 PM	27-Apr-19		FDD Checking of Embankment 6th Layer	301+940	302+100	LHS					

493	VKE-3/PIL/HW/1049	4:40 PM	27-Apr-19		FDD Checking of Embankment 10th Layer	302+500	302+570	RHS	MCW	CA	M	Done	
494	VKE-3/PIL/HW/1050	5:30 PM	27-Apr-19		FDD Checking of Embankment 4th Layer	309+560	309+700	LHS	MCW	CA	M	N/R	
495	VKE-3/PIL/HW/1051	5:00 PM	27-Apr-19		FDD Checking of Embankment 4th Layer	309+560	309+700	RHS	MCW	CA	M	N/R	ie
496	VKE-3/PIL/HW/1052	4:00 PM	27-Apr-19		FDD Checking of Embankment 11th Layer	314+160	314+280	LHS	MCW	CA	M	N/R	ie
497	VKE-3/PIL/HW/1053	3:00 PM	27-Apr-19		FDD Checking of Embankment 10th Layer	313+100	313+380	LHS	MCW	CA	M	Done	
498	VKE-3/PIL/HW/1054	4:00 PM	27-Apr-19		FDD Checking of Embankment 3rd Layer	318+200	318+500	RHS	MCW	CA	M	Done	
499	VKE-3/PIL/HW/1055	5:00 PM	27-Apr-19		FDD Checking of Embankment 2nd Layer	319+600	319+700	LHS	MCW	CA	M	Done	
500	VKE-3/PIL/HW/1056	5:30 PM	27-Apr-19		FDD Checking of Embankment 2nd Layer	319+700	319+800	LHS	MCW	CA	M	Done	
501	VKE-3/PIL/HW/1057	11:00 AM	27-Apr-19		FDD Checking of Embankment 11th Layer	321+720	321+900	BHS	MCW	CA	M	Done	
502	VKE-3/PIL/HW/1058	4:00 PM	27-Apr-19		FDD Checking of Embankment 11th Layer	321+900	322+100	RHS	MCW	CA	M	Done	
503	VKE-3/PIL/HW/1059	9:30 AM	28-Apr-19		FDD Checking of Embankment 10th Layer	302+500	302+700	LHS	MCW	CA	M	FAIL	
504	VKE-3/PIL/HW/1060	10:00 AM	28-Apr-19		FDD Checking of Embankment 3rd Layer	295+000	295+150	RHS	MCW	CA	M	N/R	
505	VKE-3/PIL/HW/1061	11:00 AM	28-Apr-19		FDD Checking of Embankment 3rd Layer	295+570	295+700	RHS	MCW	CA	M	Done	
506	VKE-3/PIL/HW/1062	10:30 AM	28-Apr-19		FDD Checking of Embankment 10th Layer	302+500	302+570	LHS	MCW	CA	M	N/R	
507	VKE-3/PIL/HW/1063	11:30 AM	28-Apr-19		FDD Checking of Embankment 2nd Layer	293+500	293+700	RHS	MCW	CA	M	Done	
508	VKE-3/PIL/HW/1064	10:30 AM	28-Apr-19		1st Layer of Backfilling with Sand around HPC (A1 & A2)	303+608		LHS	MCW	CA	M	FAIL	
509	VKE-3/PIL/HW/1065	10:30 AM	28-Apr-19		1st Layer of Backfilling with Sand around HPC (A1 & A2)	303+608		RHS	MCW	CA	M	Done	
510	VKE-3/PIL/HW/1066	2:00 PM	28-Apr-19		2nd Layer of Backfilling with Sand around HPC (A1 & A2)	303+608		LHS	MCW	CA	M	Done	
511	VKE-3/PIL/HW/1067	2:00 PM	28-Apr-19		2nd Layer of Backfilling with Sand around HPC (A1 & A2)	303+608		RHS	MCW	CA	M	Done	
512	VKE-3/PIL/HW/1068	5:30 PM	28-Apr-19		FDD Checking of Embankment 3rd Layer	305+800	305+900	LHS	MCW	CA	M	N/R	
513	VKE-3/PIL/HW/1069	6:00 PM	28-Apr-19		FDD Checking of Embankment 2nd Layer	305+430	305+550	LHS	MCW	CA	M	FAIL	
514	VKE-3/PIL/HW/1070	12:00 PM	28-Apr-19		FDD Checking of Embankment 3rd Layer	296+900	297+000	RHS	MCW	CA	M	Done	
515	VKE-3/PIL/HW/1071	5:00 PM	28-Apr-19		FDD Checking of Embankment 5th Layer	296+500	296+900	RHS	MCW	CA	M	Done	
516	VKE-3/PIL/HW/1072	3:00 PM	28-Apr-19		FDD Checking of Embankment 7th Layer	298+400	298+500	RHS	MCW	CA	M	Done	
517	VKE-3/PIL/HW/1073	5:00 PM	28-Apr-19		FDD Checking of Embankment 5th Layer	298+820	299+050	RHS	MCW	CA	M	N/R	
518	VKE-3/PIL/HW/1074	5:00 PM	28-Apr-19		FDD Checking of Embankment 6th Layer	301+940	302+100	LHS	MCW	CA	M	Done	
519	VKE-3/PIL/HW/1075	5:40 PM	28-Apr-19		FDD Checking of Embankment 6th Layer	301+940	302+100	RHS	MCW	CA	M	Done	
520	VKE-3/PIL/HW/1076	10:00 AM	28-Apr-19		FDD Checking of Embankment 3rd Layer	296+000	296+340	RHS	MCW	CA	M	Done	
521	VKE-3/PIL/HW/1077	4:15 PM	28-Apr-19		FDD Checking of Embankment 11th Layer	298+400	298+500	LHS	MCW	CA	M	Done	
522	VKE-3/PIL/HW/1078	11:00 AM	28-Apr-19		FDD Checking of Embankment 11th Layer	321+720	321+900	RHS	MCW	CA	M	Done	
523	VKE-3/PIL/HW/1079	4:00 PM	28-Apr-19		FDD Checking of Embankment 11th Layer	321+720	321+900	LHS	MCW	CA	M	Done	
524	VKE-3/PIL/HW/1080	3:00 PM	28-Apr-19		FDD Checking of Embankment 3rd Layer	317+900	318+200	RHS	MCW	CA	M	Done	
525	VKE-3/PIL/HW/1081	4:30 PM	28-Apr-19		FDD Checking of Embankment 8th Layer	311+052	311+330	RHS	MCW	CA	M	Done	
526	VKE-3/PIL/HW/1082	5:00 PM	28-Apr-19		FDD Checking of Embankment 8th Layer	311+330	311+480	RHS	MCW	CA	M	Done	
527	VKE-3/PIL/HW/1083	5:30 PM	28-Apr-19		FDD Checking of Embankment 9th Layer	311+480	311+650	RHS	MCW	CA	M	Done	
528	VKE-3/PIL/HW/1084	4:00 PM	28-Apr-19		FDD Checking of Embankment 4th Layer	309+560	309+700	LHS	MCW	CA	M	Done	
529	VKE-3/PIL/HW/1085	5:00 PM	28-Apr-19		FDD Checking of Embankment 4th Layer	309+560	309+700	RHS	MCW	CA	M	N/R	
530	VKE-3/PIL/HW/1086	4:00 PM	28-Apr-19		FDD Checking of Embankment 2nd Layer	319+400	319+500	LHS	MCW	CA	M	Done	
531	VKE-3/PIL/HW/1087	2:00 PM	28-Apr-19		FDD Checking of Embankment 2nd Layer	319+500	319+600	LHS	MCW	CA	M	Done	
532	VKE-3/PIL/HW/1088	10:00 AM	29-Apr-19		FDD Checking of Embankment 4th Layer	296+900	297+000	RHS	MCW	CA	M	Done	
533	VKE-3/PIL/HW/1089	5:00 PM	29-Apr-19		FDD Checking of Embankment 5th Layer	296+500	296+600	RHS	MCW	CA	M	N/R	
534	VKE-3/PIL/HW/1090	12:00 PM	29-Apr-19		FDD Checking of Embankment 5th Layer	296+600	296+800	RHS	MCW	CA	M	FAIL	
535	VKE-3/PIL/HW/1091	5:30 PM	29-Apr-19		FDD Checking of Embankment 5th Layer	296+800	296+900	RHS	MCW	CA	M	N/R	
536	VKE-3/PIL/HW/1092	3:00 PM	29-Apr-19		FDD Checking of Embankment 7th Layer	298+400	298+590	RHS	MCW	CA	M	Done	ie
537	VKE-3/PIL/HW/1093	6:00 PM	29-Apr-19		FDD Checking of Embankment 5th Layer	298+820	299+050	RHS	MCW	CA	M	FAIL	
538	VKE-3/PIL/HW/1094	3:30 PM	29-Apr-19		FDD Checking of Embankment 7th Layer	301+940	302+100	LHS	MCW	CA	M	Done	
539	VKE-3/PIL/HW/1095	3:45 PM	29-Apr-19		FDD Checking of Embankment 7th Layer	301+940	302+100	RHS	MCW	CA	M	Done	
540	VKE-3/PIL/HW/1096	4:00 PM	29-Apr-19		FDD Checking of Embankment 10th Layer	302+500	302+570	LHS	MCW	CA	M	Done	
541	VKE-3/PIL/HW/1097	5:15 PM	29-Apr-19		FDD Checking of Embankment 2nd Layer	305+650	306+150	RHS	MCW	CA	M	Done	
542	VKE-3/PIL/HW/1098	3:00 PM	29-Apr-19		FDD Checking of Embankment 3rd Layer	305+550	305+700	LHS	MCW	CA	M	Done	
543	VKE-3/PIL/HW/1099	11:00 AM	29-Apr-19		FDD Checking of Embankment 3rd Layer	302+800	302+980	LHS	MCW	CA	M	N/R	ie
544	VKE-3/PIL/HW/1100	11:30 AM	29-Apr-19		FDD Checking of Embankment 3rd Layer	302+800	302+980	RHS	MCW	CA	M	FAIL	
545	VKE-3/PIL/HW/1101	11:00 AM	29-Apr-19		FDD Checking of Embankment 12th Layer	321+900	322+100	RHS	MCW	CA	M	Done	ie
546	VKE-3/PIL/HW/1102	4:00 PM	29-Apr-19		FDD Checking of Embankment 8th Layer	322+100	322+300	RHS	MCW	CA	M	Done	
547	VKE-3/PIL/HW/1103	12:00 PM	29-Apr-19		FDD Checking of Embankment 3rd Layer	317+700	317+900	RHS	MCW	CA	M	Done	
548	VKE-3/PIL/HW/1104	11:00 AM	29-Apr-19		FDD Checking of Embankment 3rd Layer	318+500	318+560	RHS	MCW	CA	M	Done	
549	VKE-3/PIL/HW/1105	4:00 PM	29-Apr-19		FDD Checking of Embankment 4th Layer	318+400	318+560	LHS	MCW	CA	M	Done	
550	VKE-3/PIL/HW/1106	6:00 PM	29-Apr-19		FDD Checking of Embankment 8th Layer	308+800	308+900	RHS	MCW	CA	M	N/R	
551	VKE-3/PIL/HW/1107	5:30 PM	29-Apr-19		FDD Checking of Embankment 10th Layer	308+900	309+000	RHS	MCW	CA	M	FAIL	
552	VKE-3/PIL/HW/1108	4:00 PM	29-Apr-19		FDD Checking of Embankment 2nd Layer	319+300	319+400	LHS	MCW	CA	M	Done	
553	VKE-3/PIL/HW/1109	3:00 PM	29-Apr-19		FDD Checking of Embankment 9th Layer	311+670	311+980	RHS	MCW	CA	M	Done	
554	VKE-3/PIL/HW/1110	5:00 PM	29-Apr-19		FDD Checking of Embankment 9th Layer	311+980	312+200	RHS	MCW	CA	M	Done	
555	VKE-3/PIL/HW/1111	6:00 PM	29-Apr-19		FDD Checking of Embankment 10th Layer	312+200	312+270	RHS	MCW	CA	M	Done	
556	VKE-3/PIL/HW/1112	11:00 AM	29-Apr-19		FDD Checking of Embankment 8th Layer	308+500	308+800	RHS	MCW	CA	M	Done	
557	VKE-3/PIL/HW/1113	12:00 PM	30-Apr-19		FDD Checking of Embankment 2nd Layer	293+700	293+800	RHS	MCW	CA	M	Done	
558	VKE-3/PIL/HW/1114	4:00 PM	30-Apr-19		FDD Checking of Embankment 3rd Layer	295+800	295+900	RHS	MCW	CA	M	FAIL	
559	VKE-3/PIL/HW/1115	6:00 PM	30-Apr-19		FDD Checking of Embankment 3rd Layer	296+000	296+200	LHS	MCW	CA	M	N/R	
560	VKE-3/PIL/HW/1116	5:00 PM	30-Apr-19		FDD Checking of Embankment 5th Layer	296+800	297+000	RHS	MCW	CA	M	FAIL	
561	VKE-3/PIL/HW/1117	5:30 PM	30-Apr-19		FDD Checking of Embankment 9th Layer	297+000	297+100	LHS	MCW	CA	M	Done	
562	VKE-3/PIL/HW/1118	12:40 PM	30-Apr-19		FDD Checking of Embankment 9th Layer	300+000	300+120	LHS	MCW	CA	M	N/R	
563	VKE-3/PIL/HW/1119	3:40 PM	30-Apr-19		FDD Checking of Embankment 9th Layer	300+460	300+600	LHS	MCW	CA	M	Done	
564	VKE-3/PIL/HW/1120	11:00 AM	30-Apr-19		FDD Checking of Embankment 3rd Layer	302+800	302+980	LHS	MCW	CA	M	N/R	
565	VKE-3/PIL/HW/1121	4:30 PM	30-Apr-19		FDD Checking of Embankment 4th Layer	302+800	302+980	LHS	MCW	CA	M	FAIL	
566	VKE-3/PIL/HW/1122	4:45 PM	30-Apr-19		FDD Checking of Embankment 4th Layer	302+800	302+980	RHS	MCW	CA	M	Done	
567	VKE-3/PIL/HW/1123	3:45 PM	30-Apr-19		FDD Checking of Embankment 4th Layer	302+100	302+150	RHS	MCW	CA	M	Done	
568	VKE-3/PIL/HW/1124	5:30 PM	30-Apr-19		FDD Checking of Embankment 2nd Layer	305+650	306+150	RHS	MCW	CA	M	N/R	
569	VKE-3/PIL/HW/1125	3:00 PM	30-Apr-19		FDD Checking of Embankment 3rd Layer	305+550	305+700	LHS	MCW	CA	M	Done	
570	VKE-3/PIL/HW/1126	3:40 PM	30-Apr-19		FDD Checking of Embankment 8th Layer	300+160	300+440	LHS	MCW	CA	M	FAIL	
571	VKE-3/PIL/HW/1127	10:00 AM	30-Apr-19		Backfilling of Embankment 2nd Layer at A1	303+608		LHS	MCW	CA	M	Done	
572	VKE-3/PIL/HW/1128	10:00 AM	30-Apr-19		Backfilling of Embankment 2nd Layer at A1	303+608		RHS	MCW	CA	M	Done	
573	VKE-3/PIL/HW/1129	10:00 AM	30-Apr-19		Backfilling of Embankment 2nd Layer at A2	303+608		LHS	MCW	CA	M	Done	
574	VKE-3/PIL/HW/1130	10:00 AM	30-Apr-19		Backfilling of Embankment 2nd Layer at A2	303+608		RHS	MCW	CA	M	Done	
575	VKE-3/PIL/HW/1131	2:00 PM	30-Apr-19		Backfilling of Embankment 3rd Layer at A1	303+608		LHS	MCW	CA	M	Done	
576	VKE-3/PIL/HW/1132	2:00 PM	30-Apr-19		Backfilling of Embankment 3rd Layer at A1	303+608		RHS	MCW	CA	M	Done	
577	VKE-3/PIL/HW/1133	2:00 PM	30-Apr-19		Backfilling of Embankment 3rd Layer at A2	303+608		LHS	MCW	CA	M	FAIL	
578	VKE-3/PIL/HW/1134	2:00 PM	30-Apr-19		Backfilling of Embankment 3rd Layer at A2	303+608		RHS	MCW	CA	M	N/R	
579	VKE-3/PIL/HW/1135	4:00 PM	30-Apr-19		FDD Checking of Embankment 12th Layer	321+720	322+100	RHS	MCW	CA	M	Done	
580	VKE-3/PIL/HW/1136	4:00 PM	30-Apr-19		FDD Checking of Embankment 4th Layer	318+200	318+400	LHS	MCW	CA	M	Done	
581	VKE-3/PIL/HW/1137	3:00 PM	30-Apr-19		FDD Checking of Embankment 8th Layer	314+690	314+800	LHS	MCW	CA	M	Done	
582	VKE-3/PIL/HW/1138	4:00 PM	30-Apr-19		FDD Checking of Embankment 12th Layer	312+500	312+670	LHS	MCW	CA	M	Done	
583	VKE-3/PIL/HW/1139	4:30 PM	30-Apr-19		FDD Checking of Embankment 12th Layer	312+500	312+670	RHS	MCW	CA	M	Done	
584	VKE-3/PIL/HW/1140	3:00 PM	30-Apr-19		FDD Checking of Embankment 11th Layer	314+150	314+280	LHS	MCW	CA	M	Done	
585	VKE-3/PIL/HW/1141	10:00 AM	30-Apr-19		CNG & FDD of OGL	322+400	322+500	LHS	MCW	CA	M	Done	
586	VKE-3/PIL/HW/1142	10:30 AM	30-Apr-19		CNG & FDD of OGL	322+400	322+500	RHS	MCW	CA	M	Done	
587	VKE-3/PIL/HW/1143	4:30 PM	30-Apr-19		FDD Checking of Embankment 9th Layer	308+500	308+800	RHS	MCW	CA	M	Done	
588	VKE-3/PIL/HW/1144	5:00 PM	30-Apr-19		FDD Checking of Embankment 4th Layer	309+560	309+700	LHS	MCW	CA	M	N/R	
589	VKE-3/PIL/HW/1145	5:3											

591	VKE-3/PIL/HW/1147	11:00 AM	1-May-19		FDD Checking of Embankment 7th Layer	301+940	302+100	RHS	MCW	CA	M		
592	VKE-3/PIL/HW/1148	5:00 PM	1-May-19		FDD Checking of Embankment 9th Layer	297+100	297+360	LHS	MCW	CA	M		
593	VKE-3/PIL/HW/1149	2:30 PM	1-May-19		FDD Checking of Embankment 5th Layer	302+100	302+150	RHS	MCW	CA	M	Done	
594	VKE-3/PIL/HW/1150	5:30 PM	1-May-19		FDD Checking of Embankment 11th Layer	302+450	302+570	RHS	MCW	CA	M	Done	
595	VKE-3/PIL/HW/1151	5:30 PM	1-May-19		FDD Checking of Embankment 11th Layer	302+450	302+570	LHS	MCW	CA	M	Done	
596	VKE-3/PIL/HW/1152	11:00 AM	1-May-19		FDD Checking of Embankment 8th Layer	300+160	300+420	LHS	MCW	CA	M		
597	VKE-3/PIL/HW/1153	4:30 PM	1-May-19		FDD Checking of Embankment 4th Layer	302+800	302+980	RHS	MCW	CA	M	Done	
598	VKE-3/PIL/HW/1154	5:00 PM	1-May-19		FDD Checking of Embankment 4th Layer	302+800	302+980	LHS	MCW	CA	M	Done	
599	VKE-3/PIL/HW/1155	3:00 PM	1-May-19		FDD Checking of Embankment 3rd Layer	305+700	305+800	LHS	MCW	CA	M	Done	
600	VKE-3/PIL/HW/1156	4:00 PM	1-May-19		FDD Checking of Embankment 4th Layer	317+900	318+200	LHS	MCW	CA	M	Done	
601	VKE-3/PIL/HW/1157	12:00 PM	1-May-19		FDD Checking of Embankment 12th Layer	312+400	312+500	RHS	MCW	CA	M	Done	
602	VKE-3/PIL/HW/1158	12:00 PM	1-May-19		FDD Checking of Embankment 11th Layer	312+290	312+400	RHS	MCW	CA	M	Done	
603	VKE-3/PIL/HW/1159	12:30 PM	1-May-19		FDD Checking of Embankment 15th Layer	311+670	312+020	LHS	MCW	CA	M	Done	
604	VKE-3/PIL/HW/1160	5:00 PM	1-May-19		FDD Checking of Embankment 10th Layer	311+670	311+980	RHS	MCW	CA	M	Done	
605	VKE-3/PIL/HW/1161	4:00 PM	1-May-19		FDD Checking of Embankment 12th Layer	312+720	321+900	LHS	MCW	CA	M		
606	VKE-3/PIL/HW/1162	3:00 PM	1-May-19		FDD Checking of Embankment 2nd Layer	319+300	319+400	LHS	MCW	CA	M		
607	VKE-3/PIL/HW/1163	4:00 PM	1-May-19		FDD Checking of Embankment 2nd Layer	319+400	319+600	LHS	MCW	CA	M		
608	VKE-3/PIL/HW/1164	12:00 PM	1-May-19		FDD Checking of Embankment 8th Layer	308+800	308+900	RHS	MCW	CA	M	Done	
609	VKE-3/PIL/HW/1165	2:00 PM	1-May-19		FDD Checking of Embankment 10th Layer	308+900	309+000	RHS	MCW	CA	M	Done	
610	VKE-3/PIL/HW/1166	3:45 PM	2-May-19		FDD Checking of Embankment 8th Layer	301+940	302+100	RHS	MCW	CA	M	Done	
611	VKE-3/PIL/HW/1167	5:30 PM	2-May-19		FDD Checking of Embankment 8th Layer	301+940	302+100	LHS	MCW	CA	M	Done	
612	VKE-3/PIL/HW/1168	12:00 PM	2-May-19		FDD Checking of Embankment 2nd Layer	305+650	306+150	LHS	MCW	CA	M		
613	VKE-3/PIL/HW/1169	9:30 AM	2-May-19		FDD Checking of Embankment 2nd Layer	293+700	293+900	RHS	MCW	CA	M	Done	
614	VKE-3/PIL/HW/1170	4:00 PM	2-May-19		FDD Checking of Embankment 2nd Layer	293+900	294+080	RHS	MCW	CA	M	Done	
615	VKE-3/PIL/HW/1171	9:00 AM	2-May-19		FDD Checking of Embankment 3rd Layer	295+000	295+150	RHS	MCW	CA	M		
616	VKE-3/PIL/HW/1172	2:00 PM	2-May-19		FDD Checking of Embankment 3rd Layer	295+570	295+900	RHS	MCW	CA	M		
617	VKE-3/PIL/HW/1173	11:00 AM	2-May-19		FDD Checking of Embankment 3rd Layer	296+000	296+200	RHS	MCW	CA	M		
618	VKE-3/PIL/HW/1174	9:00 AM	2-May-19		FDD Checking of Embankment 9th Layer	297+000	297+200	LHS	MCW	CA	M	Done	
619	VKE-3/PIL/HW/1175	4:00 PM	2-May-19		FDD Checking of Embankment 9th Layer	297+230	297+360	LHS	MCW	CA	M		
620	VKE-3/PIL/HW/1176	10:00 AM	2-May-19		FDD Checking of Embankment 5th Layer	296+800	297+000	RHS	MCW	CA	M	Done	
621	VKE-3/PIL/HW/1177	4:00 PM	2-May-19		FDD Checking of Embankment 5th Layer	297+000	297+100	RHS	MCW	CA	M	Done	
622	VKE-3/PIL/HW/1178	4:40 PM	2-May-19		FDD Checking of Embankment 3rd Layer	296+000	296+340	RHS	MCW	CA	M	Done	
623	VKE-3/PIL/HW/1179	3:30 PM	2-May-19		FDD Checking of Embankment 9th Layer	300+000	300+120	LHS	MCW	CA	M		
624	VKE-3/PIL/HW/1180	12:30 PM	2-May-19		FDD Checking of Embankment 3rd Layer	305+550	305+800	LHS	MCW	CA	M	Done	
625	VKE-3/PIL/HW/1181	3:00 PM	2-May-19		FDD Checking of Embankment 2nd Layer	305+800	305+900	RHS	MCW	CA	M		
626	VKE-3/PIL/HW/1182	3:00 PM	2-May-19		FDD Checking of Embankment 9th Layer	300+460	300+530	LHS	MCW	CA	M	Done	
627	VKE-3/PIL/HW/1183	2:00 PM	2-May-19		FDD Checking of Embankment 4th Layer	317+700	317+900	LHS	MCW	CA	M	Done	
628	VKE-3/PIL/HW/1184	12:00 PM	2-May-19		FDD Checking of Embankment 9th Layer	311+050	311+330	RHS	MCW	CA	M	Done	
629	VKE-3/PIL/HW/1185	5:00 PM	2-May-19		FDD Checking of Embankment 9th Layer	311+330	311+480	RHS	MCW	CA	M	Done	
630	VKE-3/PIL/HW/1186	5:30 PM	2-May-19		FDD Checking of Embankment 10th Layer	311+480	311+650	RHS	MCW	CA	M	Done	
631	VKE-3/PIL/HW/1187	6:00 PM	2-May-19		FDD Checking of Embankment 13th Layer	311+480	311+650	LHS	MCW	CA	M		
632	VKE-3/PIL/HW/1188	5:00 PM	2-May-19		FDD Checking of Embankment 5th Layer	318+360	318+560	LHS	MCW	CA	M	Done	
633	VKE-3/PIL/HW/1189	12:00 PM	2-May-19		FDD Checking of Embankment 2nd Layer	309+020	309+350	RHS	MCW	CA	M	Done	
634	VKE-3/PIL/HW/1190	1:00 PM	2-May-19		FDD Checking of Embankment 12th Layer	321+720	321+900	RHS	MCW	CA	M	Done	
635	VKE-3/PIL/HW/1191	2:00 PM	2-May-19		FDD Checking of Embankment 12th Layer	321+720	321+900	LHS	MCW	CA	M	Done	
636	VKE-3/PIL/HW/1192	3:00 PM	2-May-19		FDD Checking of Embankment 12th Layer	321+900	322+100	LHS	MCW	CA	M		
637	VKE-3/PIL/HW/1193	10:00 AM	3-May-19		FDD Checking of Embankment 9th Layer	297+230	297+360	LHS	MCW	CA	M		
638	VKE-3/PIL/HW/1194	11:30 AM	3-May-19		FDD Checking of Embankment 4th Layer	302+800	302+980	LHS	MCW	CA	M	Done	
639	VKE-3/PIL/HW/1195	4:30 PM	3-May-19		FDD Checking of Embankment 5th Layer	302+800	302+980	RHS	MCW	CA	M		
640	VKE-3/PIL/HW/1196	2:30 PM	3-May-19		FDD Checking of Embankment 6th Layer	302+100	302+150	RHS	MCW	CA	M		
641	VKE-3/PIL/HW/1197	10:00 AM	3-May-19		FDD Checking of Embankment 3rd Layer	305+550	305+700	LHS	MCW	CA	M	Done	
642	VKE-3/PIL/HW/1198	10:30 AM	3-May-19		FDD Checking of Embankment 4th Layer	296+000	296+200	LHS	MCW	CA	M		
643	VKE-3/PIL/HW/1199	5:00 PM	3-May-19		FDD Checking of Embankment 6th Layer	296+500	296+600	RHS	MCW	CA	M		
644	VKE-3/PIL/HW/1200	11:30 AM	3-May-19		FDD Checking of Embankment 9th Layer	297+230	297+360	LHS	MCW	CA	M		
645	VKE-3/PIL/HW/1201	5:00 PM	3-May-19		FDD Checking of Embankment 5th Layer	297+000	297+260	RHS	MCW	CA	M		
646	VKE-3/PIL/HW/1202	6:00 PM	3-May-19		FDD Checking of Embankment 2nd Layer	305+430	305+550	LHS	MCW	CA	M		
647	VKE-3/PIL/HW/1203	4:00 PM	3-May-19		FDD Checking of Embankment 9th Layer	300+000	300+120	LHS	MCW	CA	M		
648	VKE-3/PIL/HW/1204	5:00 PM	3-May-19		FDD Checking of Embankment 9th Layer	300+460	300+600	LHS	MCW	CA	M		
649	VKE-3/PIL/HW/1205	11:00 AM	3-May-19		FDD Checking of Embankment 8th Layer	301+940	302+100	RHS	MCW	CA	M		
650	VKE-3/PIL/HW/1206	11:30 AM	3-May-19		FDD Checking of Embankment 2nd Layer	293+900	294+080	RHS	MCW	CA	M		
651	VKE-3/PIL/HW/1207	12:00 PM	3-May-19		FDD Checking of Embankment 13th Layer	312+500	312+670	LHS	MCW	CA	M	Done	
652	VKE-3/PIL/HW/1208	4:00 PM	3-May-19		FDD Checking of Embankment 13th Layer	312+400	312+670	RHS	MCW	CA	M	Done	
653	VKE-3/PIL/HW/1209	6:00 PM	3-May-19		FDD Checking of Embankment 12th Layer	312+290	312+400	RHS	MCW	CA	M	Done	
654	VKE-3/PIL/HW/1210	1:00 PM	3-May-19		FDD Checking of Embankment 5th Layer	318+200	318+560	LHS	MCW	CA	M	Done	
655	VKE-3/PIL/HW/1211	12:00 PM	3-May-19		FDD Checking of Embankment 2nd Layer	309+360	309+500	RHS	MCW	CA	M		
656	VKE-3/PIL/HW/1212	5:30 PM	3-May-19		FDD Checking of Embankment 9th Layer	308+800	308+900	RHS	MCW	CA	M	Done	
657	VKE-3/PIL/HW/1213	6:00 PM	3-May-19		FDD Checking of Embankment 11th Layer	308+900	309+000	RHS	MCW	CA	M		
658	VKE-3/PIL/HW/1214	4:00 PM	3-May-19		FDD Checking of Embankment 12th Layer	320+200	320+300	LHS	MCW	CA	M	Done	
659	VKE-3/PIL/HW/1215	4:30 PM	3-May-19		FDD Checking of Embankment 12th Layer	320+300	320+400	LHS	MCW	CA	M	Done	
660	VKE-3/PIL/HW/1216	4:00 PM	3-May-19		FDD Checking of Embankment 8th Layer	313+450	313+800	LHS	MCW	CA	M	Done	
661	VKE-3/PIL/HW/1217	12:00 PM	3-May-19		FDD Checking of Embankment 3rd Layer	318+500	318+560	RHS	MCW	CA	M	Done	
662	VKE-3/PIL/HW/1218	03:00PM	4-May-19		FDD Checking of Embankment 4th Layer	296+200	296+340	LHS	MCW	CA	M		
663	VKE-3/PIL/HW/1219	05:00PM	4-May-19		FDD Checking of Embankment 6th Layer	296+600	296+700	RHS	MCW	CA	M	Done	
664	VKE-3/PIL/HW/1220	04:00PM	4-May-19		FDD Checking of Embankment 4th Layer	299+800	300+000	RHS	MCW	CA	M		
665	VKE-3/PIL/HW/1221	05:30PM	4-May-19		FDD Checking of Embankment 7th Layer	299+900	300+000	LHS	MCW	CA	M		
666	VKE-3/PIL/HW/1222	12:30PM	4-May-19		FDD Checking of Embankment 9th Layer	300+000	300+120	LHS	MCW	CA	M		
667	VKE-3/PIL/HW/1223	11:00AM	4-May-19		FDD Checking of Embankment 9th Layer	300+540	300+600	LHS	MCW	CA	M		
668	VKE-3/PIL/HW/1224	02:30PM	4-May-19		FDD Checking of Embankment 6th Layer	302+100	302+150	RHS	MCW	CA	M	Done	
669	VKE-3/PIL/HW/1225	06:00PM	4-May-19		FDD Checking of Embankment 2nd Layer	305+900	306+150	RHS	MCW	CA	M		
670	VKE-3/PIL/HW/1226	10:30AM	4-May-19		FDD Checking of Embankment 9th Layer	297+230	297+360	LHS	MCW	CA	M	Done	
671	VKE-3/PIL/HW/1227	12:00PM	4-May-19		FDD Checking of Embankment 2nd Layer	305+800	305+900	RHS	MCW	CA	M	Done	
672	VKE-3/PIL/HW/1228	11:00AM	4-May-19		FDD Checking of Embankment 13th Layer	321+900	322+000	RHS	MCW	CA	M	Done	
673	VKE-3/PIL/HW/1229	04:00PM	4-May-19		FDD Checking of Embankment 12th Layer	321+900	322+100	LHS	MCW	CA	M	Done	
674	VKE-3/PIL/HW/1230	06:00PM	4-May-19		FDD Checking of Embankment 13th Layer	311+480	311+650	LHS	MCW	CA	M		
675	VKE-3/PIL/HW/1231	06:00PM	4-May-19		FDD Checking of Embankment 10th Layer	309+500	309+780	RHS	MCW	CA	M		
676	VKE-3/PIL/HW/1232	03:00PM	4-May-19		FDD Checking of Embankment 5th Layer	317+900	318+200	LHS	MCW	CA	M		
677	VKE-3/PIL/HW/1233	03:30PM	4-May-19		FDD Checking of Embankment 12th Layer	313+860	314+120	LHS	MCW	CA	M		
678	VKE-3/PIL/HW/1234	04:30PM	4-May-19		FDD Checking of Embankment 10th Layer	320+500	320+600	LHS	MCW	CA	M		
679	VKE-3/PIL/HW/1235	02:30PM	4-May-19		FDD Checking of Embankment 4th Layer	317+700	317+900	LHS	MCW	CA	M		
680	VKE-3/PIL/HW/1236	10:30AM	5-May-19		FDD Checking of Embankment 6th Layer	296+500	296+600	RHS	MCW	CA	M	Done	
681	VKE-3/PIL/HW/1237	10:30AM	5-May-19		FDD Checking of Embankment 5th Layer	297+000	297+260	RHS	MCW	CA	M		
682	VKE-3/PIL/HW/1238	05:00PM	5-May-19		FDD Checking of Embankment 2nd Layer	305+430	305+550	LHS	MCW	CA	M		
683	VKE-3/PIL/HW/1239	10:15AM	5-May-19		FDD Checking of Embankment 2nd Layer	293+900	294+080	RHS	MCW	CA	M		
684	VKE-3/PIL/HW/1240	05:00PM	5-May-19		FDD Checking of Embankment 2nd Layer	294+100	294+200	RHS	MCW	CA	M	Done	
685	VKE-3/PIL/HW/1241	12:00PM	5-May-19		FDD Checking of Embankment 4th Layer	297+260	297+360	RHS	MCW	CA	M	Done	
686	VKE-3/PIL/HW/1242	04:30PM	5-May-19		FDD Checking of Embankment 7th Layer	298+000	298+100	RHS	MCW	CA	M	Done	
687	VKE-3/PIL/HW/1243	03:00PM	5-May-19		FDD Checking of Embankment 5th Layer	302+800	302+980	LHS	MCW	CA	M	Done	
688	VKE-3/PIL/HW/1244	05:30PM	5-May-19										

689	VKE-3/PIL/HW/1245	06:00PM	5-May-19		FDD Checking of Embankment 9th Layer	301+940	302+100	RHS	MCW	CA	M		
690	VKE-3/PIL/HW/1246	06:15PM	5-May-19		FDD Checking of Embankment 4th Layer	305+550	305+800	LHS	MCW	CA	M	Done	
691	VKE-3/PIL/HW/1247	12:00pm	5-May-19		FDD Checking of Embankment 5th Layer	302+800	302+980	LHS	MCW	CA	M	Done	
692	VKE-3/PIL/HW/1248	12:40 pm	5-May-19		FDD Checking of Embankment 3rd Layer	300+000	300+080	RHS	MCW	CA	M	Done	
693	VKE-3/PIL/HW/1249	11:30AM	5-May-19		FDD Checking of Embankment 11th Layer	298+400	298+500	LHS	MCW	CA	M		
694	VKE-3/PIL/HW/1250	02:00PM	5-May-19		FDD Checking of Embankment 5th Layer	317+700	317+900	LHS	MCW	CA	M		
695	VKE-3/PIL/HW/1251	03:00PM	5-May-19		FDD Checking of Embankment 3rd Layer	318+500	318+560	RHS	MCW	CA	M		
696	VKE-3/PIL/HW/1252	04:00PM	5-May-19		FDD Checking of Embankment 2nd Layer	319+400	319+600	LHS	MCW	CA	M		
697	VKE-3/PIL/HW/1253	04:30PM	5-May-19		FDD Checking of Embankment 10th Layer	308+600	308+780	RHS	MCW	CA	M	Done	
698	VKE-3/PIL/HW/1254	05:00PM	5-May-19		FDD Checking of Embankment 2nd Layer	319+300	319+400	LHS	MCW	CA	M		
699	VKE-3/PIL/HW/1255	11:00AM	5-May-19		FDD Checking of Embankment 13th Layer	321+720	321+900	RHS	MCW	CA	M	Done	
700	VKE-3/PIL/HW/1256	04:00PM	5-May-19		FDD Checking of Embankment 9th Layer	322+100	322+400	RHS	MCW	CA	M		
701	VKE-3/PIL/HW/1257	05:00PM	5-May-19		FDD Checking of Embankment 11th Layer	311+670	311+980	RHS	MCW	CA	M	Done	
702	VKE-3/PIL/HW/1258	09:00AM	5-May-19		FDD Checking of Embankment 10th Layer	311+480	311+650	RHS	MCW	CA	M	Done	
703	VKE-3/PIL/HW/1259	06:00PM	5-May-19		FDD Checking of Embankment 10th Layer	311+980	311+200	RHS	MCW	CA	M		
704	VKE-3/PIL/HW/1260	06:00PM	5-May-19		FDD Checking of Embankment 11th Layer	312+200	312+270	RHS	MCW	CA	M		
705	VKE-3/PIL/HW/1261	06:30PM	5-May-19		FDD Checking of Embankment 10th Layer	312+052	311+330	RHS	MCW	CA	M		
706	VKE-3/PIL/HW/1262	5:45 PM	6-May-19		FDD Checking of Embankment 6th Layer	296+700	297+000	RHS	MCW	CA	M		
707	VKE-3/PIL/HW/1263	3:30 PM	6-May-19		FDD Checking of Embankment 8th Layer	298+120	298+350	RHS	MCW	CA	M		
708	VKE-3/PIL/HW/1264	2:30 PM	6-May-19		FDD Checking of Embankment 7th Layer	302+100	302+150	RHS	MCW	CA	M		
709	VKE-3/PIL/HW/1265	5:30 PM	6-May-19		FDD Checking of Embankment 6th Layer	302+800	302+980	RHS	MCW	CA	M		
710	VKE-3/PIL/HW/1266	6:30 PM	6-May-19		FDD Checking of Embankment 3rd Layer	305+550	305+800	RHS	MCW	CA	M		
711	VKE-3/PIL/HW/1267	5:45 PM	6-May-19		FDD Checking of Embankment 2nd Layer	305+440	305+550	RHS	MCW	CA	M		
712	VKE-3/PIL/HW/1268	11:00 AM	6-May-19		FDD Checking of Embankment 9th Layer	322+100	322+400	RHS	MCW	CA	M		
713	VKE-3/PIL/HW/1269	4:00 PM	6-May-19		FDD Checking of OGL Layer	321+400	321+700	BHS	MCW	CA	M		
714	VKE-3/PIL/HW/1270	3:00 PM	6-May-19		FDD Checking of Embankment 10th Layer	312+720	313+080	LHS	MCW	CA	M		
715	VKE-3/PIL/HW/1271	2:00 PM	6-May-19		FDD Checking of Embankment 4th Layer	318+200	318+560	RHS	MCW	CA	M		
716	VKE-3/PIL/HW/1272	3:30 PM	6-May-19		FDD Checking of Embankment 10th Layer	311+330	311+480	RHS	MCW	CA	M		
717	VKE-3/PIL/HW/1273	6:00 PM	6-May-19		FDD Checking of Embankment 13th Layer	311+480	311+650	LHS	MCW	CA	M		
718	VKE-3/PIL/HW/1274	4:00 PM	6-May-19		FDD Checking of Embankment 3rd Layer	309+100	309+350	RHS	MCW	CA	M		
719	VKE-3/PIL/HW/1275	5:00 PM	6-May-19		FDD Checking of Embankment 12th Layer	320+400	320+500	LHS	MCW	CA	M		
720	VKE-3/PIL/HW/1276	4:00 PM	6-May-19		FDD Checking of Embankment 10th Layer	311+070	311+330	RHS	MCW	CA	M		
721	VKE-3/PIL/HW/1277	11:00 AM	6-May-19		FDD Checking of Embankment 4th Layer	309+560	309+700	LHS	MCW	CA	M		
722	VKE-3/PIL/HW/1278	11:30 AM	6-May-19		FDD Checking of Embankment 4th Layer	309+560	309+700	RHS	MCW	CA	M		
723	VKE-3/PIL/HW/1279	6:00 PM	6-May-19		FDD Checking of Embankment 11th Layer	308+500	308+780	RHS	MCW	CA	M		
724	VKE-3/PIL/HW/1280	3:40 PM	7-May-19		FDD Checking of Embankment 2nd Layer	294+300	294+400	RHS	MCW	CA	M		
725	VKE-3/PIL/HW/1281	12:45 PM	7-May-19		FDD Checking of Embankment 4th Layer	296+200	296+340	LHS	MCW	CA	M		
726	VKE-3/PIL/HW/1282	4:45 PM	7-May-19		FDD Checking of Embankment 4th Layer	296+000	296+200	RHS	MCW	CA	M		
727	VKE-3/PIL/HW/1283	5:00 PM	7-May-19		FDD Checking of Embankment 6th Layer	297+000	297+100	RHS	MCW	CA	M		
728	VKE-3/PIL/HW/1284	3:30 PM	7-May-19		FDD Checking of Embankment 14th Layer	298+120	298+350	LHS	MCW	CA	M		
729	VKE-3/PIL/HW/1285	3:00 PM	7-May-19		FDD Checking of Embankment 6th Layer	302+800	302+980	LHS	MCW	CA	M		
730	VKE-3/PIL/HW/1286	5:15 PM	7-May-19		FDD Checking of Embankment 10th Layer	301+940	302+100	LHS	MCW	CA	M		
731	VKE-3/PIL/HW/1287	6:00 PM	7-May-19		FDD Checking of Embankment 10th Layer	301+940	302+100	RHS	MCW	CA	M		
732	VKE-3/PIL/HW/1288	6:00 PM	7-May-19		FDD Checking of Embankment 3rd Layer	305+800	305+900	RHS	MCW	CA	M		
733	VKE-3/PIL/HW/1289	3:00 PM	7-May-19		FDD Checking of Embankment 2nd Layer	305+900	306+000	RHS	MCW	CA	M		
734	VKE-3/PIL/HW/1290	12:00 PM	7-May-19		FDD Checking of Embankment 9th Layer	300+540	300+600	LHS	MCW	CA	M		
735	VKE-3/PIL/HW/1291	4:00 PM	7-May-19		FDD Checking of Embankment 9th Layer	322+100	322+400	LHS	MCW	CA	M		
736	VKE-3/PIL/HW/1292	2:00 PM	7-May-19		FDD Checking of Embankment 10th Layer	313+100	313+350	LHS	MCW	CA	M		
737	VKE-3/PIL/HW/1293	6:00 PM	7-May-19		FDD Checking of Embankment 17th Layer	311+070	311+310	LHS	MCW	CA	M		
738	VKE-3/PIL/HW/1294	12:00 PM	7-May-19		FDD Checking of Embankment 10th Layer	311+670	311+980	RHS	MCW	CA	M		
739	VKE-3/PIL/HW/1295	5:30 PM	7-May-19		FDD Checking of Embankment 11th Layer	311+980	312+200	RHS	MCW	CA	M		
740	VKE-3/PIL/HW/1296	6:00 PM	7-May-19		FDD Checking of Embankment 11th Layer	312+200	312+270	RHS	MCW	CA	M		
741	VKE-3/PIL/HW/1297	10:00 AM	7-May-19		FDD Checking of Embankment 4th Layer	318+000	318+200	RHS	MCW	CA	M		
742	VKE-3/PIL/HW/1298	4:00 PM	7-May-19		FDD Checking of Embankment 4th Layer	317+700	318+000	RHS	MCW	CA	M		
743	VKE-3/PIL/HW/1299	9:00 AM	7-May-19		FDD Checking of Embankment 10th Layer	311+330	311+480	RHS	MCW	CA	M		
744	VKE-3/PIL/HW/1300	10:00 AM	7-May-19		FDD Checking of Embankment 4th Layer	311+480	311+650	RHS	MCW	CA	M		
745	VKE-3/PIL/HW/1301	10:00 AM	7-May-19		FDD Checking of Embankment 4th Layer	309+560	309+700	RHS	MCW	CA	M		

Annexure-04 Project photographs



Pipe Laying of HPC at 303+608



Back filling of HPC at 311+329



PCC work of Box Culvert at 304+170



Concrete work of raft PUP at 304+170



Concrete work of Haunch Box culvert at 305+437



Excavation of PUP at 297+900



Concrete work of raft PUP at 304+170



Cage lowering of Pile at Minor Bridge 307+731



Cage lowering of Pile at Major Bridge 302+713



Cage lowering of Pile at Major Bridge 321+253



Concrete pouring of Pile at Major Bridge 321+253



Reinforcement checking of pile cap A2 RHS



Embankment Preparation at 296+300



Embankment Preparation at 309+140



Embankment FDD Checking at 297+000 LHS.



Embankment FDD Checking at 322+100 RHS.



Embankment FDD Checking at 311+670 RHS.



Embankment FDD Checking at 306+700 RHS.



Plate Load Test at 322+450



Dynamic Pile Load Test at Major Bridge 321+253

Project Director (NHAI) Site visit on -04-2019



Team Leader Site visit on 18-04-2019





Utility Status

Electrical Hindrance

Sr. No	Div. Name	Sub-Div. Name	Village Name	Chainage		Description	No. Of Pole	Estimate Status				Remarks
				From	To			DGVCL Submitted	IE Submitted	PD Submitted	RO Submitted	
1	Bharuch	Bharuch (Rural)	Tham	292+875	292+895	ELECTRIC LINE CROSSING	3	Yes	IE reviewed the estimate and recommended to PD for approval of competent authority vide latter no. AA/VKE/NHAI/PVKEPL/011/18-19/USW/074 on dated 13.02.2019			PVKEPL request Supervision Charges vide letter #066 on Dated 01.05.2019
				292+905	293+015	ELECTRIC LINE CROSSING	2					
			Derol	294+780	295+200	ELECTRIC LINE CROSSING	14					
				295+270	295+480	ELECTIRC CROSSING GROSSING	2					
				295+400	295+550	ELECTRIC CORSSING GROSSING	3					
				295+560		ELECTIRC CROSSING GROSSING	3					
				296+080	296+100	ELECTIRC CROSSING GROSSING	5					
			Kelod	301+920		ELECTRIC LINE CROSSING	3					
				302+140	302+230	ELECTRIC LINE CROSSING	2					
				303+770	303+830	ELECTRIC LINE CROSSING	2					
Pipaliya	304+050	304+100	ELECTRIC LINE CROSSING	2								
2	Bharuch	Palej	Tralsa	300+560	300+850	ELECTRIC LINE CROSSING	3	Yes	IE reviewed the estimate and recommended to PD for approval of competent authority vide latter no. AA/VKE/NHAI/PVKEPL/009/18-19/USW/072 on dated 13.02.2019			PVKEPL request Supervision Charges vide letter #066 on Dated 01.05.2019
				300+920		ELECTIRC CROSSING GROSSING	2					
3	Amod	Karela	Kurchan	307+170	307+180	ELECTRIC LINE CROSSING	3	Yes	IE reviewed the estimate and recommended to PD for approval of competent authority vide latter no. AA/VKE/NHAI/PVKEPL/010/18-19/USW/073 on dated 13.02.2019			PVKEPL request Supervision Charges vide letter #066 on Dated 01.05.2019
				310+000	310+080	ELECTRIC LINR CROSSING	2					


HIGH TENSION LINE CROSSING

Sl. No.	Div. Name	Sub-Div. Name	Village Name	Chainage		HT line Nos.	Estimate Status			
				From	To		Getco Submitted	IE Submitted	PD Submitted	RO Submitted
1	Bharuch	Bharuch	Derol	296+350	296+480	6	Estimate Under Progress			
			Karela	308+170	308+230					
				308+300	308+570					
			Tralsa	300+370	300+408		Estimate submitted to NHAI PD	IE reviewed the estimate and recommended to PD for approval of competent authority vide latter no #342 on 01.05.2019		
				300+100	300+020					
			Simltha	312+085	312+480					



Gas Pipe Line Status									
Sl.No.	Owner / Approving Authority	Name of Bridge	No. of Bridges	Location (VME Ch.)	Span Arrangement c/c exp (m)	Revised GAD No.	Letter of Approval	Approval Status	Remarks
1	GAIL GAIL Baroda/ Mr. Hemendra Sharma, Chf Mgr (NG P/L O&M- Undera Gas Station , Growa Refinery Road, Opp. RIL Corporate Office, Undera, Distt. Vadodara-391330 (Gujarat), 0265-2265258/59, hrsharma@gail.co.in	Minor Bridge over Gas Pipe Line (sk 37°) R	3	296+430	1 x 27.846	NHAI/MVE/GPB-296+430/GAD/R1 (Sheet 1 of 2 & Sheet 2 of 2)	Approval Letter No. GAIL/UND/O&M/NHAI-ROB/12 dtd. 05.03.2013 along with Invoice or processing fee and supervision charges vide its no. GAIL\BDA\CONSULTANCY\15\12-13 dtd. 05.03.2013 addressed to PD, NHAI	GADs Approved in principle	NHAI to deposit Supervision Charges and Processing Fee and to execute crossing aggrement for issue of final approval of GADs. Amount Rs. 1,57,304/-
2		Minor Bridge over Gas Pipe Line (sk 20°) R		304+430	1 x 22.687	NHAI/MVE/GPB-304+430/GAD/R1 (Sheet 1 of 2 & Sheet 2 of 2)			
3		Minor Bridge over Gas Pipe Line (sk 55°) R		309+070	1 x 45.20	NHAI/MVE/GPB-309+790/GAD/R1 (Sheet 1 of 2 & Sheet 2 of 2)			
4	GSPL GSPL Pipeline/ Mr. Chinmay Tripathi, AGM, (O&M)- Phaguthan Terminal, Post: Haldar, Opp. GPEC Power Plant, Dist. Bharuch-392210. chinmay@gspc.in, Cell No.- 09825035755, Tel: 02642-288650, 288889.	Minor Bridge over Gas Pipe Line (sk 69°) R	1	310+732	1 x 21.35	NHAI/MEV/GPB-310+732/GAD/RO, (Sheet 1 of 2 & Sheet 2 of 2)	Approval Letter No. GSPL/O&M/RoU/MVE/2.4.2/140213/01 dtd. 14.02.13 addressed to PD, NHAI- Forwarded to ICT vide PD Letter No. "NHAI/PIU-Surat(Expressway)/2103/51-1/2013/51-2/625 DTD. 15.02.2013	GADs Approved	No action required.

Sl. No.	Division	Sub-Division	Chainage	Status	Remarks
Water Pipeline					
1	GWSSB Executive Engineer Public Health Works Division Bharuch	Jambusar	–	1) Estimated Received. (2) PD,Surat has written vide letter no. NHA/PIU-SURAT/P-3/2019/51-utility/524 to Executive Enginner for Submit revised estimate because estimate are very old.	–
2		Bharuch	–		–


MNB - CH:307+733 (LHS)

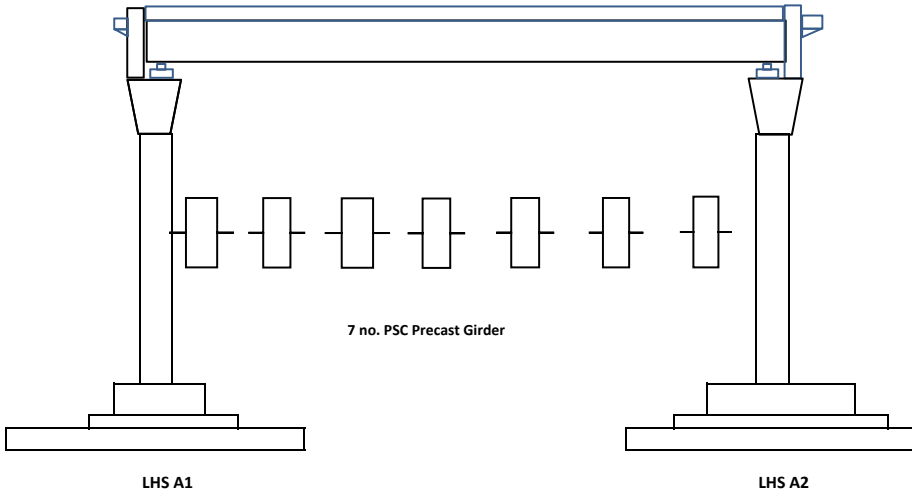


	Slab
	PSC Girder
	RCC Girder
	Dirt Wall
	Pedestal
	Abutment Cap
	Final lift
	Lift-4
	Lift-3
	Lift-2
	Lift-1
	Pile cap
	Pile Cap PCC
	Pile
	Excavation
	Work not started




MNB - CH: 307+733 (RHS)

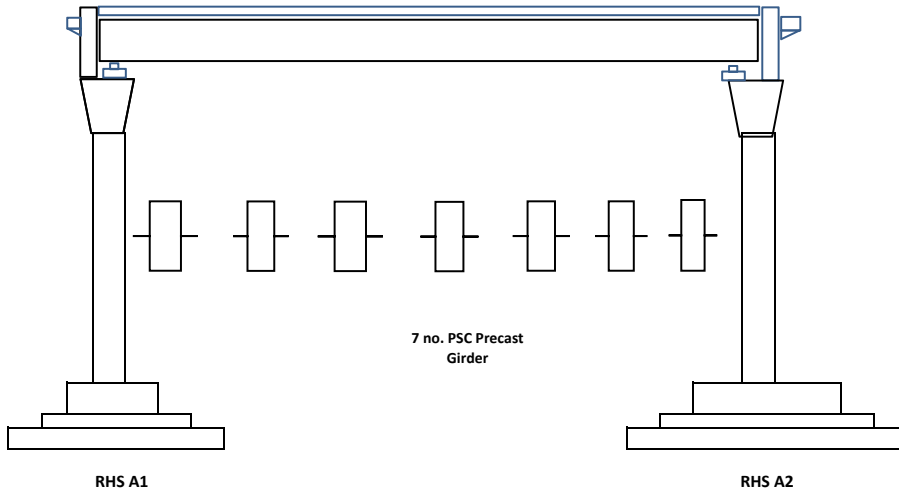

	Slab
	PSC Girder
	RCC Girder
	Dirt Wall
	Pedestal
	Abutment Cap
	Final lift
	Lift-4
	Lift-3
	Lift-2
	Lift-1
	Pile cap
	Pile Cap PCC
	Pile
	Excavation
	Work not started



MJB - CH: 302+713 (LHS)

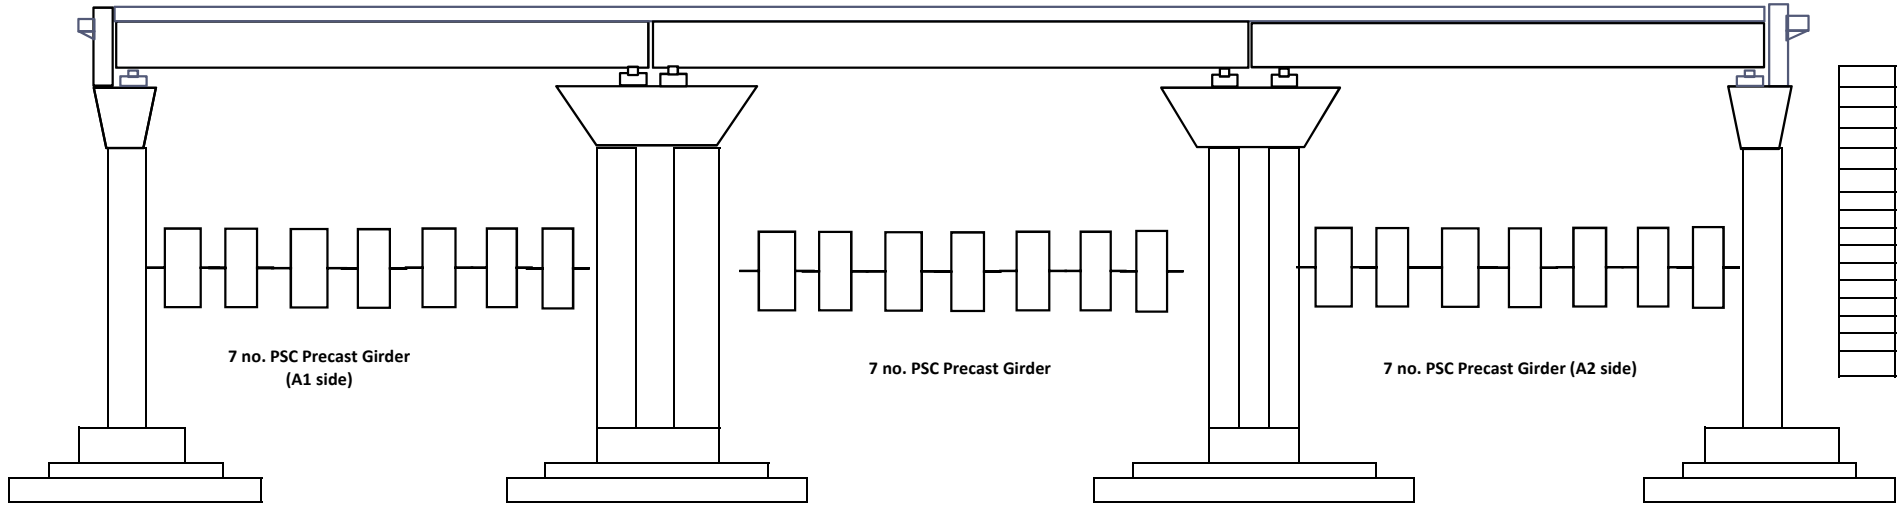




	Slab
	PSC Girder
	RCC Girder
	Dirt Wall
	Pedestal
	Abutment Cap
	Final lift
	Lift-4
	Lift-3
	Lift-2
	Lift-1
	Pile cap
	Pile Cap PCC
	Pile
	Excavation
	Work not started

LHS A1


LHS P1

LHS P2

LHS A2

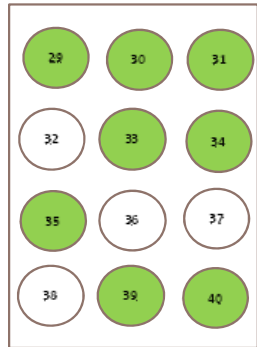

MJB - CH: 302+713 (RHS)



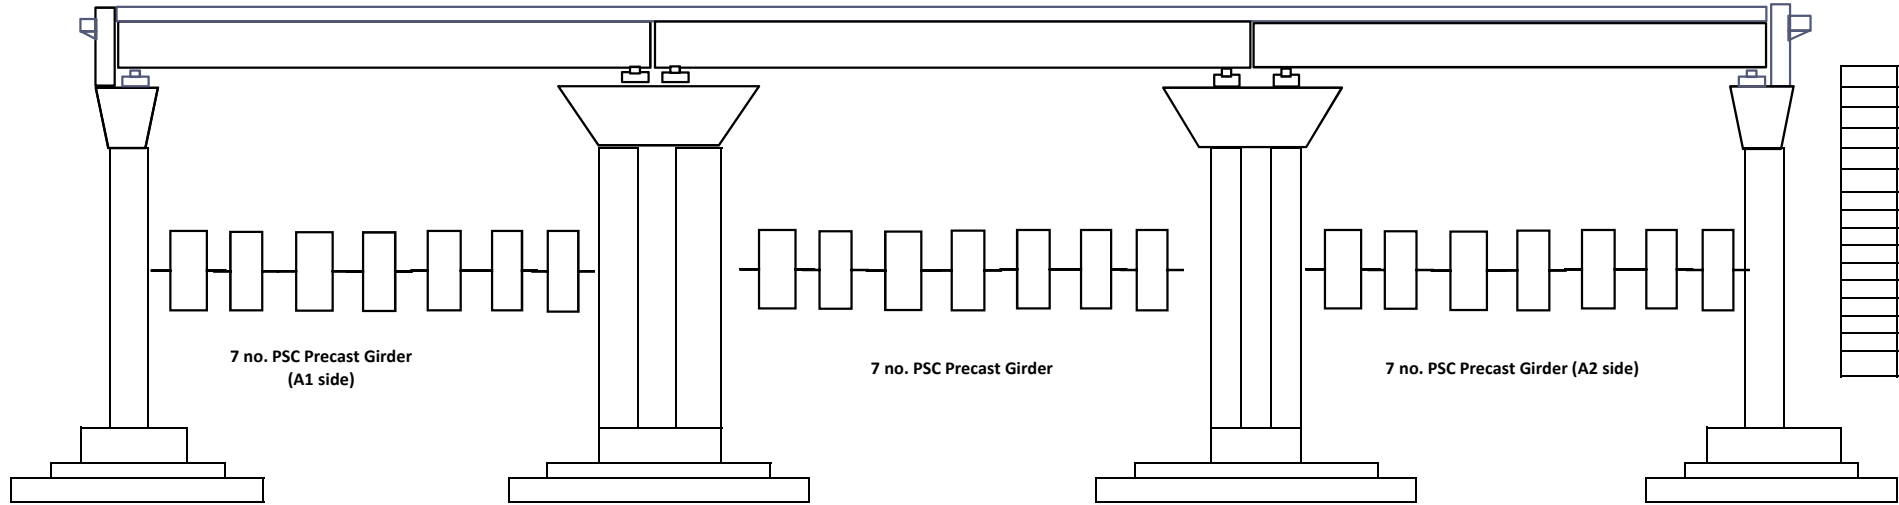


RHS A1




RHS P1

RHS P2


RHS A2

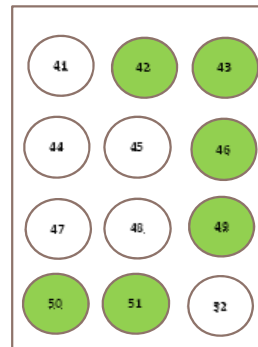

MJB - CH: 321+253 (RHS)

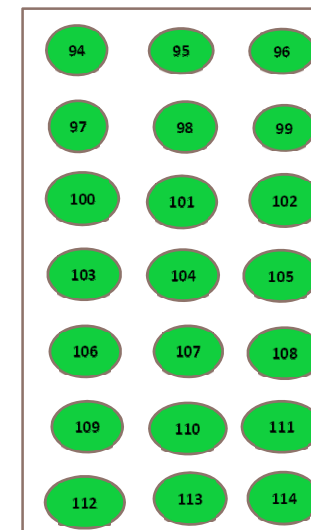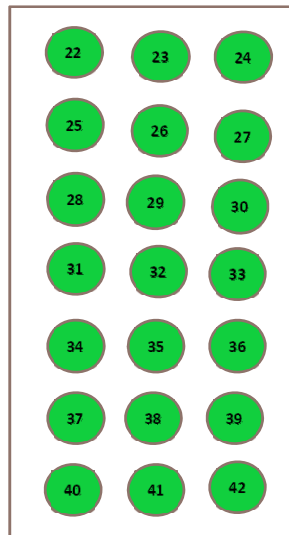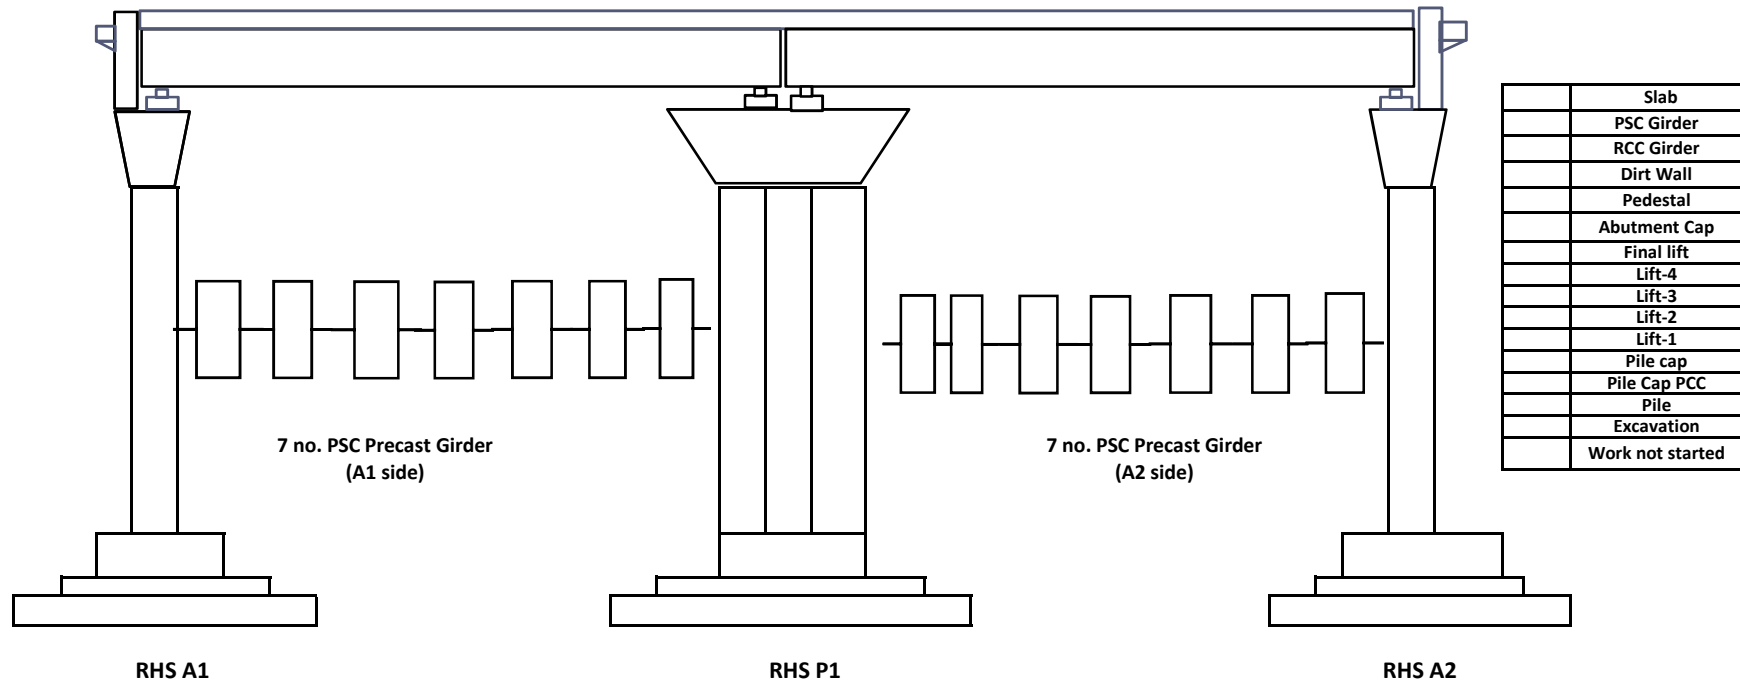

MJB - CH: 321+253 (LHS)

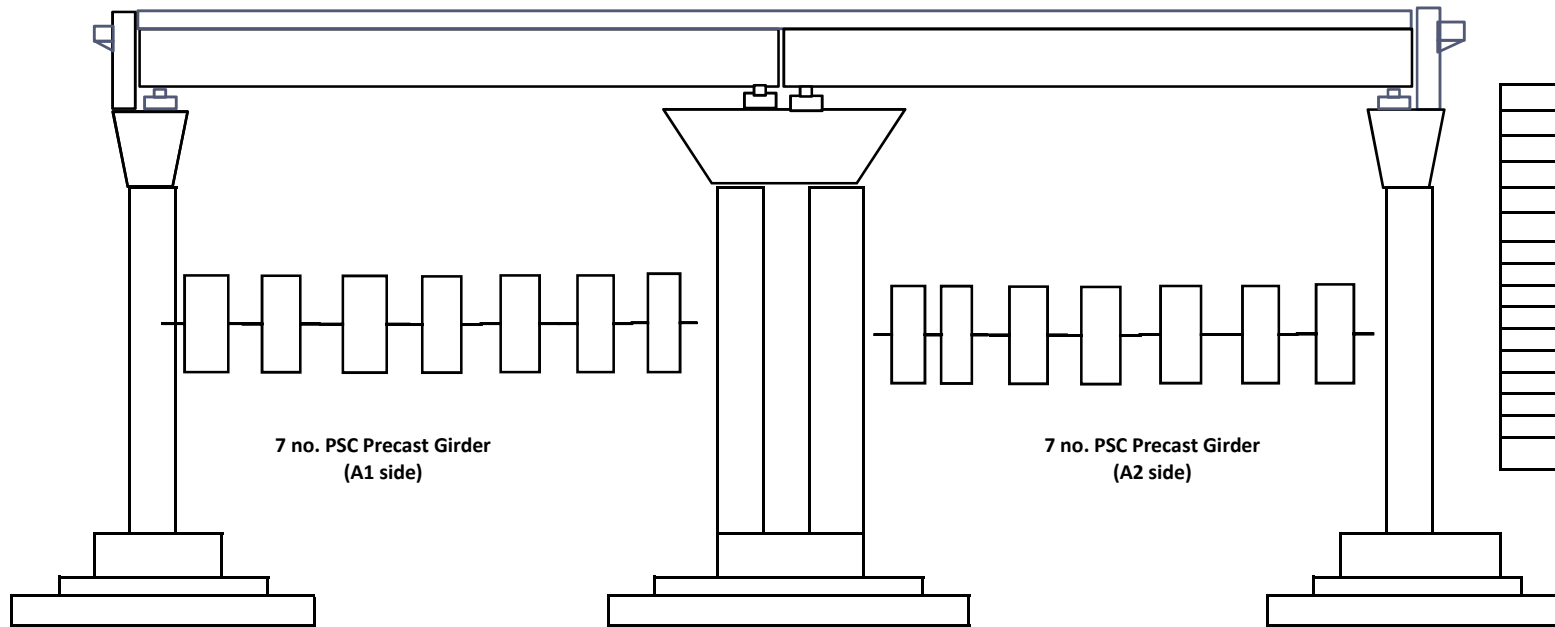

	Slab
	PSC Girder
	RCC Girder
	Dirt Wall
	Pedestal
	Abutment Cap
	Final lift
	Lift-4
	Lift-3
	Lift-2
	Lift-1
	Pile cap
	Pile Cap PCC
	Pile
	Excavation
	Work not started

LHS A1

LHS P1

LHS A2

